

February 12, 2010



Mr. Christopher Meyer  
CEC Project Manager  
Attn: Docket No. 08-AFC-13  
California Energy Commission  
1516 Ninth Street  
Sacramento, CA 95814-5512

Mr. Jim Stobaugh  
BLM Project Manager  
Attn: Docket No. 08-AFC-13  
Bureau of Land Management  
P.O. Box 12000  
Reno, NV 89520

<b>DOCKET</b>	
<b>08-AFC-13</b>	
DATE	<u>FEB 12 2010</u>
RECD.	<u>FEB 16 2010</u>

RE: Calico Solar (Formerly Solar One) Project  
Applicant's Submittal of the Calico Solar Construction Milestone Schedule and Project Layout Figure

Dear Mr. Meyer and Mr. Stobaugh,

Tessera Solar hereby submits the Applicant's Construction Milestone Schedule and Project Layout Figure for the Calico Solar Project. I certify under penalty of perjury that the foregoing is true, correct, and complete to the best of my knowledge.

Sincerely,


Felicia Bellows  
Vice President of Development

## Calico Solar Construction Schedule – Major Milestones

Activity	Time Frame
Phase I	
Start Phase I Construction	October 2010
Fence Installation	October 2010
All tortoise within Phase I translocated <5 km; potentially complete clearance surveys and translocations for tortoises outside of Phase I	October 2010
Begin Road Preparation and Dust Control	November 2010
Begin to bury electrical lines, hydrogen lines and start Transmission Pole Placement	November 2010
Begin construction of the series of transformers for each group of SunCatchers	November 2010
Complete Main Services Complex Construction – including evaporation ponds, if needed	May 2011
Substation Infrastructure (first two-fifths)	June 2011
Onsite Transmission Lines (first Circuit)	June 2011
First Units Online	July 2011
Waterline Construction Completed	June 2011
Start debris basins North of Project	July 2011
Complete Bridge Construction	October 2011
SunCatcher Assembly Complete	August 2012
Complete series of transformers for each group of 60 SunCatchers	August 2012
Final Road Preparation and Dust Control	June 2013
Phase I Construction Complete	June 2013
Phase II	
Begin desert tortoise clearance surveys and disease testing for Phase II area, complete eligible translocations	March 2011
Continue desert tortoise clearance surveys and disease testing for Phase II area, complete eligible translocations	September 2011
If necessary, complete all desert tortoise translocations	March 2012
Start Phase II Construction	June 2013
Begin Road Preparation and Dust Control	June 2013
Begin to bury electrical lines, hydrogen lines and start Transmission Pole Placement	June 2013
Begin construction of the series of transformers for each group of SunCatchers	June 2013
Onsite Transmission (second circuit)	December 2013
Remaining Substation Infrastructure	December 2013
Complete series of transformers for each group of 60 SunCatchers	August 2015
SunCatcher Assembly Complete	August 2015
All Construction Complete	August 2015

Please also see attached Project Layout figure showing Phase I and Phase II boundaries

Path: G:\gis\projects\137127658\100\mxd\project\_layout.mxd, 02/09/10, Lisa Garvey

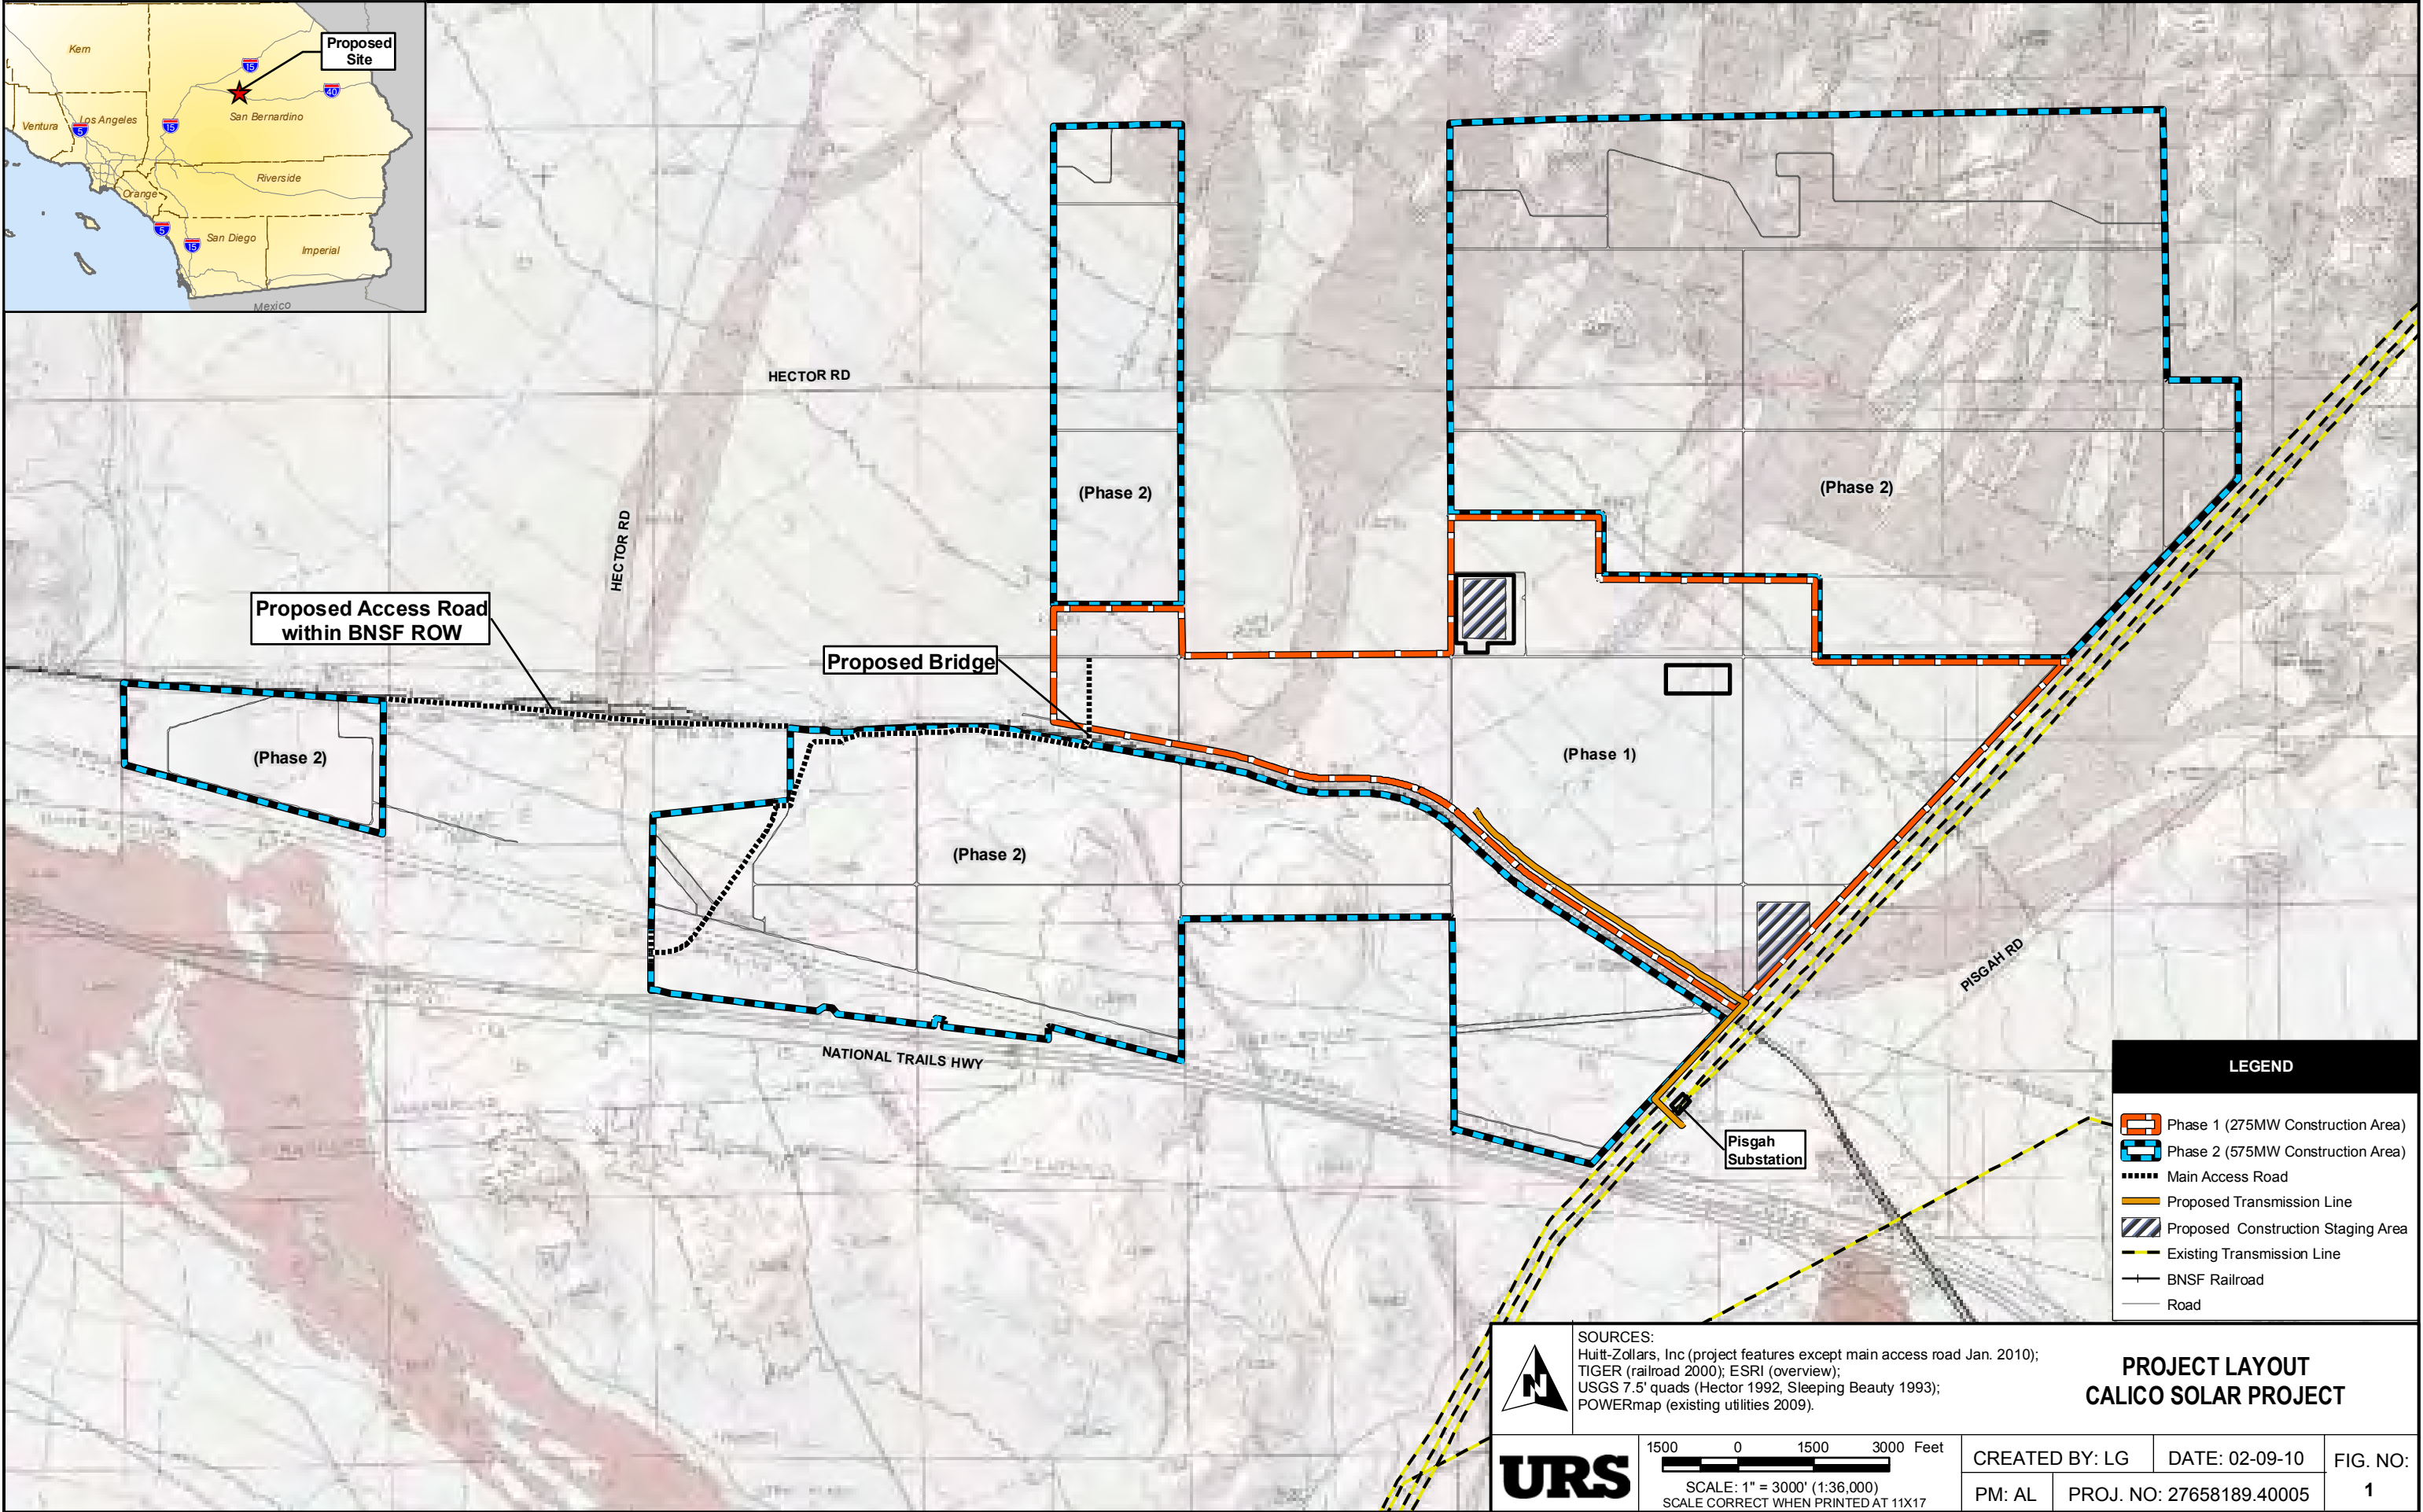



**BEFORE THE ENERGY RESOURCES CONSERVATION AND DEVELOPMENT  
COMMISSION OF THE STATE OF CALIFORNIA  
1516 NINTH STREET, SACRAMENTO, CA 95814  
1-800-822-6228 – WWW.ENERGY.CA.GOV**

**APPLICATION FOR CERTIFICATION  
For the SES SOLAR ONE PROJECT**

**Docket No. 08-AFC-13**

**PROOF OF SERVICE**

*(Revised 12/2/09)*

**APPLICANT**

Felicia Bellows,  
Vice President of Development  
Tessera Solar  
4800 North Scottsdale Road,  
Ste. 5500  
Scottsdale, AZ 85251  
[felicia.bellows@tesseractosolar.com](mailto:felicia.bellows@tesseractosolar.com)

Camille Champion  
Project Manager  
Tessera Solar  
4800 North Scottsdale Road,  
Suite 5500  
Scottsdale, AZ 85251  
[camille.champion@tesseractosolar.com](mailto:camille.champion@tesseractosolar.com)

**CONSULTANT**

**\*Angela Leiba**  
**AFC Project Manager**  
**URS Corporation**  
**1615 Murray Canyon Rd.,**  
**Ste. 1000**  
**San Diego, CA 92108**  
[Angela\\_Leiba@URSCorp.com](mailto:Angela_Leiba@URSCorp.com)

**APPLICANT'S COUNSEL**

Allan J. Thompson  
Attorney at Law  
21 C Orinda Way #314  
Orinda, CA 94563  
[allanori@comcast.net](mailto:allanori@comcast.net)

**INTERESTED AGENCIES**

California ISO  
[e-recipient@caiso.com](mailto:e-recipient@caiso.com)

Jim Stobaugh  
BLM – Nevada State Office  
P.O. Box 12000  
Reno, NV 89520  
[jim\\_stobaugh@blm.gov](mailto:jim_stobaugh@blm.gov)

Rich Rotte, Project Manager  
Bureau of Land Management  
Barstow Field Office  
2601 Barstow Road  
Barstow, CA 92311  
[Richard\\_Rotte@blm.gov](mailto:Richard_Rotte@blm.gov)

Becky Jones  
California Department of  
Fish & Game  
36431 41st Street East  
Palmdale, CA 93552  
[dfgpalm@adelphia.net](mailto:dfgpalm@adelphia.net)

**INTERVENORS**

California Unions for Reliable  
Energy (CURE)  
Loulana A. Miles,  
Marc D. Joseph  
Adams Broadwell Joseph &  
Cardozo  
601 Gateway Boulevard,  
Ste. 1000  
South San Francisco, CA 94080  
[lmiles@adamsbroadwell.com](mailto:lmiles@adamsbroadwell.com)

Defenders of Wildlife  
Joshua Basofin  
1303 J Street, Suite 270  
Sacramento, California 95814  
e-mail service preferred  
[jbasofin@defenders.org](mailto:jbasofin@defenders.org)

Basin and Range Watch  
Laura Cunningham  
Kevin Emmerich  
P.O. Box 70  
Beatty, NV 89003  
[atomicoadranch@netzero.net](mailto:atomicoadranch@netzero.net)

Patrick C. Jackson  
600 N. Darwood Avenue  
San Dimas, CA 91773  
e-mail service preferred  
[ochsjack@earthlink.net](mailto:ochsjack@earthlink.net)

**ENERGY COMMISSION**

JAMES D. BOYD  
Vice Chair and Presiding Member  
[jboyd@energy.state.ca.us](mailto:jboyd@energy.state.ca.us)

JEFFREY D. BYRON  
Commissioner and Associate Member  
[jbyron@energy.state.ca.us](mailto:jbyron@energy.state.ca.us)

Paul Kramer  
Hearing Officer  
[pkramer@energy.state.ca.us](mailto:pkramer@energy.state.ca.us)

Caryn Holmes, Staff Counsel  
1516 9<sup>th</sup> Street, MS-14  
Sacramento, California 95814  
[cholmes@energy.state.ca.us](mailto:cholmes@energy.state.ca.us)

Christopher Meyer  
Project Manager  
[cmeyer@energy.state.ca.us](mailto:cmeyer@energy.state.ca.us)

Public Adviser  
[publicadviser@energy.state.ca.us](mailto:publicadviser@energy.state.ca.us)

## DECLARATION OF SERVICE

I Corinne Lytle, declare that on February 12, 2010, I served and filed copies of the attached Applicant's Submittal of Construction Milestones and Project Layout. The original document, filed with the Docket Unit, is accompanied by a copy of the most recent Proof of Service list, located on the web page for this project at:

**[[www.energy.ca.gov/sitingcases/solarone](http://www.energy.ca.gov/sitingcases/solarone)].**

The documents have been sent to both the other parties in this proceeding (as shown on the Proof of Service list) and to the Commission's Docket Unit, in the following manner:

**(Check all that Apply)**

**FOR SERVICE TO ALL OTHER PARTIES:**

sent electronically to all email addresses on the Proof of Service list;

by personal delivery or by depositing in the United States mail at \_\_\_\_\_ with first-class postage thereon fully prepaid and addressed as provided on the Proof of Service list above to those addresses **NOT** marked "email preferred."

**AND**

**FOR FILING WITH THE ENERGY COMMISSION:**

sending an original paper copy and one electronic copy, mailed and emailed respectively, to the address below (**preferred method**);

~~OR~~\_\_\_\_\_

depositing in the mail an original and 12 paper copies, as follows:

**CALIFORNIA ENERGY COMMISSION**

Attn: Docket No. 08-AFC-13  
1516 Ninth Street, MS-4  
Sacramento, CA 95814-5512  
[docket@energy.state.ca.us](mailto:docket@energy.state.ca.us)

I declare under penalty of perjury that the foregoing is true and correct.

Original signed by

Corinne Lytle
