

Preliminary Draft Plan

**Drainage, Erosion, and Sediment
Control Plan**

Victorville 2 Hybrid Power Plant

City of Victorville, California
(07-AFC-01)

Submitted to the:
California Energy Commission

Submitted by:
Inland Energy, LLC
With Technical Assistance by:
Bibb and Associates
Lenexa, Kansas
July 2007

Contents

Section	Page
1. Introduction.....	1-1
1.1 Drainage, Erosion, and Sediment Control Plan Elements	1-1
1.2 Project Overview	1-2
1.3 Watercourses and Critical Areas	1-3
1.4 Project Ownership	1-4
2. Drainage	2-1
3. Clearing and Grading	3-1
3.1 Areas to be Cleared and Graded	3-1
3.2 Location of Disposal Areas, Fills, or Other Special Areas	3-1
3.3 Existing and Proposed Topography	3-1
3.4 Volumes of Cut and Fill.....	3-1
3.4.1 Gas Pipeline.....	3-1
3.4.2 Water Pipelines	3-2
4. Best Management Practices	4-1
4.1 General Erosion Control Measures	4-1
4.1.1 Access Road, Entrance and Parking, and Laydown Areas.....	4-2
4.1.2 WCEP Site and Linear Facilities	4-3
4.1.3 Foundations.....	4-4
4.1.4 Site Stabilization and Demobilization.....	4-4
4.2 Other Controls.....	4-4
4.2.1 Material Handling and Storage	4-4
4.2.2 Solid and Hazardous Waste Management.....	4-5
4.2.2 Potential Contaminated Soil	4-6
4.2.3 Groundwater/Dewatering Controls.....	4-6
4.2.4 Offsite Vehicle Tracking	4-7
4.2.5 Dust Suppression and Control	4-7

Drawings

1A, 1B, 1C	Regional Location and Project vicinity
2	VICTORVILLE 2 Site Delineation
3	VICTORVILLE 2 Watercourses and Critical Areas
4A, 4B	Drainage Map
5A, 5B	Clearing and Grading Plans

Appendixes

A	Pre- and Post-Construction Drainage Plans
B	Drainage Calculations
C	Best Management Practices

SECTION 1

Introduction

This Preliminary Draft Drainage, Erosion, and Sediment Control Plan (DESCP) has been prepared in anticipation of the California Energy Commission's (CEC) approval of the proposed Victorville 2 Hybrid Power Plant (Victorville 2) Project (07-AFC-01). The Victorville 2 plant includes two natural gas-fired combustion turbine-generators rated at 154 MW each, two heat recovery steam generators, one steam turbine-generator rated at 268 MW, and 250 acres of parabolic solar-thermal collectors with associated heat transfer equipment. The solar-thermal collectors would contribute up to 50 MW of the steam turbine generator's 268 MW output, and with plant auxiliary loads of about 13 MW, Victorville 2's net output would be 563 MW. The plant is located in the City of Victorville, San Bernardino County, California. This preliminary draft DESCP, prepared in response to CEC Staff Data Request #83. In order "to determine the potential impacts to water and soil resources from the construction and operation of the Victorville 2 Energy Center project, the Energy Commission requires a draft and final Drainage Erosion and Sediment Control Plan (DESCP). The DESCP would be updated and revised as the project moves from the preliminary to final design phases and would be a separate document from the Construction Storm Water Pollution Prevention Plan (SWPPP). The DESCP submitted prior to site mobilization must be designed and sealed by a professional engineer/erosion control specialist.

Among staff's specific drainage and erosion concerns is that the solar field would create approximately 250 acres of exposed soil with a high erosion potential, and absent vegetative cover, would need some other form of maintainable erosion control protection. In addition, the project would alter natural drainage and swale features that currently cross the site, and could affect beneficial uses of natural flows.

This draft DESCP is preliminary because it is prepared in advance of the final phase of construction planning and engineering design, during which the details regarding construction schedule and certain aspects of erosion control design will be finalized. This will take place after licensing and will be included in a future draft of the DESCP. This document contains placeholders for some of these future items (detailed schedule, final BMP map).

1.1 Drainage, Erosion, and Sediment Control Plan Elements

CEC Data Request #83 requests a draft DESCP "outlining site management activities to be implemented during site mobilization, excavation, and construction." This draft DESCP includes the following elements:

Vicinity Map – A map at minimum scale 1"=100' indicating the location of all project elements with depictions of all significant geographic features including swales, storm drains, and sensitive areas.

Site Delineation – All areas subject to soil disturbance for the Victorville 2 project (project site, laydown/demolition areas, all linear facilities, landscaping areas, and any other project elements) are delineated showing boundary lines of all construction/demolition areas and the location of all existing and proposed structures, pipelines, roads, and drainage facilities.

Watercourses and Critical Areas – The DESCP shows the location of all nearby watercourses including swales, storm drains, and drainage ditches, as well as their proximity to the Victorville 2 project site.

Drainage – The DESCOP provides a topographic site map at a scale of 1"=100' showing all existing, interim and proposed drainage systems and drainage area boundaries. On the map, spot elevations shown where relatively flat conditions exist.

Clearing and Grading – The DESCOP provides a delineation of all areas to be cleared of vegetation and areas to be preserved. The plan provides elevations, slopes, locations, and the extent of all proposed grading as shown by contours. Existing and proposed topography are tied together.

Best Management Practices – The DESCOP describes the location, timing, and maintenance schedule of BMPs to be used. Final design and placement of the BMPs will take place during the final phase of construction planning after licensing.

1.2 Project Overview

Victorville 2 will be a 563 MW facility consisting of two natural gas fired turbine generators, one steam turbine generator, and two hundred and fifty (250) acres of solar thermal collectors. The facility will be located near the intersection of Helendale Road and Colusa Road in the City of Victorville, San Bernardino County, California. Figure 1 shows the vicinity map of the Project (all drawings are located at the end of this report). Figure 2 shows the Project site and linear facilities locations. The parcel is a total of roughly two hundred and seventy five (275) acres of mostly undeveloped land. The land cover consists of sandy soil and various small brush. Victorville 2 will be located in an area zoned for industrial uses.

Figure 3 shows the project site plan, watercourses, and electric transmission line, as well as a map of nearby rivers and streams. Victorville 2 will connect to the electrical transmission station through a transmission line leading away from the southeast corner of the site in a southeasterly direction. The Project will receive natural gas through a pipeline that travels beneath Colusa Road. The Project will comply with all local, state, and federal regulatory requirements associated with the protection of water quality and soil resources.

1.3 Watercourses and Critical Areas

The project is located within the Mojave River Watershed (MRW). Characteristics of the site are that only natural swales exist, and there are no drainage ditches or storm drains on site. There are no significant creeks. The Mojave River runs north and south roughly 1 mile east of the site.

1.4 Project Ownership

Victorville 2 will be owned by Inland Energy.

SECTION 2 Drainage

The existing topographic conditions of the Victorville 2 Project site depict an average slope of one percent toward the north. Moreover, a ridgeline located in the middle of the site causes the surface runoff to flow to the west or east of the site. The east side of the proposed site

has a steep slope of 7 to 12 percent to the east, while the west side slopes at 0.8 to 1 percent to the west.

For purposes of developing drainage plans for the Project site, the Power Block (the roughly 25-acre area of the overall site where the combined-cycle generating equipment will be located) and the Solar Field (the remaining approximately 250 acres of the site) were divided into independent drainage systems. Each area has its own discharge location. The Solar Field will discharge along the entire length of the north side of the development area, while the Power Block will discharge through the outlet pipe of the Sediment Retention Facility (see Drawings 4A and 4B which illustrate the conceptual drainage plans).

The Power Block Area, located at the southeast corner of the property, is situated at the high point of the existing site. The Power Block Area will drain to the north and south by means of sheet flow, swales, inlets, and/or storm sewer pipes. At the north and south sides of the Power Block the runoff will be intercepted by a system of channels, culverts and/or storm sewers that will convey the storm water to the east. The storm water runoff will then be discharged into the Sediment Retention Facility located on the east side of the Power Block Area.

The Solar Field will be graded at a 0.5 percent slope and storm water will drain to the north. The small slope will keep storm water flow rates low, thus minimizing the amount of sediments picked up by the runoff. In addition, applying a dust-controlling agent such as Dirt Glue or a similar product will stabilize sediments in the solar field.

The Sediment Retention Facility and all other Project drainage features are designed to contain and/or convey the 100-year frequency return storm as specified on page 1 of the City of Victorville's, Standard Specifications for Public Improvements (City of Victorville, 1976)¹ and in section A.2 of the San Bernardino County Hydrology Manual (County of San Bernardino, 1986).² Table 2.1 shows precipitation and discharge data for 2-year and 100-year storm events for predevelopment and post development conditions for both the Power Block and Solar Field areas. These data provide the basis for sizing the Sediment Retention Facility shown on Drawings 4A and 4B. The objective was to size the Sediment Retention Facility and outfall structure such that the discharge from the facility will not exceed the predevelopment conditions. It should be noted that the current design approach is based on preliminary assumptions and may require modifications during final design; however, the design concept will remain the same.

The peak flow rates shown on Table 2.1 were determined using a computer aided, watershed modeling software called Hydraflow Hydrographs. This program utilizes the Natural Resources Conservation Service's TR-55 methods. Precipitation data and soil group information were obtained from the San Bernardino County Hydrology Manual.

¹ City of Victorville, California Standard Specifications for Public Improvements. Victorville, 1976.

² Williamson and Schmid, Civil Engineers, Irvine, California. County of San Bernardino Hydrology Manual. Irvine, 1986.

**Table 2.1
Hydrologic Analyses for Predevelopment and Post Development
Conditions**

	Power Block Predevelopment	Power Block Post Development	Solar Field Predevelopment	Solar Field Post Development
Area	25.85 acres	25.85 acres	250.14 acres	250.14 acres
Curve Number³	75	97	75	75
Precipitation - 2-Year Storm	1.2 inches	1.2 inches	1.2 inches	1.2 inches
Precipitation - 100-Year Storm	3.5 inches	3.5 inches	3.5 inches	3.5 inches
Discharge - 2-Year Storm	0.16 cfs (cubic feet/sec)	18.09 cfs	1.53 cfs	1.53 cfs
Discharge - 100-Year Storm	13.65 cfs	60.93 cfs	67.71 cfs	67.71 cfs

One purpose of the Sediment Retention Facility is to provide the capacity to make up the difference between the pre- and post development runoff conditions. The facility also provides detention time; which allows sediments to settle out of the runoff before it is discharged to the existing drainage features. The design of the proposed Sediment Retention Facility was based on document SE-2 of the California Stormwater BMP Handbook – Construction (California Stormwater BMP, 2003)⁴ and the San Bernardino County Hydrology Manual.⁵ The Sediment Retention Facility is protected from erosion by placing riprap stone at all runoff entrance points to the facility. The riprap stone is placed from the discharge point and is continued down the slope to at least the bottom of the facility.

The Sediment Retention Facility will have at least 3 feet of freeboard above the 100-year storm event. The berm of the facility will be protected against storms greater than the 100-year event by a riprap lined emergency overflow spillway. The outlet structure for the Sediment Retention Facility will consist of a concrete riser with a grated opening on top, a small orifice near the bottom, and an outlet pipe to direct the flow to the existing ground. The existing ground at the discharge point of the outlet pipe will be protected from erosion using riprap stone.

During Project construction, silt fence will be constructed to prevent sediments in storm water runoff from leaving the site. The silt fence depicted in figure 6.17-3 will be in place prior to any clearing or grading operations. Since the grading of the site will take place in phases, temporary silt fence will be added around the perimeter of the phase area on the sides not

³ The curve number is a coefficient used in the TR-55 method of the Natural Resources Conservation Service. The number classifies the land use and soil type of the watershed that is being analyzed.

⁴ California Stormwater BMP Handbook – Construction. California, 2003.

⁵ County of San Bernardino, 1986.

bounded by the Project site silt fence. After silt fence is installed, the Sediment Retention Facility and outlet structure will be constructed first during Power Block grading. A temporary swale on the west side of the Sediment Retention Facility will be constructed as depicted in figure 6.17-3 to drain the Power Block into the Facility during the remaining 3 to 4 months of the Power Block grading. The largest amount of sediments will be produced during construction. Therefore, sediments, which have accumulated in the Sediment Retention Facility during construction, may need to be removed during and at the end of construction to ensure that the facility functions properly. Temporary and permanent ditches that carry runoff to the Sediment Retention Facility will be protected against erosion, during construction, using flow check dams constructed of hay bales. As permanent storm sewer pipes and culverts are added during construction, they will be protected from receiving sediments using silt fence that will enclose the inlets.

Areas disturbed during construction, in the Power Block Area, will be stabilized with straw or other suitable material until the final surface is established. The Solar Field will be stabilized with Dirt Glue or a similar product. All construction entrances will have a granular area to remove soil from vehicle tires prior to leaving the site. Dust will be controlled during construction by watering and using Dirt Glue or a similar product. All erosion control measures will be in accordance to Section 3 of the California Stormwater BMP Handbook – Construction.⁶

SECTION 3

Clearing and Grading

3.1 Areas to be Cleared and Graded

Victorville 2 site is located entirely within an undeveloped area. Brush and Joshua trees will need to be cleared before grading is performed.

3.2 Location of Disposal Areas, Fills, or Other Special Areas

It is anticipated that all excavated soil will be used onsite for grading and leveling purposes. In the event that some of the excavated soil will not be reused onsite, classification of the soil for disposal would be made on the basis of sampling. Sampling would be completed once the soil is excavated and stockpiled. Soil that is determined to be nonhazardous could be suitable for reuse at a construction site or disposal at a regional disposal facility, depending on the chemical quality.

3.3 Existing and Proposed Topography

The existing site depicts an average slope of 1% toward the north. However, there is a ridge in the center of the site that would direct runoff to the east or west of the site. Moreover, the east side of the proposed site has steep slopes of 7%-12% in the east, while the west slopes at roughly 1% to the west. At completion of Victorville 2, surface grading will direct storm water runoff off the site via overland flow at a typical slope of 0.5 percent. The main plant complex area will be graded with moderate slopes for effective drainage.

3.4 Volumes of Cut and Fill

In order to balance the cut and fill, it is expected that 1.9 million cubic yards of dirt will be cut from the west side of the site and reused as fill material on the east side. It is expected that it will not be necessary to haul dirt onto or off of the site. There will be no topsoil removed from the site.

⁶ California Stormwater BMP, 2003.

3.4.1 Gas Pipeline

The trench excavated for the short pipeline tie-in will be entirely refilled. No surplus soil is expected.

SECTION 4

Best Management Practices

The project has been designed to impact as small an area as possible at any given time, thereby limiting the amount of exposed, untreated soil. Construction is expected to proceed as expediently and efficiently as possible, thereby ensuring that as little soil is exposed for as short a time as possible. The following sections present standard construction Best Management Practices (BMPs) most of which are described in the California Storm Water Best Management Practice Handbook (2003) and the Caltrans Storm Water Quality Handbook (2003).

These resource handbooks provide comprehensive details on BMP implementation and will be obtained and reviewed by managers for all construction contractors that may have an impact on implementation of the DESCP.

The following sections present the recommended construction BMPs for stormwater pollution prevention at the WCEP construction laydown areas, plant site, and linear facilities. Each section provides information on BMP implementation as it relates to the activity being performed. BMPs that may have an impact on implementation of the DESCP will be reviewed by managers and construction contractors. While performing the work, the contractors may implement additional control measures if necessary.

4.1 General Erosion Control Measures

The project has been designed to impact as small an area as possible at any given time, thereby limiting the amount of exposed, untreated soil. BMPs will be used to help maintain water quality, protect property from erosion damage, and prevent accelerated soil erosion or dust generation. Temporary erosion control measures would be implemented before construction begins and they would be evaluated and maintained during construction. These measures typically include revegetation, mulching, physical stabilization, dust suppression, berms, ditches, and sediment barriers. These measures would be removed from the site after the completion of construction (except for silt fences).

A mitigation monitoring plan will also be developed in conjunction with CEC Staff to set performance standards and monitor the effectiveness of BMPs. This plan will address the timing and methods of such measures, as well as reporting and response requirements. Personnel will receive training to conduct their jobs properly and recognize and report abnormal/adverse situations so that they can be quickly corrected.

The following general control measures may be used during various phases of the project:

- Proper scheduling and sequencing of activities (SS-1)
- Preservation of existing vegetation (EC-2)
- Silt fences and fiber rolls (SC-1 and SC-5)
- Drainage swales (EC-9)
- Straw mulch (SS-6)
- Placement of geotextiles, plastic covers, and erosion control blankets/mats (SS-7)

- Placement of hydro seeding (EC-4), mulching (EC-6), or geotextile/erosion control blankets (EC-7) on slopes
- Gravel bag berm (SC-6)
- Street sweeping (SC-7)
- Sandbag barrier (SC-8)
- Storm drain inlet protection (SC-10)
- Stockpile management (WM-3)
- Dust control (WE-1)
- Solid and hazardous waste management (WM-5 and WM-6)
- Sanitary and septic waste management (WM-9)
- Vehicle and equipment maintenance (NS-10)
- Vehicle and equipment fueling (NS-9)
- Spill prevention and control (WM-4)
- Sediment basins (SC-2)
- Employee and contractor training

4.1.1 Access Road, Entrance and Parking, and Laydown Areas

During construction, primary access to the Victorville 2 site will be from an entrance via Colusa Road. The entrance will be maintained to limit sediment tracking and creation of dust. The parking and laydown areas will be stabilized with coarse gravel. All surfaces will be regularly watered to reduce generation of dust, but will not be excessively watered so as to generate runoff. Silt fencing may be used at edges of these areas, as necessary to minimize sediment discharging into swales or ditches.

All construction equipment will be maintained to control leaks and spills, and fueling will only be conducted within contained areas. Any contaminated soils resulting from spills will be dug up as quickly as possible, and then removed from the site for proper disposal.

The following BMPs are recommended for construction access areas:

- Silt fencing (SC-1)
- Stabilizing entrances and surfaces with coarse aggregate (TC-1 and TC- -2)
- Compacting access road surfaces (TC-2)
- Proper scheduling and sequencing of activities (SS-1)
- Street sweeping and vacuuming (SC-7)
- Placement of hydro seeding (SS-4), mulching (SS-6), or geotextile/erosion control blankets (SS-7).
- Dust control (WE-1)
- Temporary drains and swales (SS-9)
- Hay/straw bale barriers (SC-9)
- Vehicle and equipment cleaning (NS-8)
- Establishing vehicle and equipment fueling (NS-9) and maintenance areas (NS-10)

4.1.2 Victoville 2 Site and Linear Facilities

The site will be constructed somewhat rolling, dusty ground. Therefore, it will be surrounded by silt fences. These sediment barriers will be used to control sediments transported by runoff, and will remain after construction.

The project linear facilities will be constructed within the rights-of-way associated with Colusa Road and Helendale Road. Temporary erosion control might include asphalt patching in the streets until permanent paving can be completed.

During construction, temporary erosion control might include outlet protection and hay or straw bale barriers. The following BMPs will be considered during site and linear facilities constructions:

- Preservation of existing vegetation (SS-2)
- Temporary drains and swales (SS-9)
- Petroleum-absorbing fabric (WM-4)
- Check dams (SC-4)
- Fiber rolls (SC-5)
- Hay/straw bale barriers (SC-9)
- Sediment basins (SC-2)
- Outlet protection (SS-10)

4.1.3 Foundations

During construction of the foundations, a concrete washout area will be required. Dumping of excess concrete and washing out of delivery vehicles will be prohibited at other locations onsite. Notices will be posted to inform all drivers.

The following BMPs will be considered during the construction of foundations:

- Solid waste management (WM-5)
- Concrete waste management (WM-8)

4.1.4 Site Stabilization and Demobilization

As construction nears completion, areas used for parking, storage and laydown will be cleared and stabilized. Areas that will continue to be used for parking or storage will have permanent storm water collection and conveyance structures provided.

4.2 Other Controls

4.2.1 Material Handling and Storage

There will be a variety of chemicals stored and used during the construction and operation of the Victorville 2. Chemicals will be stored in appropriate chemical storage facilities. Bulk chemicals will be stored in storage tanks and other chemicals will be stored in returnable delivery containers. Chemical storage and chemical feed areas will be designed to contain leaks and spills. Berm and drain piping design will allow a full-tank capacity spill without overflowing the berms. For multiple tanks located within the same bermed area, the capacity of the largest single tank will determine the volume of the bermed area and drain piping. Drain piping for volatile chemicals will be trapped and isolated from other drains to eliminate noxious or toxic vapors. After neutralization, if required, water collected from the chemical storage areas will be directed to the cooling tower basin. The aqueous ammonia storage area will have spill containment and ammonia vapor detection equipment.

Safety showers and eyewashes will be provided in the vicinity of all chemical storage and use areas. Hose connections will be provided near the chemical storage and feed areas to flush spills and leaks to the plant wastewater collection system. Approved personal protective equipment will be used by plant personnel during chemical spill containment and

cleanup activities. In case of a chemical spill or accidental release, personnel will be properly trained in the handling of these chemicals and instructed in the procedures to follow. Adequate supplies of absorbent material will be stored onsite for spill cleanup.

The following BMPs will be considered for material handling and storage:

- Solid waste management (WM-5)
- Vehicle and equipment refueling (NS-9)
- Vehicle and equipment maintenance (NS-10)
- Material delivery and storage (WM-1)
- Material use (WM-2)
- Concrete waste management (WM-8)

4.2.2 Solid and Hazardous Waste Management

Wastewater. Wastewater generated during construction will include sanitary waste, storm water runoff, equipment washdown water, and water from excavation dewatering during construction (if dewatering is required). Depending on the chemical quality of these wastewaters, they could be classified as hazardous or nonhazardous. Sanitary waste will be collected in portable, self-contained toilets. Storm water runoff will be managed in accordance with a storm water management permit, which will be obtained prior to the start of construction. Equipment washdown water will be contained at designated wash areas and will be disposed of offsite. Excavation dewatering water will be contained in portable tanks and sampled prior to disposal offsite. Water used for dust control and soil compaction during construction will not result in discharge.

Hazardous Waste. Most of the hazardous waste generated during construction will consist of liquid waste, such as water from excavation dewatering, flushing and cleaning fluids, passivating fluid (to prepare pipes for use), and solvents. Some hazardous solid waste, such as welding materials and dried paint, may also be generated.

Flushing and cleaning waste liquid will be generated as pipes are cleaned and flushed. The volume of flushing and cleaning liquid waste generated is estimated to be one to two times the internal volume of the pipes cleaned. The quantity of welding, solvent, and paint waste is expected to be minimal. Wastewaters generated during construction could be considered hazardous.

The construction contractor will be considered the generator of hazardous construction waste and will be responsible for proper handling of hazardous waste in compliance with all applicable federal, state, and local laws and regulations. This responsibility will include licensing, personnel training, accumulation limits and times, and reporting and recordkeeping.

The hazardous waste will be collected in satellite accumulation containers near the points of generation. It will be moved daily to the contractor's 90-day hazardous waste storage area located at the site construction laydown area. The waste will be removed from the site by a certified hazardous waste collection company and delivered to an authorized hazardous waste management facility, before expiration of the 90-day storage limit.

The following BMPs will be considered at the designated storage locations:

- Cover or store hazardous materials indoors, if possible (WM-1)
- Material delivery and storage (WM-1)
- Material use (WM-2)

- Spill prevention and control (WM-4)
- Solid waste management (WM-5)
- Hazardous waste management (WM-6)
- Use of covered dumpsters and containers for waste (WM-5)

4.2.2 Potential Contaminated Soil

It is unlikely that contaminated soil will be encountered during construction. However, operators and construction personnel will be asked to report unusual conditions to the appropriate personnel and the area and/or material will be properly contained during investigative actions. If soils require temporary stockpiling, piles will be covered with plastic sheeting or tarps that are secured safely with sand bags and bermed with hay bales or silt fencing to prevent runoff from leaving the area. If required, samples will be collected and sent to a certified analytical laboratory for characterization. If contamination is detected, the waste will be handled and properly disposed of in an authorized waste management facility.

4.2.3 Groundwater/Dewatering Controls

The construction phase of Victorville 2 will require no groundwater removal. Storm water is expected to result in only several days of dewatering during construction, and this will be in accordance with BMPs. With an unusual storm year, this could be as many as 5 to 10 days.

If any contamination is detected via odors or visible sheens, the collected storm water will be handled and properly disposed in a manner consistent with federal, state, and local regulations. The following control methods will be considered for groundwater/dewatering controls, as necessary:

- Dewatering operations (NS-2)
- Hazardous waste management (WM-6)

4.2.4 Offsite Vehicle Tracking

Because sediment reaching public roads generally has a clear path to wetlands and water bodies, controls will be in place to minimize or eliminate soils from being tracked off the project site from vehicles. The site will have paved access roads and entrances/exits made of coarse aggregate to limit the amount of material adhering to tires. These areas will be inspected daily and cleaned as necessary using manual or mechanical street sweepers. The following control methods will be considered for offsite vehicle tracking, as necessary:

- Stabilized construction entrance/exit (TC-1)
- Stabilized construction roadway (TC-2)
- Entrance/exit tire wash (TC-3)

4.2.5 Dust Suppression and Control

During construction of the project and the related linear facilities, dust erosion control measures would be implemented to minimize the wind-blown loss of soil from the site.

Water of a quality equal to or better than existing surface runoff would be sprayed on the soil in construction areas to control dust during revegetation.

The following control method will be considered for dust suppression, as necessary:

- Wind erosion control (WE-1)

-APPENDIX A



Pre- and Post-Construction Drainage Plans

-APPENDIX B

Drainage Calculations

-APPENDIX C

Best Management Practices

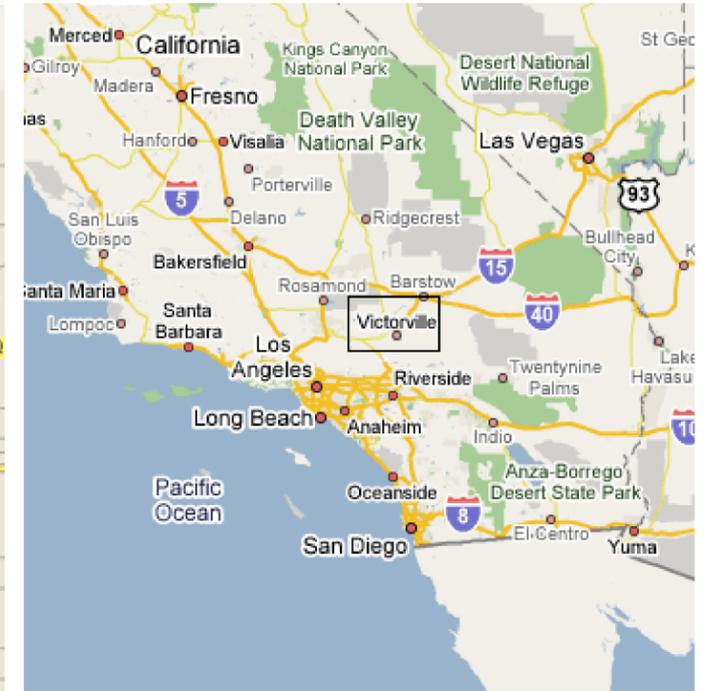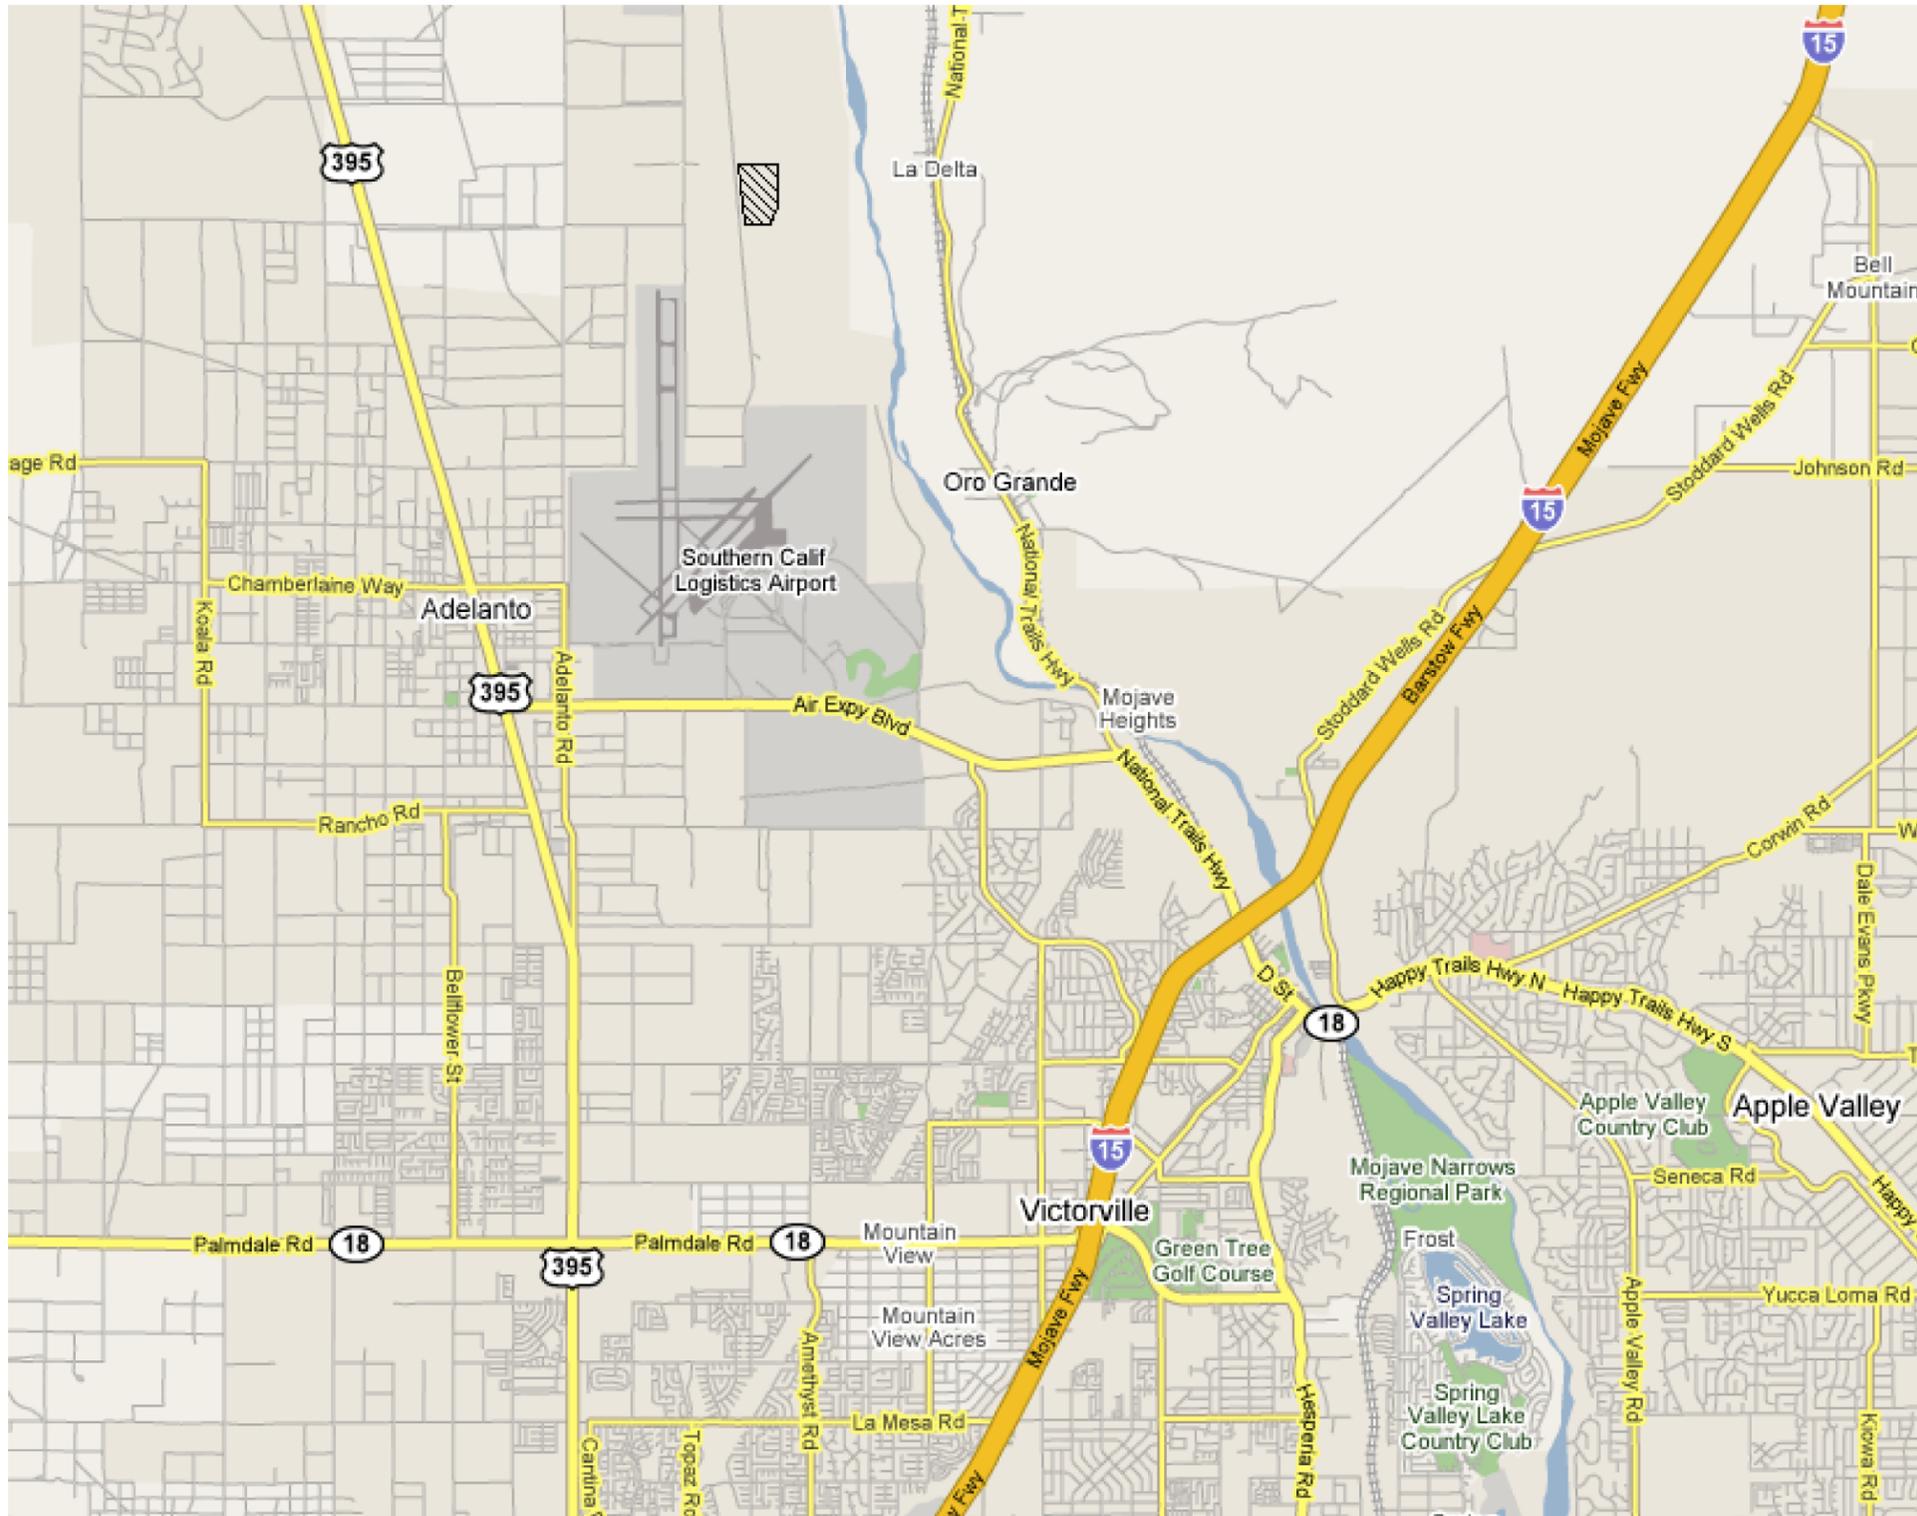

**VICTORVILLE #2
PLANT SITE**




- PRELIMINARY -
NOT FOR CONSTRUCTION

CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY AGREEMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY ANY PARTY SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT WE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO 6186.

REV	DESCRIPTION	DWN	CHK	APP	DATE
 KIEWIT INDUSTRIAL CO. <i>A Kiewit Company</i>					
INLAND ENERGY					
VICTORVILLE COMBINED CYCLE POWER PROJECT					
 8455 Lenexa Drive Lenexa, Kansas 66214					
VICINITY MAP					
DESIGNED by _____ date _____			DRAWING NUMBER		
DRAWN SMC 07-10-07			SKC-2005038-CP-071007-1A		
CHECKED _____					
APPROVED _____					



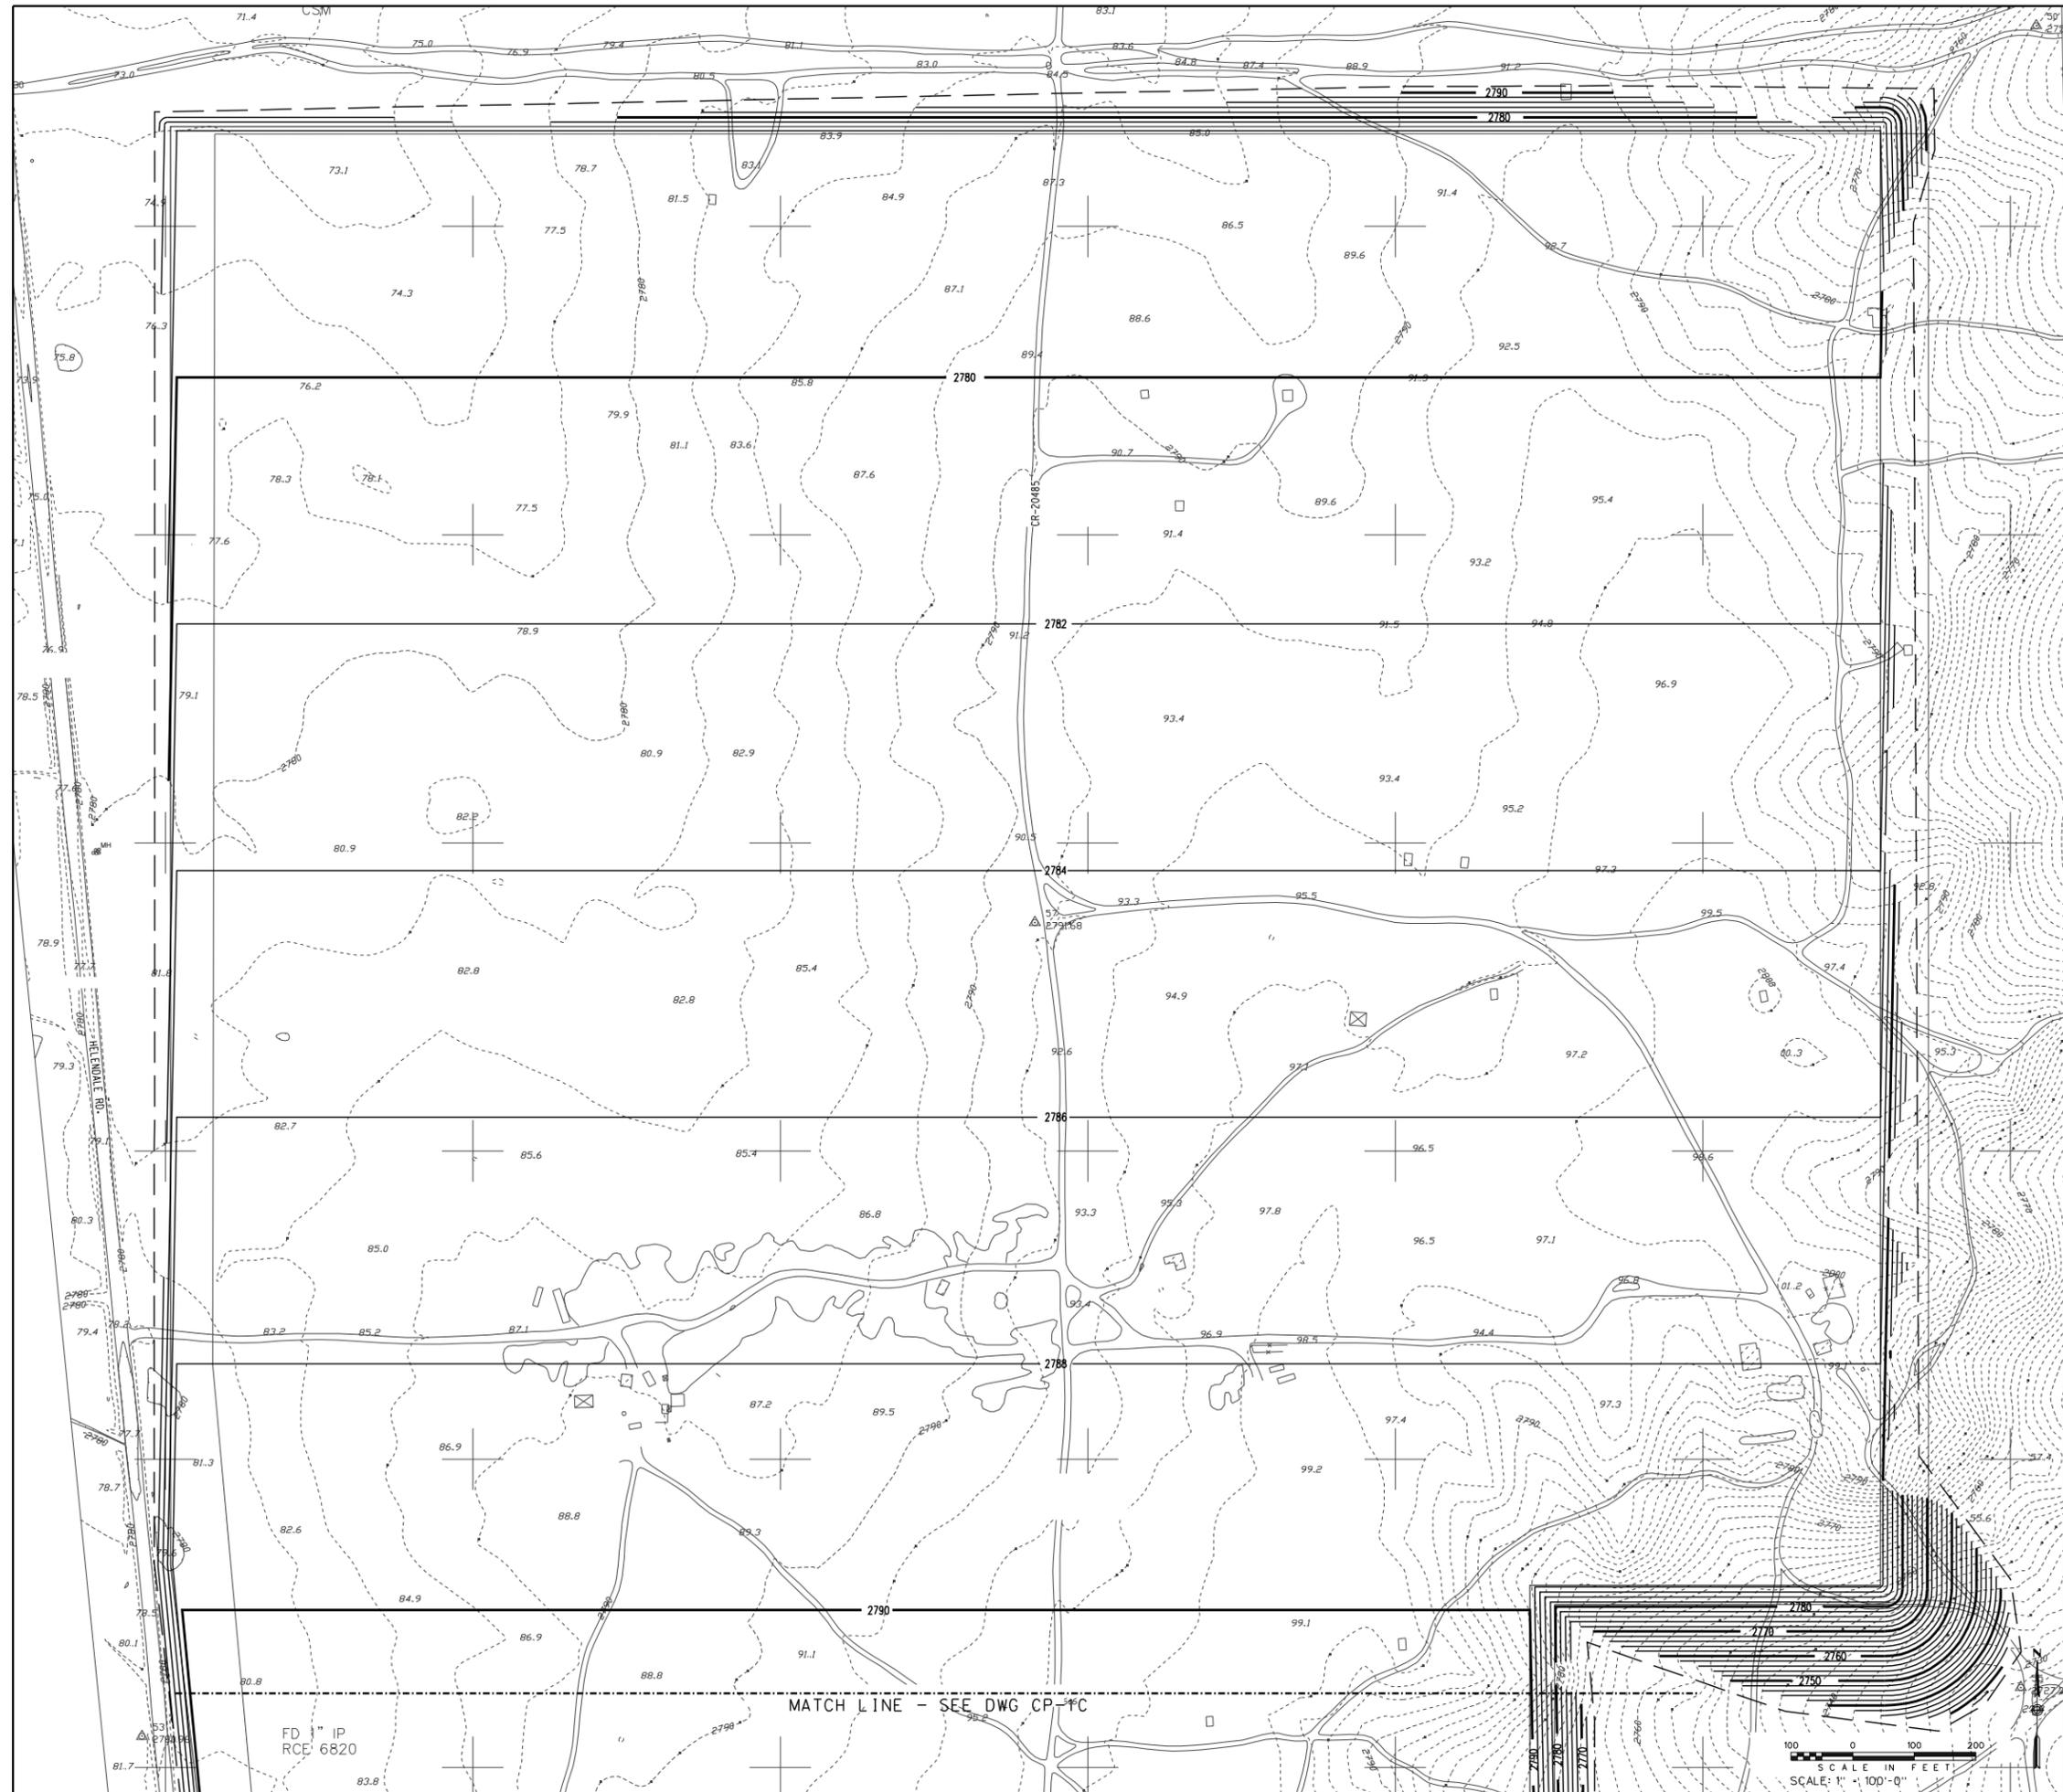

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT WE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.


REV	DESCRIPTION	DWN	CHK	APP	DATE
 KIEWIT INDUSTRIAL CO. <i>A Kiewit Company</i>					
INLAND ENERGY					
VICTORVILLE COMBINED CYCLE POWER PROJECT					
 8455 Lenexa Drive Lenexa, Kansas 66214					
VICINITY MAP					
DESIGNED by _____ date _____					DRAWING NUMBER
DRAWN _____					SKC-2005038-CP-071007-1B
CHECKED SMC 03-20-07					
APPROVED _____					



- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT HE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

A	ISSUED FOR REVIEW	SMC		03-29-07	
REV	DESCRIPTION	DWN	CHK	APP	DATE




INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT





8455 Lenexa Drive
Lenexa, Kansas 66214

VICINITY MAP



DESIGNED	by	date
DRAWN	SMC	03-20-07
CHECKED		
APPROVED		

DRAWING NUMBER
SKC-2005038-CP-071007-1C

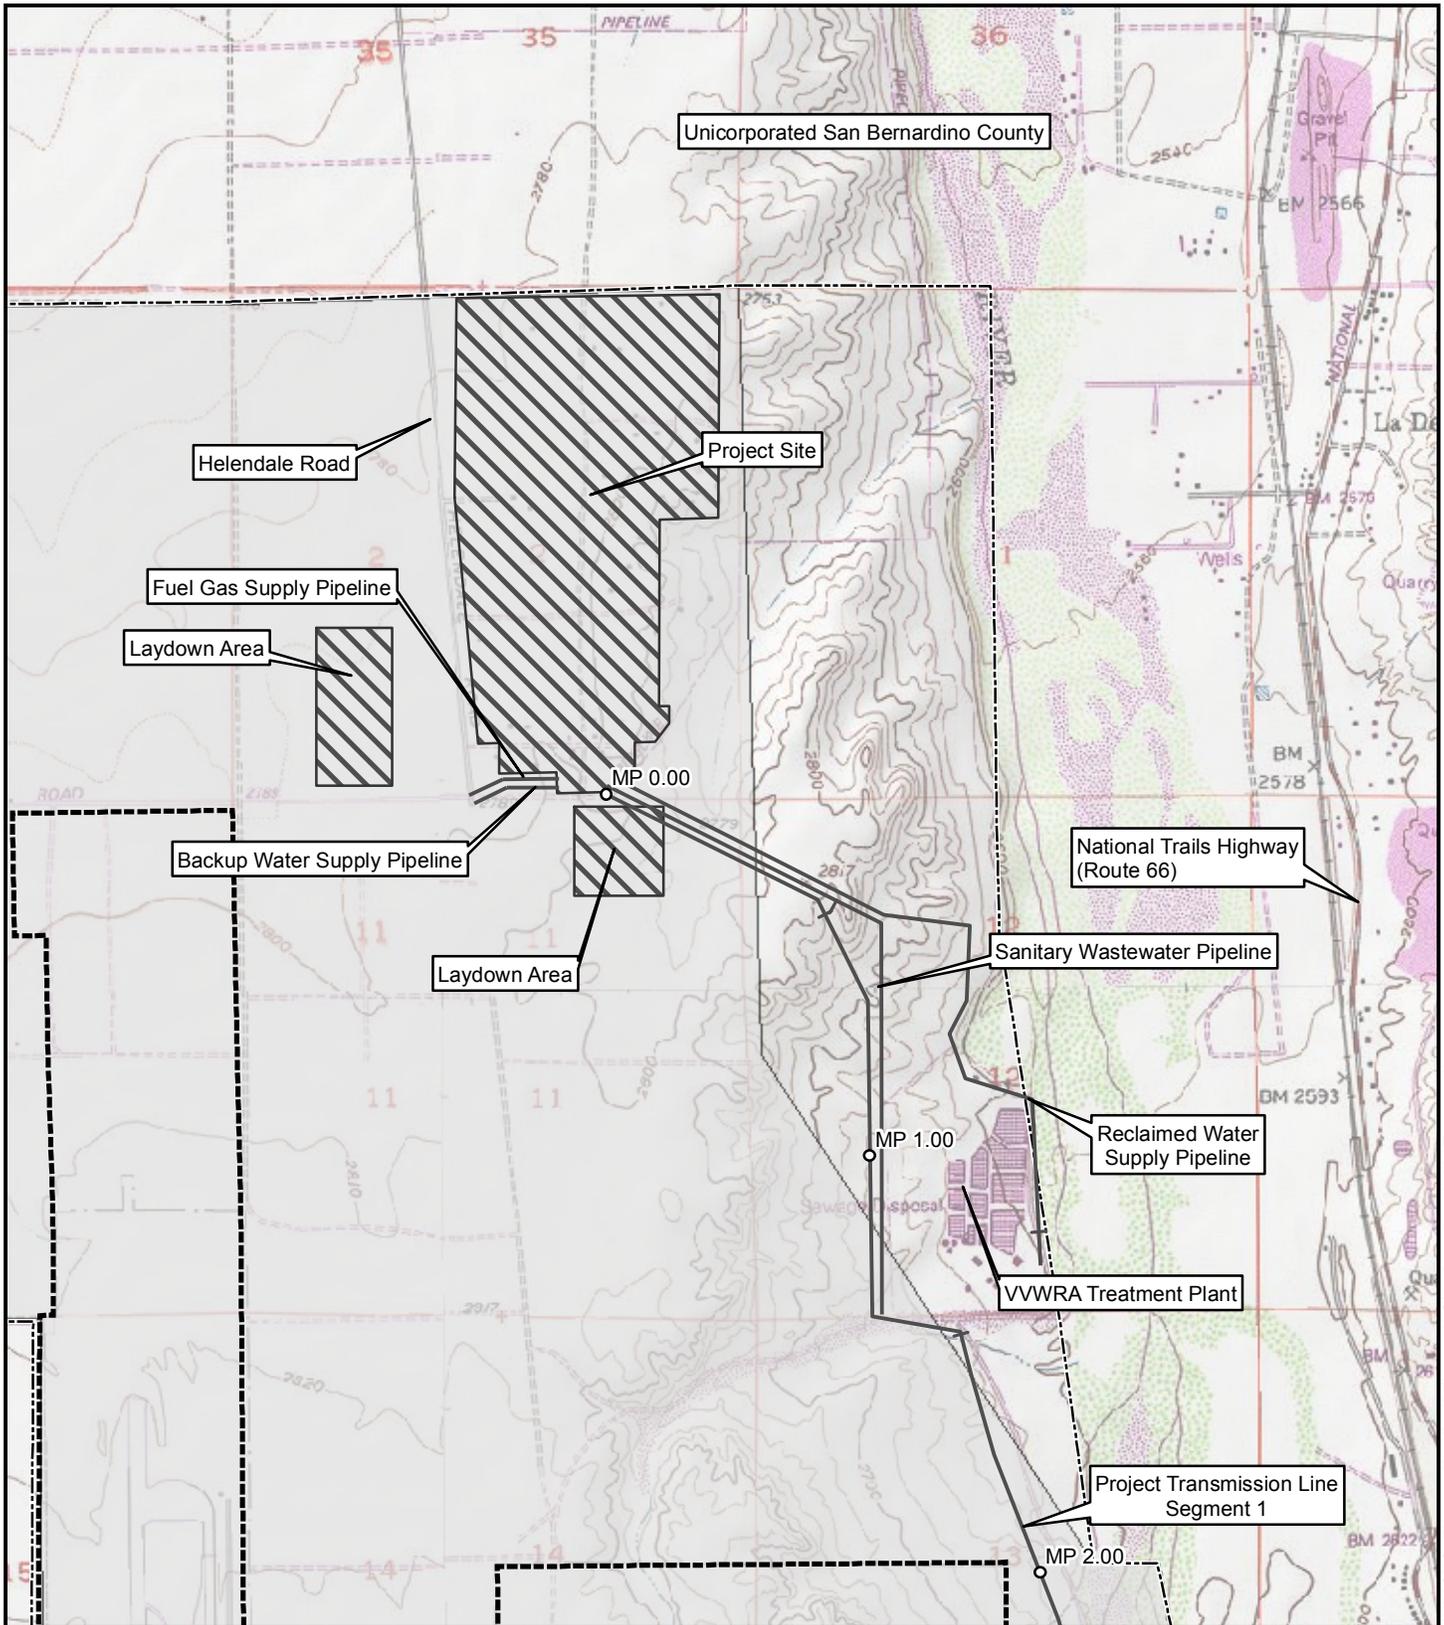

Project Site and Linear Facilities
Victorville 2 Hybrid Power Project

Legend

- Victorville City Boundary
- SCLA Boundary
- SCLA Planning Area
- Mile Post (MP)
- Half-Mile Hatch

Base Imagery: USGS 24K Topo Quadrangles
Scale: 1:24,000


0 1,000 2,000 4,000 6,000 Feet




Inland Energy, Inc.
ENSR | AECOM

Mapsheet 1 of 7
Figure: 2-1
Date: February 2007

Y:\Projects\InlandEnergy\Victorville\MXD\DEC_Figures_Finalized\Figure_2_Site_Location_24K_Topo.mxd

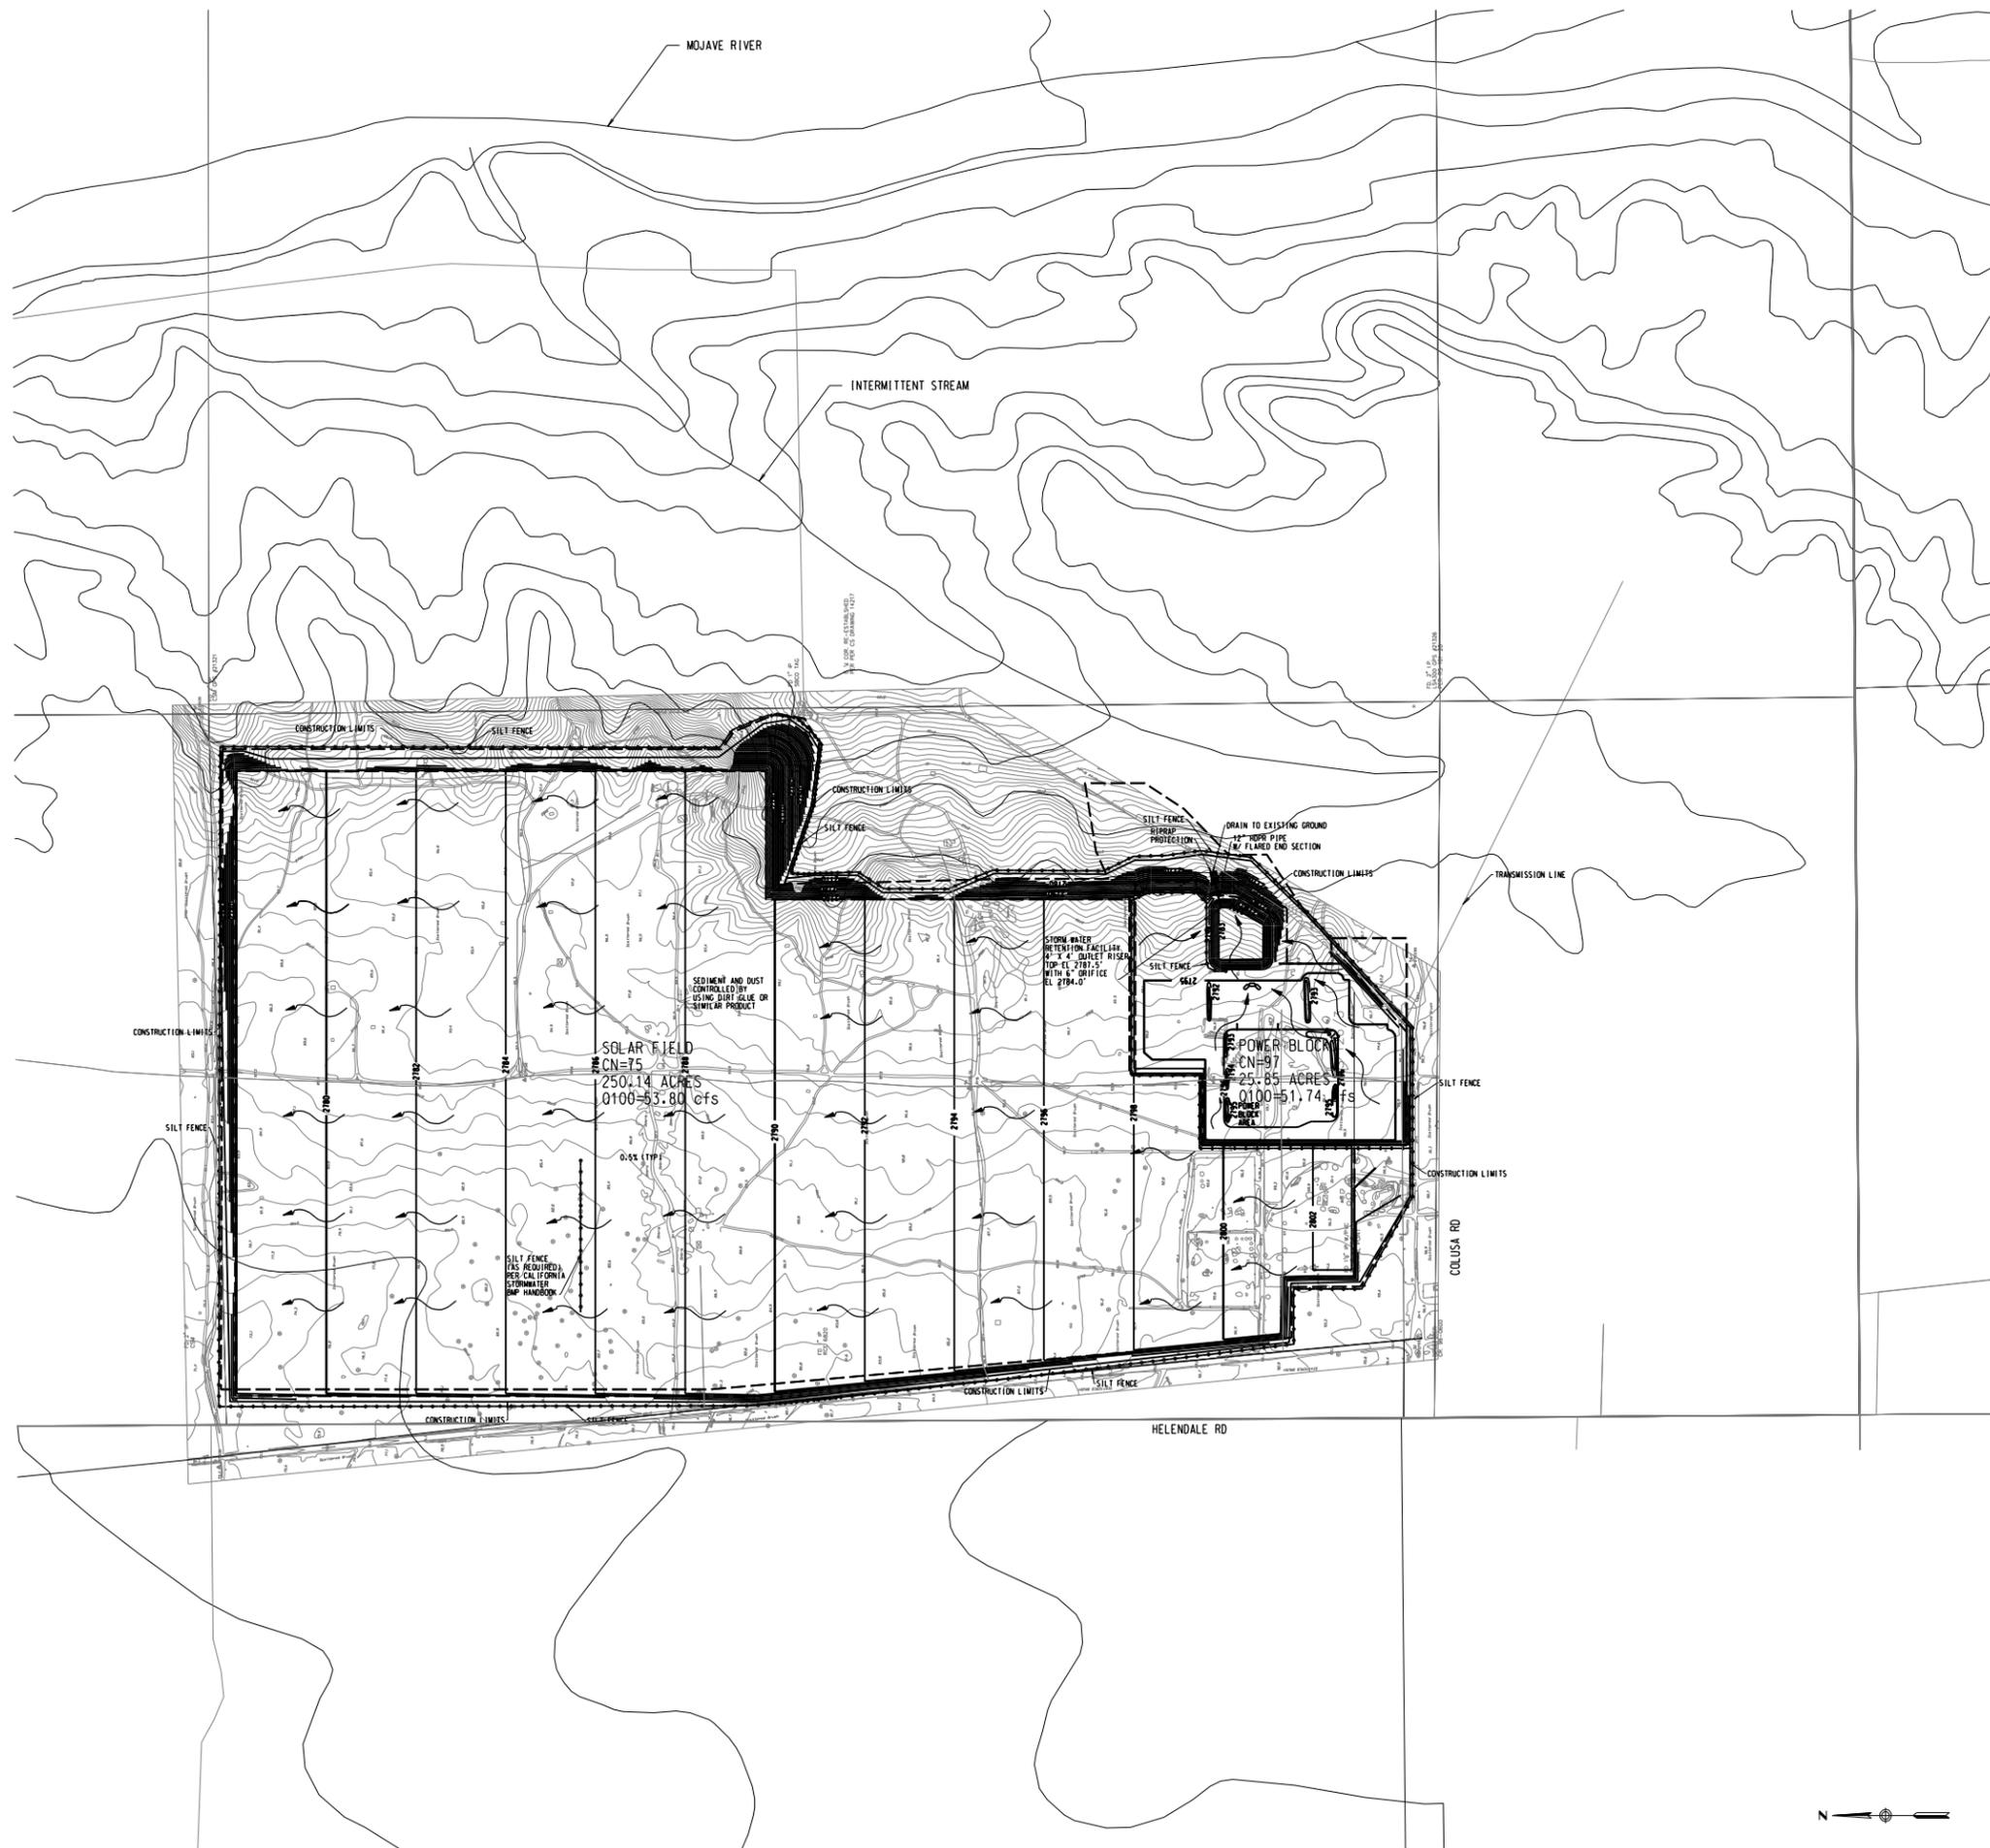

A	PRELIMINARY	CED	RSG	CKB	07-13-07
REV	DESCRIPTION	DWN	CHK	APP	DATE
 KIEWIT INDUSTRIAL CO. <i>A Kiewit Company</i>					
INLAND ENERGY					
VICTORVILLE COMBINED CYCLE POWER PROJECT					
 Bibb and associates <small>8455 Lenexa Drive Lenexa, Kansas 66214</small>					
WATER COURSES AND CRITICAL AREAS					
		by date		DRAWING NUMBER	
DESIGNED	MAA	07-12-07			
DRAWN	PRB	07-12-07			
CHECKED					
APPROVED					
			SKC-2005038-CP-071007-3		

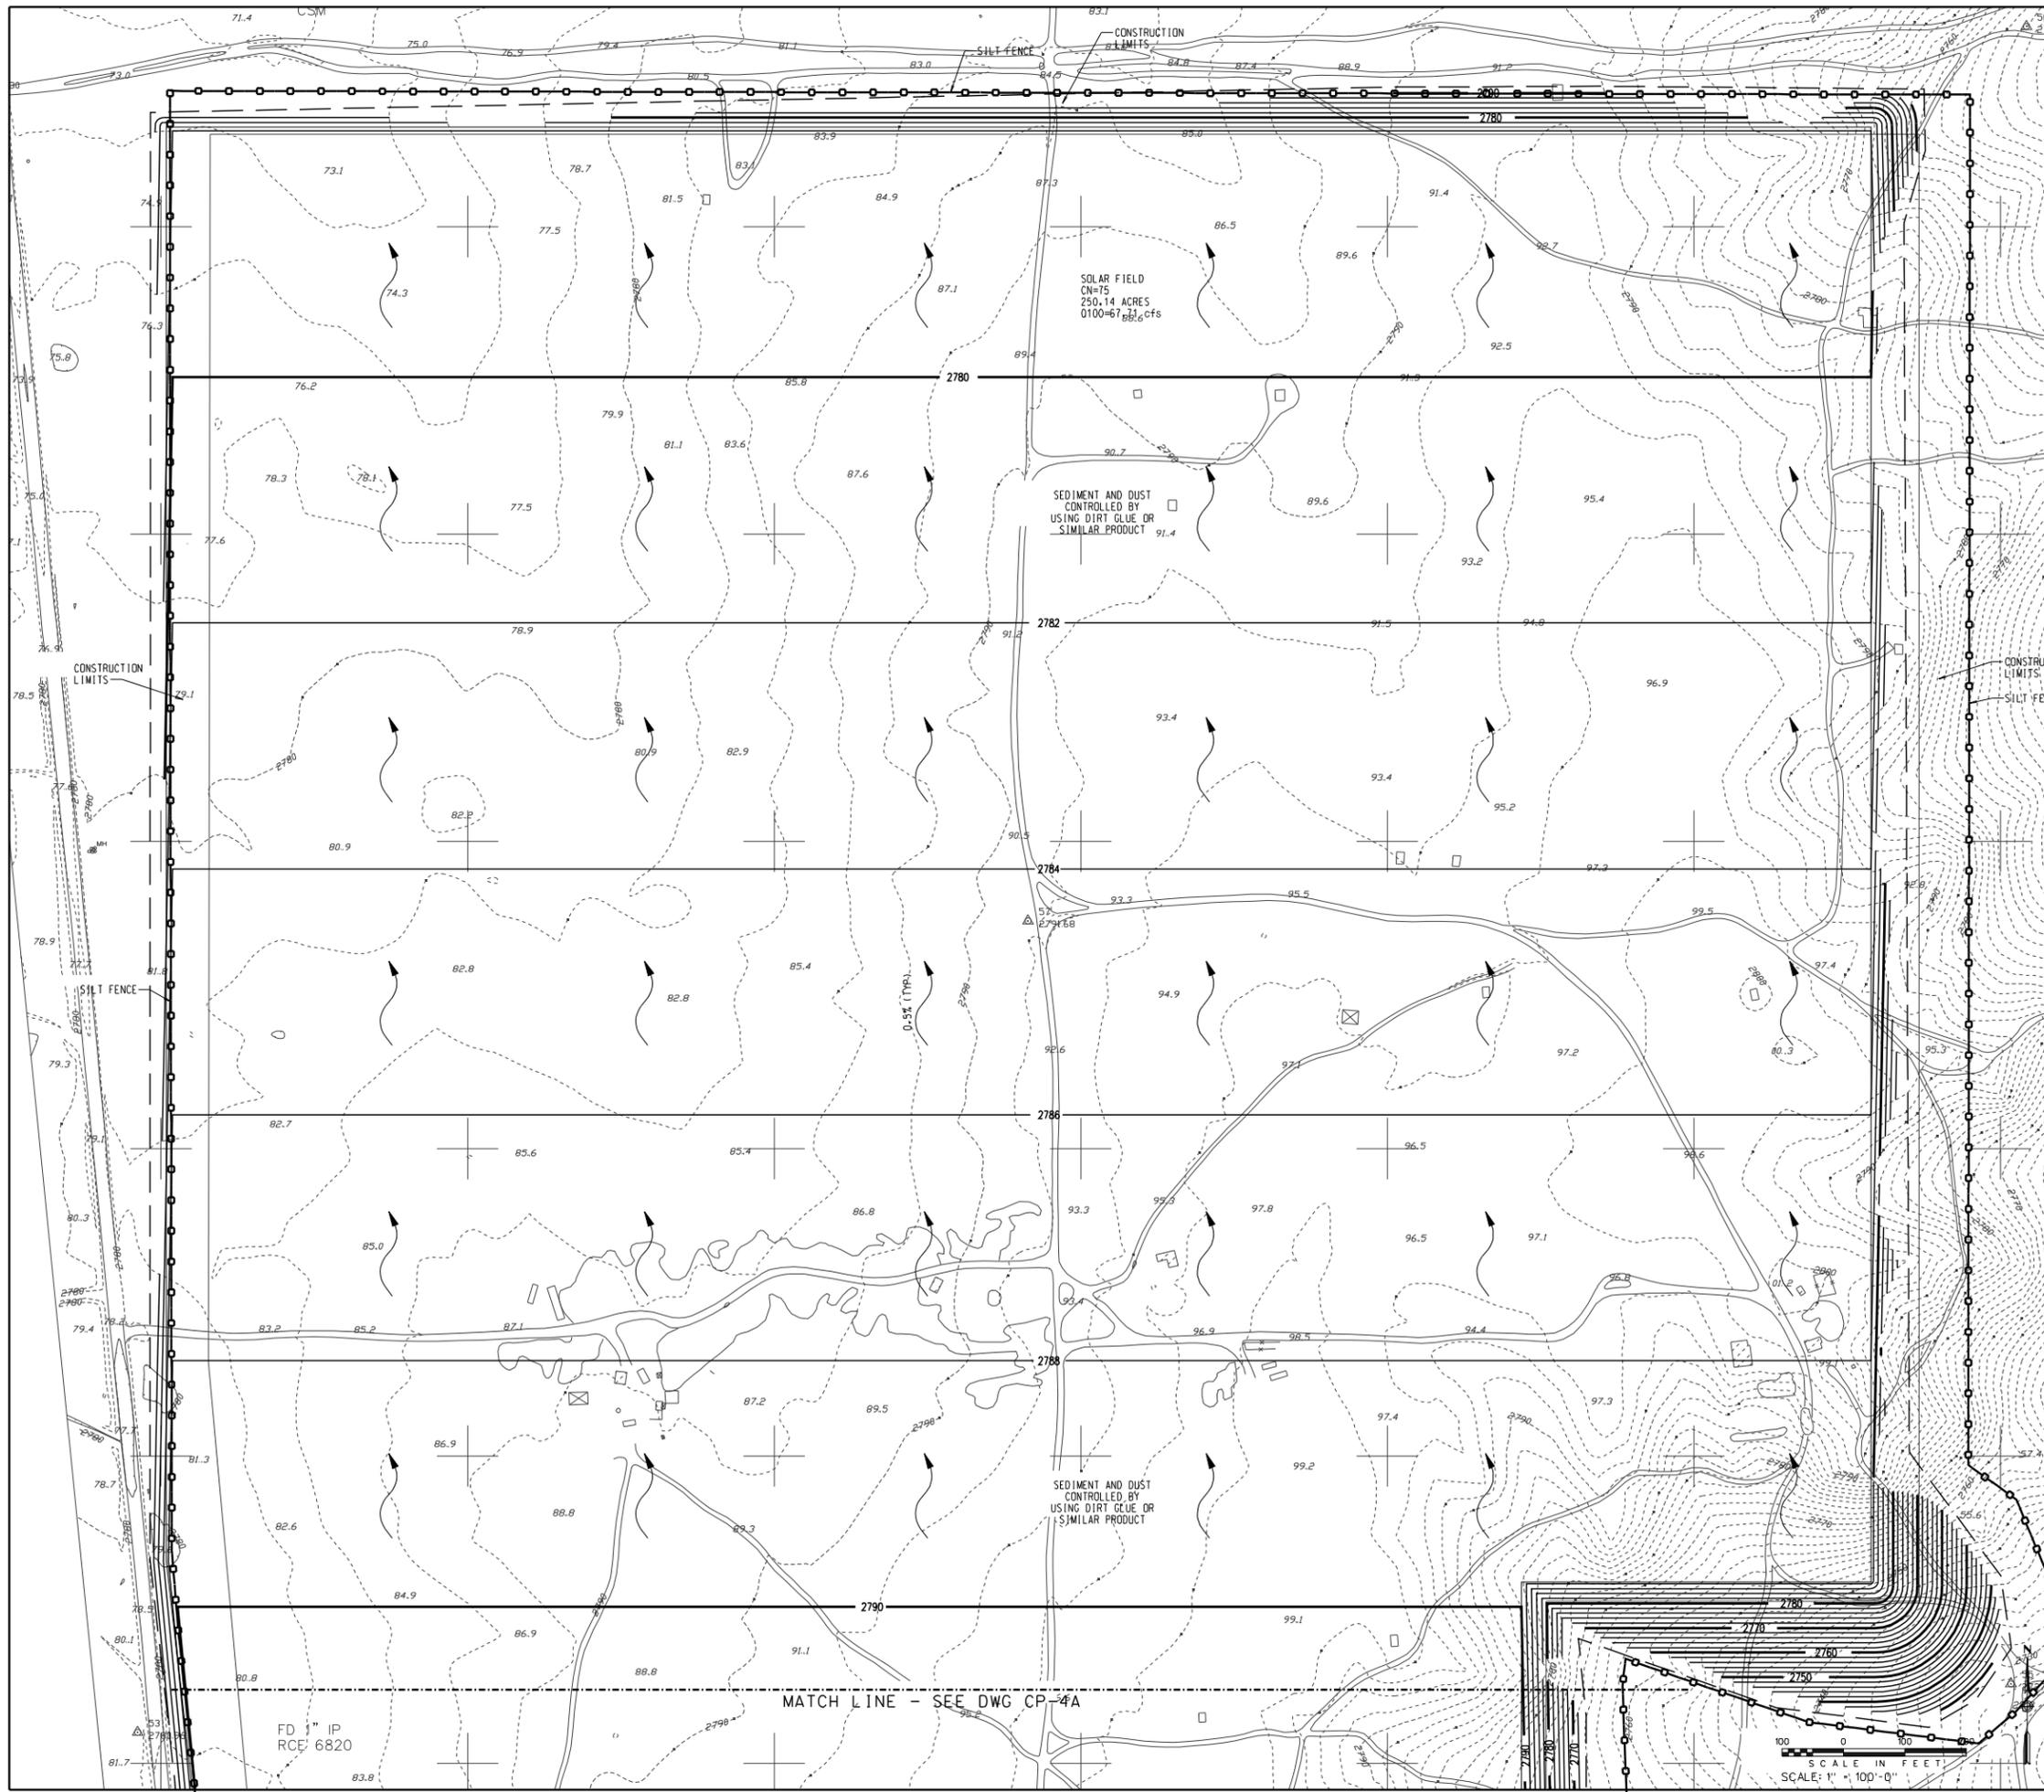

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT HE MAY HAVE EXECUTED. IN OBTAINING THIS INFORMATION FROM THIRD PARTY, IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

REV	ISSUED FOR	DESCRIPTION	DWN	CHK	APP	DATE
A						03-20-07



INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT



8455 Lenexa Drive
Lenexa, Kansas 66214

DRAINAGE MAP

DESIGNED	by	date
DRAWN	03-20-07	03-20-07
CHECKED		
APPROVED		

DRAWING NUMBER
SKC-2005038-CP-071007-4B

SCALE: 1" = 100'-0"

FD 1" IP
RCE 6820

MATCH LINE - SEE DWG CP-4A



STORM WATER RETENTION FACILITY DESCRIPTION	
CAPACITY	= 16,090 CY
PRE DEVELOPMENT DISCHARGE	= 13.65cfs
POST DEVELOPMENT DISCHARGE	= 1.70cfs
POST DEVELOPMENT DISCHARGE VELOCITY	= 6.87 FT/S

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT WE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

REV	DESCRIPTION	SMC	DWN	CHK	APP	DATE
A	ISSUED FOR REVIEW					03-29-07


KIEWIT INDUSTRIAL CO.
A Kiewit Company


INLAND ENERGY


VICTORVILLE COMBINED CYCLE
POWER PROJECT


 8455 Lenexa Drive
 Lenexa, Kansas 66214

CLEARING AND GRADING PLANS

DESIGNED	DATE	DRAWING NUMBER
by SMC	03-20-07	SKC-2005038-CP-071007-5A
CHECKED		
APPROVED		



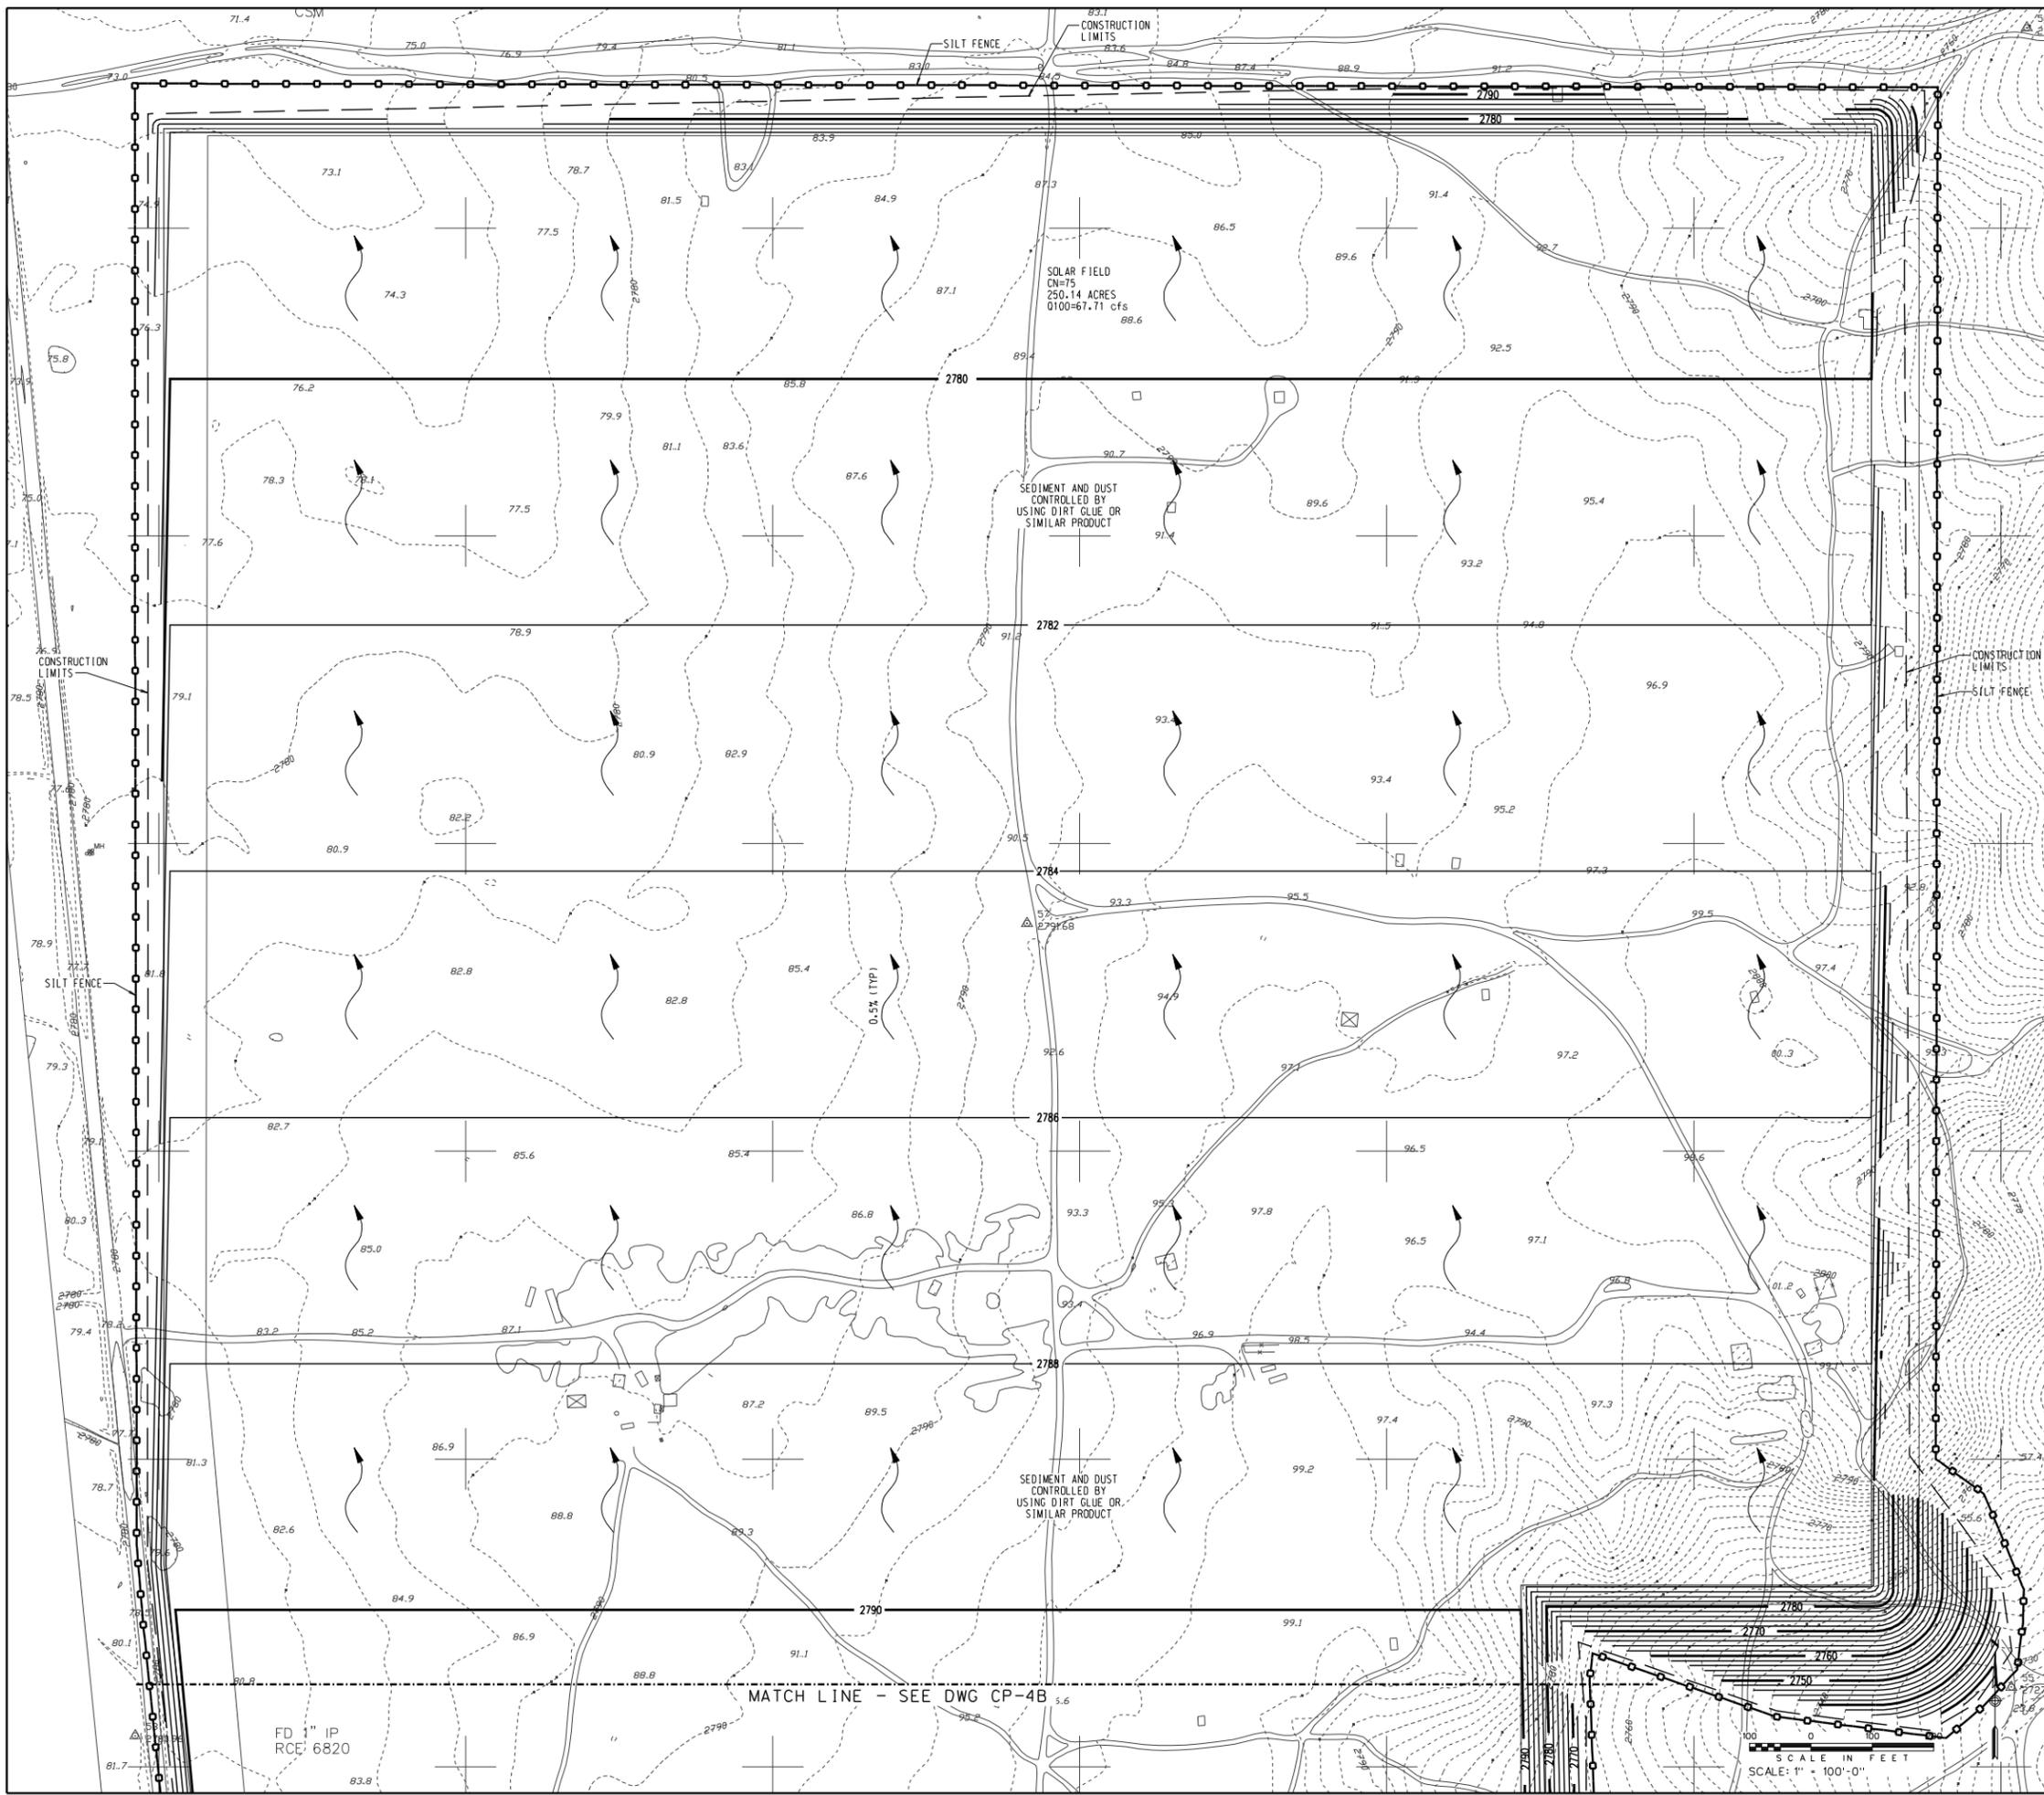

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT WE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

A	ISSUED FOR REVIEW	SMC			03-29-07
REV	DESCRIPTION	DWN	CHK	APP	DATE



INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT



8455 Lenexa Drive
Lenexa, Kansas 66214

CLEARING AND GRADING PLANS

DESIGNED	by	date	DRAWING NUMBER
DRAWN	SMC	03-20-07	SKC-2005038-CP-071007-5B
CHECKED			
APPROVED			



MATCH LINE - SEE DWG CP-5B

FD 1" IP
RCE 6820

SEDIMENT AND DUST
CONTROLLED BY
USING DIRT GLUE OR
SIMILAR PRODUCT

SILT FENCE (AS REQUIRED)
PER CALIFORNIA STORMWATER
BMP HANDBOOK

SEDIMENT AND DUST
CONTROLLED BY
USING DIRT GLUE OR
SIMILAR PRODUCT

STORM WATER
RETENTION FACILITY
4" x 4" OUTLET RISER
TOP EL 2787.5'
WITH 6" ORIFICE
EL 2784.0'

POWER
BLOCK
AREA

POWER BLOCK
CN=97
25.85 ACRES
02=18.09 cfs
0100=60.93 cfs

FD 1 1/2" IP W/PVC
PLUS V YOT

CONTROL POINT

STORM WATER RETENTION FACILITY DESCRIPTION	
CAPACITY	= 16,090 CY
PRE DEVELOPMENT DISCHARGE	= 13.65cfs
POST DEVELOPMENT DISCHARGE	= 1.70cfs
POST DEVELOPMENT DISCHARGE VELOCITY	= 6.87 FT/S

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT HE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

REV	DESCRIPTION	SMC	DWN	CHK	APP	DATE
A	ISSUED FOR REVIEW					03-29-07




INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT




8455 Lenexa Drive
Lenexa, Kansas 66214

BEST MANAGEMENT PRACTICES PLAN



DESIGNED	by	date	DRAWING NUMBER
DRAWN	SMC	03-20-07	SKC-2005038-CP-071007-6A
CHECKED			
APPROVED			

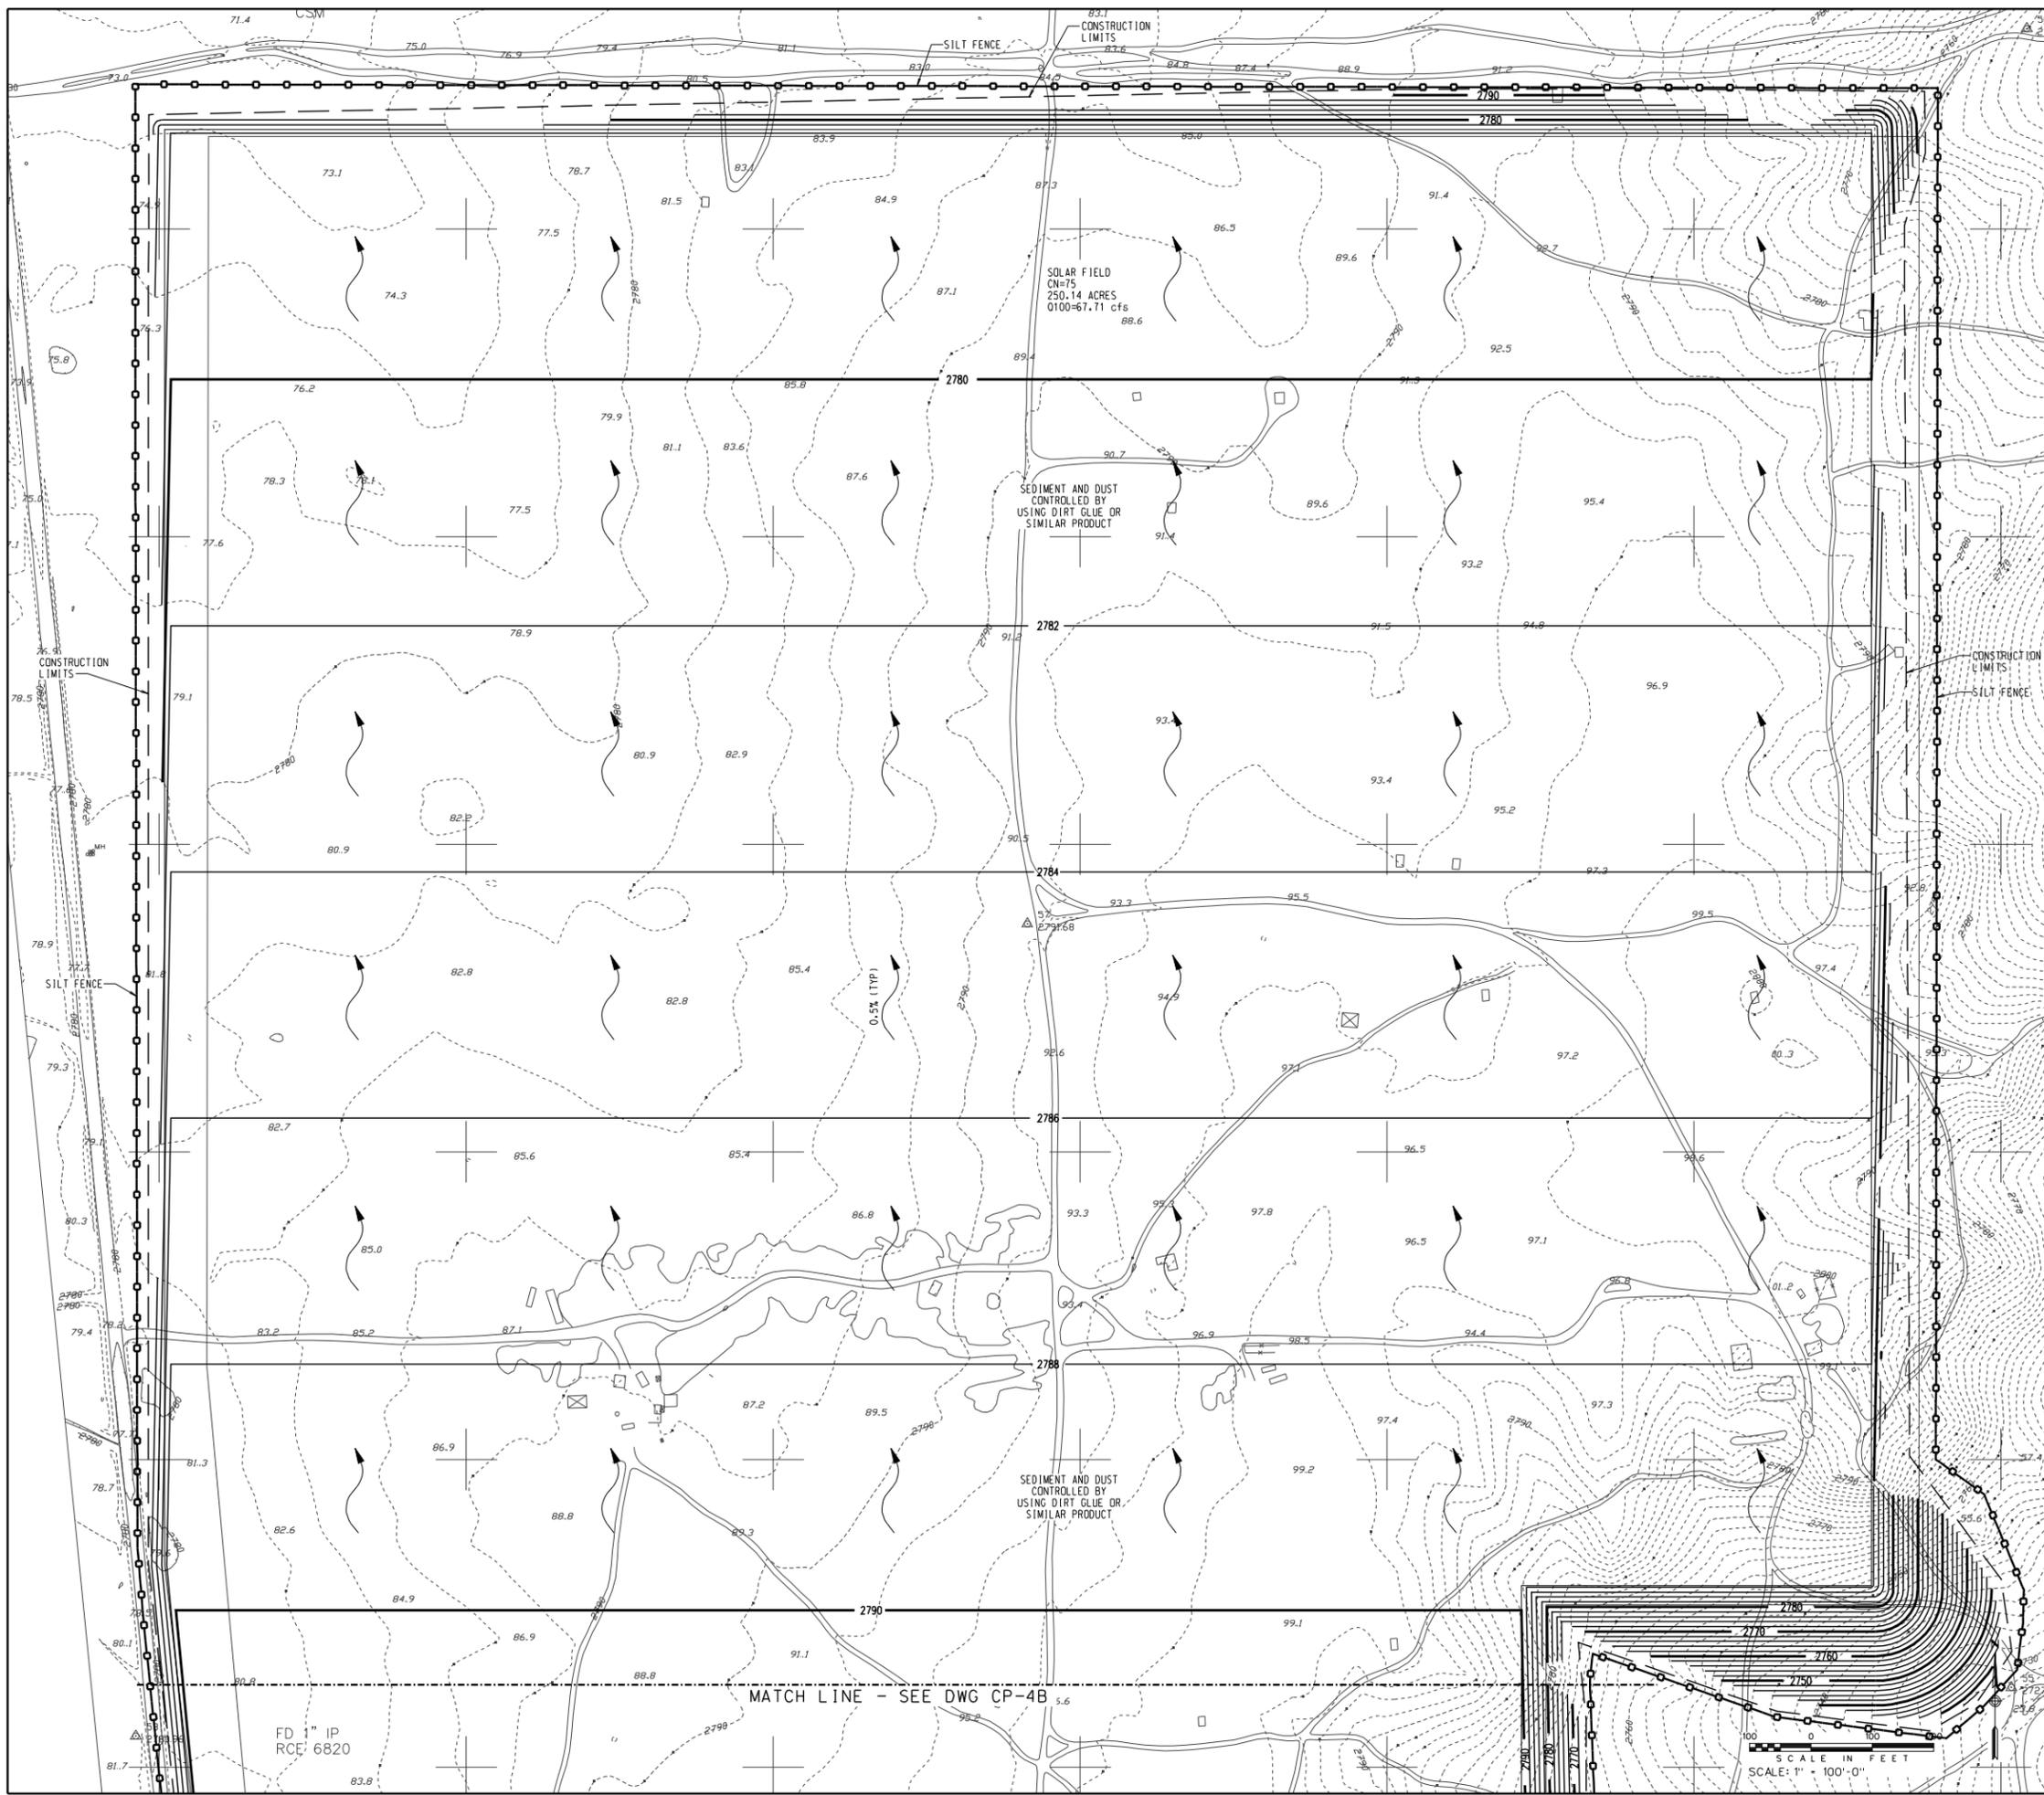

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY MISUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY REQUIREMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT WE MAY HAVE EXECUTED IN OBTAINING THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIBB.

A	ISSUED FOR REVIEW	SMC			03-29-07
---	-------------------	-----	--	--	----------

REV	DESCRIPTION	DWN	CHK	APP	DATE



INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT



8455 Lenexa Drive
Lenexa, Kansas 66214

BEST MANAGEMENT PRACTICES PLAN


DESIGNED	by	date	DRAWING NUMBER
DRAWN	SMC	03-20-07	SKC-2005038-CP-071007-6B
CHECKED			
APPROVED			

FD 1" IP
RCE: 6820

MATCH LINE - SEE DWG CP-4B

SCALE IN FEET
SCALE: 1" = 100'-0"


APPENDIX A:
Pre and Post Development Drainage Plans

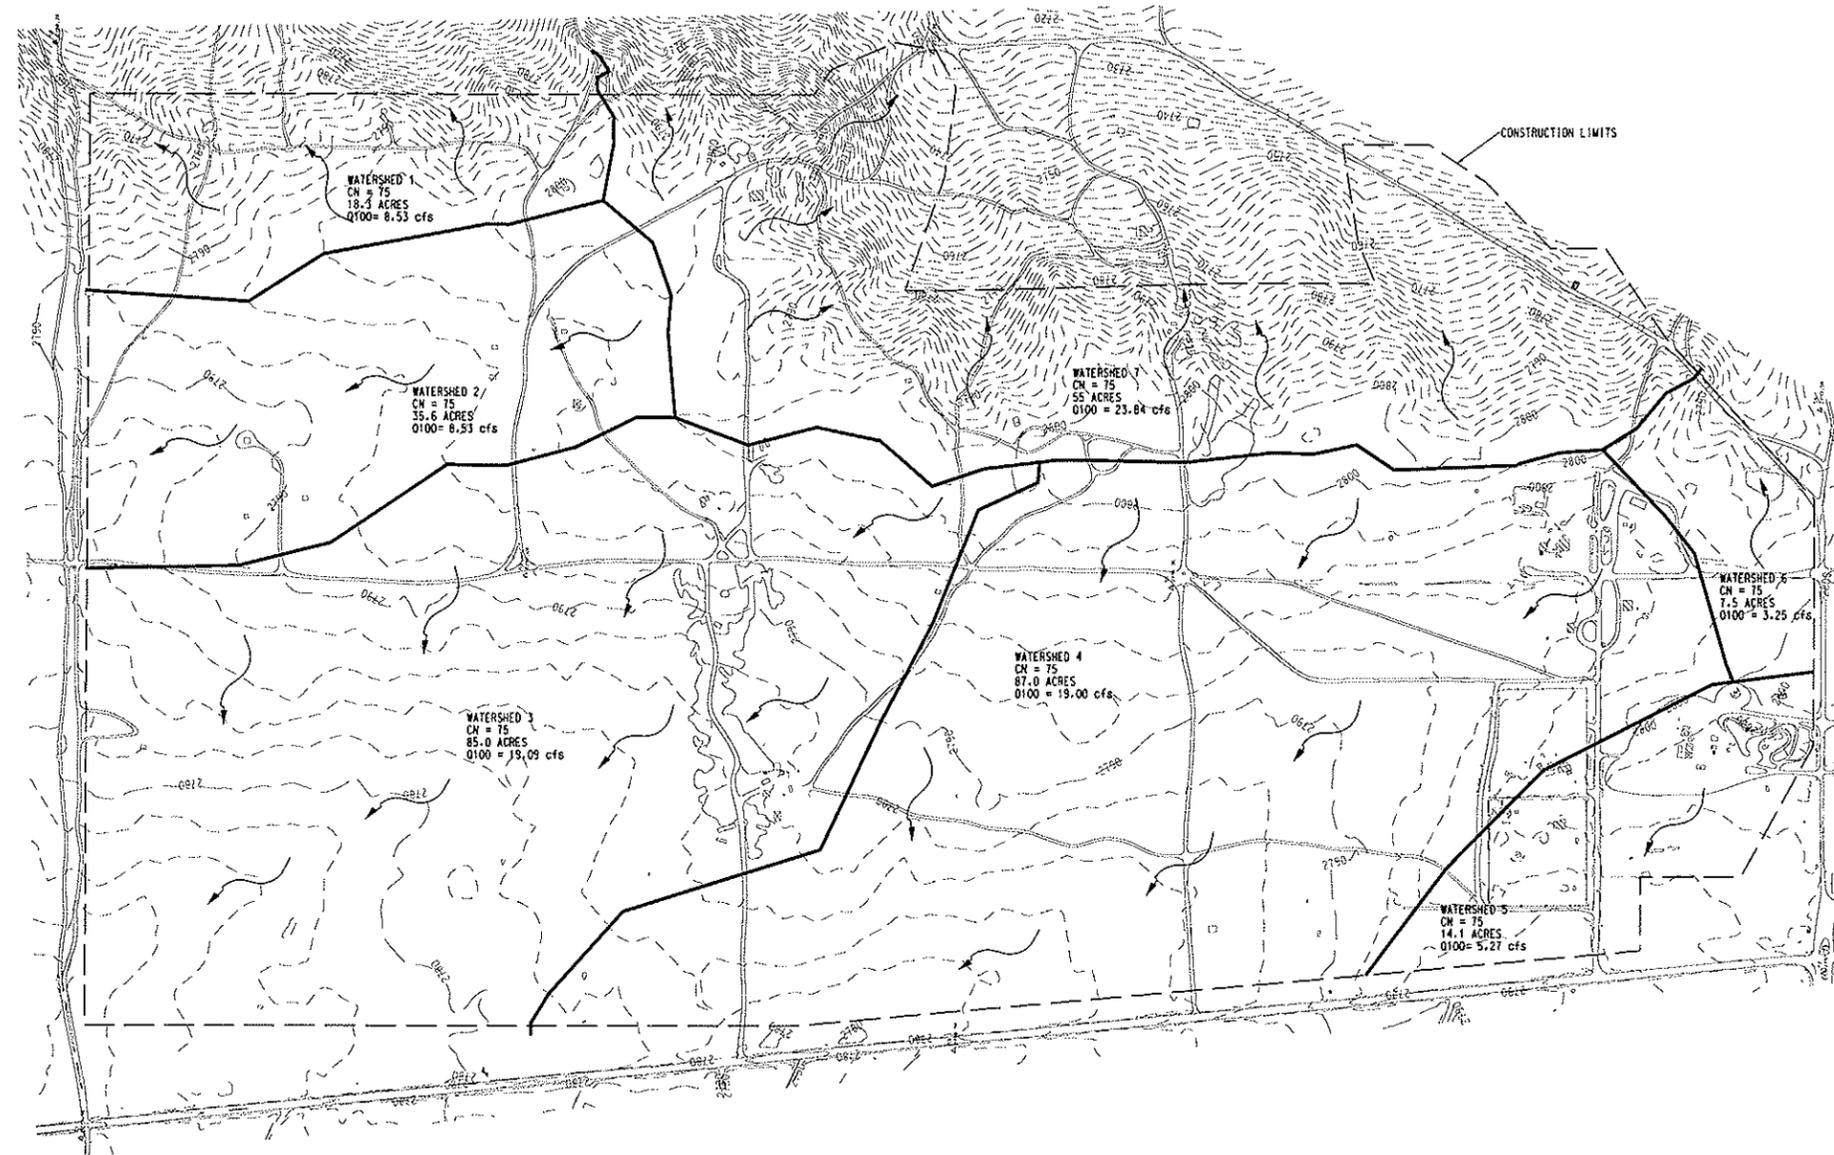

- PRELIMINARY -
NOT FOR CONSTRUCTION
CONFIDENTIAL

THESE DRAWINGS ARE CONFIDENTIAL IN NATURE. ANY REUSE OR UNAUTHORIZED DISTRIBUTION OF THE DRAWINGS CONTAINED HEREIN WILL BE A VIOLATION OF THIS CONFIDENTIALITY AGREEMENT AND SUBJECT THE VIOLATOR TO LIABILITY. REVIEW OF THESE MATERIALS BY RECIPIENT SHALL CONSTITUTE AN ACCEPTANCE OF THESE TERMS AND THE TERMS OF ANY UNDERLYING CONFIDENTIALITY AGREEMENT. NO MAY HAVE CHANGED OR OBTAINED THIS INFORMATION FROM A THIRD PARTY. IF THE RECIPIENT IS NOT IN AGREEMENT WITH THE OBLIGATION OF CONFIDENTIALITY THEN THE DRAWINGS SHALL BE RETURNED TO BIER.

A	PRELIMINARY	MAA			07-12-07
REV	DESCRIPTION	DWN	CHK	APP	DATE




INLAND ENERGY

VICTORVILLE COMBINED CYCLE
POWER PROJECT



PREDEVELOPMENT DRAINAGE

DESIGNED	by	date	DRAWING NUMBER
DRAWN	MAA	07-12-07	
CHECKED	MAA	07-12-07	
APPROVED			
			P-2005038-CP-071007-2



**APPENDIX B:
Drainage Calculations**

**HYDROLOGY AND HYDRAULIC
CALCULATIONS FOR**

**VICTORVILLE 2 HYBRID POWER PROJECT
CONCEPTUAL DESIGN**

BIBB PROJECT NO. 2007-020

ISSUED: July 12, 2007

Revision A: Issue For CEC Application

**BIBB AND ASSOCIATES, INC.
Engineers • Consultants**

**Corporate Office: 8455 Lenexa Drive
Lenexa • Kansas 66214 • USA
PHN 913-928-7000 • FAX 913-928-7500**

Table of Contents

Predevelopment

Hydrograph Return Period Recap.....	1
Summary Report.....	2
Hydrograph No. 1, SCS Runoff Area 1.....	3
TR-55 Time of Concentration Worksheet.....	4
Hydrograph No. 2, SCS Runoff Area 2	5
TR-55 Time of Concentration Worksheet.....	6
Hydrograph No. 3, SCS Runoff Area 3	7
TR-55 Time of Concentration Worksheet	8
Hydrograph No. 1, SCS Runoff Area 4	9
TR-55 Time of Concentration Worksheet	10
Hydrograph No. 1, SCS Runoff Area 5	11
TR-55 Time of Concentration Worksheet.....	12
Hydrograph No. 1, SCS Runoff Area 6	13
TR-55 Time of Concentration Worksheet.....	14
Hydrograph No. 1, SCS Runoff Area 7	15
TR-55 Time of Concentration Worksheet.....	16

Post Development

Hydrograph Return Period Recap.....	17
Summary Report.....	18
Hydrograph No. 1, SCS Runoff, Post Development.....	19
TR-55 Time of Concentration Worksheet.....	20
Hydrograph No. 2, Sediment Retention Facility.....	21
Pond Report	22
Hydrograph No. 3, SCS Runoff, Solar Field.....	23
TR-55 Time of Concentration Worksheet.....	24

Hydraflow Rainfall Report25
Culvert Master Culvert Post Development26

Sediment Retention Facility

Section View.....27
Front View.....28
Pond Report, Stage/Discharge Graph29

Hydrograph Return Period Recap

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No.	Hydrograph type (origin)	Inflow Hyd(s)	Peak Outflow (cfs)								Hydrograph description	
			1-Yr	2-Yr	3-Yr	5-Yr	10-Yr	25-Yr	50-Yr	100-Yr		
1	SCS Runoff	-----	-----	0.056	-----	-----	-----	-----	-----	-----	8.530	Area 1
2	SCS Runoff	-----	-----	0.109	-----	-----	-----	-----	-----	-----	8.526	Area 2
3	SCS Runoff	-----	-----	0.259	-----	-----	-----	-----	-----	-----	19.09	Area 3
4	SCS Runoff	-----	-----	0.266	-----	-----	-----	-----	-----	-----	19.00	Area 4
5	SCS Runoff	-----	-----	0.043	-----	-----	-----	-----	-----	-----	5.272	Area 5
6	SCS Runoff	-----	-----	0.023	-----	-----	-----	-----	-----	-----	3.251	Area 6
7	SCS Runoff	-----	-----	0.171	-----	-----	-----	-----	-----	-----	23.84	Area 7

Hydrograph Summary Report

Hydraflow Hydrographs by intelisolve v9.23

Hyd. No.	Hydrograph type (origin)	Peak flow (cfs)	Time interval (min)	Time to peak (min)	Hyd. volume (cuft)	Inflow hyd(s)	Maximum elevation (ft)	Total strge used (cuft)	Hydrograph description
1	SCS Runoff	8.530	2	606	63,824	----	-----	-----	Area 1
2	SCS Runoff	8.526	2	636	124,977	----	-----	-----	Area 2
3	SCS Runoff	19.09	2	640	296,450	----	-----	-----	Area 3
4	SCS Runoff	19.00	2	642	305,149	----	-----	-----	Area 4
5	SCS Runoff	5.272	2	612	49,176	----	-----	-----	Area 5
6	SCS Runoff	3.251	2	608	26,624	----	-----	-----	Area 6
7	SCS Runoff	23.84	2	608	195,246	----	-----	-----	Area 7
Hydraflow Victorville Pre Condition for constant flow					Return Period 100 Year			Wednesday, Jul 11, 2007	

Hydrograph Report

Hydraflow Hydrographs by Intellisolve v9.23


Wednesday, Jul 11, 2007

Hyd. No. 1

Area 1

Hydrograph type = SCS Runoff
 Storm frequency = 100 yrs
 Time interval = 2 min
 Drainage area = 18,300 ac
 Basin Slope = 0.0 %
 Tc method = TR55
 Total precip. = 3.00 in
 Storm duration = 24 hrs

Peak discharge = 8.530 cfs
 Time to peak = 606 min
 Hyd. volume = 63,824 cuft
 Curve number = 75
 Hydraulic length = 0 ft
 Time of conc. (Tc) = 18.10 min
 Distribution = Type I
 Shape factor = 484

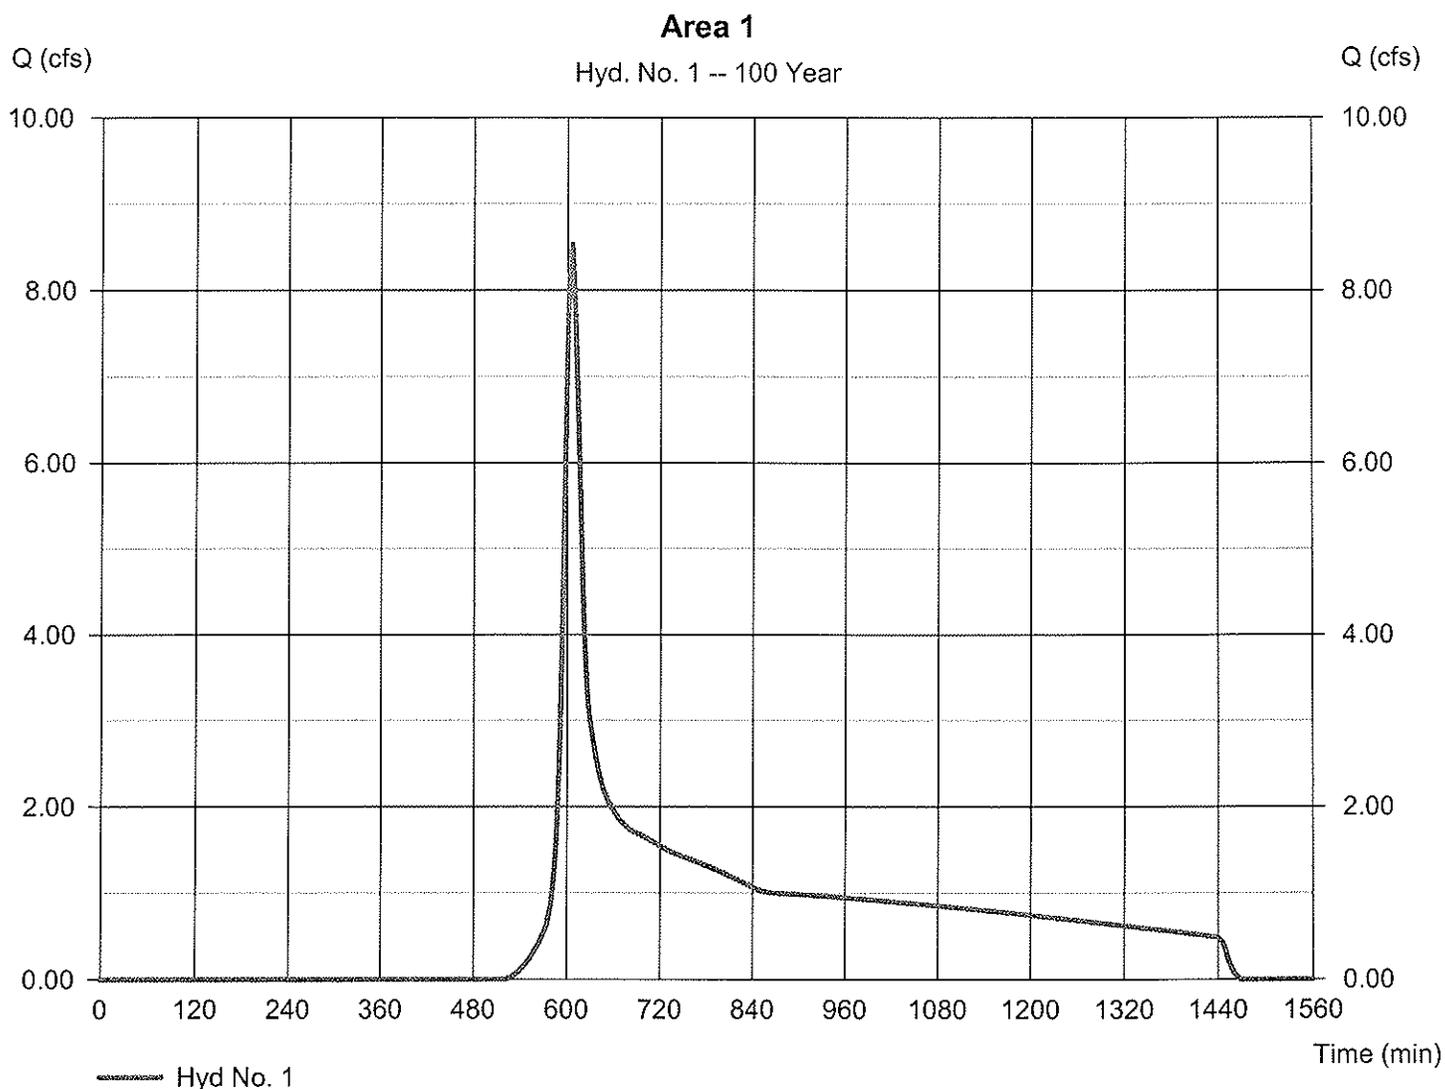

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 1

Area 1

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 4.00	0.00	0.00	
Travel Time (min)	= 13.28	+ 0.00	+ 0.00	= 13.28
Shallow Concentrated Flow				
Flow length (ft)	= 0.00	0.00	0.00	
Watercourse slope (%)	= 0.00	0.00	0.00	
Surface description	= Paved	Paved	Paved	
Average velocity (ft/s)	= 0.00	0.00	0.00	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Channel Flow				
X sectional flow area (sqft)	= 100.00	105.00	0.00	
Wetted perimeter (ft)	= 100.00	105.00	0.00	
Channel slope (%)	= 5.70	5.00	0.00	
Manning's n-value	= 0.150	0.150	0.015	
Velocity (ft/s)	= 2.37	2.22	0.00	
Flow length (ft)	= 450.0	225.0	0.0	
Travel Time (min)	= 3.16	+ 1.69	+ 0.00	= 4.85
Total Travel Time, Tc				18.10 min


Hydrograph Report

Hyd. No. 2

Area 2

Hydrograph type = SCS Runoff
Storm frequency = 100 yrs
Time interval = 2 min
Drainage area = 35.600 ac
Basin Slope = 0.0 %
Tc method = TR55
Total precip. = 3.00 in
Storm duration = 24 hrs

Peak discharge = 8.526 cfs
Time to peak = 636 min
Hyd. volume = 124,977 cuft
Curve number = 75
Hydraulic length = 0 ft
Time of conc. (Tc) = 62.50 min
Distribution = Type I
Shape factor = 484

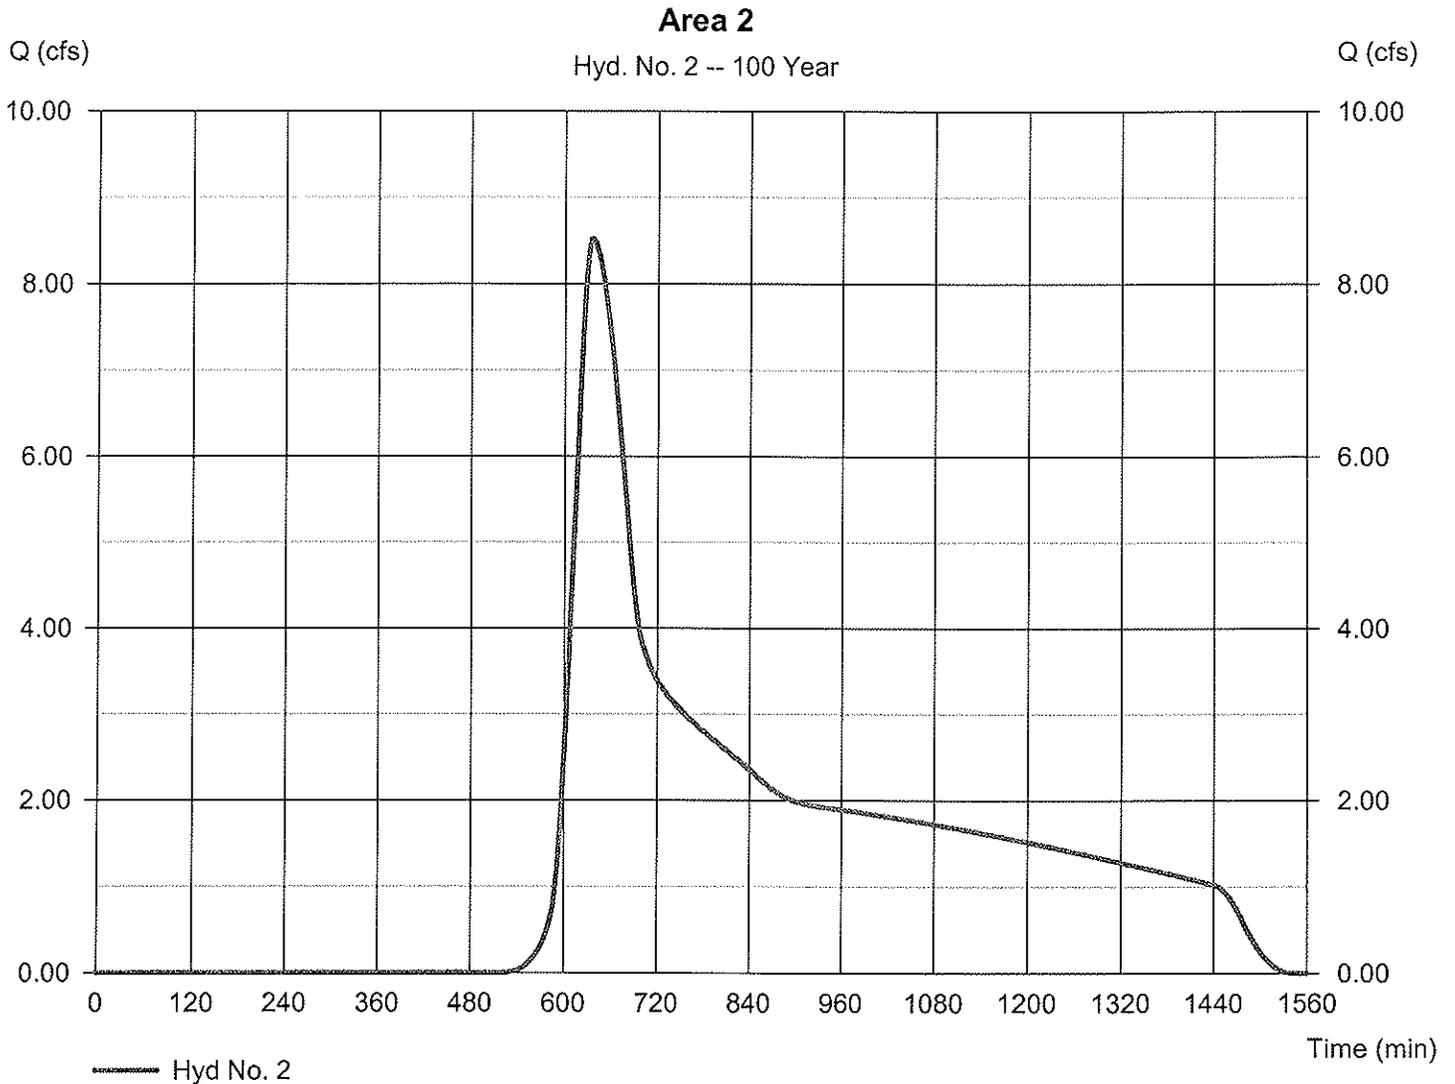

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 2

Area 2

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 0.60	0.00	0.00	
Travel Time (min)	= 28.37	+ 0.00	+ 0.00	= 28.37
Shallow Concentrated Flow				
Flow length (ft)	= 0.00	0.00	0.00	
Watercourse slope (%)	= 0.00	0.00	0.00	
Surface description	= Paved	Paved	Paved	
Average velocity (ft/s)	= 0.00	0.00	0.00	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Channel Flow				
X sectional flow area (sqft)	= 430.00	0.00	0.00	
Wetted perimeter (ft)	= 430.00	0.00	0.00	
Channel slope (%)	= 0.70	0.00	0.00	
Manning's n-value	= 0.150	0.015	0.015	
Velocity (ft/s)	= 0.83	0.00	0.00	
Flow length (ft)	= 1700.0	0.0	0.0	
Travel Time (min)	= 34.09	+ 0.00	+ 0.00	= 34.09
Total Travel Time, Tc				62.50 min

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Wednesday, Jul 11, 2007

Hyd. No. 3

Area 3

Hydrograph type = SCS Runoff
 Storm frequency = 100 yrs
 Time interval = 2 min
 Drainage area = 85.000 ac
 Basin Slope = 0.0 %
 Tc method = TR55
 Total precip. = 3.00 in
 Storm duration = 24 hrs

Peak discharge = 19.09 cfs
 Time to peak = 640 min
 Hyd. volume = 296,450 cuft
 Curve number = 75
 Hydraulic length = 0 ft
 Time of conc. (Tc) = 69.20 min
 Distribution = Type I
 Shape factor = 484

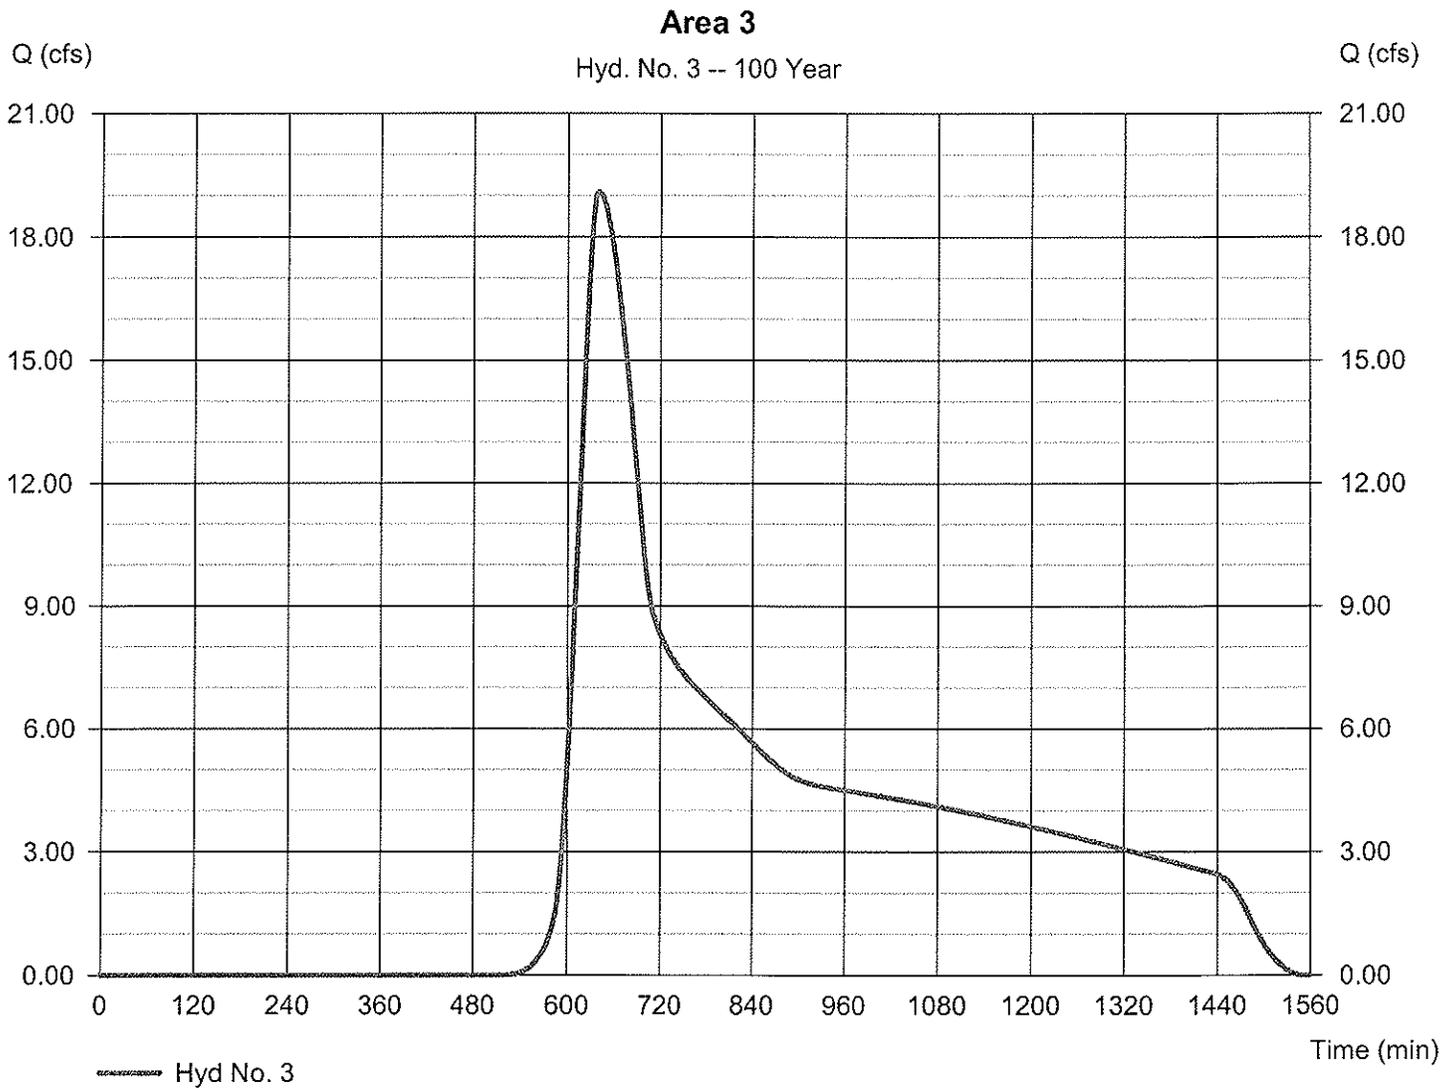

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 3

Area 3

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 1.90	0.00	0.00	
Travel Time (min)	= 17.89	+ 0.00	+ 0.00	= 17.89
Shallow Concentrated Flow				
Flow length (ft)	= 0.00	0.00	0.00	
Watercourse slope (%)	= 0.00	0.00	0.00	
Surface description	= Unpaved	Paved	Paved	
Average velocity (ft/s)	= 0.00	0.00	0.00	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Channel Flow				
X sectional flow area (sqft)	= 460.00	600.00	0.00	
Wetted perimeter (ft)	= 460.00	600.00	0.00	
Channel slope (%)	= 0.70	1.30	0.00	
Manning's n-value	= 0.150	0.150	0.015	
Velocity (ft/s)	= 0.83	1.13	0.00	
Flow length (ft)	= 1900.0	900.0	0.0	
Travel Time (min)	= 38.10	+ 13.24	+ 0.00	= 51.35
Total Travel Time, Tc				69.20 min

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Wednesday, Jul 11, 2007

Hyd. No. 4

Area 4

Hydrograph type = SCS Runoff
 Storm frequency = 100 yrs
 Time interval = 2 min
 Drainage area = 87.000 ac
 Basin Slope = 0.0 %
 Tc method = TR55
 Total precip. = 3.00 in
 Storm duration = 24 hrs

Peak discharge = 19.00 cfs
 Time to peak = 642 min
 Hyd. volume = 305,149 cuft
 Curve number = 75
 Hydraulic length = 0 ft
 Time of conc. (Tc) = 72.90 min
 Distribution = Type I
 Shape factor = 484

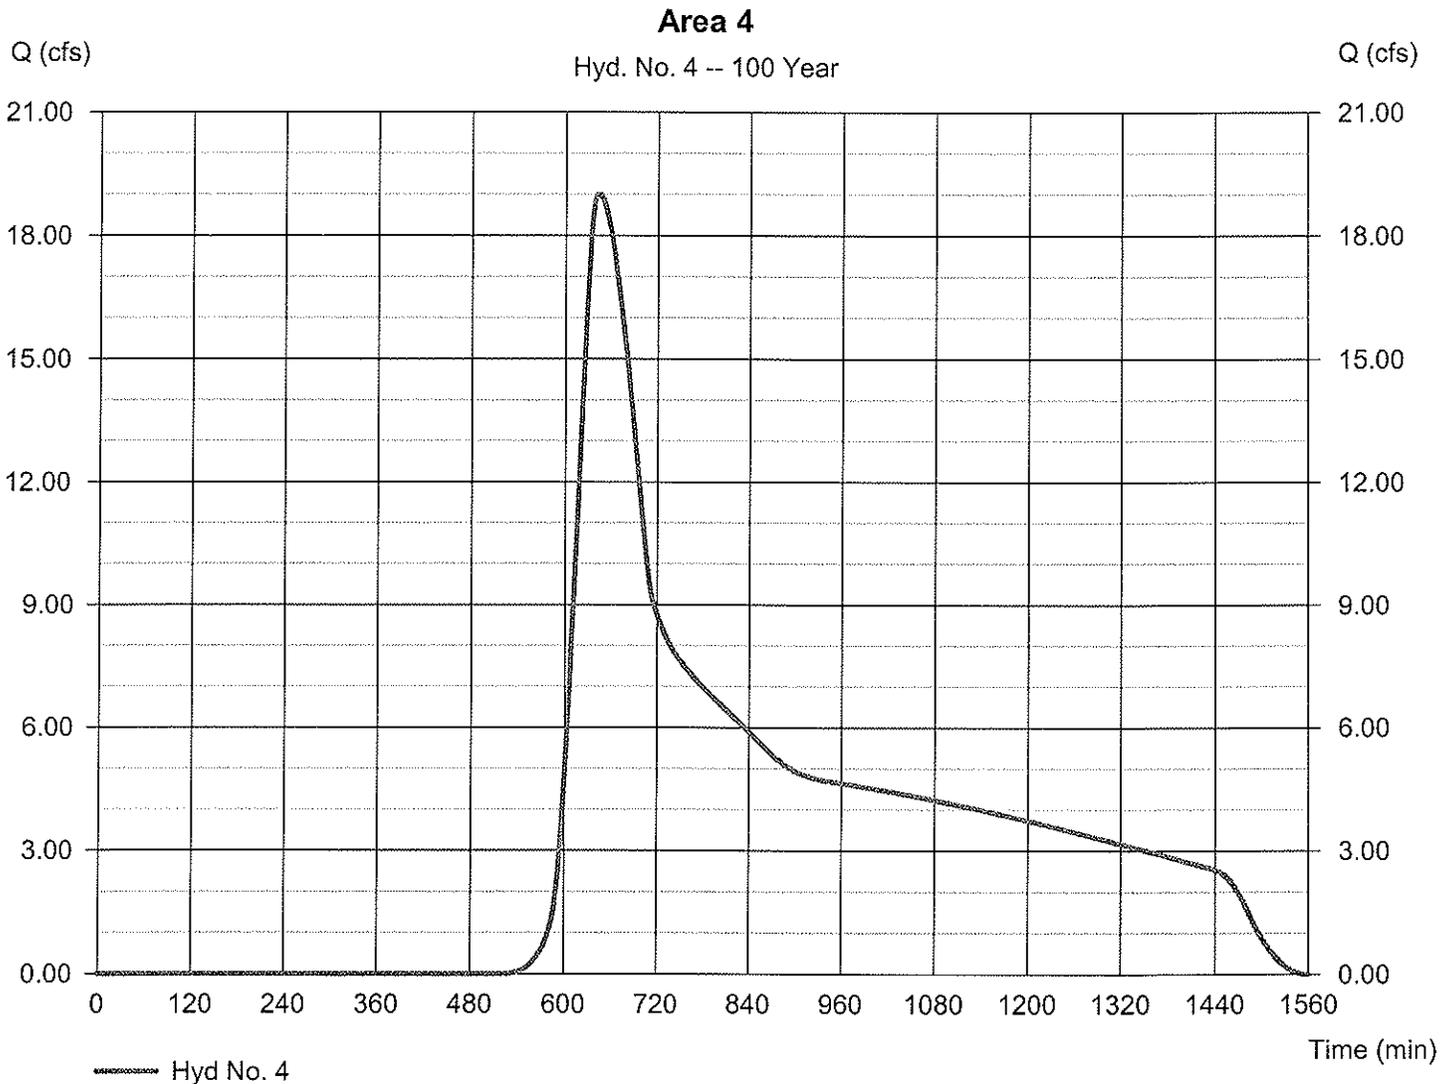

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 4

Area 4

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 1.70	0.00	0.00	
Travel Time (min)	= 18.70	+ 0.00	+ 0.00	= 18.70
Shallow Concentrated Flow				
Flow length (ft)	= 0.00	0.00	0.00	
Watercourse slope (%)	= 0.00	0.00	0.00	
Surface description	= Paved	Paved	Paved	
Average velocity (ft/s)	= 0.00	0.00	0.00	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Channel Flow				
X sectional flow area (sqft)	= 640.00	0.00	0.00	
Wetted perimeter (ft)	= 640.00	0.00	0.00	
Channel slope (%)	= 0.70	0.00	0.00	
Manning's n-value	= 0.150	0.150	0.015	
Velocity (ft/s)	= 0.83	0.00	0.00	
Flow length (ft)	= 2700.0	0.0	0.0	
Travel Time (min)	= 54.15	+ 0.00	+ 0.00	= 54.15
Total Travel Time, Tc				72.90 min


Hydrograph Report

Hyd. No. 5

Area 5

Hydrograph type = SCS Runoff
Storm frequency = 100 yrs
Time interval = 2 min
Drainage area = 14.100 ac
Basin Slope = 0.0 %
Tc method = TR55
Total precip. = 3.00 in
Storm duration = 24 hrs

Peak discharge = 5.272 cfs
Time to peak = 612 min
Hyd. volume = 49,176 cuft
Curve number = 75
Hydraulic length = 0 ft
Time of conc. (Tc) = 30.00 min
Distribution = Type I
Shape factor = 484

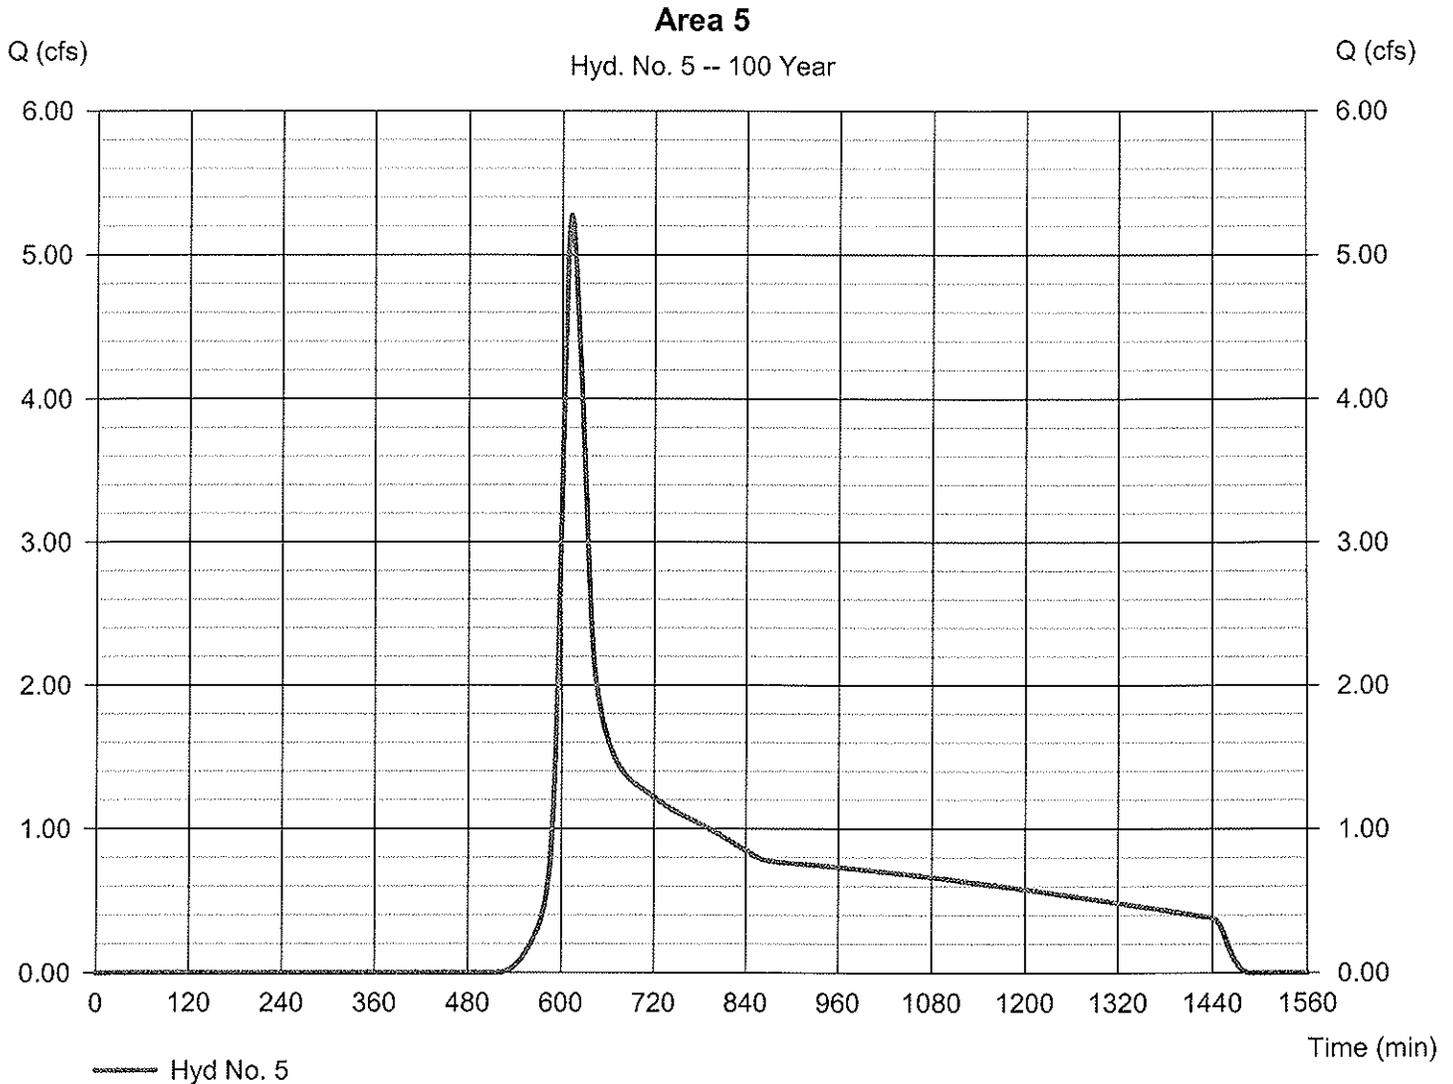

TR55 Tc Worksheet

Hydraflow Hydrographs by Intefisoive v9.23

Hyd. No. 5

Area 5

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 1.00	0.00	0.00	
Travel Time (min)	= 23.13	+ 0.00	+ 0.00	= 23.13
Shallow Concentrated Flow				
Flow length (ft)	= 500.00	0.00	0.00	
Watercourse slope (%)	= 0.70	0.00	0.00	
Surface description	= Unpaved	Paved	Paved	
Average velocity (ft/s)	= 1.35	0.00	0.00	
Travel Time (min)	= 6.17	+ 0.00	+ 0.00	= 6.17
Channel Flow				
X sectional flow area (sqft)	= 50.00	0.00	0.00	
Wetted perimeter (ft)	= 50.00	0.00	0.00	
Channel slope (%)	= 1.60	0.00	0.00	
Manning's n-value	= 0.015	0.015	0.015	
Velocity (ft/s)	= 12.56	0.00	0.00	
Flow length (ft)	= 500.0	0.0	0.0	
Travel Time (min)	= 0.66	+ 0.00	+ 0.00	= 0.66
Total Travel Time, Tc				30.00 min


Hydrograph Report

Hyd. No. 6

Area 6

Hydrograph type = SCS Runoff
Storm frequency = 100 yrs
Time interval = 2 min
Drainage area = 7.500 ac
Basin Slope = 0.0 %
Tc method = TR55
Total precip. = 3.00 in
Storm duration = 24 hrs

Peak discharge = 3.251 cfs
Time to peak = 608 min
Hyd. volume = 26,624 cuft
Curve number = 75
Hydraulic length = 0 ft
Time of conc. (Tc) = 20.60 min
Distribution = Type I
Shape factor = 484

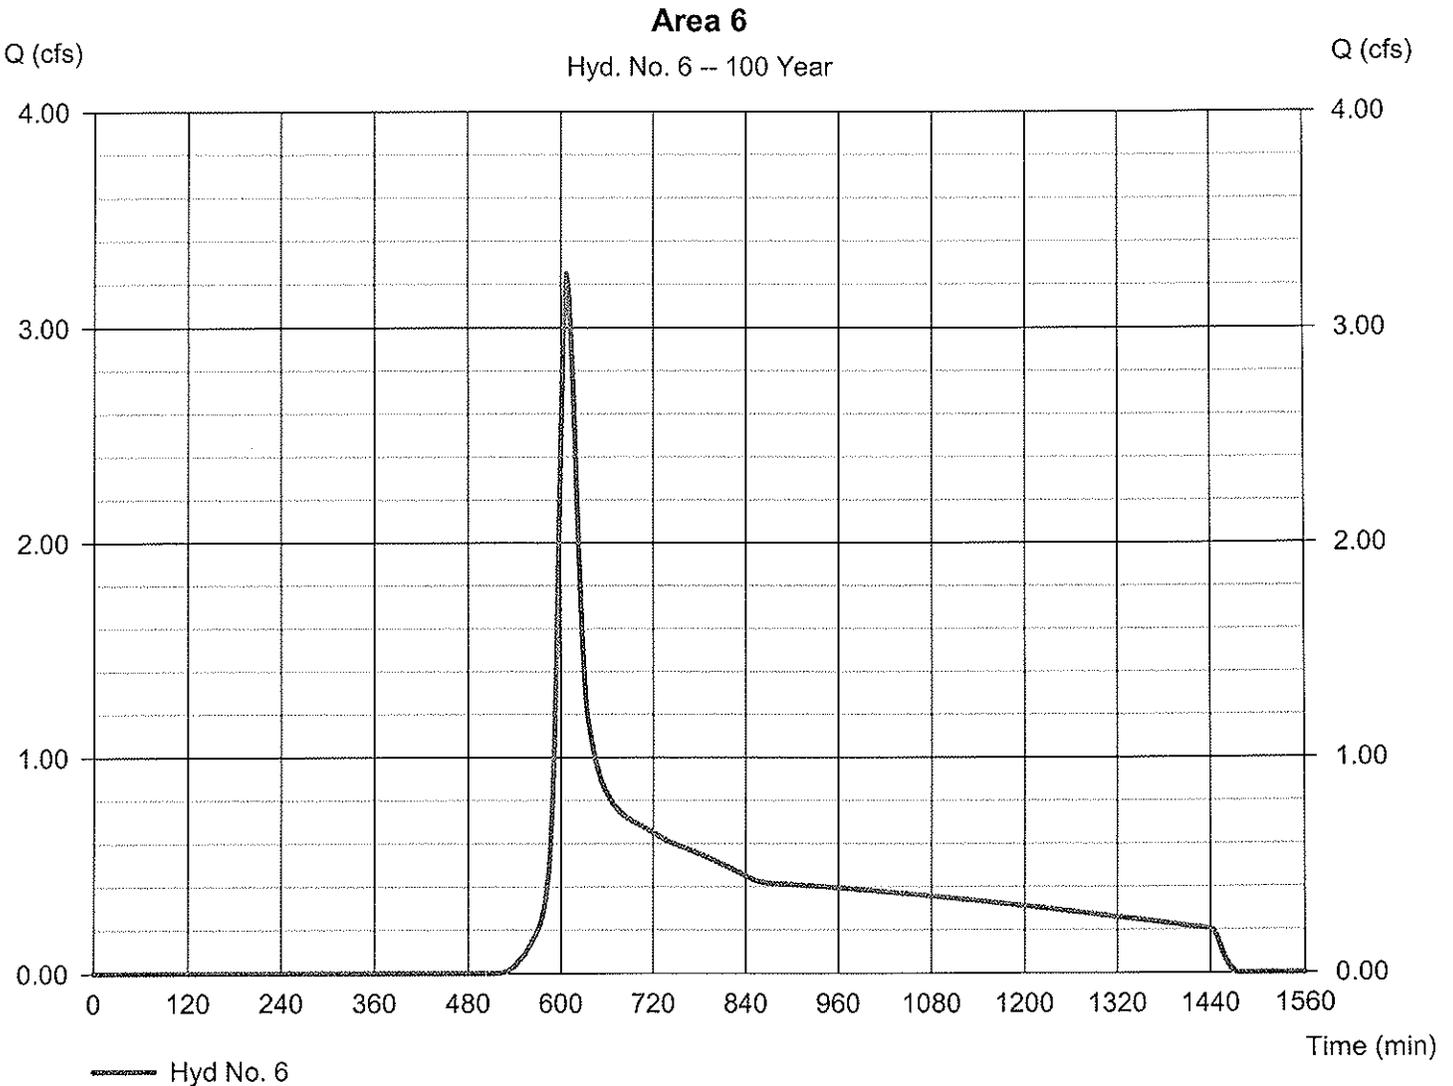

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 6

Area 6

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 1.90	0.00	0.00	
Travel Time (min)	= 17.89	+ 0.00	+ 0.00	= 17.89
Shallow Concentrated Flow				
Flow length (ft)	= 450.00	0.00	0.00	
Watercourse slope (%)	= 2.00	0.00	0.00	
Surface description	= Paved	Paved	Paved	
Average velocity (ft/s)	= 2.87	0.00	0.00	
Travel Time (min)	= 2.61	+ 0.00	+ 0.00	= 2.61
Channel Flow				
X sectional flow area (sqft)	= 125.00	0.00	0.00	
Wetted perimeter (ft)	= 125.00	0.00	0.00	
Channel slope (%)	= 4.80	0.00	0.00	
Manning's n-value	= 0.015	0.015	0.015	
Velocity (ft/s)	= 21.76	0.00	0.00	
Flow length (ft)	= 130.0	0.0	0.0	
Travel Time (min)	= 0.10	+ 0.00	+ 0.00	= 0.10
Total Travel Time, Tc				20.60 min

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Wednesday, Jul 11, 2007

Hyd. No. 7

Area 7

Hydrograph type = SCS Runoff
Storm frequency = 100 yrs
Time interval = 2 min
Drainage area = 55.000 ac
Basin Slope = 0.0 %
Tc method = TR55
Total precip. = 3.00 in
Storm duration = 24 hrs

Peak discharge = 23.84 cfs
Time to peak = 608 min
Hyd. volume = 195,246 cuft
Curve number = 75
Hydraulic length = 0 ft
Time of conc. (Tc) = 22.90 min
Distribution = Type I
Shape factor = 484

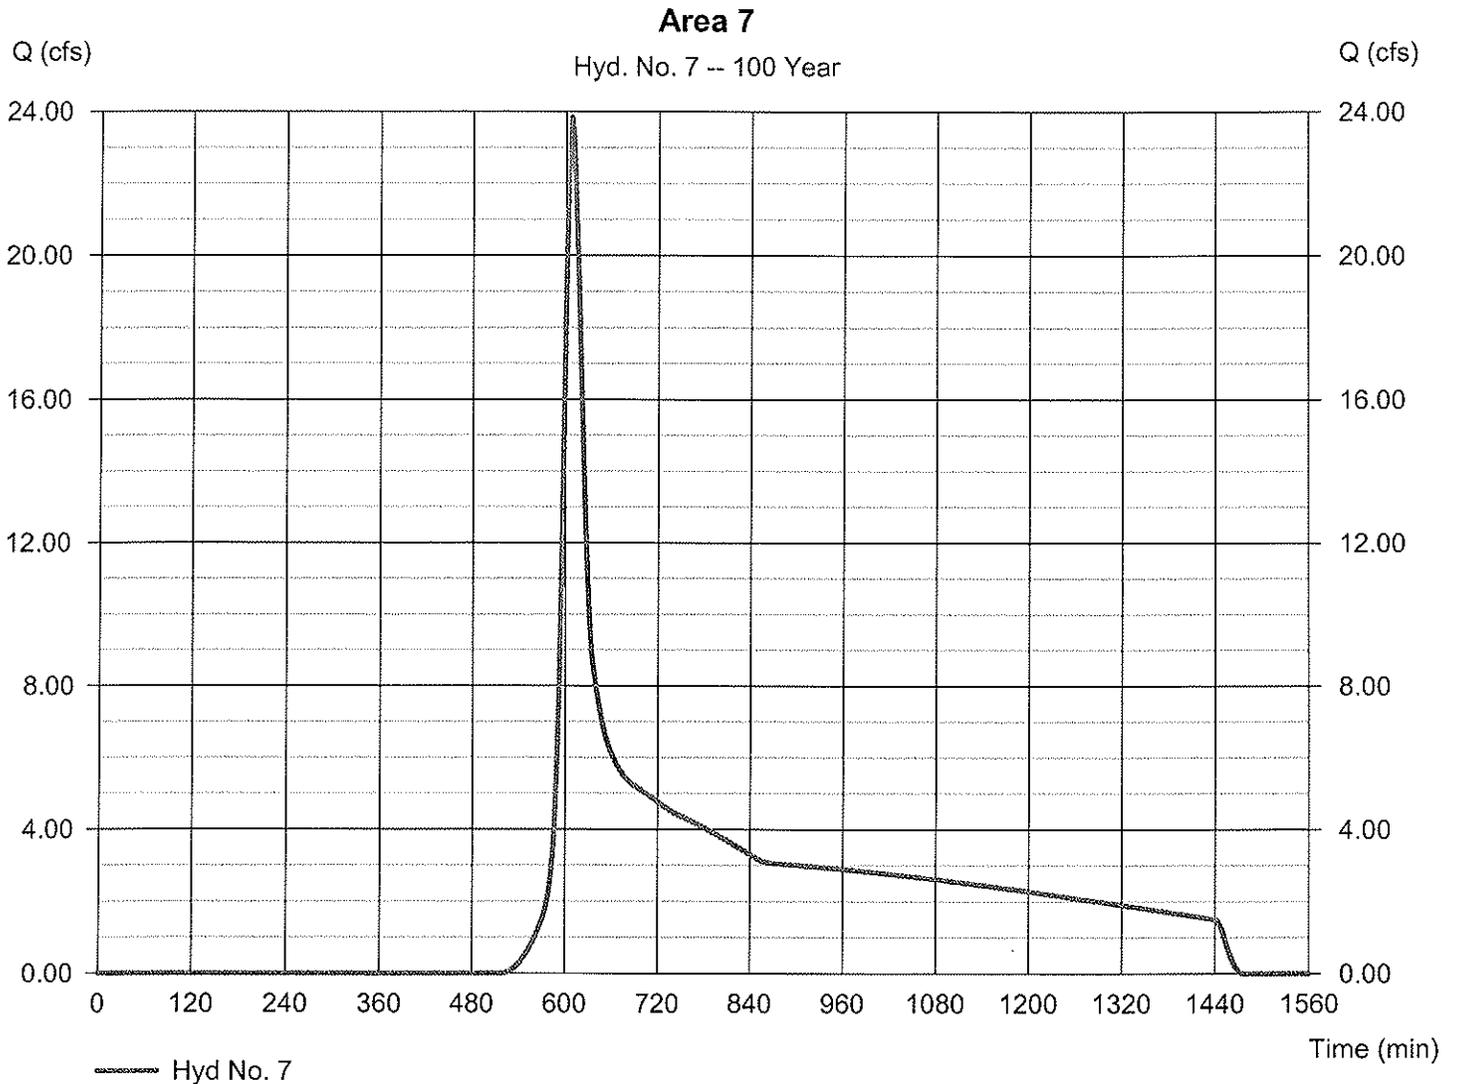

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 7

Area 7

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.150	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.00	0.00	0.00	
Land slope (%)	= 2.20	0.00	0.00	
Travel Time (min)	= 16.87	+ 0.00	+ 0.00	= 16.87
Shallow Concentrated Flow				
Flow length (ft)	= 0.00	0.00	0.00	
Watercourse slope (%)	= 0.00	0.00	0.00	
Surface description	= Paved	Paved	Paved	
Average velocity (ft/s)	= 0.00	0.00	0.00	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Channel Flow				
X sectional flow area (sqft)	= 100.00	90.00	200.00	
Wetted perimeter (ft)	= 100.00	90.00	200.00	
Channel slope (%)	= 7.00	4.20	5.30	
Manning's n-value	= 0.150	0.150	0.015	
Velocity (ft/s)	= 2.63	2.04	22.87	
Flow length (ft)	= 350.0	450.0	200.0	
Travel Time (min)	= 2.22	+ 3.68	+ 0.15	= 6.05
Total Travel Time, Tc				22.90 min

Hydrograph Return Period Recap

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No.	Hydrograph type (origin)	Inflow Hyd(s)	Peak Outflow (cfs)								Hydrograph description	
			1-Yr	2-Yr	3-Yr	5-Yr	10-Yr	25-Yr	50-Yr	100-Yr		
1	SCS Runoff	-----	-----	14.29	-----	-----	-----	-----	-----	-----	51.74	Post Development
2	Reservoir	1	-----	0.314	-----	-----	-----	-----	-----	-----	1.510	Sediment Retention Fac
3	SCS Runoff	-----	-----	0.761	-----	-----	-----	-----	-----	-----	53.80	Solar Field

Hydrograph Summary Report

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No.	Hydrograph type (origin)	Peak flow (cfs)	Time interval (min)	Time to peak (min)	Hyd. volume (cuft)	Inflow hyd(s)	Maximum elevation (ft)	Total strge used (cuft)	Hydrograph description
1	SCS Runoff	51.74	1	599	249,445	---	-----	-----	Post Development
2	Reservoir	1.510	1	1252	169,994	1	2786.80	178,100	Sediment Retention Fac
3	SCS Runoff	53.80	1	645	872,400	---	-----	-----	Solar Field
Prelim Pond Sizing idf curve modified Post. Return Period: 100 Year								Thursday, Jul 12, 2007	

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Thursday, Jul 12, 2007

Hyd. No. 1

Post Development

Hydrograph type = SCS Runoff
 Storm frequency = 100 yrs
 Time interval = 1 min
 Drainage area = 25.850 ac
 Basin Slope = 0.0 %
 Tc method = TR55
 Total precip. = 3.00 in
 Storm duration = 24 hrs

Peak discharge = 51.74 cfs
 Time to peak = 599 min
 Hyd. volume = 249,445 cuft
 Curve number = 97
 Hydraulic length = 0 ft
 Time of conc. (Tc) = 9.50 min
 Distribution = Type I
 Shape factor = 484

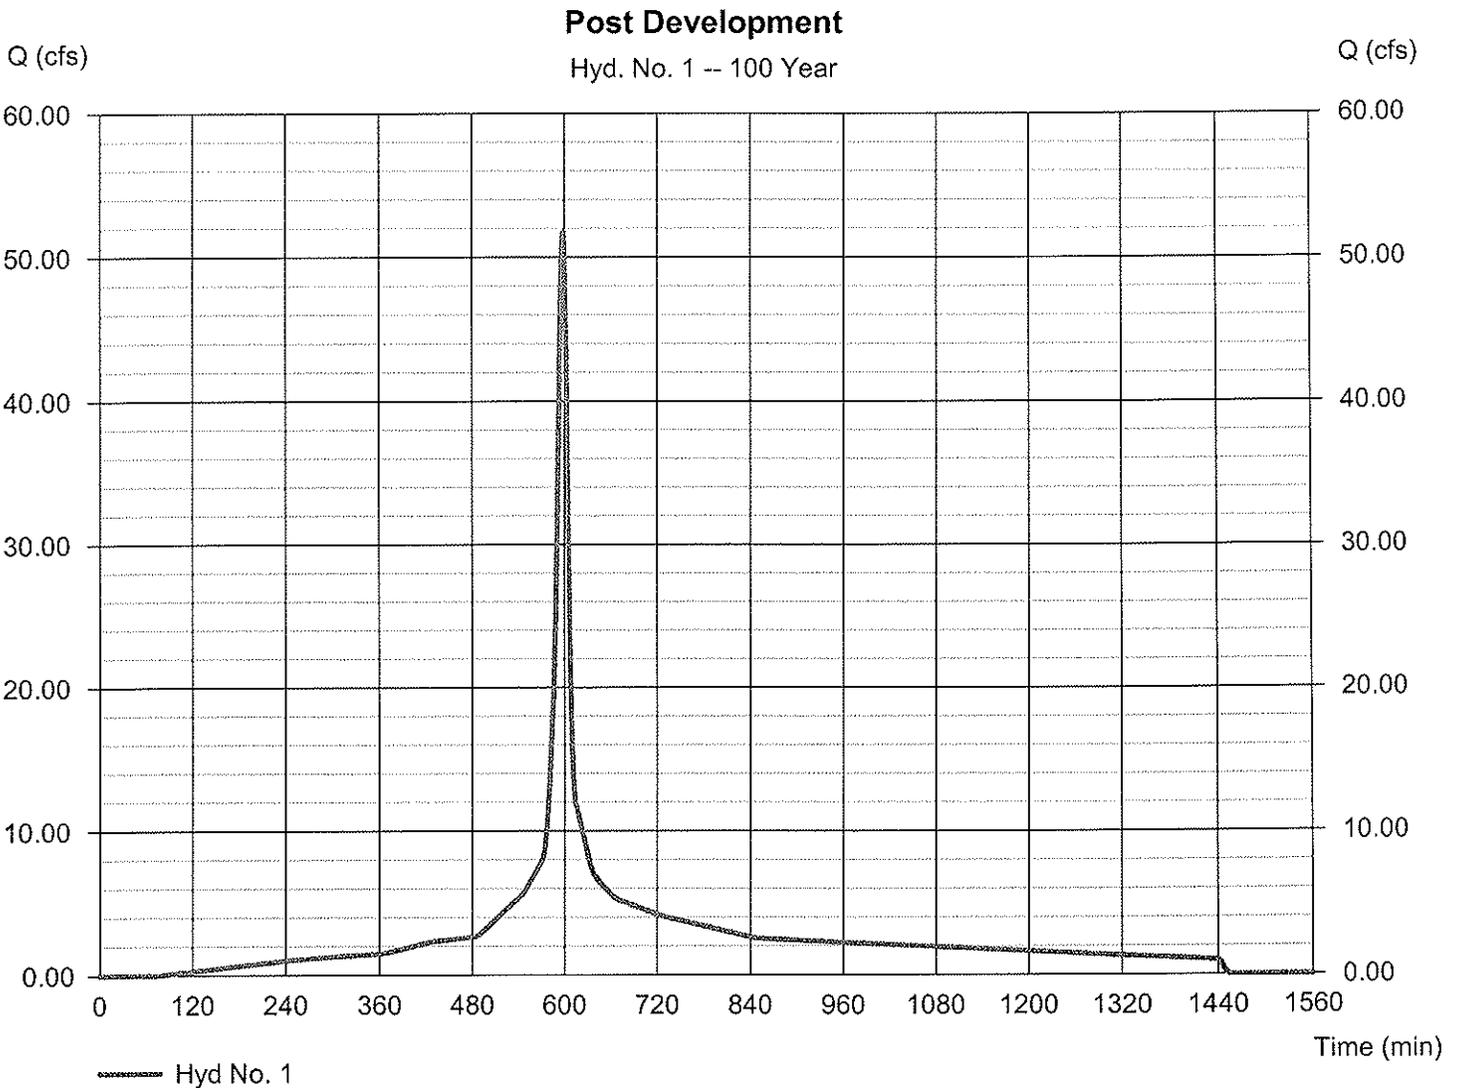

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 1

Post Development

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.011	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.20	0.00	0.00	
Land slope (%)	= 0.50	0.00	0.00	
Travel Time (min)	= 3.44	+ 0.00	+ 0.00	= 3.44
Shallow Concentrated Flow				
Flow length (ft)	= 100.00	0.00	0.00	
Watercourse slope (%)	= 0.50	0.00	0.00	
Surface description	= Paved	Unpaved	Paved	
Average velocity (ft/s)	= 1.44	0.00	0.00	
Travel Time (min)	= 1.16	+ 0.00	+ 0.00	= 1.16
Channel Flow				
X sectional flow area (sqft)	= 16.00	0.00	0.00	
Wetted perimeter (ft)	= 16.50	0.00	0.00	
Channel slope (%)	= 0.50	0.00	0.00	
Manning's n-value	= 0.035	0.015	0.015	
Velocity (ft/s)	= 2.95	0.00	0.00	
Flow length (ft)	= 859.0	0.0	0.0	
Travel Time (min)	= 4.86	+ 0.00	+ 0.00	= 4.86
Total Travel Time, Tc				9.50 min

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Thursday, Jul 12, 2007

Hyd. No. 2

Sediment Retention Fac

Hydrograph type	= Reservoir	Peak discharge	= 1,510 cfs
Storm frequency	= 100 yrs	Time to peak	= 1252 min
Time interval	= 1 min	Hyd. volume	= 169,994 cuft
Inflow hyd. No.	= 1 - Post Development	Max. Elevation	= 2786.80 ft
Reservoir name	= Sediment Retention Fac	Max. Storage	= 178,100 cuft

Storage Indication method used.

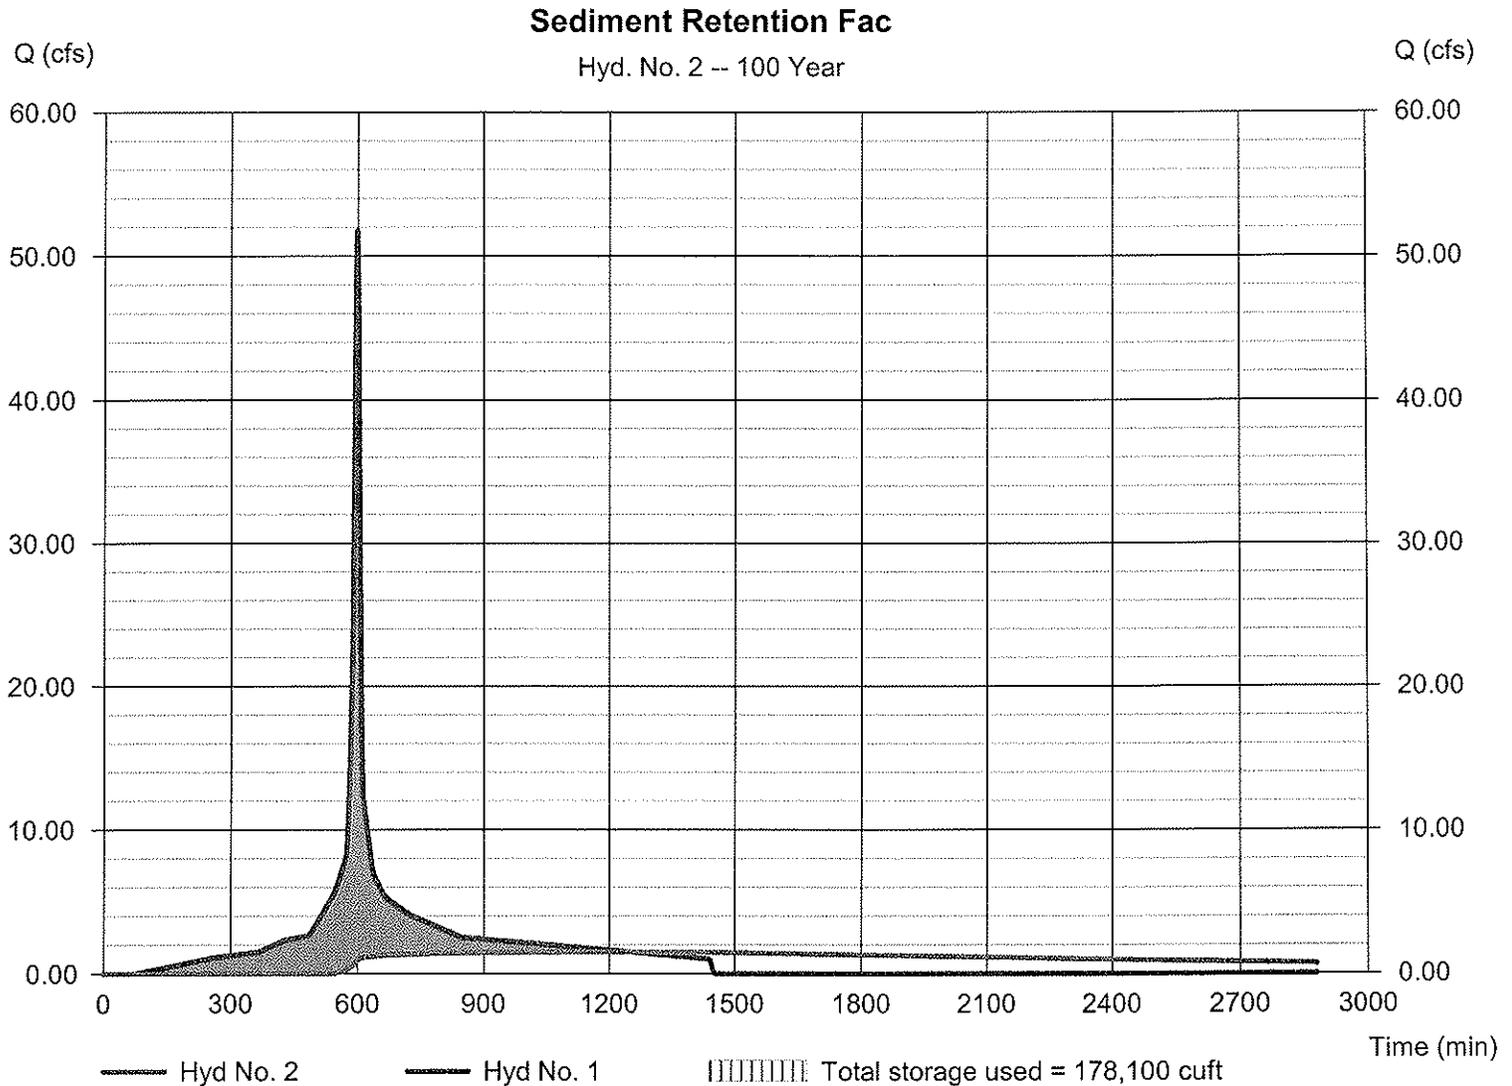

Pond Report

Pond No. 1 - Sediment Retention Fac

Pond Data

Contours - User-defined contour areas. Average end area method used for volume calculation. Beginning Elevation = 2783.00 ft

Stage / Storage Table

Stage (ft)	Elevation (ft)	Contour area (sqft)	Incr. Storage (cuft)	Total storage (cuft)
0.00	2783.00	40,501	0	0
1.00	2784.00	43,723	42,112	42,112
2.00	2785.00	47,047	45,385	87,497
3.00	2786.00	50,471	48,759	136,256
4.00	2787.00	53,995	52,233	188,489
5.00	2788.00	57,620	55,808	244,297
6.00	2789.00	61,646	59,633	303,930
7.00	2790.00	65,172	63,409	367,339
8.00	2791.00	69,098	67,135	434,474
9.00	2792.00	73,125	71,112	505,585
10.00	2793.00	77,253	75,189	580,774
11.00	2794.00	81,481	79,367	660,141

Culvert / Orifice Structures

	[A]	[B]	[C]	[PrfRsr]
Rise (in)	= 12.00	6.00	0.00	0.00
Span (in)	= 12.00	6.00	0.00	0.00
No. Barrels	= 1	1	0	0
Invert El. (ft)	= 2783.00	2784.00	0.00	0.00
Length (ft)	= 110.00	0.00	0.00	0.00
Slope (%)	= 2.73	0.00	0.00	n/a
N-Value	= .013	.013	.000	n/a
Orifice Coeff.	= 0.60	0.60	0.00	0.00
Multi-Stage	= n/a	Yes	No	No

Weir Structures

	[A]	[B]	[C]	[D]
Crest Len (ft)	= 16.00	0.00	0.00	0.00
Crest El. (ft)	= 2787.50	0.00	0.00	0.00
Weir Coeff.	= 3.33	0.00	0.00	0.00
Weir Type	= Riser	---	---	---
Multi-Stage	= Yes	No	No	No
Exfil.(in/hr)	= 0.000 (by Contour)			
TW Elev. (ft)	= 0.00			

Note: Culvert/Orifice outflows are analyzed under inlet (ic) and outlet (oc) control. Weir risers checked for orifice conditions (ic) and submergence (s).

Stage / Storage / Discharge Table

Stage ft	Storage cuft	Elevation ft	Civ A cfs	Civ B cfs	Civ C cfs	PrfRsr cfs	Wr A cfs	Wr B cfs	Wr C cfs	Wr D cfs	Exfil cfs	User cfs	Total cfs
0.00	0	2783.00	0.00	0.00	---	---	0.00	---	---	---	---	---	0.000
1.00	42,112	2784.00	0.00	0.00	---	---	0.00	---	---	---	---	---	0.000
2.00	87,497	2785.00	0.84 IC	0.82 IC	---	---	0.00	---	---	---	---	---	0.819
3.00	136,256	2786.00	1.27 IC	1.25 IC	---	---	0.00	---	---	---	---	---	1.251
4.00	188,489	2787.00	1.58 IC	1.57 IC	---	---	0.00	---	---	---	---	---	1.568
5.00	244,297	2788.00	7.51 OC	0.16 IC	---	---	7.34 s	---	---	---	---	---	7.505
6.00	303,930	2789.00	8.05 OC	0.04 IC	---	---	7.91 s	---	---	---	---	---	7.946
7.00	367,339	2790.00	8.54 OC	0.00	---	---	0.00	---	---	---	---	---	8.535
8.00	434,474	2791.00	9.00 OC	0.00	---	---	0.00	---	---	---	---	---	8.997
9.00	505,585	2792.00	9.44 OC	0.00	---	---	0.00	---	---	---	---	---	9.436
10.00	580,774	2793.00	9.86 OC	0.00	---	---	0.00	---	---	---	---	---	9.855
11.00	660,141	2794.00	10.26 OC	0.00	---	---	0.00	---	---	---	---	---	10.26

Hydrograph Report

Hydraflow Hydrographs by Intelisolve v9.23


Thursday, Jul 12, 2007

Hyd. No. 3

Solar Field

Hydrograph type = SCS Runoff
 Storm frequency = 100 yrs
 Time interval = 1 min
 Drainage area = 250.140 ac
 Basin Slope = 0.0 %
 Tc method = TR55
 Total precip. = 3.00 in
 Storm duration = 24 hrs

Peak discharge = 53.80 cfs
 Time to peak = 645 min
 Hyd. volume = 872,400 cuft
 Curve number = 75
 Hydraulic length = 0 ft
 Time of conc. (Tc) = 74.90 min
 Distribution = Type I
 Shape factor = 484

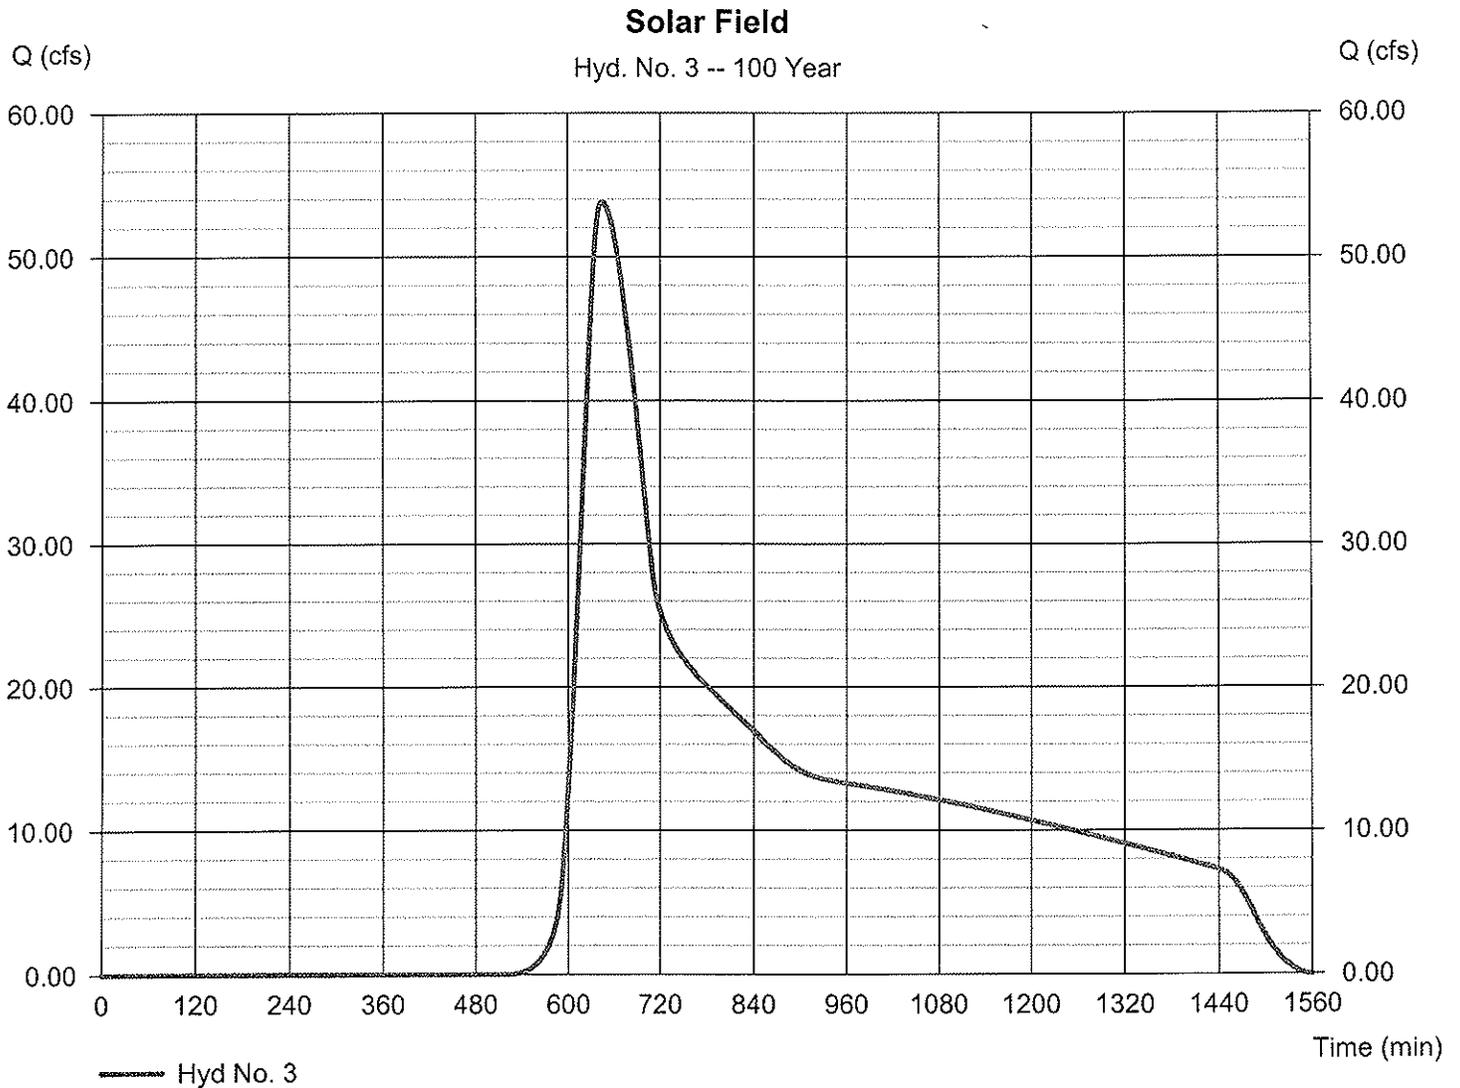

TR55 Tc Worksheet

Hydraflow Hydrographs by Intelisolve v9.23

Hyd. No. 3

Solar Field

<u>Description</u>	<u>A</u>	<u>B</u>	<u>C</u>	<u>Totals</u>
Sheet Flow				
Manning's n-value	= 0.011	0.011	0.011	
Flow length (ft)	= 100.0	0.0	0.0	
Two-year 24-hr precip. (in)	= 1.20	0.00	0.00	
Land slope (%)	= 0.50	0.00	0.00	
Travel Time (min)	= 3.44	+ 0.00	+ 0.00	= 3.44
Shallow Concentrated Flow				
Flow length (ft)	= 4890.00	0.00	0.00	
Watercourse slope (%)	= 0.50	0.00	0.00	
Surface description	= Unpaved	Paved	Paved	
Average velocity (ft/s)	= 1.14	0.00	0.00	
Travel Time (min)	= 71.44	+ 0.00	+ 0.00	= 71.44
Channel Flow				
X sectional flow area (sqft)	= 0.00	0.00	0.00	
Wetted perimeter (ft)	= 0.00	0.00	0.00	
Channel slope (%)	= 0.00	0.00	0.00	
Manning's n-value	= 0.015	0.015	0.015	
Velocity (ft/s)	= 0.00	0.00	0.00	
Flow length (ft)	= 0.0	0.0	0.0	
Travel Time (min)	= 0.00	+ 0.00	+ 0.00	= 0.00
Total Travel Time, Tc				74.90 min

Hydraflow Rainfall Report

Hydraflow Hydrographs by Intelisolve v9.23

Thursday, Jul 12, 2007

Return Period (Yrs)	Intensity-Duration-Frequency Equation Coefficients (FHA)			
	B	D	E	(N/A)
1	0.0000	0.0000	0.0000	-----
2	19.2449	10.7000	0.8283	-----
3	0.0000	0.0000	0.0000	-----
5	32.6525	10.7000	0.8283	-----
10	42.8731	10.7000	0.8283	-----
25	54.4124	10.7000	0.8283	-----
50	64.3033	10.7000	0.8283	-----
100	73.0952	10.7000	0.8283	-----

File name: Victorville IDF.IDF

$$\text{Intensity} = B / (T_c + D)^E$$

Return Period (Yrs)	Intensity Values (in/hr)											
	5 min	10	15	20	25	30	35	40	45	50	55	60
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2	1.97	1.56	1.31	1.13	1.00	0.89	0.81	0.74	0.69	0.64	0.60	0.57
3	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5	3.34	2.65	2.22	1.91	1.69	1.52	1.38	1.26	1.17	1.09	1.02	0.96
10	4.38	3.48	2.91	2.51	2.22	1.99	1.81	1.66	1.53	1.43	1.34	1.26
25	5.56	4.42	3.70	3.19	2.82	2.53	2.29	2.11	1.95	1.81	1.70	1.60
50	6.57	5.23	4.37	3.77	3.33	2.98	2.71	2.49	2.30	2.14	2.01	1.89
100	7.47	5.94	4.97	4.29	3.78	3.39	3.08	2.83	2.62	2.44	2.28	2.15

Tc = time in minutes. Values may exceed 60.

Precip. file name: victorville event manager.pcp

Storm Distribution	Rainfall Precipitation Table (in)							
	1-yr	2-yr	3-yr	5-yr	10-yr	25-yr	50-yr	100-yr
SCS 24-hour	0.00	1.00	0.00	2.60	3.30	4.30	4.70	3.00
SCS 6-Hr	0.00	0.70	0.00	1.40	1.55	1.75	1.90	1.80
Huff-1st	0.00	1.55	0.00	2.75	4.00	5.38	6.50	8.00
Huff-2nd	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Huff-3rd	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Huff-4th	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Huff-Indy	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Custom	0.00	1.75	0.00	2.80	3.90	5.25	6.00	7.10


Culvert Calculator Report 12" at 3.85%

Solve For: Headwater Elevation

Culvert Summary			
Allowable HW Elevation	2,784.00 ft	Headwater Depth/Height	0.82
Computed Headwater Elev.	2,783.82 ft	Discharge	1.70 cfs
Inlet Control HW Elev.	2,783.78 ft	Tailwater Elevation	0.00 ft
Outlet Control HW Elev.	2,783.82 ft	Control Type	Entrance Control
Grades			
Upstream Invert	2,783.00 ft	Downstream Invert	2,780.00 ft
Length	110.00 ft	Constructed Slope	0.027273 ft/ft
Hydraulic Profile			
Profile	S2	Depth, Downstream	0.35 ft
Slope Type	Steep	Normal Depth	0.35 ft
Flow Regime	Supercritical	Critical Depth	0.55 ft
Velocity Downstream	6.87 ft/s	Critical Slope	0.005514 ft/ft
Section			
Section Shape	Circular	Mannings Coefficient	0.012
Section Material	HDPE (Smooth Interior)	Span	1.00 ft
Section Size	12 inch	Rise	1.00 ft
Number Sections	1		
Outlet Control Properties			
Outlet Control HW Elev.	2,783.82 ft	Upstream Velocity Head	0.22 ft
Ke	0.20	Entrance Loss	0.04 ft
Inlet Control Properties			
Inlet Control HW Elev.	2,783.78 ft	Flow Control	N/A
Inlet Type	Beveled ring, 33.7° bevels	Area Full	0.8 ft ²
K	0.00180	HDS 5 Chart	3
M	2.50000	HDS 5 Scale	B
C	0.02430	Equation Form	1
Y	0.83000		

Pond No. 1 - Sediment Retention Fac

Hydraflow Hydrographs by Intellisolve v9.23

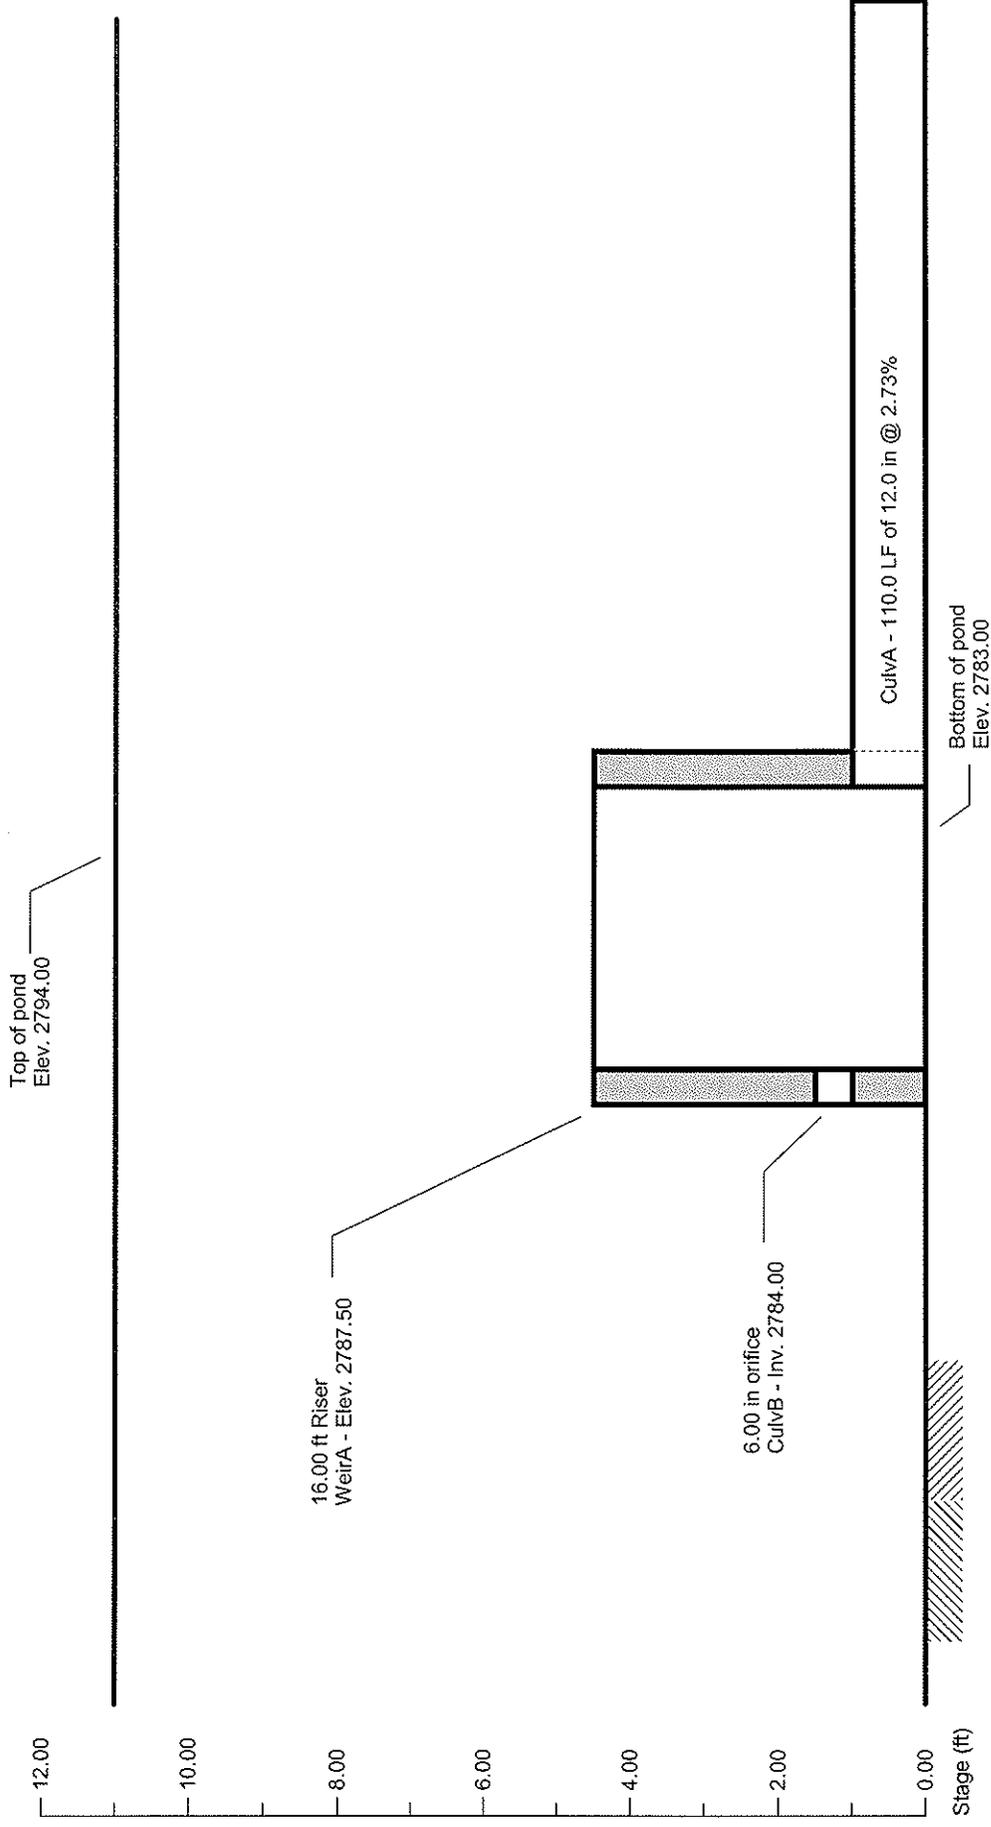


Section
NTS

----- 100-yr
----- 2-yr

Pond No. 1 - Sediment Retention Fac

Hydratlow Hydrographs by Intellisolve v9.23

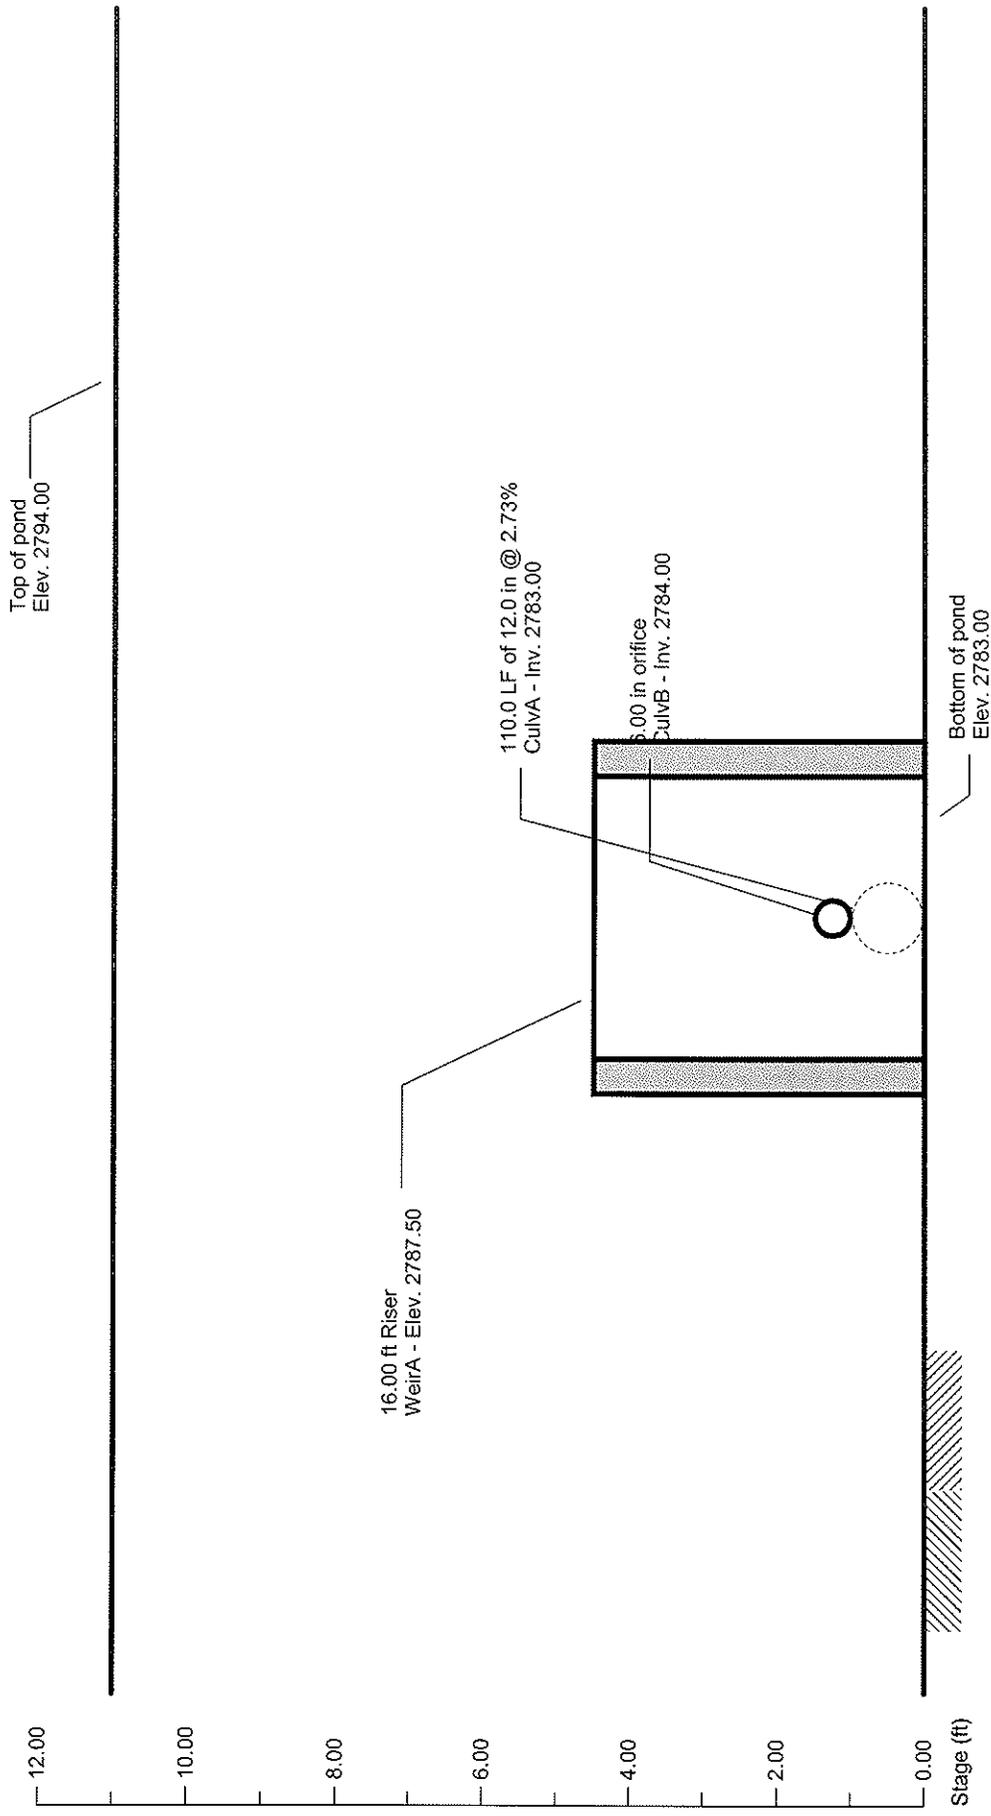

Front View
NTS - Looking Downstream

100-yr
2-yr

Pond Report

Hydraflow Hydrographs by Intelisolve v9.23

Wednesday, Jul 11, 2007

Pond No. 1 - Sediment Retention Fac

Pond Data

Contours - User-defined contour areas. Average end area method used for volume calculation. Beginning Elevation = 2783.00 ft

Stage / Storage Table

Stage (ft)	Elevation (ft)	Contour area (sqft)	Incr. Storage (cuft)	Total storage (cuft)
0.00	2783.00	40,501	0	0
1.00	2784.00	43,723	42,112	42,112
2.00	2785.00	47,047	45,385	87,497
3.00	2786.00	50,471	48,759	136,256
4.00	2787.00	53,995	52,233	188,489
5.00	2788.00	57,620	55,808	244,297
6.00	2789.00	61,646	59,633	303,930
7.00	2790.00	65,172	63,409	367,339
8.00	2791.00	69,098	67,135	434,474
9.00	2792.00	73,125	71,112	505,585
10.00	2793.00	77,253	75,189	580,774
11.00	2794.00	81,481	79,367	660,141


Culvert / Orifice Structures

	[A]	[B]	[C]	[PrfRsr]
Rise (in)	= 12.00	6.00	0.00	0.00
Span (in)	= 12.00	6.00	0.00	0.00
No. Barrels	= 1	1	0	0
Invert El. (ft)	= 2783.00	2784.00	0.00	0.00
Length (ft)	= 110.00	0.00	0.00	0.00
Slope (%)	= 2.73	0.00	0.00	n/a
N-Value	= .013	.013	.000	n/a
Orifice Coeff.	= 0.60	0.60	0.00	0.00
Multi-Stage	= n/a	Yes	No	No

Weir Structures


	[A]	[B]	[C]	[D]
Crest Len (ft)	= 16.00	0.00	0.00	0.00
Crest El. (ft)	= 2787.50	0.00	0.00	0.00
Weir Coeff.	= 3.33	0.00	0.00	0.00
Weir Type	= Riser	---	---	---
Multi-Stage	= Yes	No	No	No
Exfil.(in/hr)	= 0.000 (by Contour)			
TW Elev. (ft)	= 0.00			

Note: Culvert/Orifice outflows are analyzed under inlet (ic) and outlet (oc) control. Weir risers checked for orifice conditions (ic) and submergence (s).

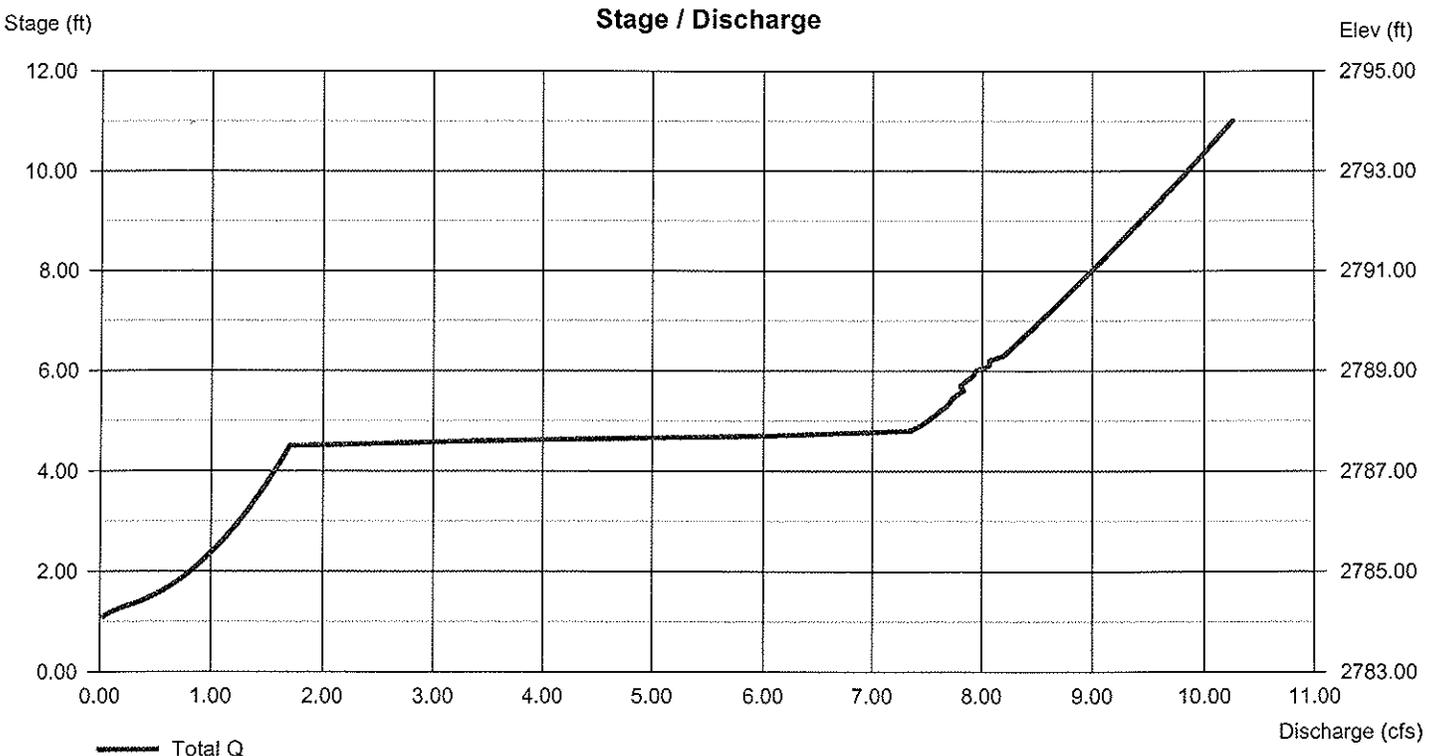

APPENDIX C:
Best Management Practices

Preservation Of Existing Vegetation EC-2

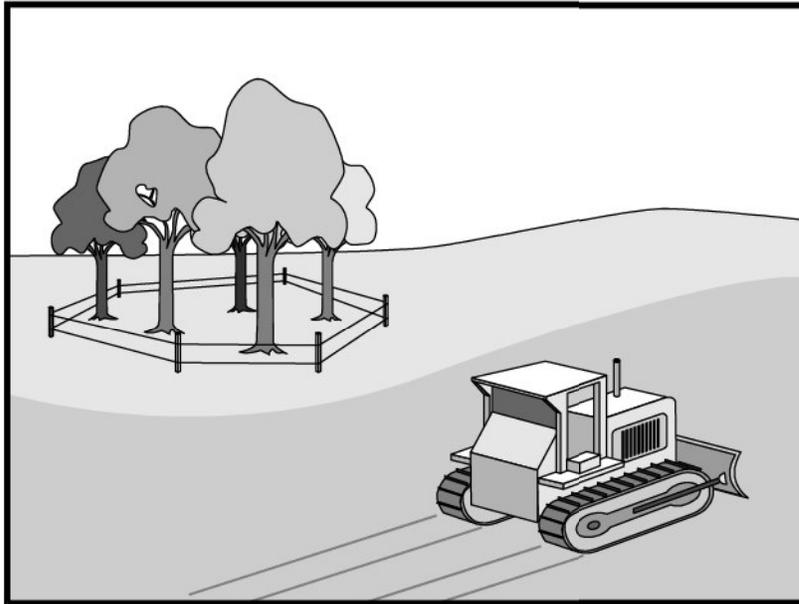

Description and Purpose

Carefully planned preservation of existing vegetation minimizes the potential of removing or injuring existing trees, vines, shrubs, and grasses that protect soil from erosion.

Suitable Applications

Preservation of existing vegetation is suitable for use on most projects. Large project sites often provide the greatest opportunity for use of this BMP. Suitable applications include the following:

- Areas within the site where no construction activity occurs, or occurs at a later date. This BMP is especially suitable to multi year projects where grading can be phased.
- Areas where natural vegetation exists and is designated for preservation. Such areas often include steep slopes, watercourse, and building sites in wooded areas.
- Areas where local, state, and federal government require preservation, such as vernal pools, wetlands, marshes, certain oak trees, etc. These areas are usually designated on the plans, or in the specifications, permits, or environmental documents.
- Where vegetation designated for ultimate removal can be temporarily preserved and be utilized for erosion control and sediment control.

Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	
TR	Tracking Control	
WE	Wind Erosion Control	
NS	Non-Stormwater Management Control	
WM	Waste Management and Materials Pollution Control	

Legend:

- Primary Objective
- Secondary Objective

Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

Potential Alternatives

None



EC-2 Preservation Of Existing Vegetation

Limitations

- Requires forward planning by the owner/developer, contractor, and design staff.
- Limited opportunities for use when project plans do not incorporate existing vegetation into the site design.
- For sites with diverse topography, it is often difficult and expensive to save existing trees while grading the site satisfactory for the planned development.

Implementation

The best way to prevent erosion is to not disturb the land. In order to reduce the impacts of new development and redevelopment, projects may be designed to avoid disturbing land in sensitive areas of the site (e.g., natural watercourses, steep slopes), and to incorporate unique or desirable existing vegetation into the site's landscaping plan. Clearly marking and leaving a buffer area around these unique areas during construction will help to preserve these areas as well as take advantage of natural erosion prevention and sediment trapping.

Existing vegetation to be preserved on the site must be protected from mechanical and other injury while the land is being developed. The purpose of protecting existing vegetation is to ensure the survival of desirable vegetation for shade, beautification, and erosion control. Mature vegetation has extensive root systems that help to hold soil in place, thus reducing erosion. In addition, vegetation helps keep soil from drying rapidly and becoming susceptible to erosion. To effectively save existing vegetation, no disturbances of any kind should be allowed within a defined area around the vegetation. For trees, no construction activity should occur within the drip line of the tree.

Timing

- Provide for preservation of existing vegetation prior to the commencement of clearing and grubbing operations or other soil disturbing activities in areas where no construction activity is planned or will occur at a later date.

Design and Layout

- Mark areas to be preserved with temporary fencing. Include sufficient setback to protect roots.
 - Orange colored plastic mesh fencing works well.
 - Use appropriate fence posts and adequate post spacing and depth to completely support the fence in an upright position.
- Locate temporary roadways, stockpiles, and layout areas to avoid stands of trees, shrubs, and grass.
- Consider the impact of grade changes to existing vegetation and the root zone.
- Maintain existing irrigation systems where feasible. Temporary irrigation may be required.
- Instruct employees and subcontractors to honor protective devices. Prohibit heavy equipment, vehicular traffic, or storage of construction materials within the protected area.

Preservation Of Existing Vegetation EC-2

Costs

There is little cost associated with preserving existing vegetation if properly planned during the project design, and these costs may be offset by aesthetic benefits that enhance property values. During construction, the cost for preserving existing vegetation will likely be less than the cost of applying erosion and sediment controls to the disturbed area. Replacing vegetation inadvertently destroyed during construction can be extremely expensive, sometimes in excess of \$10,000 per tree.

Inspection and Maintenance

During construction, the limits of disturbance should remain clearly marked at all times. Irrigation or maintenance of existing vegetation should be described in the landscaping plan. If damage to protected trees still occurs, maintenance guidelines described below should be followed:

- Verify that protective measures remain in place. Restore damaged protection measures immediately.
- Serious tree injuries shall be attended to by an arborist.
- Damage to the crown, trunk, or root system of a retained tree shall be repaired immediately.
- Trench as far from tree trunks as possible, usually outside of the tree drip line or canopy. Curve trenches around trees to avoid large roots or root concentrations. If roots are encountered, consider tunneling under them. When trenching or tunneling near or under trees to be retained, place tunnels at least 18 in. below the ground surface, and not below the tree center to minimize impact on the roots.
- Do not leave tree roots exposed to air. Cover exposed roots with soil as soon as possible. If soil covering is not practical, protect exposed roots with wet burlap or peat moss until the tunnel or trench is ready for backfill.
- Cleanly remove the ends of damaged roots with a smooth cut.
- Fill trenches and tunnels as soon as possible. Careful filling and tamping will eliminate air spaces in the soil, which can damage roots.
- If bark damage occurs, cut back all loosened bark into the undamaged area, with the cut tapered at the top and bottom and drainage provided at the base of the wood. Limit cutting the undamaged area as much as possible.
- Aerate soil that has been compacted over a trees root zone by punching holes 12 in. deep with an iron bar, and moving the bar back and forth until the soil is loosened. Place holes 18 in. apart throughout the area of compacted soil under the tree crown.
- Fertilization
 - Fertilize stressed or damaged broadleaf trees to aid recovery.
 - Fertilize trees in the late fall or early spring.

EC-2 Preservation Of Existing Vegetation

- Apply fertilizer to the soil over the feeder roots and in accordance with label instructions, but never closer than 3 ft to the trunk. Increase the fertilized area by one-fourth of the crown area for conifers that have extended root systems.
- Retain protective measures until all other construction activity is complete to avoid damage during site cleanup and stabilization.


References

County of Sacramento Tree Preservation Ordinance, September 1981.

Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

Stormwater Management of the Puget Sound Basin, Technical Manual, Publication #91-75, Washington State Department of Ecology, February 1992.

Water Quality Management Plan for The Lake Tahoe Region, Volume II, Handbook of Management Practices, Tahoe Regional Planning Agency, November 1988.

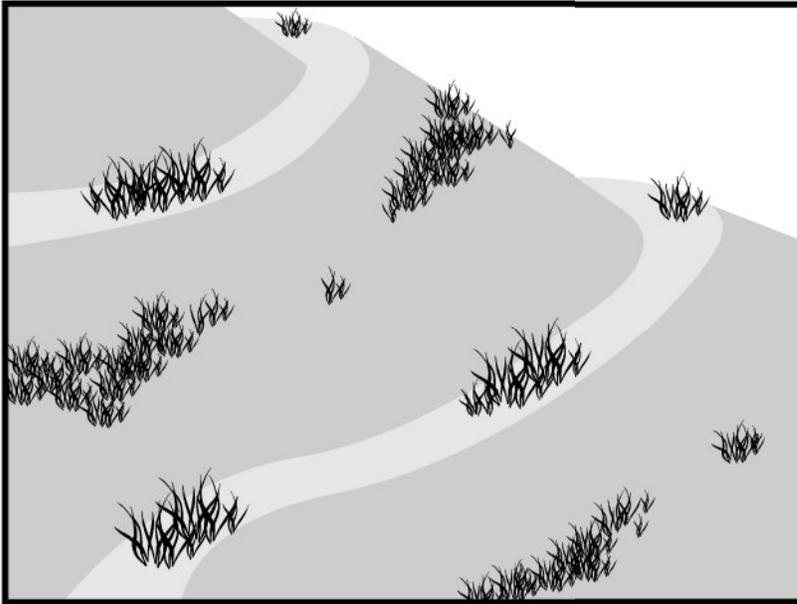

Description and Purpose

Hydroseeding typically consists of applying a mixture of wood fiber, seed, fertilizer, and stabilizing emulsion with hydro-mulch equipment, to temporarily protect exposed soils from erosion by water and wind.

Suitable Applications

Hydroseeding is suitable for soil disturbed areas requiring temporary protection until permanent stabilization is established, and disturbed areas that will be re-disturbed following an extended period of inactivity.

Limitations

- Hydroseeding may be used alone only when there is sufficient time in the season to ensure adequate vegetation establishment and coverage to provide adequate erosion control. Otherwise, hydroseeding must be used in conjunction with mulching (i.e., straw mulch).
- Steep slopes are difficult to protect with temporary seeding.
- Temporary seeding may not be appropriate in dry periods without supplemental irrigation.
- Temporary vegetation may have to be removed before permanent vegetation is applied.
- Temporary vegetation is not appropriate for short term inactivity.

Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	
TR	Tracking Control	
WE	Wind Erosion Control	<input checked="" type="checkbox"/>
NS	Non-Stormwater Management Control	
WM	Waste Management and Materials Pollution Control	

Legend:

- Primary Objective
- Secondary Objective

Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

Potential Alternatives

- EC-3 Hydraulic Mulch
- EC-5 Soil Binders
- EC-6 Straw Mulch
- EC-7 Geotextiles and Mats
- EC-8 Wood Mulching



Implementation

In order to select appropriate hydroseeding mixtures, an evaluation of site conditions shall be performed with respect to:

- Soil conditions
- Site topography
- Season and climate
- Vegetation types
- Maintenance requirements
- Sensitive adjacent areas
- Water availability
- Plans for permanent vegetation

The local office of the U.S.D.A. Natural Resources Conservation Service (NRCS) is an excellent source of information on appropriate seed mixes.

The following steps shall be followed for implementation:

- Avoid use of hydroseeding in areas where the BMP would be incompatible with future earthwork activities and would have to be removed.
- Hydroseeding can be accomplished using a multiple step or one step process. The multiple step process ensures maximum direct contact of the seeds to soil. When the one step process is used to apply the mixture of fiber, seed, etc., the seed rate shall be increased to compensate for all seeds not having direct contact with the soil.
- Prior to application, roughen the area to be seeded with the furrows trending along the contours.
- Apply a straw mulch to keep seeds in place and to moderate soil moisture and temperature until the seeds germinate and grow.
- All seeds shall be in conformance with the California State Seed Law of the Department of Agriculture. Each seed bag shall be delivered to the site sealed and clearly marked as to species, purity, percent germination, dealer's guarantee, and dates of test. The container shall be labeled to clearly reflect the amount of Pure Live Seed (PLS) contained. All legume seed shall be pellet inoculated. Inoculant sources shall be species specific and shall be applied at a rate of 2 lb of inoculant per 100 lb seed.
- Commercial fertilizer shall conform to the requirements of the California Food and Agricultural Code. Fertilizer shall be pelleted or granular form.
- Follow up applications shall be made as needed to cover weak spots and to maintain adequate soil protection.
- Avoid over spray onto roads, sidewalks, drainage channels, existing vegetation, etc.

Costs

Average cost for installation and maintenance may vary from as low as \$300 per acre for flat slopes and stable soils, to \$1600 per acre for moderate to steep slopes and/or erosive soils.

Hydroseeding		Installed Cost per Acre
High Density	Ornamentals	\$400 - \$1600
	Turf Species	\$350
	Bunch Grasses	\$300 - \$1300
Fast Growing	Annual	\$350 - \$650
	Perennial	\$300 - \$800
Non-Competing	Native	\$300 - \$1600
	Non-Native	\$400 - \$500
Sterile	Cereal Grain	\$500

Source: Caltrans Guidance for Soil Stabilization for Temporary Slopes, Nov. 1999


Inspection and Maintenance

- Inspect BMPs prior to forecast rain, daily during extended rain events, after rain events, weekly during the rainy season, and at two-week intervals during the non-rainy season.
- Areas where erosion is evident shall be repaired and BMPs re-applied as soon as possible. Care should be exercised to minimize the damage to protected areas while making repairs, as any area damaged will require re-application of BMPs.
- Where seeds fail to germinate, or they germinate and die, the area must be re-seeded, fertilized, and mulched within the planting season, using not less than half the original application rates.
- Irrigation systems, if applicable, should be inspected daily while in use to identify system malfunctions and line breaks. When line breaks are detected, the system must be shut down immediately and breaks repaired before the system is put back into operation.
- Irrigation systems shall be inspected for complete coverage and adjusted as needed to maintain complete coverage.

References

Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

Guidance Document: Soil Stabilization for Temporary Slopes, State of California Department of Transportation (Caltrans), November 1999.

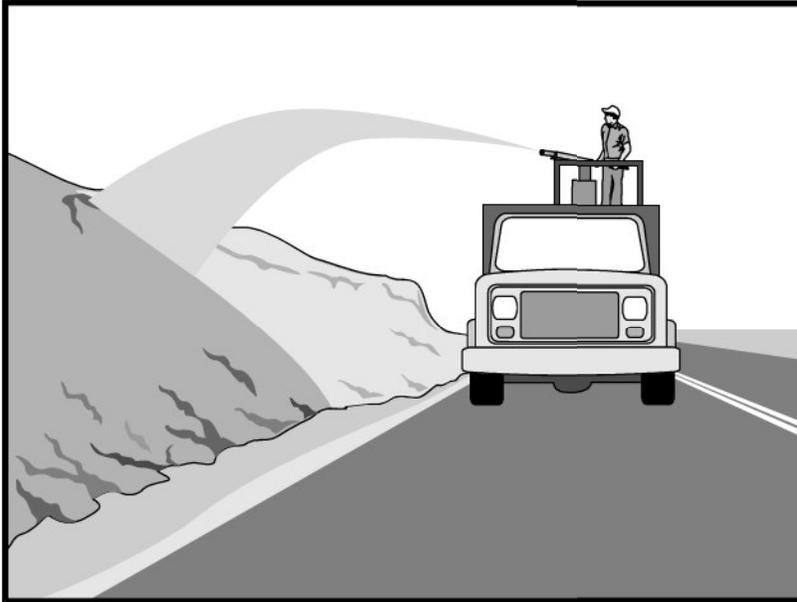

Description and Purpose

Straw mulch consists of placing a uniform layer of straw and incorporating it into the soil with a studded roller or anchoring it with a tackifier stabilizing emulsion. Straw mulch protects the soil surface from the impact of rain drops, preventing soil particles from becoming dislodged.

Suitable Applications

Straw mulch is suitable for soil disturbed areas requiring temporary protection until permanent stabilization is established. Straw mulch is typically used for erosion control on disturbed areas until soils can be prepared for permanent vegetation. Straw mulch is also used in combination with temporary and/or permanent seeding strategies to enhance plant establishment.

Limitations

- Availability of straw and straw blowing equipment may be limited just prior to the rainy season and prior to storms due to high demand.
- There is a potential for introduction of weed seed and unwanted plant material.
- When straw blowers are used to apply straw mulch, the treatment areas must be within 150 ft of a road or surface capable of supporting trucks.
- Straw mulch applied by hand is more time intensive and potentially costly.

Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	
TR	Tracking Control	
WE	Wind Erosion Control	
NS	Non-Stormwater Management Control	
WM	Waste Management and Materials Pollution Control	

Legend:

- Primary Objective
- Secondary Objective

Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

Potential Alternatives

- EC-3 Hydraulic Mulch
- EC-4 Hydroseeding
- EC-5 Soil Binders
- EC-7 Geotextiles and Mats
- EC-8 Wood Mulching



- Wind may limit application of straw and blow straw into undesired locations.
- May have to be removed prior to permanent seeding or prior to further earthwork.
- “Punching” of straw does not work in sandy soils, necessitating the use of tackifiers.

Implementation

- Straw shall be derived from wheat, rice, or barley. Where required by the plans, specifications, permits, or environmental documents, native grass straw shall be used.
- A tackifier is the preferred method for anchoring straw mulch to the soil on slopes.
- Crimping, punch roller-type rollers, or track walking may also be used to incorporate straw mulch into the soil on slopes. Track walking shall only be used where other methods are impractical.
- Avoid placing straw onto roads, sidewalks, drainage channels, sound walls, existing vegetation, etc.
- Straw mulch with tackifier shall not be applied during or immediately before rainfall.
- In San Diego, use of straw near wood framed home construction has been frowned on by the Fire Marshall.

Application Procedures

- Apply straw at a minimum rate of 4,000 lb/acre, either by machine or by hand distribution.
- Roughen embankments and fill rills before placing the straw mulch by rolling with a crimping or punching type roller or by track walking.
- Evenly distribute straw mulch on the soil surface.
- Anchor straw mulch to the soil surface by "punching" it into the soil mechanically (incorporating). Alternatively, use a tackifier to adhere straw fibers.
- Methods for holding the straw mulch in place depend upon the slope steepness, accessibility, soil conditions, and longevity.
 - On small areas, a spade or shovel can be used to punch in straw mulch.
 - On slopes with soils that are stable enough and of sufficient gradient to safely support construction equipment without contributing to compaction and instability problems, straw can be "punched" into the ground using a knife blade roller or a straight bladed coulter, known commercially as a "crimper".
 - On small areas and/or steep slopes, straw can also be held in place using plastic netting or jute. The netting shall be held in place using 11 gauge wire staples, geotextile pins or wooden stakes as described in EC-7, Geotextiles and Mats.
 - A tackifier acts to glue the straw fibers together and to the soil surface. The tackifier shall be selected based on longevity and ability to hold the fibers in place. A tackifier is

typically applied at a rate of 125 lb/acre. In windy conditions, the rates are typically 180 lb/acre.

Costs

Average annual cost for installation and maintenance (3-4 months useful life) is \$2,500 per acre. Application by hand is more time intensive and potentially costly.

Inspection and Maintenance

- Inspect BMPs prior to forecast rain, daily during extended rain events, after rain events, weekly during the rainy season, and at two-week intervals during the non-rainy season.
- Areas where erosion is evident should be repaired and BMPs re-applied as soon as possible. Care should be exercised to minimize the damage to protected areas while making repairs, as any area damaged will require re-application of BMPs.
- The key consideration in inspection and maintenance is that the straw needs to last long enough to achieve erosion control objectives.
- Maintain an unbroken, temporary mulched ground cover while disturbed soil areas are inactive. Repair any damaged ground cover and re-mulch exposed areas.
- Reapplication of straw mulch and tackifier may be required to maintain effective soil stabilization over disturbed areas and slopes.

References

Controlling Erosion of Construction Sites, Agricultural Information Bulletin #347, U.S. Department of Agriculture (USDA), Natural Resources Conservation Service (NRCS) (formerly Soil Conservation Service – SCS).

Guides for Erosion and Sediment Control in California, USDA Soils Conservation Service, January 1991.


Manual of Standards of Erosion and Sediment Control Measures, Association of Bay Area Governments, May 1995.

Soil Erosion by Water, Agricultural Information Bulletin #513, U.S. Department of Agriculture, Soil Conservation Service.

Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

Stormwater Management of the Puget Sound Basin, Technical Manual, Publication #91-75, Washington State Department of Ecology, February 1992.

Water Quality Management Plan for the Lake Tahoe Region, Volume II, Handbook of Management Practices, Tahoe Regional Planning Agency, November 1988.

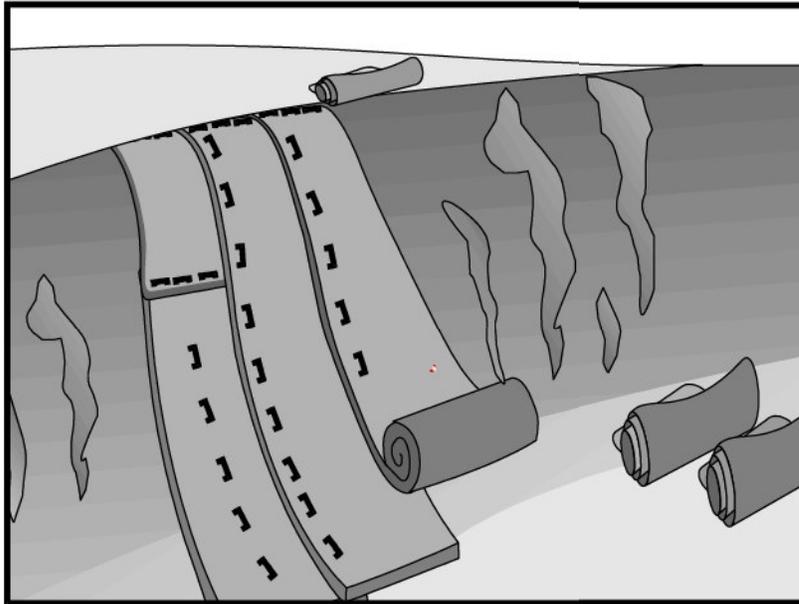

Description and Purpose

Mattings of natural materials are used to cover the soil surface to reduce erosion from rainfall impact, hold soil in place, and absorb and hold moisture near the soil surface. Additionally, matting may be used to stabilize soils until vegetation is established.

Suitable Applications

Mattings are commonly applied on short, steep slopes where erosion hazard is high and vegetation will be slow to establish. Mattings are also used on stream banks where moving water at velocities between 3 ft/s and 6 ft/s are likely to wash out new vegetation, and in areas where the soil surface is disturbed and where existing vegetation has been removed. Matting may also be used when seeding cannot occur (e.g., late season construction and/or the arrival of an early rain season). Erosion control matting should be considered when the soils are fine grained and potentially erosive. These measures should be considered in the following situations.

- Steep slopes, generally steeper than 3:1 (H:V)
- Slopes where the erosion potential is high
- Slopes and disturbed soils where mulch must be anchored
- Disturbed areas where plants are slow to develop
- Channels with flows exceeding 3.3 ft/s

Objectives

EC	Erosion Control	<input checked="" type="checkbox"/>
SE	Sediment Control	
TR	Tracking Control	
WE	Wind Erosion Control	3
NS	Non-Stormwater Management Control	
WM	Waste Management and Materials Pollution Control	

Legend:

- Primary Objective
- Secondary Objective

Targeted Constituents

Sediment	<input checked="" type="checkbox"/>
Nutrients	
Trash	
Metals	
Bacteria	
Oil and Grease	
Organics	

Potential Alternatives

- EC-3 Hydraulic Mulch
- EC-4 Hydroseeding
- EC-5 Soil Binders
- EC-6 Straw Mulch
- EC-8 Wood Mulching



- Channels to be vegetated
- Stockpiles
- Slopes adjacent to water bodies of Environmentally Sensitive Areas (ESAs)

Limitations

- Properly installed mattings provide excellent erosion control but do so at relatively high cost. This high cost typically limits the use of mattings to areas of concentrated channel flow and steep slopes.
- Mattings are more costly than other BMP practices, limiting their use to areas where other BMPs are ineffective (e.g. channels, steep slopes).
- Installation is critical and requires experienced contractors. The contractor should install the matting material in such a manner that continuous contact between the material and the soil occurs.
- Geotextiles and Mats may delay seed germination, due to reduction in soil temperature.
- Blankets and mats are generally not suitable for excessively rocky sites or areas where the final vegetation will be mowed (since staples and netting can catch in mowers).
- Blankets and mats must be removed and disposed of prior to application of permanent soil stabilization measures.
- Plastic sheeting is easily vandalized, easily torn, photodegradable, and must be disposed of at a landfill.
- Plastic results in 100% runoff, which may cause serious erosion problems in the areas receiving the increased flow.
- The use of plastic should be limited to covering stockpiles or very small graded areas for short periods of time (such as through one imminent storm event) until alternative measures, such as seeding and mulching, may be installed.
- Geotextiles, mats, plastic covers, and erosion control covers have maximum flow rate limitations; consult the manufacturer for proper selection.
- Not suitable for areas that have heavy foot traffic (tripping hazard) – e.g., pad areas around buildings under construction.

Implementation

Material Selection

Organic matting materials have been found to be effective where re-vegetation will be provided by re-seeding. The choice of matting should be based on the size of area, side slopes, surface conditions such as hardness, moisture, weed growth, and availability of materials.

The following natural and synthetic mattings are commonly used:

Geotextiles

- Material should be a woven polypropylene fabric with minimum thickness of 0.06 in., minimum width of 12 ft and should have minimum tensile strength of 150 lbs (warp), 80 lbs (fill) in conformance with the requirements in ASTM Designation: D 4632. The permittivity of the fabric should be approximately 0.07 sec^{-1} in conformance with the requirements in ASTM Designation: D4491. The fabric should have an ultraviolet (UV) stability of 70 percent in conformance with the requirements in ASTM designation: D4355. Geotextile blankets must be secured in place with wire staples or sandbags and by keying into tops of slopes to prevent infiltration of surface waters under geotextile. Staples should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.
- Geotextiles may be reused if they are suitable for the use intended.

Plastic Covers

- Plastic sheeting should have a minimum thickness of 6 mils, and must be keyed in at the top of slope and firmly held in place with sandbags or other weights placed no more than 10 ft apart. Seams are typically taped or weighted down their entire length, and there should be at least a 12 in. to 24 in. overlap of all seams. Edges should be embedded a minimum of 6 in. in soil.
- All sheeting must be inspected periodically after installation and after significant rainstorms to check for erosion, undermining, and anchorage failure. Any failures must be repaired immediately. If washout or breakages occur, the material should be re-installed after repairing the damage to the slope.

Erosion Control Blankets/Mats

- Biodegradable rolled erosion control products (RECPs) are typically composed of jute fibers, curled wood fibers, straw, coconut fiber, or a combination of these materials. In order for an RECP to be considered 100% biodegradable, the netting, sewing or adhesive system that holds the biodegradable mulch fibers together must also be biodegradable.
 - **Jute** is a natural fiber that is made into a yarn that is loosely woven into a biodegradable mesh. It is designed to be used in conjunction with vegetation and has longevity of approximately one year. The material is supplied in rolled strips, which should be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Excelsior** (curled wood fiber) blanket material should consist of machine produced mats of curled wood excelsior with 80 percent of the fiber 6 in. or longer. The excelsior blanket should be of consistent thickness. The wood fiber must be evenly distributed over the entire area of the blanket. The top surface of the blanket should be covered with a photodegradable extruded plastic mesh. The blanket should be smolder resistant without the use of chemical additives and should be non-toxic and non-injurious to plant and animal life. Excelsior blankets should be furnished in rolled strips, a minimum of 48 in. wide, and should have an average weight of 0.8 lb/yd^2 , ± 10 percent, at the time of manufacture. Excelsior blankets must be secured in place with wire staples. Staples

should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.

- **Straw blanket** should be machine produced mats of straw with a lightweight biodegradable netting top layer. The straw should be attached to the netting with biodegradable thread or glue strips. The straw blanket should be of consistent thickness. The straw should be evenly distributed over the entire area of the blanket. Straw blanket should be furnished in rolled strips a minimum of 6.5 ft wide, a minimum of 80 ft long and a minimum of 0.5 lb/yd². Straw blankets must be secured in place with wire staples. Staples should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.
- **Wood fiber blanket** is composed of biodegradable fiber mulch with extruded plastic netting held together with adhesives. The material is designed to enhance re-vegetation. The material is furnished in rolled strips, which must be secured to the ground with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Coconut fiber blanket** should be a machine produced mat of 100 percent coconut fiber with biodegradable netting on the top and bottom. The coconut fiber should be attached to the netting with biodegradable thread or glue strips. The coconut fiber blanket should be of consistent thickness. The coconut fiber should be evenly distributed over the entire area of the blanket. Coconut fiber blanket should be furnished in rolled strips with a minimum of 6.5 ft wide, a minimum of 80 ft. long and a minimum of 0.5 lb/yd². Coconut fiber blankets must be secured in place with wire staples. Staples should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.
- **Coconut fiber mesh** is a thin permeable membrane made from coconut or corn fiber that is spun into a yarn and woven into a biodegradable mat. It is designed to be used in conjunction with vegetation and typically has longevity of several years. The material is supplied in rolled strips, which must be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Straw coconut fiber blanket** should be machine produced mats of 70 percent straw and 30 percent coconut fiber with a biodegradable netting top layer and a biodegradable bottom net. The straw and coconut fiber should be attached to the netting with biodegradable thread or glue strips. The straw coconut fiber blanket should be of consistent thickness. The straw and coconut fiber should be evenly distributed over the entire area of the blanket. Straw coconut fiber blanket should be furnished in rolled strips a minimum of 6.5 ft wide, a minimum of 80 ft long and a minimum of 0.5 lb/yd². Straw coconut fiber blankets must be secured in place with wire staples. Staples should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.
- Non-biodegradable RECPs are typically composed of polypropylene, polyethylene, nylon or other synthetic fibers. In some cases, a combination of biodegradable and synthetic fibers is used to construct the RECP. Netting used to hold these fibers together is typically non-biodegradable as well.

- **Plastic netting** is a lightweight biaxially oriented netting designed for securing loose mulches like straw or paper to soil surfaces to establish vegetation. The netting is photodegradable. The netting is supplied in rolled strips, which must be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Plastic mesh** is an open weave geotextile that is composed of an extruded synthetic fiber woven into a mesh with an opening size of less than ¼ in. It is used with re-vegetation or may be used to secure loose fiber such as straw to the ground. The material is supplied in rolled strips, which must be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Synthetic fiber with netting** is a mat that is composed of durable synthetic fibers treated to resist chemicals and ultraviolet light. The mat is a dense, three dimensional mesh of synthetic (typically polyolefin) fibers stitched between two polypropylene nets. The mats are designed to be re-vegetated and provide a permanent composite system of soil, roots, and geomatrix. The material is furnished in rolled strips, which must be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Bonded synthetic fibers** consist of a three dimensional geomatrix nylon (or other synthetic) matting. Typically it has more than 90 percent open area, which facilitates root growth. It's tough root reinforcing system anchors vegetation and protects against hydraulic lift and shear forces created by high volume discharges. It can be installed over prepared soil, followed by seeding into the mat. Once vegetated, it becomes an invisible composite system of soil, roots, and geomatrix. The material is furnished in rolled strips that must be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Combination synthetic and biodegradable RECPs** consist of biodegradable fibers, such as wood fiber or coconut fiber, with a heavy polypropylene net stitched to the top and a high strength continuous filament geomatrix or net stitched to the bottom. The material is designed to enhance re-vegetation. The material is furnished in rolled strips, which must be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.

Site Preparation

- Proper site preparation is essential to ensure complete contact of the blanket or matting with the soil.
- Grade and shape the area of installation.
- Remove all rocks, clods, vegetation or other obstructions so that the installed blankets or mats will have complete, direct contact with the soil.
- Prepare seedbed by loosening 2 to 3 in. of topsoil.

Seeding

Seed the area before blanket installation for erosion control and revegetation. Seeding after mat installation is often specified for turf reinforcement application. When seeding prior to blanket

installation, all check slots and other areas disturbed during installation must be re-seeded. Where soil filling is specified, seed the matting and the entire disturbed area after installation and prior to filling the mat with soil.

Fertilize and seed in accordance with seeding specifications or other types of landscaping plans. When using jute matting on a seeded area, apply approximately half the seed before laying the mat and the remainder after laying the mat. The protective matting can be laid over areas where grass has been planted and the seedlings have emerged. Where vines or other ground covers are to be planted, lay the protective matting first and then plant through matting according to design of planting.

Check Slots

Check slots are made of glass fiber strips, excelsior matting strips or tight folded jute matting blanket or strips for use on steep, highly erodible watercourses. The check slots are placed in narrow trenches 6 to 12 in. deep across the channel and left flush with the soil surface. They are to cover the full cross section of designed flow.

Laying and Securing Matting

- Before laying the matting, all check slots should be installed and the friable seedbed made free from clods, rocks, and roots. The surface should be compacted and finished according to the requirements of the manufacturer's recommendations.
- Mechanical or manual lay down equipment should be capable of handling full rolls of fabric and laying the fabric smoothly without wrinkles or folds. The equipment should meet the fabric manufacturer's recommendations or equivalent standards.

Anchoring

- U-shaped wire staples, metal geotextile stake pins, or triangular wooden stakes can be used to anchor mats and blankets to the ground surface.
- Wire staples should be made of minimum 11 gauge steel wire and should be U-shaped with 8 in. legs and 2 in. crown.
- Metal stake pins should be 0.188 in. diameter steel with a 1.5 in. steel washer at the head of the pin, and 8 in. in length.
- Wire staples and metal stakes should be driven flush to the soil surface.

Installation on Slopes

Installation should be in accordance with the manufacturer's recommendations. In general, these will be as follows:

- Begin at the top of the slope and anchor the blanket in a 6 in. deep by 6 in. wide trench. Backfill trench and tamp earth firmly.
- Unroll blanket down slope in the direction of water flow.
- Overlap the edges of adjacent parallel rolls 2 to 3 in. and staple every 3 ft.

- When blankets must be spliced, place blankets end over end (shingle style) with 6 in. overlap. Staple through overlapped area, approximately 12 in. apart.
- Lay blankets loosely and maintain direct contact with the soil. Do not stretch.
- Staple blankets sufficiently to anchor blanket and maintain contact with the soil. Staples should be placed down the center and staggered with the staples placed along the edges. Steep slopes, 1:1 (H:V) to 2:1 (H:V), require a minimum of 2 staples/yd². Moderate slopes, 2:1 (H:V) to 3:1 (H:V), require a minimum of 1 1/2 staples/yd².

Installation in Channels

Installation should be in accordance with the manufacturer's recommendations. In general, these will be as follows:

- Dig initial anchor trench 12 in. deep and 6 in. wide across the channel at the lower end of the project area.
- Excavate intermittent check slots, 6 in. deep and 6 in. wide across the channel at 25 to 30 ft intervals along the channels.
- Cut longitudinal channel anchor trenches 4 in. deep and 4 in. wide along each side of the installation to bury edges of matting, whenever possible extend matting 2 to 3 in. above the crest of the channel side slopes.
- Beginning at the downstream end and in the center of the channel, place the initial end of the first roll in the anchor trench and secure with fastening devices at 12 in. intervals. Note: matting will initially be upside down in anchor trench.
- In the same manner, position adjacent rolls in anchor trench, overlapping the preceding roll a minimum of 3 in.
- Secure these initial ends of mats with anchors at 12 in. intervals, backfill and compact soil.
- Unroll center strip of matting upstream. Stop at next check slot or terminal anchor trench. Unroll adjacent mats upstream in similar fashion, maintaining a 3 in. overlap.
- Fold and secure all rolls of matting snugly into all transverse check slots. Lay mat in the bottom of the slot then fold back against itself. Anchor through both layers of mat at 12 in. intervals, then backfill and compact soil. Continue rolling all mat widths upstream to the next check slot or terminal anchor trench.
- Alternate method for non-critical installations: Place two rows of anchors on 6 in. centers at 25 to 30 ft. intervals in lieu of excavated check slots.
- Staple shingled lap spliced ends a minimum of 12 in. apart on 12 in. intervals.
- Place edges of outside mats in previously excavated longitudinal slots; anchor using prescribed staple pattern, backfill, and compact soil.
- Anchor, fill, and compact upstream end of mat in a 12 in. by 6 in. terminal trench.

- Secure mat to ground surface using U-shaped wire staples, geotextile pins, or wooden stakes.
- Seed and fill turf reinforcement matting with soil, if specified.

Soil Filling (if specified for turf reinforcement)

- Always consult the manufacturer's recommendations for installation.
- Do not drive tracked or heavy equipment over mat.
- Avoid any traffic over matting if loose or wet soil conditions exist.
- Use shovels, rakes, or brooms for fine grading and touch up.
- Smooth out soil filling just exposing top netting of mat.

Temporary Soil Stabilization Removal

- Temporary soil stabilization removed from the site of the work must be disposed of if necessary.

Costs

Relatively high compared to other BMPs. Biodegradable materials: \$0.50 - \$0.57/yd². Permanent materials: \$3.00 - \$4.50/yd². Staples: \$0.04 - \$0.05/staple. Approximate costs for installed materials are shown below:

Rolled Erosion Control Products		Installed Cost per Acre
Biodegradable	Jute Mesh	\$6,500
	Curled Wood Fiber	\$10,500
	Straw	\$8,900
	Wood Fiber	\$8,900
	Coconut Fiber	\$13,000
	Coconut Fiber Mesh	\$31,200
	Straw Coconut Fiber	\$10,900
Non-Biodegradable	Plastic Netting	\$2,000
	Plastic Mesh	\$3,200
	Synthetic Fiber with Netting	\$34,800
	Bonded Synthetic Fibers	\$50,000
	Combination with Biodegradable	\$32,000

Source: Caltrans Guidance for Soil Stabilization for Temporary Slopes, Nov. 1999

Inspection and Maintenance

- Inspect BMPs prior to forecast rain, daily during extended rain events, after rain events, weekly during the rainy season, and at two-week intervals during the non-rainy season, and at two-week intervals during the non-rainy season.
- Inspect BMPs subject to non-stormwater discharges daily while non-stormwater discharges occur.

- Areas where erosion is evident shall be repaired and BMPs reapplied as soon as possible. Care should be exercised to minimize the damage to protected areas while making repairs, as any area damaged will require reapplication of BMPs.
- If washout or breakage occurs, re-install the material after repairing the damage to the slope or channel.
- Make sure matting is uniformly in contact with the soil.
- Check that all the lap joints are secure.
- Check that staples are flush with the ground.
- Check that disturbed areas are seeded.

References

Guides for Erosion and Sediment Controls in California, USDA Soils Conservation Service, January 1991.


National Management Measures to Control Nonpoint Source Pollution from Urban Areas, United States Environmental Protection Agency, 2002.

Stormwater Quality Handbooks Construction Site Best Management Practices (BMPs) Manual, State of California Department of Transportation (Caltrans), November 2000.

Guidance Document: Soil Stabilization for Temporary Slopes, State of California Department of Transportation (Caltrans), November 1999

Stormwater Management of the Puget Sound Basin, Technical Manual, Publication #91-75, Washington State Department of Ecology, February 1992.


Water Quality Management Plan for The Lake Tahoe Region, Volume II, Handbook of Management Practices, Tahoe Regional Planning Agency, November 1988.

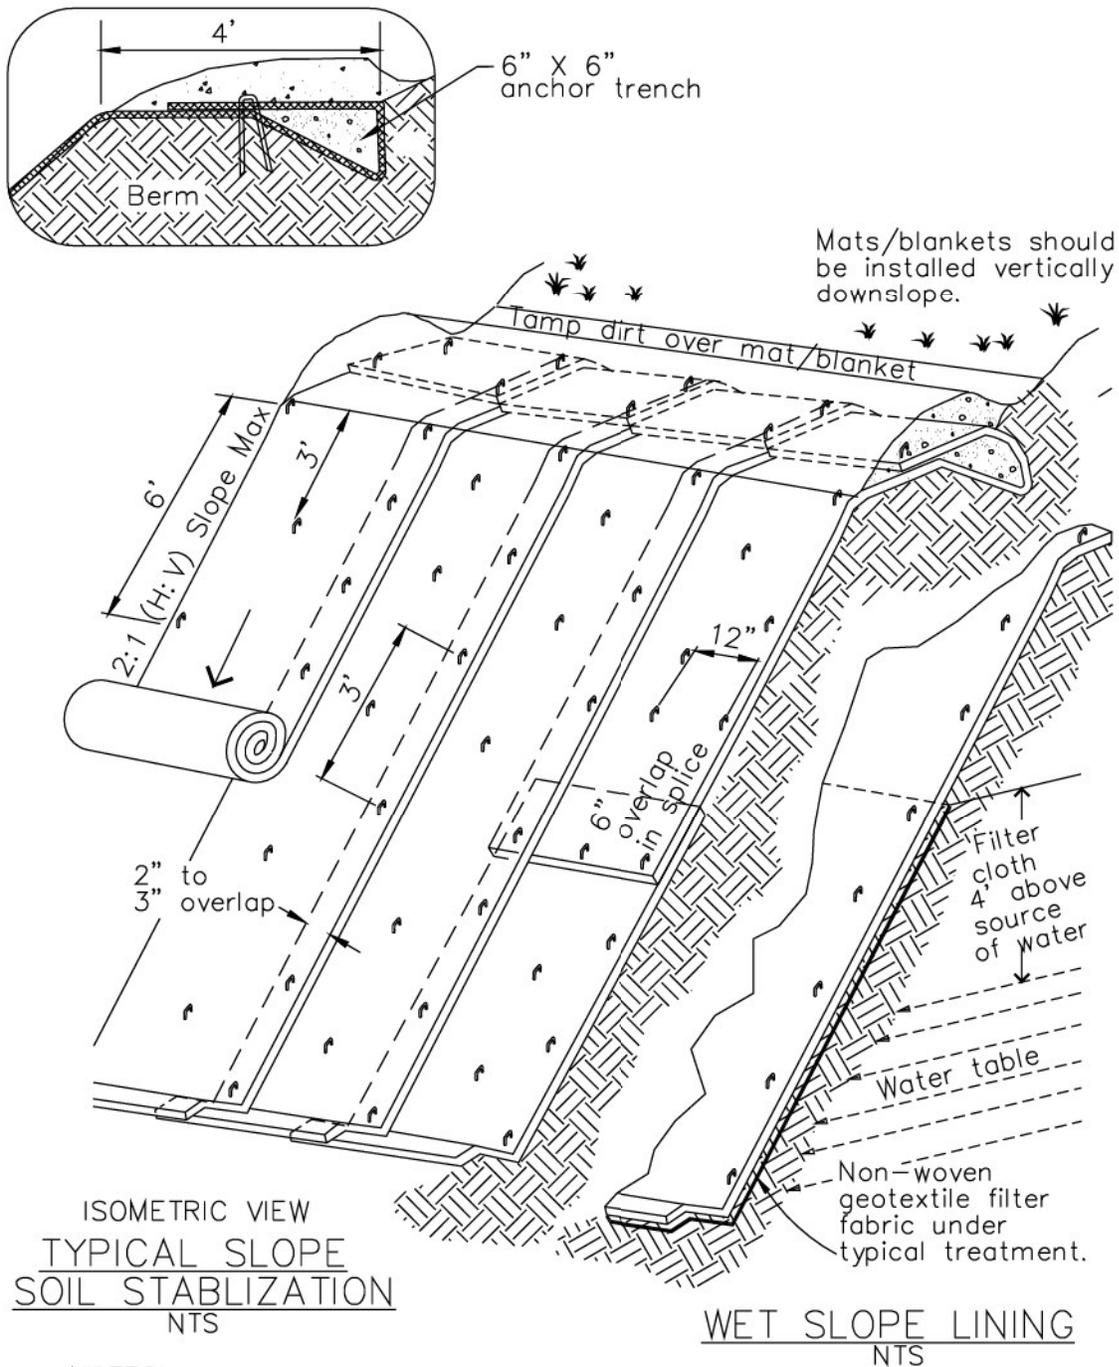


NOTES:

1. Slope surface shall be free of rocks, clods, sticks and grass. Mats/blankets shall have good soil contact.
2. Lay blankets loosely and stake or staple to maintain direct contact with the soil. Do not stretch.
3. Install per manufacturer's recommendations


TYPICAL INSTALLATION DETAIL

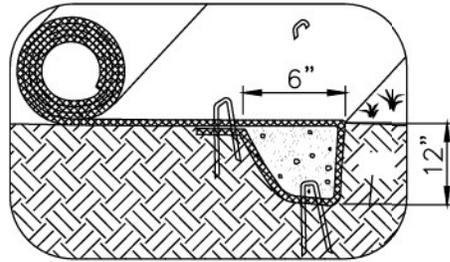


INITIAL CHANNEL ANCHOR TRENCH
NTS

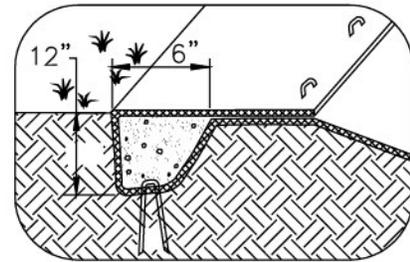


TERMINAL SLOPE AND CHANNEL ANCHOR TRENCH
NTS

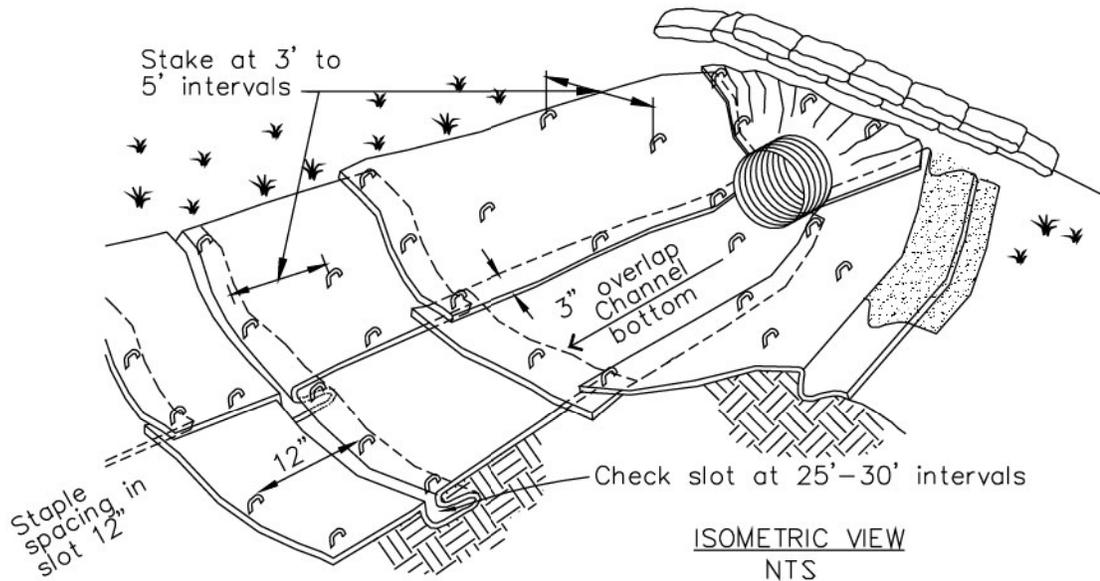

ISOMETRIC VIEW
NTS

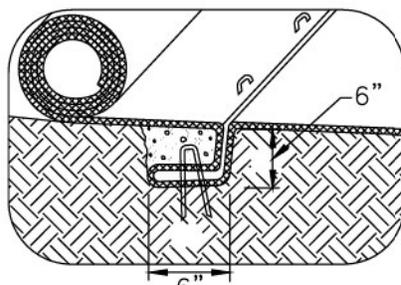

INTERMITTENT CHECK SLOT
NTS

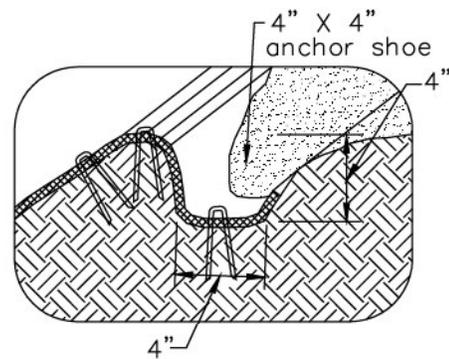


LONGITUDINAL ANCHOR TRENCH
NTS

NOTES:

1. Check slots to be constructed per manufacturers specifications.
2. Staking or stapling layout per manufacturers specifications.
3. Install per manufacturer's recommendations

TYPICAL INSTALLATION DETAIL



Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose

Dewatering Operations are practices that manage the discharge of pollutants when non-storm water and accumulated precipitation (storm water) must be removed from a work location so that construction work may be accomplished.

Appropriate Applications

- These practices are implemented for discharges of non-storm water and storm water (accumulated rain water) from construction sites. Non-storm water includes, but is not limited to, groundwater, dewatering of piles, water from cofferdams, water diversions, and water used during construction activities that must be removed from a work area.
- Practices identified in this section are also appropriate for implementation when managing the removal of accumulated precipitation (storm water) from depressed areas at a construction site.
- Storm water mixed with non-storm water should be managed as non-storm water.

Limitations

- Dewatering operations for non-storm water will require, and must comply with, applicable local permits, project-specific permits, and regulations.
- Site conditions will dictate design and use of dewatering operations.
- A dewatering plan shall be submitted as part of the SWPPP/WPCP detailing the location of dewatering activities, equipment, and discharge point.
- The controls discussed in this best management practice (BMP) address sediment only. If the presence of polluted water with hazardous substances is identified in the contract, the contractor shall implement dewatering pollution controls as required by the contract documents. If the quality of water to be removed by dewatering is not identified as polluted in the contract documents, but is later determined by observation or testing to be polluted, the contractor shall notify the Resident Engineer (RE) and comply with Standard Specifications Section 5-1.116, "Differing Site Conditions."


Standards and Specifications

- Avoid dewatering discharges where possible by using the water for dust control, by infiltration, etc.
- Dewatering shall be conducted in accordance with the Field Guide to Construction Site Dewatering, October 2001, CTSW-RT-01-010.
- Dewatering for accumulated precipitation (storm water) shall follow this BMP and use treatment measures specified herein.
- The RWQCB may require a separate NPDES permit prior to the dewatering discharge of non-storm water. These permits will have specific testing, monitoring, and discharge requirements and can take significant time to obtain.
- Except in RWQCB Regions 1 and 2, the discharge of accumulated precipitation (storm water) to a water body or storm drain is subject to the requirements of Caltrans NPDES permit. Sediment control and other appropriate BMPs (e.g., outlet protection/energy dissipation) must be employed when this water is discharged.
- RWQCB Regions 1 and 2 require notification and approval prior to any discharge of water from construction sites.
- In RWQCB Regions 3, 5, 7, and 9 non-storm water dewatering for discharges meeting certain conditions are allowed under an RWQCB general dewatering NPDES Permit. Notification and approval from the RWQCB is required prior to conducting these operations. This includes storm water that is mixed with groundwater or other non-storm water sources. Once the discharge is allowed, appropriate BMPs must be implemented to ensure that the discharge complies with all permit requirements. Conditions for potential discharge under an RWQCB general dewatering NPDES Permit include:
 - Regions 3, 5, 7: Non-storm water discharges, free of pollutants other than sediment, <0.25 MGD, with a duration of 4 or fewer months.
 - Region 9: Groundwater, free of pollutants other than sediment, <0.10 MGD, to surface waters other than San Diego Bay.
- The flow chart shown on Page 4 shall be utilized to guide dewatering operations.
- The RE will coordinate monitoring and permit compliance.
- Discharges must comply with regional and watershed-specific discharge requirements.
- Additional permits or permissions from other agencies may be required for dewatering cofferdams or diversions.
- Dewatering discharges must not cause erosion at the discharge point.

Maintenance and Inspection

- Dewatering records shall be maintained for a period of 3 years.
- Inspect all BMPs implemented to comply with permit requirements frequently and repair or replace to ensure the BMPs function as designed.
- Accumulated sediment removed during the maintenance of a dewatering device may be incorporated in the project at locations designated by the RE or disposed of outside the right-of-way in conformance with the Standard Specifications.
- Accumulated sediment that is commingled with other pollutants must be disposed of in accordance with all applicable laws and regulations and as approved by the RE.

Dewatering Operations

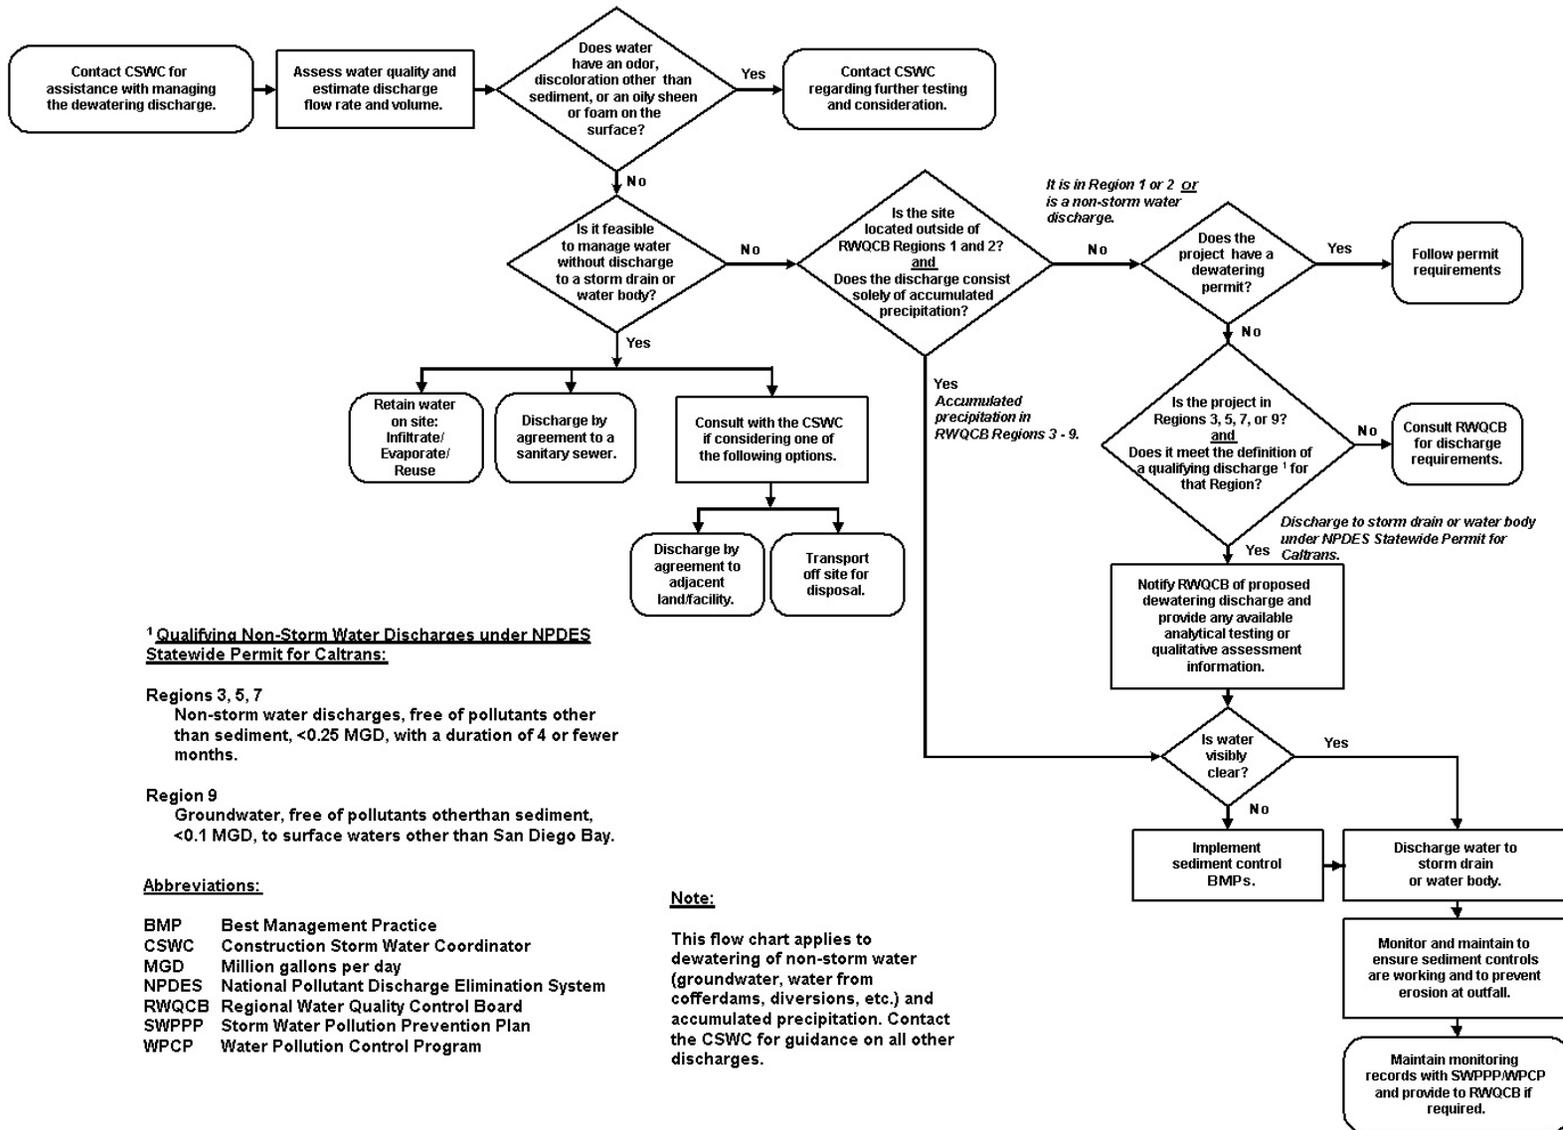

=

Sediment Treatment A variety of methods can be used to treat water during dewatering operations from the construction site. Several devices are presented in this section that provide options to achieve sediment removal. The size of particles present in the sediment and Permit or receiving water limitations on sediment are key considerations for selecting sediment treatment option(s); in some cases, the use of multiple devices may be appropriate.

Category 1: Constructed Settling Technologies

The devices discussed in this category are to be used exclusively for dewatering operations only.

Sediment/Desilting Basin (SC-2)

Description:

A desilting basin is a temporary basin with a controlled release structure that is formed by excavation and/or construction of an embankment to detain sediment-laden runoff and allow sediment to settle out before discharging.

Appropriate Applications:

- Effective for the removal of trash, gravel, sand, and silt and some metals that settle out with the sediment.

Implementation:

- Excavation and construction of related facilities is required.
- Temporary desilting basins must be fenced if safety is a concern.
- Outlet protection is required to prevent erosion at the outfall location.

Maintenance:

- Maintenance is required for safety fencing, vegetation, embankment, inlet and outfall structures, as well as other features.
- Removal of sediment is required when the storage volume is reduced by one-third.

Sediment Trap (SC-3)

Description:

A sediment trap is a temporary basin formed by excavation and/or construction of an earthen embankment across a waterway or low drainage area to detain sediment-laden runoff and allow sediment to settle out before discharging.

Appropriate Applications:

- Effective for the removal of large and medium sized particles (sand and gravel) and some metals that settle out with the sediment.

Implementation:

- Excavation and construction of related facilities is required.
- Trap inlets shall be located to maximize the travel distance to the trap outlet.
- Use rock or vegetation to protect the trap outlets against erosion.

Maintenance:

- Maintenance is required for vegetation, embankment, inlet and outfall structures, as well as other features.
- Removal of sediment is required when the storage volume is reduced by one-third.

Category 2: Mobile Settling Technologies

The devices discussed in this category are typical of tanks that can be used for sediment treatment of dewatering operations. A variety of vendors are available who supply these tanks.

Weir Tank

Description:

A weir tank separates water and waste by using weirs. The configuration of the weirs (over and under weirs) maximizes the residence time in the tank and determines the waste to be removed from the water, such as oil, grease, and sediments.

Appropriate Applications:

- The tank removes trash, some settleable solids (gravel, sand, and silt), some visible oil and grease, and some metals (removed with sediment). To achieve high levels of flow, multiple tanks can be used in parallel. If additional treatment is desired, the tanks can be placed in series or as pre-treatment for other methods.


Implementation:

- Tanks are delivered to the site by the vendor, who can provide assistance with set-up and operation.
- Tank size will depend on flow volume, constituents of concern, and residency period required. Vendors shall be consulted to appropriately size tank.

Maintenance:

- Periodic cleaning is required based on visual inspection or reduced flow.
- Oil and grease disposal must be by licensed waste disposal company.

Schematic Diagrams:

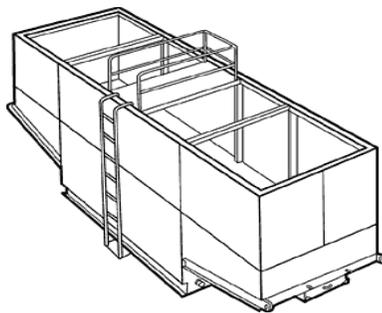

Weir Tanks

Dewatering Tank

Description:

A dewatering tank removes debris and sediment. Flow enters the tank through the top, passes through a fabric filter, and is discharged through the bottom of the tank. The filter separates the solids from the liquids.

Appropriate Applications:

- The tank removes trash, gravel, sand, and silt, some visible oil and grease, and some metals (removed with sediment). To achieve high levels of flow, multiple tanks can be used in parallel. If additional treatment is desired, the tanks can be placed in series or as pre-treatment for other methods.

Implementation:

- Tanks are delivered to the site by the vendor, who can provide assistance with set-up and operation.
- Tank size will depend on flow volume, constituents of concern, and residency period required. Vendors shall be consulted to appropriately size tank.

Maintenance:

- Periodic cleaning is required based on visual inspection or reduced flow.
- Oil and grease disposal must be by licensed waste disposal company.

Schematic Diagrams:



Dewatering Tanks

Category 3: Basic Filtration Technologies

Gravity Bag Filter

Description:

A gravity bag filter, also referred to as a dewatering bag, is a square or rectangular bag made of non-woven geotextile fabric that collects sand, silt, and fines.

Appropriate Applications:

- Effective for the removal of sediments (gravel, sand, and silt). Some metals are removed with the sediment.


Implementation:

- Water is pumped into one side of the bag and seeps through the bottom and sides of the bag.
- A secondary barrier, such as a rock filter bed or straw/hay bale barrier, is placed beneath and beyond the edges of the bag to capture sediments that escape the bag.

Maintenance:

- Inspection of the flow conditions, bag condition, bag capacity, and the secondary barrier is required.
- Replace the bag when it no longer filters sediment or passes water at a reasonable rate.
- The bag is disposed off-site, or on-site as directed by the RE.

Schematic Diagrams:

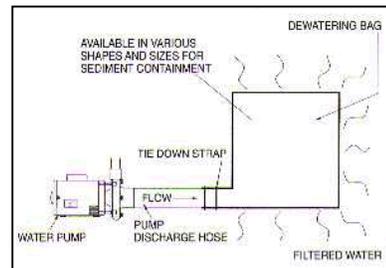

Gravity Bag Filter

Category 4: Advanced Filtration Technologies

Sand Media Particulate Filter

Description:

Water is treated by passing it through canisters filled with sand media. Generally, sand filters provide a final level of treatment. They are often used as a secondary or higher level of treatment after a significant amount of sediment and other pollutants have been removed.

Appropriate Applications:

- Effective for the removal of trash, gravel, sand, and silt and some metals, as well as the reduction of biochemical oxygen demand (BOD) and turbidity.
- Sand filters can be used for standalone treatment or in conjunction with bag and cartridge filtration if further treatment is required.
- Sand filters can also be used to provide additional treatment to water treated via settling or basic filtration.

Implementation:

- The filters require delivery to the site and initial set up. The vendor can provide assistance with installation and operation.

Maintenance:

- The filters require monthly service to monitor and maintain the sand media.

Schematic Diagrams:



Sand Media Particulate Filters

Pressurized Bag Filter

Description:

A pressurized bag filter is a unit composed of single filter bags made from polyester felt material. The water filters through the unit and is discharged through a header, allowing for the discharge of flow in series to an additional treatment unit. Vendors provide pressurized bag filters in a variety of configurations. Some units include a combination of bag filters and cartridge filters for enhanced contaminant removal.

Appropriate Applications:

- Effective for the removal of sediment (sand and silt) and some metals, as well as the reduction of BOD, turbidity, and hydrocarbons. Oil absorbent bags are available for hydrocarbon removal.
- Filters can be used to provide secondary treatment to water treated via settling or basic filtration.

Implementation:

- The filters require delivery to the site and initial set up. The vendor can provide assistance with installation and operation.

Maintenance:

- The filter bags require replacement when the pressure differential exceeds the manufacturer's recommendation.

Schematic Diagrams:



Pressurized Bag Filter

Cartridge Filter

Description:

Cartridge filters provide a high degree of pollutant removal by utilizing a number of individual cartridges as part of a larger filtering unit. They are often used as a secondary or higher (polishing) level of treatment after a significant amount of sediment and other pollutants are removed. Units come with various cartridge configurations (for use in series with pressurized bag filters) or with a larger single cartridge filtration unit (with multiple filters within).

Appropriate Applications:

- Effective for the removal of sediment (sand, silt, and some clays) and metals, as well as the reduction of BOD, turbidity, and hydrocarbons. Hydrocarbons can effectively be removed with special resin cartridges.
- Filters can be used to provide secondary treatment to water treated via settling or basic filtration.

Implementation:

- The filters require delivery to the site and initial set up. The vendor can provide assistance.



Maintenance:

- The cartridges require replacement when the pressure differential exceeds the manufacturer's recommendation.

Schematic Designs:



Cartridge Filter

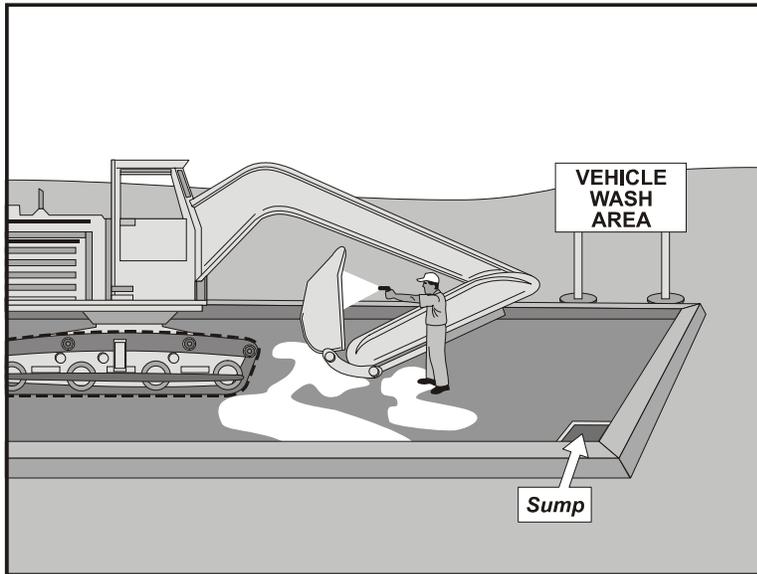

Standard Symbol

- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose Vehicle and equipment cleaning procedures and practices are used to minimize or eliminate the discharge of pollutants from vehicle and equipment cleaning operations to storm drain system or to watercourses.

Appropriate Applications These procedures are applied on all construction sites where vehicle and equipment cleaning is performed.

Limitations ■ None.



- Standards and Specifications**
- On-site vehicle and equipment washing is discouraged.
 - Cleaning of vehicles and equipment with soap, solvents or steam shall not occur on the project site unless the Resident Engineer (RE) has been notified in advance and the resulting wastes are fully contained and disposed of outside the highway right-of-way in conformance with the provisions in the Standard Specifications Section 7-1.13. Resulting wastes and by-products shall not be discharged or buried within the highway right-of-way, and must be captured and recycled or disposed according to the requirements of WM-10, "Liquid Waste Management" or WM-6, "Hazardous Waste Management," depending on the waste characteristics. Minimize use of solvents. The use of diesel for vehicle and equipment cleaning is prohibited.
 - Vehicle and equipment wash water shall be contained for percolation or evaporative drying away from storm drain inlets or watercourses and shall not be discharged within the highway right-of-way. Apply sediment control BMPs if applicable.
 - All vehicles/equipment that regularly enter and leave the construction site must be cleaned off-site.
 - When vehicle/equipment washing/cleaning must occur onsite, and the

operation cannot be located within a structure or building equipped with appropriate disposal facilities, the outside cleaning area shall have the following characteristics, and shall be arranged with the construction storm water coordinator:

- Located away from storm drain inlets, drainage facilities, or watercourses.
- Paved with concrete or asphalt and bermed to contain wash waters and to prevent run-on and runoff.
- Configured with a sump to allow collection and disposal of wash water.
- Wash waters shall not be discharged to storm drains or watercourses.
- Used only when necessary.
- When cleaning vehicles/equipment with water:
 - Use as little water as possible. High pressure sprayers may use less water than a hose, and shall be considered.
 - Use positive shutoff valve to minimize water usage.
 - Facility wash racks shall discharge to a sanitary sewer, recycle system or other approved discharge system and shall not discharge to the storm drainage system or watercourses.

Maintenance and Inspection

- The control measure shall be inspected at a minimum of once a week.
- Monitor employees and subcontractors throughout the duration of the construction project to ensure appropriate practices are being implemented.
- Inspect sump regularly and remove liquids and sediment as needed or as directed by the RE.

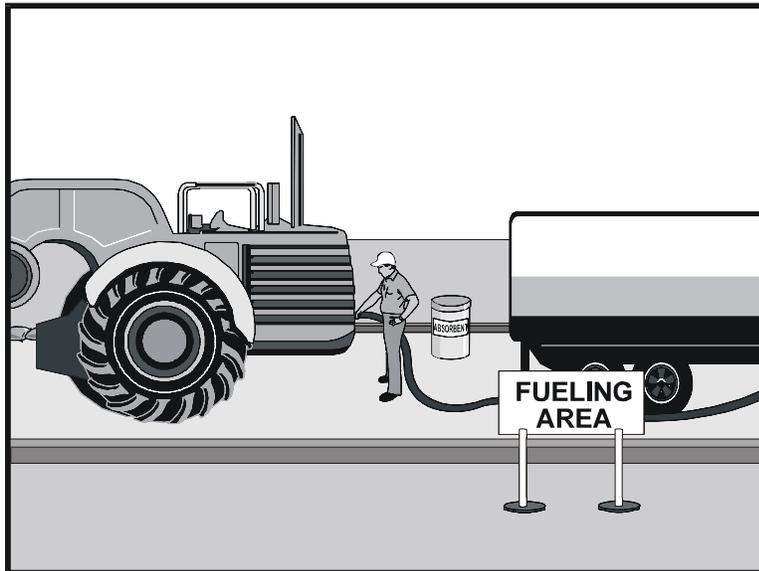

Standard Symbol

- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose Vehicle and equipment fueling procedures and practices are designed to minimize or eliminate the discharge of fuel spills and leaks into storm drain systems or to watercourses.

Appropriate Applications These procedures are applied on all construction sites where vehicle and equipment fueling takes place.

Limitations



- Onsite vehicle and equipment fueling shall only be used where it's impractical to send vehicles and equipment off-site for fueling.

- Standards and Specifications**
- When fueling must occur onsite, the contractor shall select and designate an area to be used, subject to approval of the Resident Engineer (RE).
 - Absorbent spill clean-up materials and spill kits shall be available in fueling areas and on fueling trucks and shall be disposed of properly after use.
 - Drip pans or absorbent pads shall be used during vehicle and equipment fueling, unless the fueling is performed over an impermeable surface in a dedicated fueling area.
 - Dedicated fueling areas shall be protected from storm water run-on and runoff, and shall be located at least 15 m (50 ft) from downstream drainage facilities and watercourses. Fueling must be performed on level-grade areas.
 - Nozzles used in vehicle and equipment fueling shall be equipped with an automatic shut-off to control drips. Fueling operations shall not be left unattended.
 - Protect fueling areas with berms and/or dikes to prevent run-on, runoff, and to contain spills.

- Use vapor recovery nozzles to help control drips as well as air pollution where required by Air Quality Management Districts (AQMD). Ensure the nozzle is secured upright when not in use.
- Fuel tanks shall not be "topped-off."
- Vehicles and equipment shall be inspected on each day of use for leaks. Leaks shall be repaired immediately or problem vehicles or equipment shall be removed from the project site.
- Absorbent spill clean-up materials shall be available in fueling and maintenance areas and used on small spills instead of hosing down or burying techniques. The spent absorbent material shall be removed promptly and disposed of properly.
- Federal, state, and local requirements shall be observed for any stationary above ground storage tanks. Refer to WM-1, "Material Delivery and Storage."
- Mobile fueling of construction equipment throughout the site shall be minimized. Whenever practical, equipment shall be transported to the designated fueling area.

Maintenance and Inspection

- Fueling areas and storage tanks shall be inspected regularly.
- Keep an ample supply of spill cleanup material on the site.
- Immediately cleanup spills and properly dispose of contaminated soil and cleanup materials.

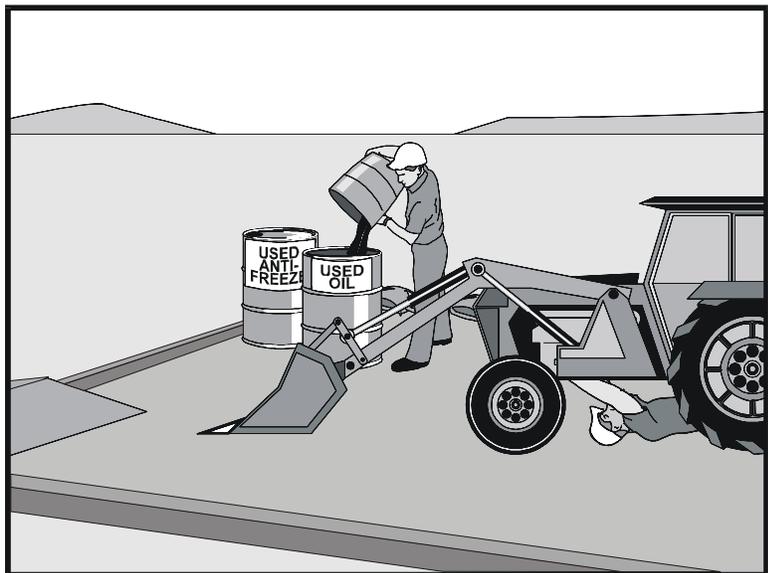

Standard Symbol

- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose Procedures and practices to minimize or eliminate the discharge of pollutants to the storm drain systems or to watercourses from vehicle and equipment maintenance procedures.

Appropriate Applications These procedures are applied on all construction projects where an onsite yard area is necessary for storage and maintenance of heavy equipment and vehicles.



Limitations ■ None identified.

- Standards and Specifications**
- Drip pans or absorbent pads shall be used during vehicle and equipment maintenance work that involves fluids, unless the maintenance work is performed over an impermeable surface in a dedicated maintenance area.
 - All maintenance areas are required to have spill kits and/or use other spill protection devices.
 - Dedicated maintenance areas shall be protected from storm water run-on and runoff, and shall be located at least 15 m (50 ft) from downstream drainage facilities and watercourses.
 - Drip Pans or plastic sheeting shall be placed under all vehicles and equipment placed on docks, barges, or other structures over water bodies when the vehicle or equipment is planned to be idle for more than one hour.
 - Absorbent spill clean-up materials shall be available in maintenance areas and shall be disposed of properly after use. Substances used to coat asphalt transport trucks and asphalt-spreading equipment shall be non-toxic.
 - Use off-site maintenance facilities whenever practical.

- For long-term projects, consider constructing roofs or using portable tents over maintenance areas.
- Properly dispose of used oils, fluids, lubricants, and spill cleanup materials.
- Do not dump fuels and lubricants onto the ground.
- Do not place used oil in a dumpster or pour into a storm drain or watercourse.
- Properly dispose or recycle used batteries.
- Do not bury used tires.
- Repair of fluid and oil leaks immediately.
- Provide spill containment dikes or secondary containment around stored oil and chemical drums.

Maintenance and Inspection

- Maintain waste fluid containers in leak proof condition.
- Vehicle and equipment maintenance areas shall be inspected regularly.
- Vehicles and equipment shall be inspected on each day of use. Leaks shall be repaired immediately or the problem vehicle(s) or equipment shall be removed from the project site.
- Inspect equipment for damaged hoses and leaky gaskets routinely. Repair or replace as needed.

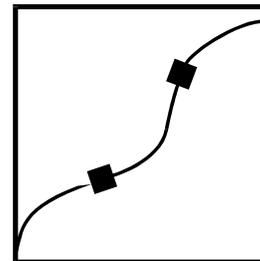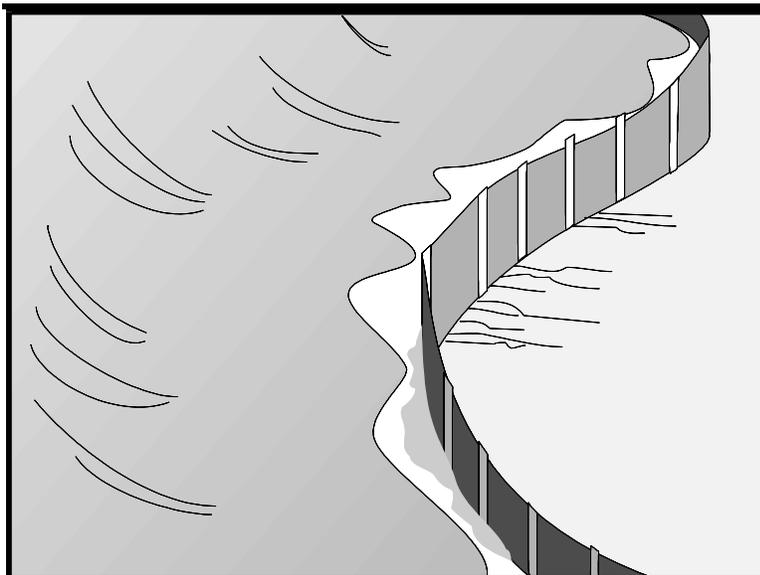

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A silt fence is a temporary linear sediment barrier of permeable fabric designed to intercept and slow the flow of sediment-laden sheet flow runoff. Silt fences allow sediment to settle from runoff before water leaves the construction site.

- Appropriate Applications** Silt fences are placed:
- Below the toe of exposed and erodible slopes.
 - Down-slope of exposed soil areas.
 - Around temporary stockpiles.
 - Along streams and channels.
 - Along the perimeter of a project.

- Limitations**
- Not effective unless trenched and keyed in.
 - Not intended for use as mid-slope protection on slopes greater than 1:4 (V:H).
 - Must be maintained.
 - Must be removed and disposed of.
 - Don't use below slopes subject to creep, slumping, or landslides.
 - Don't use in streams, channels, drain inlets, or anywhere flow is concentrated.
 - Don't use silt fences to divert flow.

Standards and Specifications *Design and Layout*

- The maximum length of slope draining to any point along the silt fence shall be 61 m (200 ft) or less.
- Slope of area draining to silt fence shall be less than 1:1 (V:H).
- Limit to locations suitable for temporary ponding or deposition of sediment.
- Fabric life span generally limited to between five and eight months. Longer periods may require fabric replacement.
- Silt fences shall not be used in concentrated flow areas.
- Lay out in accordance with Pages 5 and 6 of this BMP.
- For slopes steeper than 1:2 (V:H) and that contain a high number of rocks or large dirt clods that tend to dislodge, it may be necessary to install additional protection immediately adjacent to the bottom of the slope, prior to installing silt fence. Additional protection may be a chain link fence or a cable fence.
- For slopes adjacent to water bodies or Environmentally Sensitive Areas (ESAs), additional temporary soil stabilization BMPs shall be used.

Materials

- Silt fence fabric shall be woven polypropylene with a minimum width of 900 mm (36 inches) and a minimum tensile strength of 0.45-kN. The fabric shall conform to the requirements in ASTM designation D4632 and shall have an integral reinforcement layer. The reinforcement layer shall be a polypropylene, or equivalent, net provided by the manufacturer. The permittivity of the fabric shall be between 0.1 sec^{-1} and 0.15 sec^{-1} in conformance with the requirements in ASTM designation D4491. Contractor must submit certificate of compliance in accordance with Standard Specifications Section 6-1.07.
- Wood stakes shall be commercial quality lumber of the size and shape shown on the plans. Each stake shall be free from decay, splits or cracks longer than the thickness of the stake or other defects that would weaken the stakes and cause the stakes to be structurally unsuitable.
- Bar reinforcement may be used, and its size shall be equal to a number four (4) or greater. End protection shall be provided for any exposed bar reinforcement.
- Staples used to fasten the fence fabric to the stakes shall be not less than 45 mm (1.75 inches) long and shall be fabricated from 1.57 mm (0.06 inch) or heavier wire. The wire used to fasten the tops of the stakes together when

joining two sections of fence shall be 3.05 mm (0.12 inch) or heavier wire. Galvanizing of the fastening wire is not required.


Installation

- Generally, silt fences shall be used in conjunction with soil stabilization source controls up slope to provide effective erosion and sediment control.
- Bottom of the silt fence shall be keyed-in a minimum of 150 mm (12 inches).
- Trenches shall not be excavated wider and deeper than necessary for proper installation of the temporary linear sediment barriers.
- Excavation of the trenches shall be performed immediately before installation of the temporary linear sediment barriers.
- Construct silt fences with a set-back of at least 1m (3 ft) from the toe of a slope. Where a silt fence is determined to be not practical due to specific site conditions, the silt fence may be constructed at the toe of the slope, but shall be constructed as far from the toe of the slope as practical.
- Construct the length of each reach so that the change in base elevation along the reach does not exceed 1/3 the height of the barrier; in no case shall the reach exceed 150 meters (490 ft).
- Cross barriers shall be a minimum of 1/3 and a maximum of 1/2 the height of the linear barrier.
- Install in accordance with Pages 5 and 6 of this BMP.

Maintenance and Inspection

- Repair undercut silt fences.
- Repair or replace split, torn, slumping, or weathered fabric.
- Inspect silt fence when rain is forecast. Perform necessary maintenance, or maintenance required by the Resident Engineer (RE).
- Inspect silt fence following rainfall events. Perform maintenance as necessary, or as required by the RE.
- Maintain silt fences to provide an adequate sediment holding capacity. Sediment shall be removed when the sediment accumulation reaches one-third (1/3) of the barrier height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the right-of-way in conformance with the Standard Specifications.
- Silt fences that are damaged and become unsuitable for the intended purpose, as determined by the RE, shall be removed from the site of work, disposed of outside the highway right-of-way in conformance with the Standard Specifications, and replaced with new silt fence barriers.

- Holes, depressions or other ground disturbance caused by the removal of the temporary silt fences shall be backfilled and repaired in conformance with the Standard Specifications.
- Remove silt fence when no longer needed or as required by the RE. Fill and compact post holes and anchorage trench, remove sediment accumulation, and grade fence alignment to blend with adjacent ground.


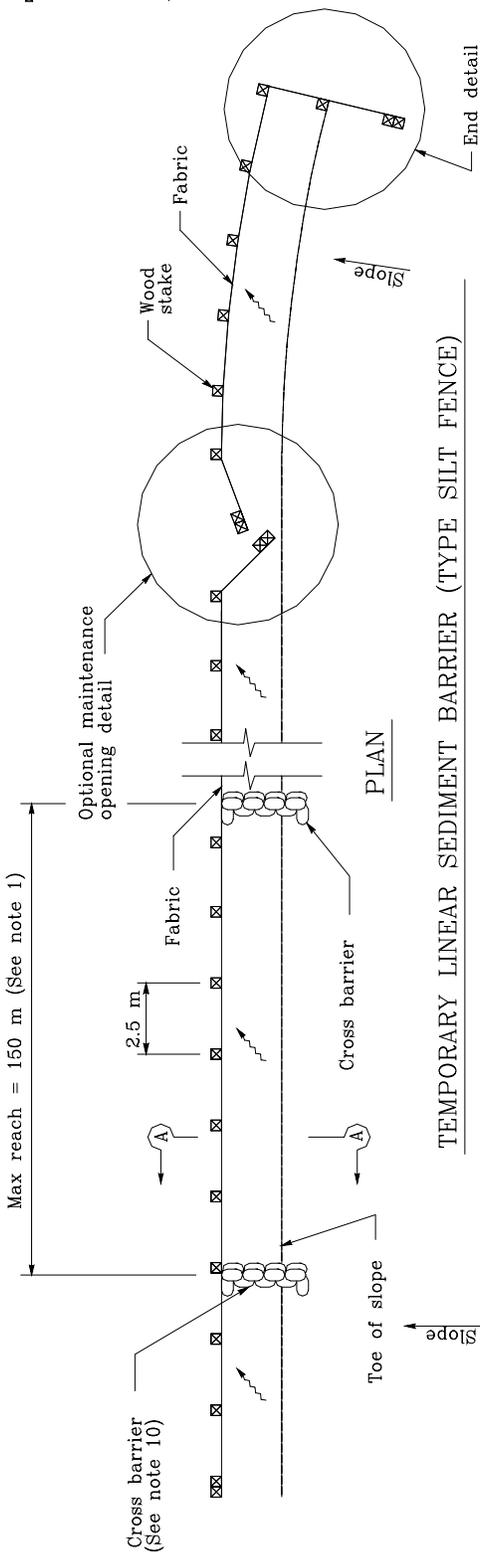


TEMPORARY LINEAR SEDIMENT BARRIER (TYPE SILT FENCE)

NOTES

1. Construct the length of each reach so that the change in base elevation along the reach does not exceed 1/3 the height of the linear barrier, in no case shall the reach length exceed 150m.
2. The last 2.5 m of fence shall be turned up slope.
3. Stake dimensions are nominal.
4. Dimension may vary to fit field condition.
5. Stakes shall be spaced at 2.5 m maximum and shall be positioned on downstream side of fence.
6. Stakes to overlap and fence fabric to fold around each stake one full turn. Secure fabric to stake with 4 staples.
7. Stakes shall be driven tightly together to prevent potential flow-through of sediment at joint. The tops of the stakes shall be secured with wire.
8. For end stake, fence fabric shall be folded around two stakes one full turn and secured with 4 staples.
9. Minimum 4 staples per stake. Dimensions shown are typical.
10. Cross barriers shall be a minimum of 1/3 and a maximum of 1/2 the height of the linear barrier.
11. Maintenance openings shall be constructed in a manner to ensure sediment remains behind silt fence.
12. Joining sections shall not be placed at sump locations.
13. Sandbag rows and layers shall be offset to eliminate gaps.

LEGEND






STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

TEMPORARY LINEAR SEDIMENT BARRIER (TYPE SILT FENCE)

NO SCALE

ALL DIMENSIONS ARE IN
MILLIMETERS UNLESS OTHERWISE SHOWN

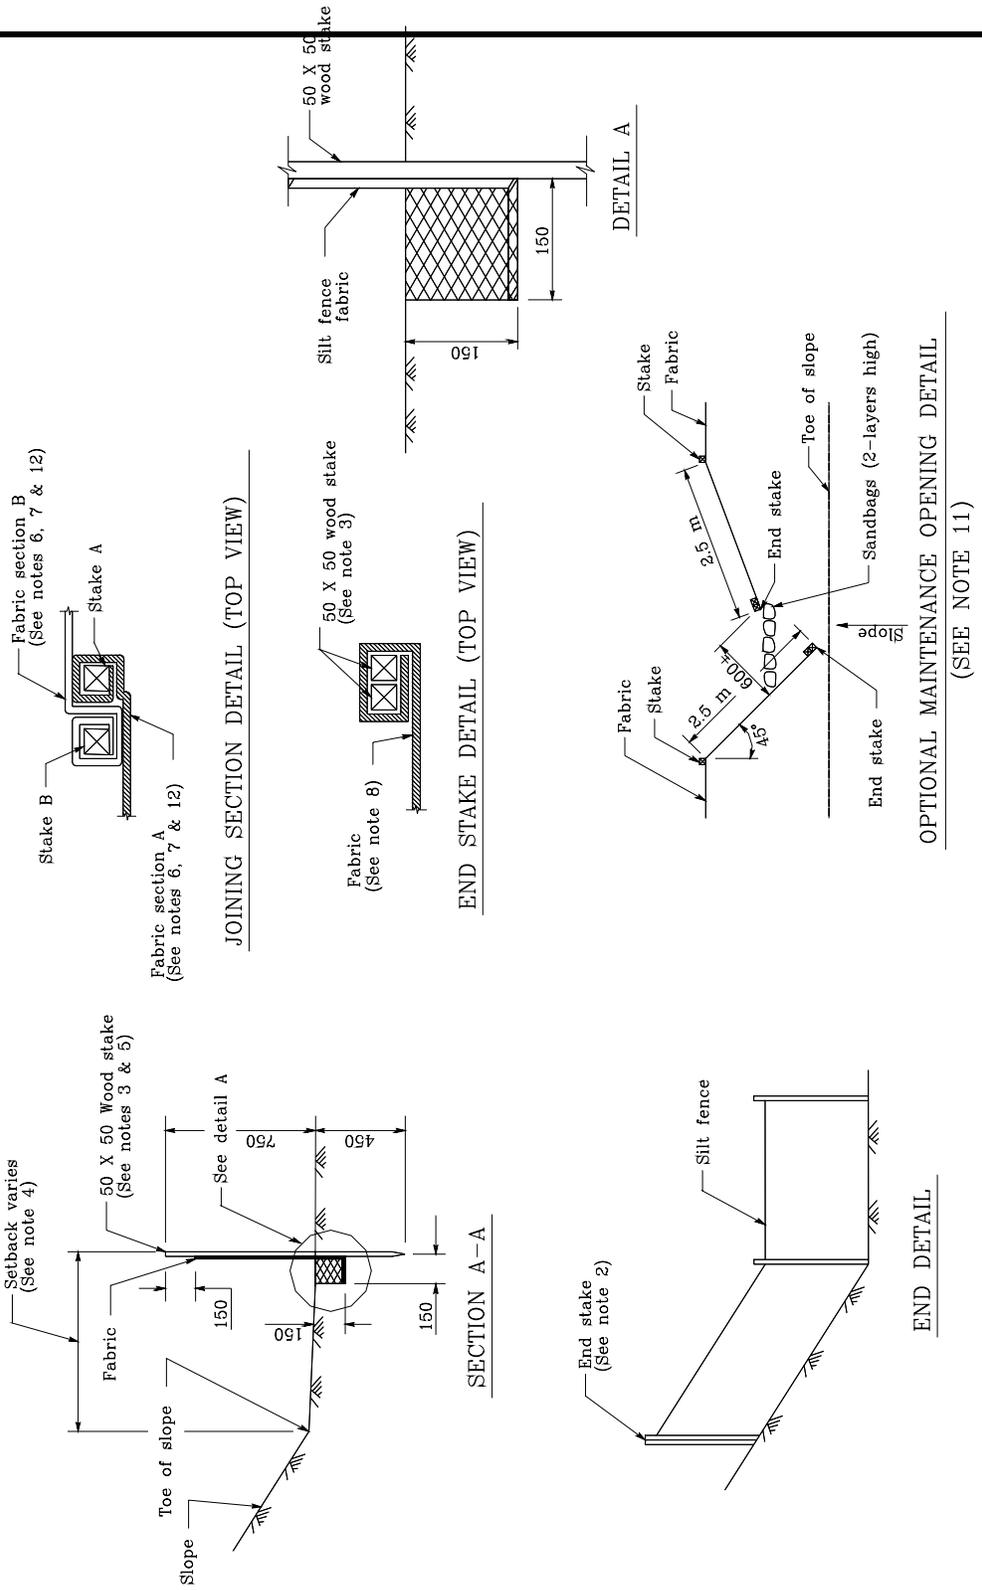

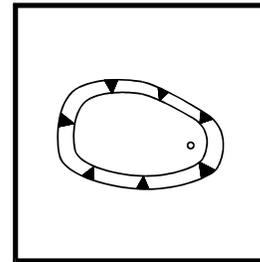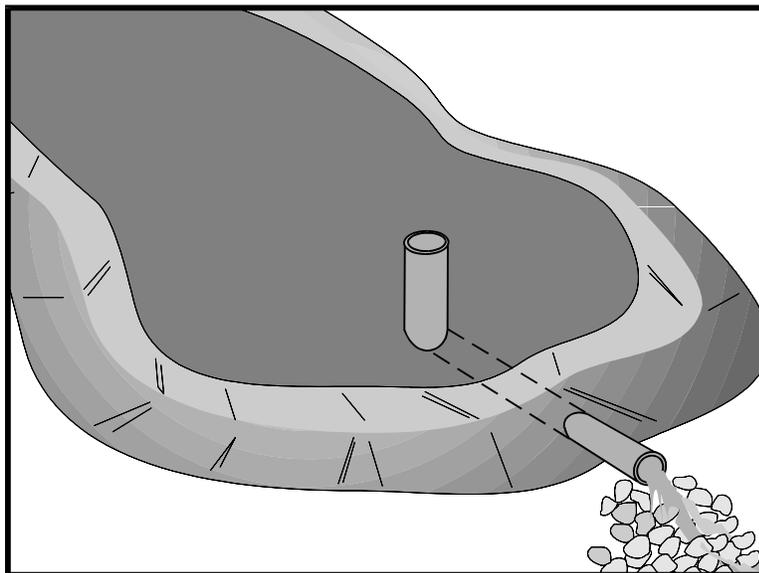

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose

A sediment/desilting basin is a temporary basin formed by excavating and/or constructing an embankment so that sediment-laden runoff is temporarily detained under quiescent conditions, allowing sediment to settle out before the runoff is discharged (refer to Figures 1 and 2).

Appropriate Applications

Sediment basins shall be designed in accordance with Section A of the State of California NPDES General Permit for Storm Water Discharges Associated with Construction Activities (General Permit). If there is insufficient area to construct a sediment basin in accordance with the General Permit requirements, then the alternate desilting design standards specified herein may be used. This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the RE.

Sediment/Desilting Basins shall be considered for use:

- On construction projects with disturbed areas during the rainy season.
- Where sediment-laden water may enter the drainage system or watercourses.
- At outlets of disturbed soil areas with areas between 2 ha and 4 ha (5 ac and 10 ac).

Limitations

- Alternative BMPs must be thoroughly investigated for erosion control before selecting temporary desilting basins.
- Requires large surface areas to permit settling of sediment.
- Not appropriate for drainage areas greater than 30 ha (75 ac).
- Not to be located in live streams

Standards and Specifications

- For safety reasons, basins shall have protective fencing.
- Size may be limited by availability of right-of-way.
- Limit the contributing area to the sediment/desilting basin to only the runoff from the disturbed soil areas. Use temporary concentrated flow conveyance controls to divert runoff from undisturbed areas away from the sediment/desilting basin.

Sediment Basin

- Sediment basins shall, at a minimum, be designed as follows:
 - Option 1: Pursuant to local ordinance for sediment basin design and maintenance, provided that the design efficiency is as protective or more protective of water quality than Option 3.

OR

- Option 2: Sediment basin(s), as measured from the bottom of the basin to the principal outlet, shall have at least a capacity equivalent to 102 cubic meters (3,600 cubic feet) of storage per 0.4 hectare (1 acre) draining into the sediment basin. The length of the basin shall be more than twice the width of the basin. The length is determined by measuring the distance between the inlet and the outlet; and the depth must not be less than 0.9 m (3 ft) nor greater than 1.5 m (5 ft) for safety reasons and for maximum efficiency.

OR

- Option 3: Sediment basin(s) shall be designed using the standard equation:

$$A_s = 1.2Q/V_s \quad (\text{Eq. 1})$$

Where:

A_s = Minimum surface area for trapping soil particles of a certain size

V_s = Settling velocity of the design particle size chosen

$$Q = CIA$$

Where:

Q = Discharge rate measured in cubic feet per second

C = Runoff coefficient

I = Precipitation intensity for the 10-year, 6-hour rain event

A = Area draining into the sediment basin in acres

The design particle size shall be the smallest soil grain size determined by wet sieve analysis, or the fine silt sized (0.01mm) particle, and the V_s used shall be 100 percent of the calculated settling velocity.

The length is determined by measuring the distance between the inlet and the outlet; the length shall be more than twice the dimension as the width; the depth shall not be less than 0.9 m (3 ft) nor greater than 1.5 m (5 ft) for safety reasons and for maximum efficiency [0.6 m (2 ft) of sediment storage, 0.6 m (2 ft) of capacity]. The basin(s) shall be located on the site where it can be maintained on a year-round basis and shall be maintained on a schedule to retain the 0.6 m (2 ft) of capacity.

OR

- Option 4: The use of an equivalent surface area design or equation, provided that the design efficiency is as protective or more protective of water quality than Option 3.

Desilting Basin

- Desilting basins shall be designed to have a capacity equivalent to 100 cubic meters of storage (as measured from the top of the basin to the principal outlet) per hectare of contributory area. This design is less than the required to capture the 0.01 mm particle size but larger than that required to capture particles 0.02 mm or larger.
- The length of the basin shall be more than twice the width of the basin; the length shall be determined by measuring the distance between the inlet and the outlet.
- The depth must be no less than one (1) meter nor greater than 1.5 m.
- Basins with an impounding levee greater than 1.5 m (5 ft) tall, measured from the lowest point to the impounding area to the highest point of the levee, and basins capable of impounding more than 1000 cubic meters (35,300 cubic feet), shall be designed by a professional Civil Engineer registered with the state of California. The design must be submitted to the Resident Engineer (RE) for approval at least 7 days prior to the basin construction. The design shall include maintenance requirements, including sediment and vegetation removal, to ensure continuous function of the basin outlet and bypass structures.

General Requirements

- Design and locate sediment/desilting basins so that they can be maintained. Construct desilting basins prior to the rainy season and construction activities.
- Sediment/desilting basins, regardless of size and storage volume, shall include features to accommodate overflow or bypass flows that exceed the design storm event. The calculated basin volume and proposed location shall be submitted to

the RE for approval at least 3 days prior to the basin construction.

- Construct an emergency spillway to accommodate flows not carried by the principal spillway. Spillway shall consist of an open channel (earthen or vegetated) over undisturbed material (not fill) or constructed of a non-erodible riprap.
- Spillway control section, which is a level portion of the spillway channel at the highest elevation in the channel, shall be a minimum of 6 m (20 ft) in length.
- A forebay, constructed upstream of the basin may be provided to remove debris and larger particles.
- Basin inlets shall be located to maximize travel distance to the basin outlet.
- Rock or vegetation shall be used to protect the basin inlet and slopes against erosion.
- The outflow from the basins shall be provided with outlet protection to prevent erosion and scouring of the embankment and channel. See BMP SS-10, "Outlet Protection/Velocity Dissipation Devices."
- Basin shall be located: (1) by excavating a suitable area or where a low embankment can be constructed across a swale, (2) where post-construction (permanent) detention basins will be constructed, (3) where failure would not cause loss of life or property damage, (4) where the basins can be maintained on a year-round basins to provide access for maintenance, including sediment removal and sediment stockpiling in a protected area, and to maintain the basin to provide the required capacity.
- Areas under embankments, structural works, and sediment/desilting basin must be cleared, stripped of vegetation in accordance with Standard Specifications Section 16 – "Clearing and Grubbing."
- Earthwork shall be in accordance with Standard Specifications Section 19 – "Earthwork". Contractor is specifically directed to Standard Specifications Sections 19-5, "Compaction," and 19-6, "Embankment Construction."
- Structure shall be placed on a firm, smooth foundation with the base securely anchored with concrete or other means to prevent floatation.
- Discharge from the basin shall be accomplished through a water quality outlet. An example is shown in Figure 3. The Principal outlet shall consist of a corrugated metal, high density polyethylene (HDPE), or reinforced concrete riser pipe with dewatering holes and an anti-vortex device and trash rack attached to the top of the riser, to prevent floating debris from flowing out of the basin or obstructing the system. This principal structure shall be designed

to accommodate the inflow design storm.

- A rock pile or rock-filled gabions can serve as alternatives to the debris screen, although the designer should be aware of the potential for extra maintenance involved should the pore spaces in the rock pile clog.
- Proper hydraulic design of the outlet is critical to achieving the desired performance of the basin. The water quality outlet should be designed to drain the basin within 24 to 72 hours (also referred to as “drawdown time”). (The 24-hour limit is specified to provide adequate settling time; the 72-hour limit is specified to mitigate vector control concerns.)
- The two most common outlet problems that occur are: (1) the capacity of the outlet is too great resulting in only partial filling of the basin and drawdown time less than designed for; and (2) the outlet clogs because it is not adequately protected against trash and debris. To avoid these problems, the following outlet types are recommended for use: (1) a single orifice outlet with or without the protection of a riser pipe, and (2) perforated riser. Design guidance for single orifice and perforated riser outlets are as follows:

Flow Control Using a Single Orifice At The Bottom Of The Basin

(Figure 1): The outlet control orifice should be sized using the following equation:

$$a = \frac{2A(H - Ho)^{0.5}}{3600CT(2g)^{0.5}} = \frac{(7 \times 10^{-5})A(H - Ho)^{0.5}}{CT} \quad (\text{Eq. 2})$$

where:

- a = area of orifice (ft²) (1 ft² = 0.0929m²)
- A = surface area of the basin at mid elevation (ft²)
- C = orifice coefficient
- T = drawdown time of full basin (hrs)
- G = gravity (32.2 ft/s²)
- H = elevation when the basin is full (ft)
- Ho = final elevation when basin is empty (ft)

With a drawdown time of 40 hours, the equation becomes:

$$a = \frac{(1.75 \times 10^{-6})A(H - Ho)^{0.5}}{C} \quad (\text{Eq. 3})$$

Flow Control Using Multiple Orifices (see Figure2):

$$a_t = \frac{2A(h_{max})}{CT(2g[h_{max} - h_{centroid\ of\ orifices}])^{0.5}} \quad (\text{Eq. 4})$$

With terms as described above except:

a_t = total area of orifices

h_{max} = maximum height from lowest orifice to the maximum water surface (ft)

$h_{centroid\ of\ orifices}$ = height from the lowest orifice to the centroid of the orifice configuration (ft)

Allocate the orifices evenly on two rows; separate the holes by 3x hole diameter vertically, and by 120 degrees horizontally (refer to Figure 3).

Because basins are not maintained for infiltration, water loss by infiltration should be disregarded when designing the hydraulic capacity of the outlet structure.

Care must be taken in the selection of "C"; 0.60 is most often recommended and used. However, based on actual tests, GKY (1989), "Outlet Hydraulics of Extended Detention Facilities for Northern Virginia Planning District Commission", recommends the following:

C = 0.66 for thin materials; where the thickness is equal to or less than the orifice diameter, or

C = 0.80 when the material is thicker than the orifice diameter

- The Contractor shall verify that the outlet is properly designed to handle the design and peak flows.
- Attach riser pipe (watertight connection) to a horizontal pipe (barrel), which extends through the embankment to toe of fill. Provide anti-seep collars on the barrel.
- Cleanout level shall be clearly marked on the riser pipe
- Avoid dewatering of groundwater to the sediment/desilting basin during the rainy season. Insignificant quantities of accumulated precipitation may be dewatered to the sediment/desilting basin unless precipitation is forecasted within 24 hours. Refer to NS-2 "Dewatering Operations."
- Chain link fencing shall be provided around each sediment/desilting basin to prevent unauthorized entry to the basin or if safety is a concern. Fencing shall be in accordance with Standard Specifications Section 80 – "Fencing."

Maintenance and Inspection


- Inspect sediment/desilting basins before and after rainfall events and weekly during the rest of the rainy season. During extended rainfall events, inspect at

least every 24 hours.

- Examine basin banks for seepage and structural soundness.
- Check inlet and outlet structures and spillway for any damage or obstructions. Repair damage and remove obstructions as needed, or as directed by the RE.
- Remove standing water from the basin within 72 hours after accumulation.
- Check inlet and outlet area for erosion and stabilize if required, or if directed by the RE.
- Remove accumulated sediment when its volume reaches one-third the volume of the sediment storage. Properly dispose of sediment and debris removed from the basin.
- Check fencing for damage and repair as needed or as directed by the RE.

Sediment/Desilting Basin

SC-2

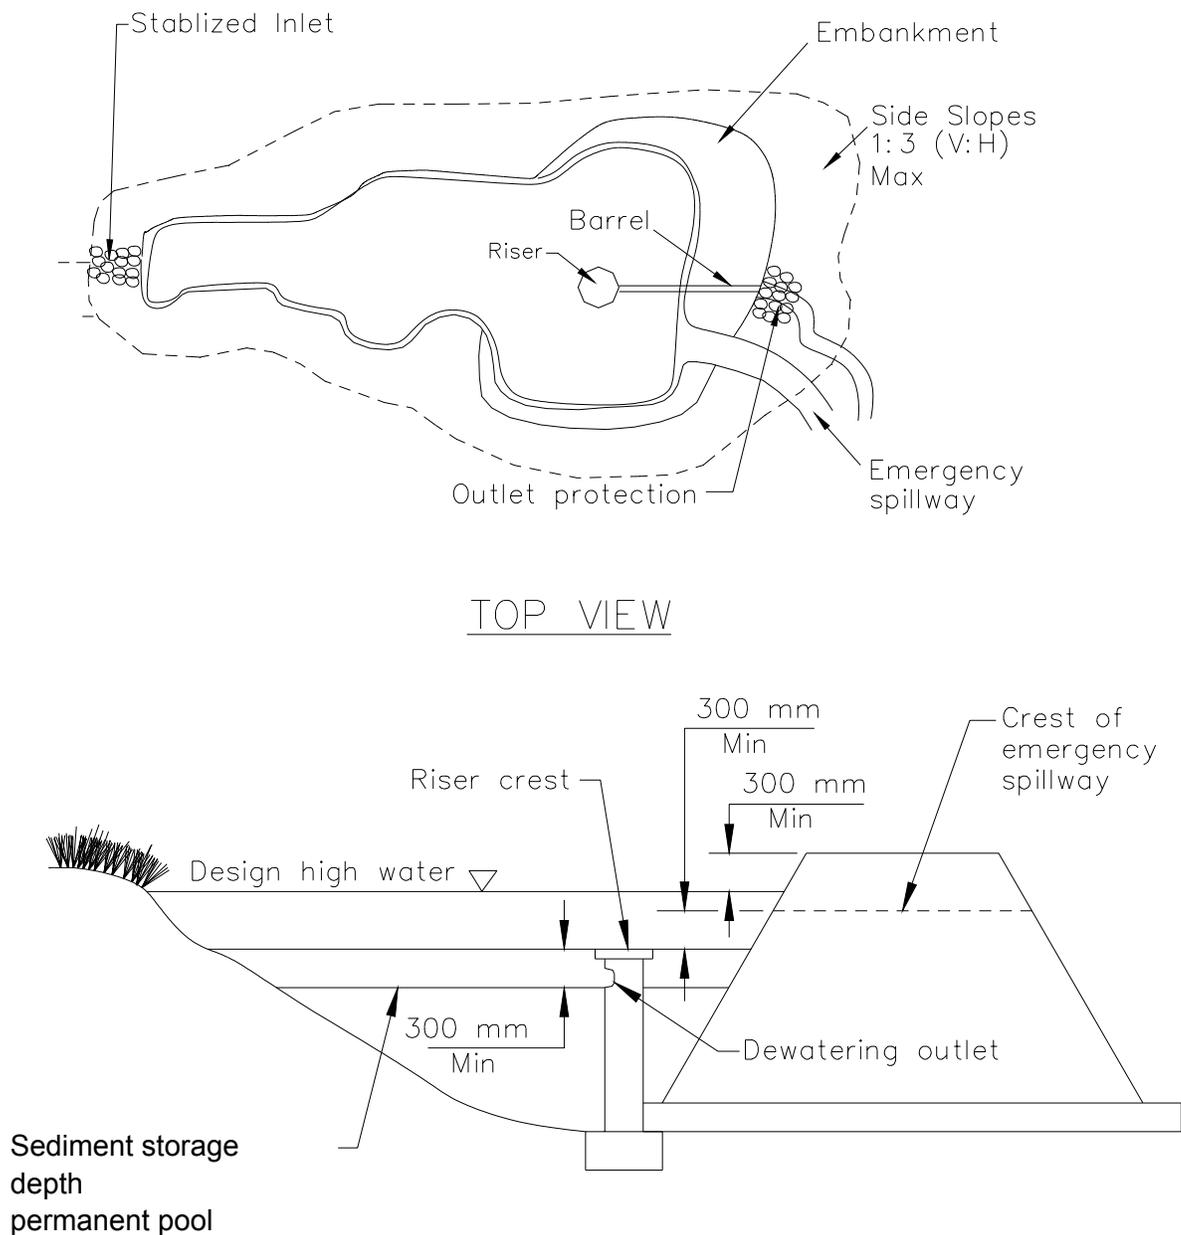

This outlet provides no drainage for permanent pool.

FIGURE 1: SINGLE ORIFICE DESIGN
NOT TO SCALE


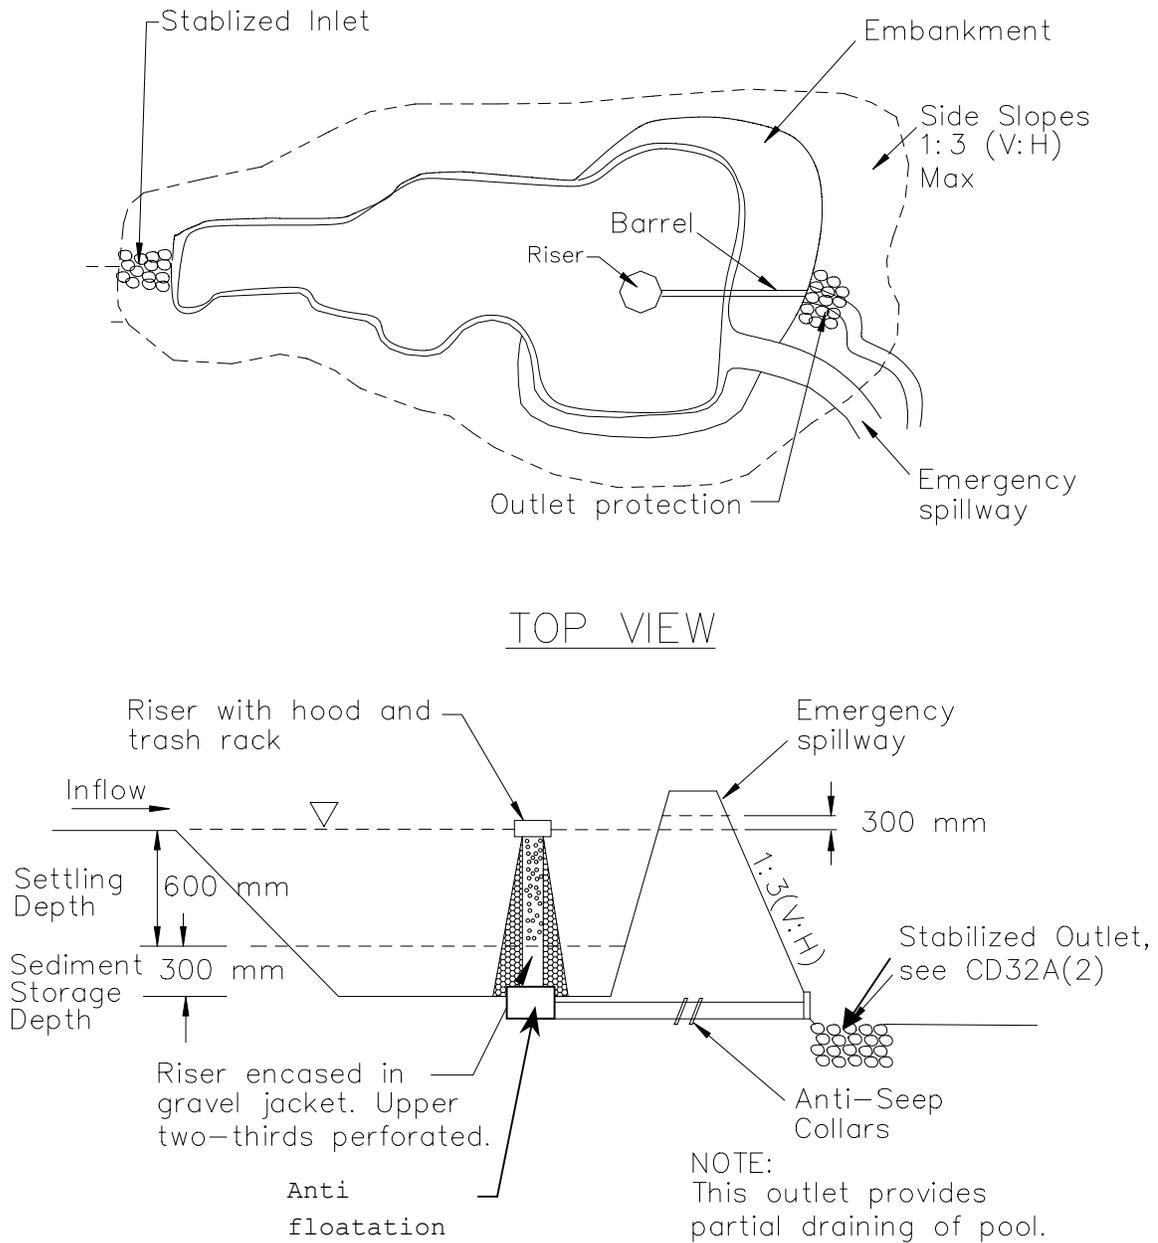


FIGURE 2: MULTIPLE ORIFICE DESIGN
NOT TO SCALE


Sediment/Desilting Basin

SC-2



Plan

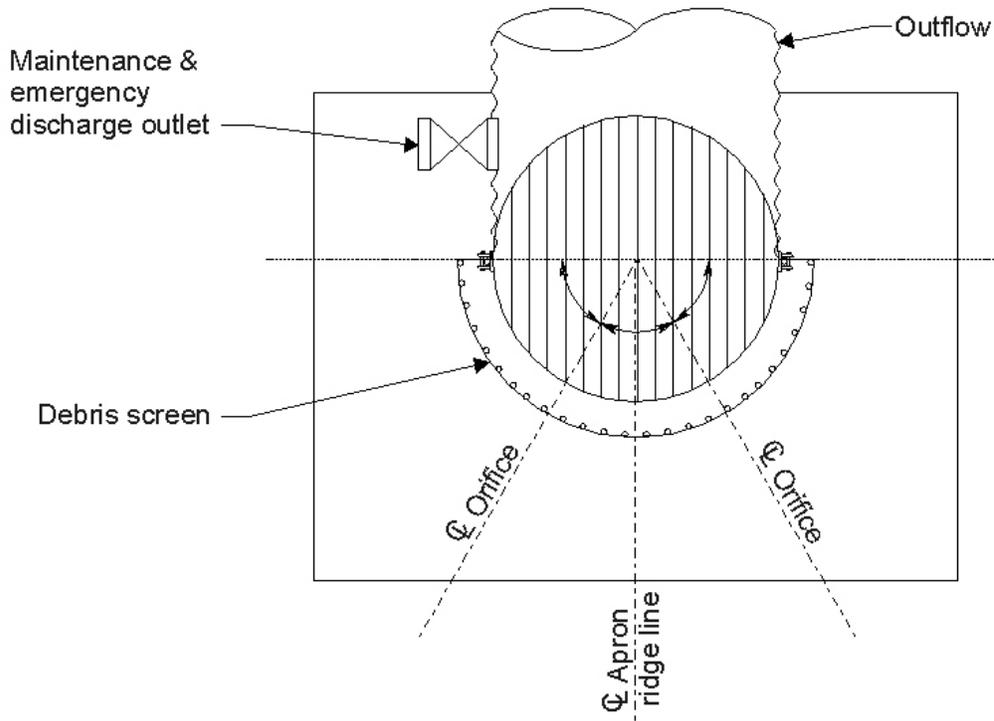

Profile

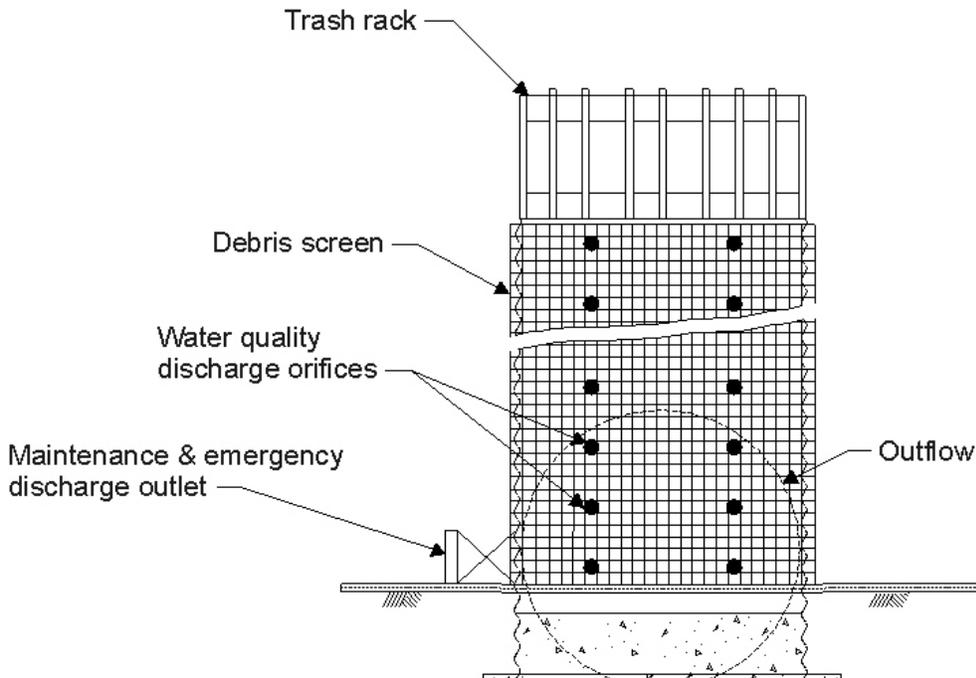

**FIGURE 3: MULTIPLE ORIFICE OUTLET RISER
NOT TO SCALE**

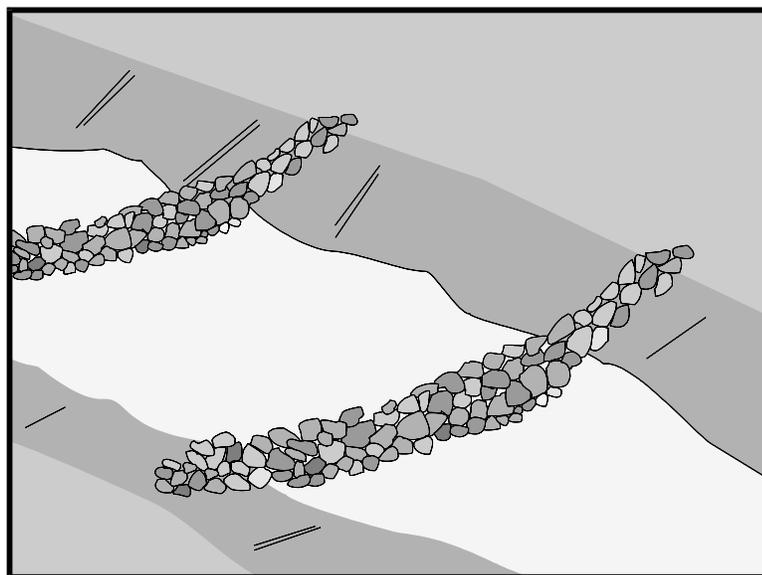

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Check dams reduce scour and channel erosion by reducing flow velocity and encouraging sediment settlement. A check dam is a small device constructed of rock, gravel bags, sandbags, fiber rolls, or other proprietary product placed across a natural or man-made channel or drainage ditch.

- Appropriate Applications**
- Check dams may be installed:
 - In small open channels that drain 4 ha (10 ac) or less.
 - In steep channels where storm water runoff velocities exceed 1.5 m/s (4.9 ft/sec).
 - During the establishment of grass linings in drainage ditches or channels.
 - In temporary ditches where the short length of service does not warrant establishment of erosion-resistant linings.
 - This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the Resident Engineer (RE).

- Limitations**
- Not to be used in live streams.
 - Not appropriate in channels that drain areas greater than 4 ha (10 ac).
 - Not to be placed in channels that are already grass lined unless erosion is expected, as installation may damage vegetation.
 - Require extensive maintenance following high velocity flows.
 - Promotes sediment trapping, which can be re-suspended during subsequent storms or removal of the check dam.

Standards and Specifications

- Not to be constructed from straw bales or silt fence.
- Check dams shall be placed at a distance and height to allow small pools to form behind them. Install the first check dam approximately 5 meters (16 ft) from the outfall device and at regular intervals based on slope gradient and soil type.
- For multiple check dam installation, backwater from downstream check dam shall reach the toe of the upstream dam.
- High flows (typically a 2-year storm or larger) shall safely flow over the check dam without an increase in upstream flooding or damage to the check dam.
- Where grass is used to line ditches, check dams shall be removed when grass has matured sufficiently to protect the ditch or swale.
- Rock shall be placed individually by hand or by mechanical methods (no dumping of rock) to achieve complete ditch or swale coverage.
- Fiber rolls may be used as check dams if approved by the RE or the Construction NPDES Coordinator. Refer to SC-5 “Fiber Rolls.”
- Gravel bags may be used as check dams with the following specifications:

Materials

- **Bag Material:** Bags shall be either polypropylene, polyethylene or polyamide woven fabric, minimum unit weight 135 g/m² (four ounces per square yard), mullen burst strength exceeding 2,070 kPa (300 psi) in conformance with the requirements in ASTM designation D3786, and ultraviolet stability exceeding 70% in conformance with the requirements in ASTM designation D4355.
- **Bag Size:** Each gravel-filled bag shall have a length of 450 mm (18 in), width of 300 mm (12 in), thickness of 75 mm (3 in), and mass of approximately 15 kg (33 lb). Bag dimensions are nominal, and may vary based on locally available materials. Alternative bag sizes shall be submitted to the RE for approval prior to deployment.
- **Fill Material:** Fill material shall be between 10 mm and 20 mm (0.4 and 0.8 inch) in diameter, and shall be clean and free from clay balls, organic matter, and other deleterious materials. The opening of gravel-filled bags shall be secured such that gravel does not escape. Gravel-filled bags shall be between 13 kg and 22 kg (28 and 48 lb) in mass. Fill material is subject to approval by the RE.


Installation

- Install along a level contour.
- Tightly abut bags and stack gravel bags using a pyramid approach.


Gravel bags shall not be stacked any higher than 1 meter (3.2 ft).

- Maintenance and Inspection
- Upper rows of gravel bags shall overlap joints in lower rows.
 - Inspect check dams after each significant rainfall event. Repair damage as needed or as required by the RE.
 - Remove sediment when depth reaches one-third of the check dam height.
 - Remove accumulated sediment prior to permanent seeding or soil stabilization.
 - Remove check dam and accumulated sediment when check dams are no longer needed or when required by the RE.
 - Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.


Check Dams

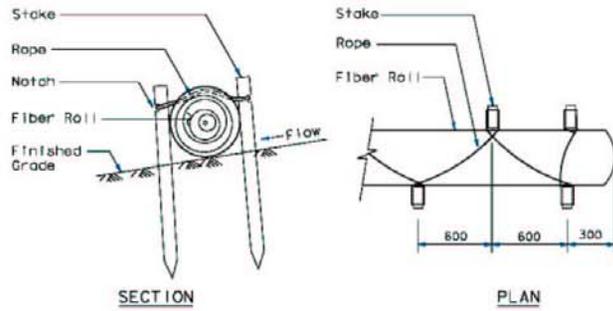

STAKING AND LASHING DETAIL



NOTCH DETAIL




SECTION


NOTE

1. Spillway depth 'd' shall be maintained to prevent flanking of concentrated flow around the ends of check dam.


TEMPORARY CHECK DAM (TYPE 2)

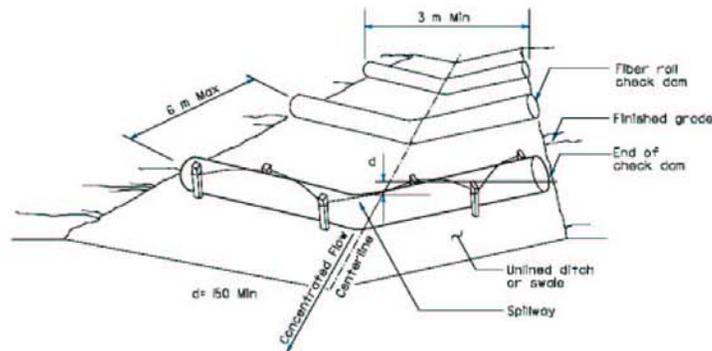


**PERSPECTIVE
TEMPORARY CHECK DAM (TYPE 1)**

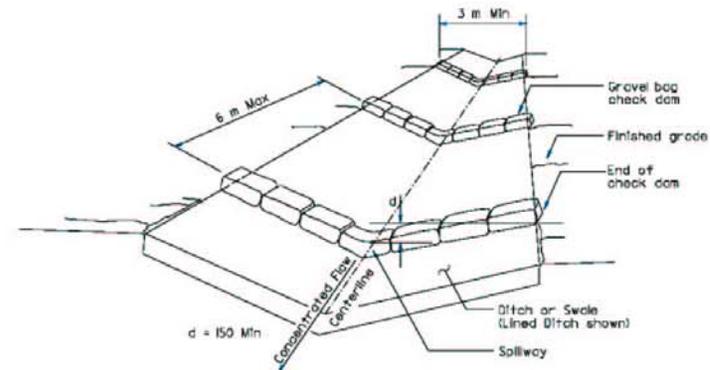

**PERSPECTIVE
TEMPORARY CHECK DAM (TYPE 2)**

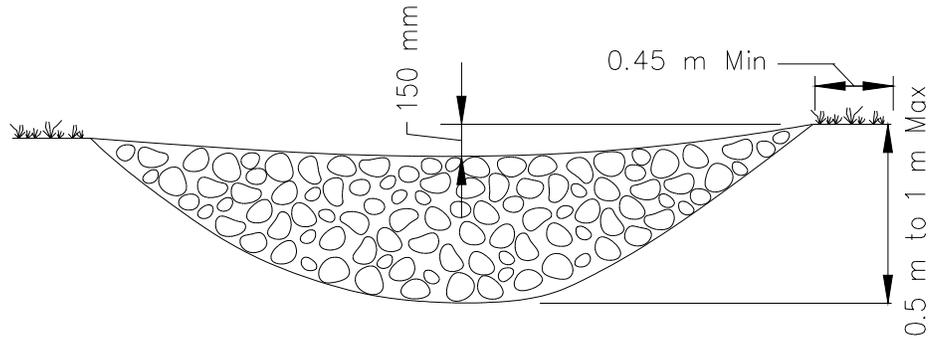


ELEVATION



TYPICAL ROCK CHECK DAM SECTION

ROCK CHECK DAM
NOT TO SCALE



Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A fiber roll consists of wood excelsior, rice or wheat straw, or coconut fibers that is rolled or bound into a tight tubular roll and placed on the toe and face of slopes to intercept runoff, reduce its flow velocity, release the runoff as sheet flow and provide removal of sediment from the runoff. Fiber rolls may also be used for inlet protection and as check dams under certain situations.

- Appropriate Applications**
- This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the RE.
 - Along the toe, top, face, and at grade breaks of exposed and erodible slopes to shorten slope length and spread runoff as sheet flow.
 - Below the toe of exposed and erodible slopes.
 - Fiber rolls may be used as check dams in unlined ditches if approved by the Resident Engineer (RE) or the District Construction Storm Water Coordinator (refer to SC-4 “Check Dams”).
 - Fiber rolls may be used for drain inlet protection if approved by the RE or the District Construction Storm Water Coordinator (refer to SC-10 “Storm Drain Inlet Protection”).
 - Down-slope of exposed soil areas.
 - Around temporary stockpiles.
 - Along the perimeter of a project.

- Limitations**
- Runoff and erosion may occur if fiber roll is not adequately trenched in.
 - Fiber rolls at the toe of slopes greater than 1:5 may require the use of 500 mm (20" diameter) or installations achieving the same protection (i.e., stacked smaller diameter fiber rolls, etc.).
 - Fiber rolls may be used for drainage inlet protection if they can be properly anchored.
 - Difficult to move once saturated.
 - Fiber rolls could be transported by high flows if not properly staked and trenched in.
 - Fiber rolls have limited sediment capture zone.
 - Do not use fiber rolls on slopes subject to creep, slumping, or landslide.

Standards and Specifications

Fiber Roll Materials

- Fiber rolls shall be either:
 - (1) Prefabricated rolls.
 - (2) Rolled tubes of erosion control blanket.

Assembly of Field Rolled Fiber Roll

- Roll length of erosion control blanket into a tube of minimum 200 mm (8 in) diameter.
- Bind roll at each end and every 1.2 m (4 ft) along length of roll with jute-type twine.

Installation

- Slope inclination of 1:4 or flatter: fiber rolls shall be placed on slopes 6.0 m apart.
- Slope inclination of 1:4 to 1:2: fiber rolls shall be placed on slopes 4.5 m apart.
- Slope inclination 1:2 or greater: fiber rolls shall be placed on slopes 3.0 m apart.
- Stake fiber rolls into a 50 to 100 mm (2 to 4 in) trench.

- Drive stakes at the end of each fiber roll and spaced 600 mm (2 ft) apart if Type 2 installation is used (refer to Page 4). Otherwise, space stakes 1.2 m (4 ft) maximum on center if installed as shown on Pages 5 and 6.
- Use wood stakes with a nominal classification of 19 by 19 mm (3/4 by 3/4 in), and minimum length of 600 mm (24 in).
- If more than one fiber roll is placed in a row, the rolls shall be overlapped; not abutted.





Removal

- Fiber rolls are typically left in place.
- If fiber rolls are removed, collect and dispose of sediment accumulation, and fill and compact holes, trenches, depressions or any other ground disturbance to blend with adjacent ground.



Maintenance and Inspection


- Repair or replace split, torn, unraveling, or slumping fiber rolls.
- Inspect fiber rolls when rain is forecast. Perform maintenance as needed or as required by the RE.
- Inspect fiber rolls following rainfall events and at least daily during prolonged rainfall. Perform maintenance as needed or as required by the RE.
- Maintain fiber rolls to provide an adequate sediment holding capacity. Sediment shall be removed when the sediment accumulation reaches three quarters (3/4) of the barrier height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.

Fiber Rolls

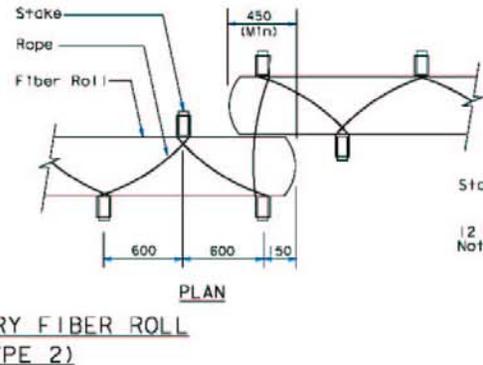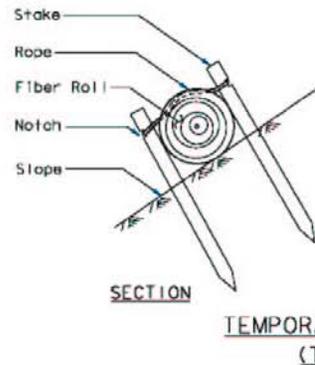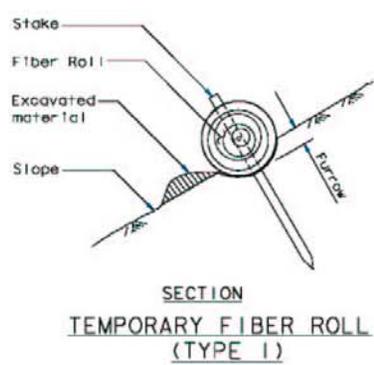


NOTE
1. Temporary fiber roll spacing varies depending upon slope inclination.

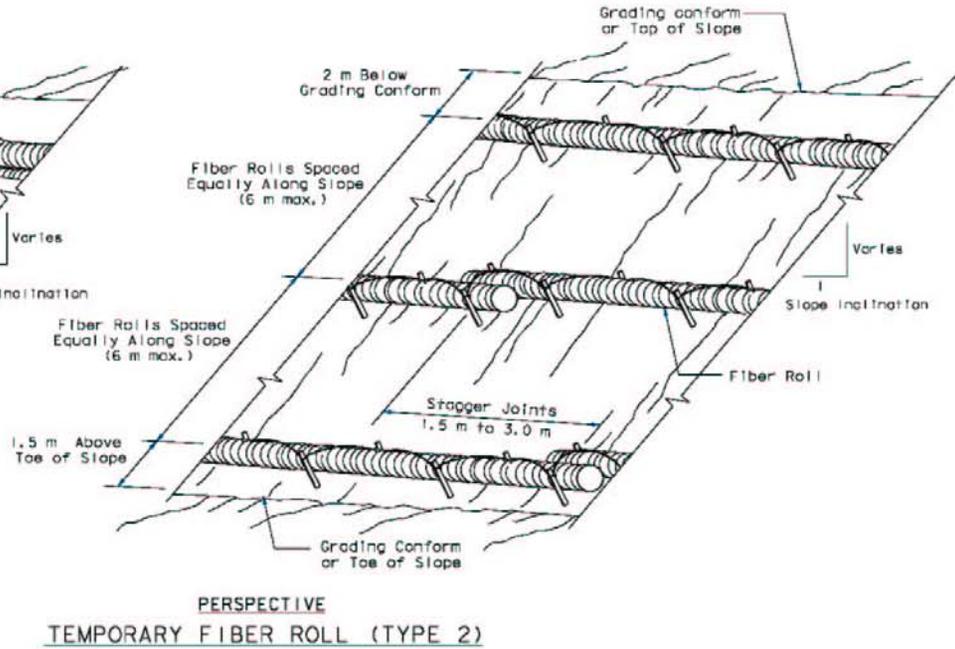
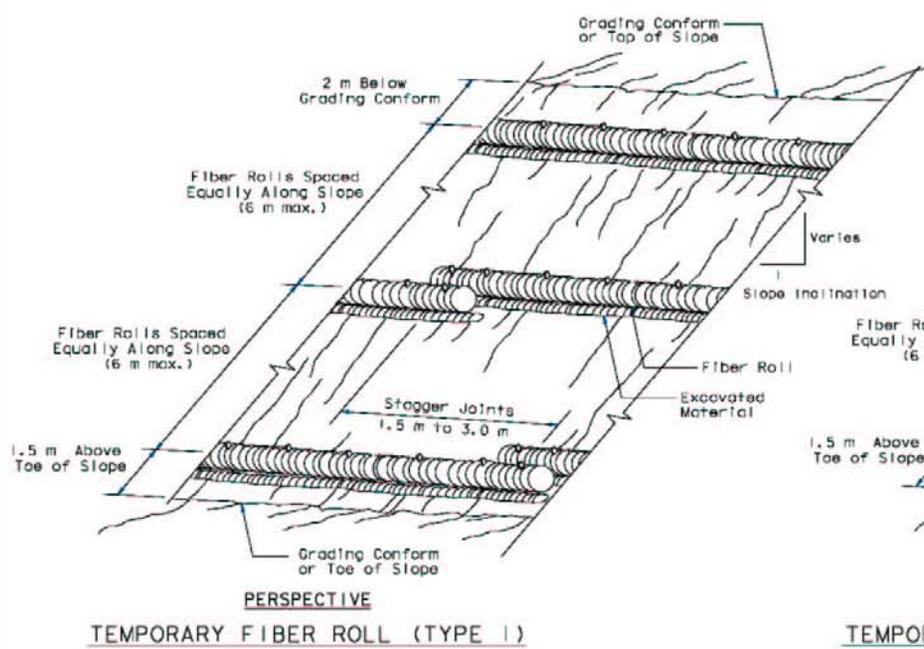


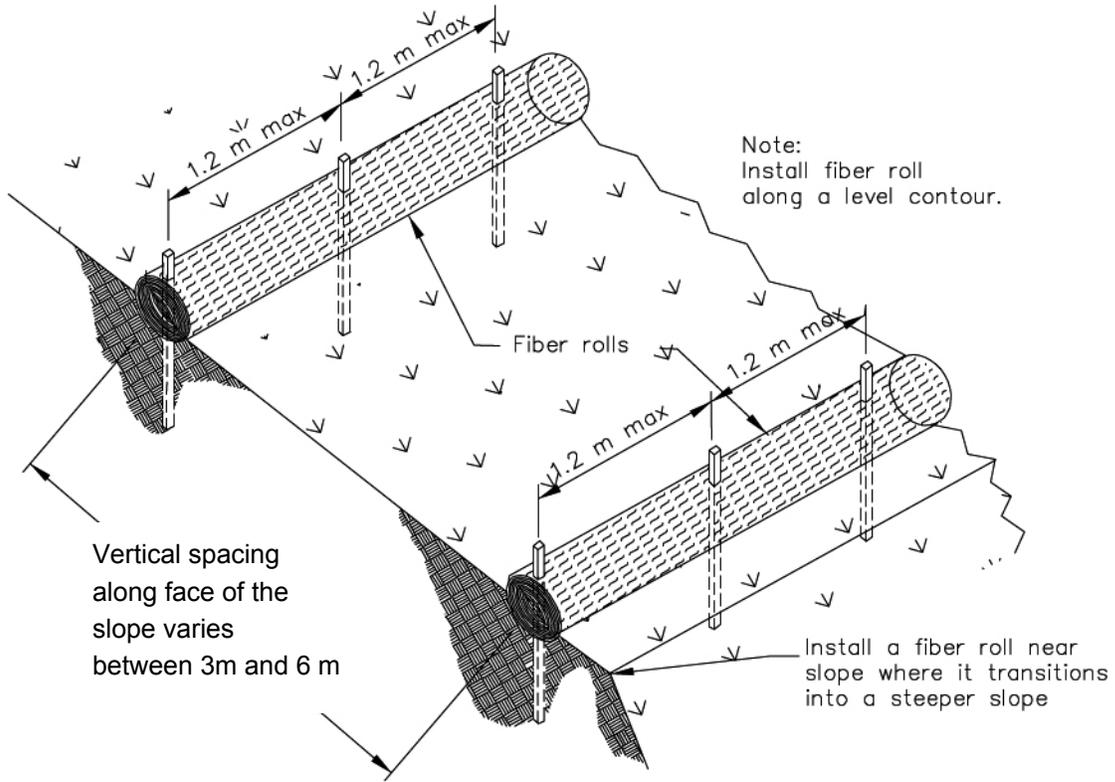

TYPICAL FIBER ROLL INSTALLATION
N.T.S.


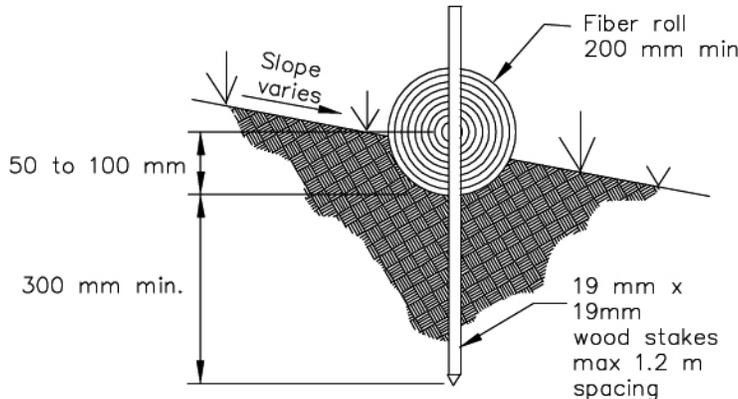


ENTRENCHMENT DETAIL
N.T.S.

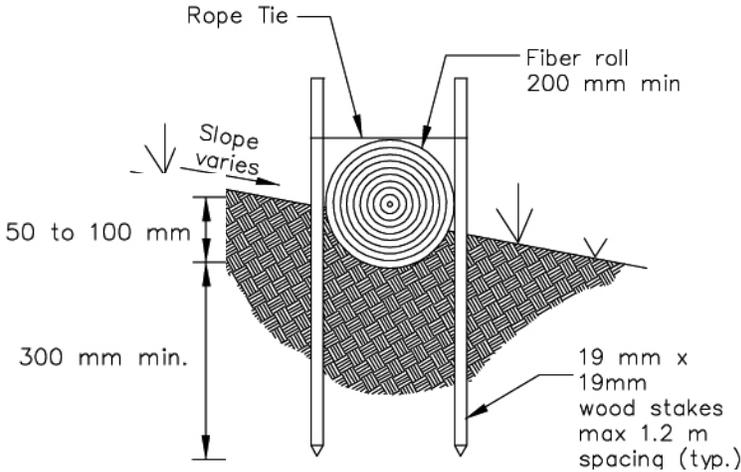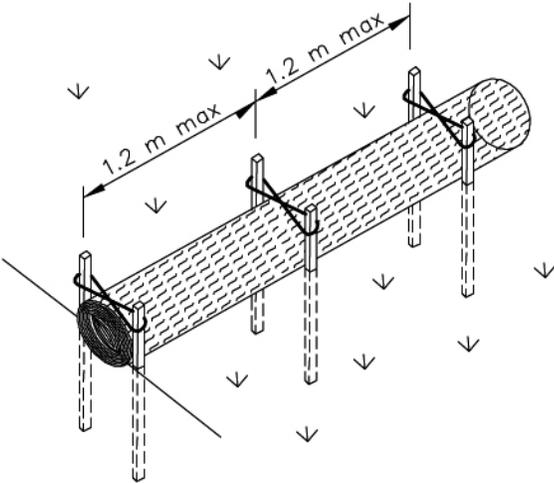

OPTIONAL ENTRENCHMENT DETAIL

N.T.S.

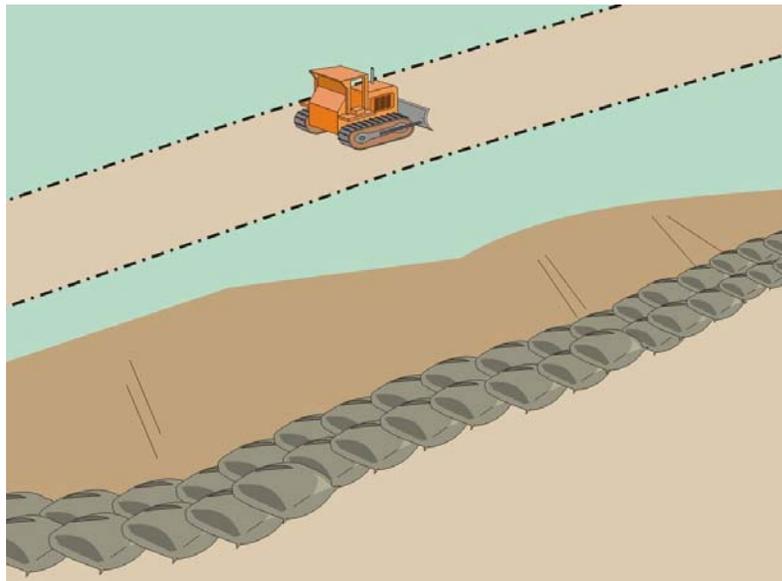

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A gravel bag berm consists of a single row of gravel bags that are installed end to end to form a barrier across a slope to intercept runoff, reduce its flow velocity, release the runoff as sheet flow and provide some sediment removal. Gravel bags can be used where flows are moderately concentrated, such as ditches, swales, and storm drain inlets (see BMP SC-10, Storm Drain Inlet Protection) to divert and/or detain flows.

- Appropriate Applications**
- BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the RE.
 - Along streams and channels.
 - Below the toe of exposed and erodible slopes.
 - Down slope of exposed soil areas.
 - Around stockpiles.
 - Across channels to serve as a barrier for utility trenches or provide a temporary channel crossing for construction equipment, to reduce stream impacts.
 - Parallel to a roadway to keep sediment off paved areas.
 - At the top of slopes to divert roadway runoff away from disturbed slopes.
 - Along the perimeter of a site.
 - To divert or direct flow or create a temporary sediment basin.
 - During construction activities in stream beds when the contributing drainage

area is less than 2 ha (5 ac).

- When extended construction period limits the use of either silt fences or straw bale barriers.
- When site conditions or construction sequencing require adjustments or relocation of the barrier to meet changing field conditions and needs during construction.
- At grade breaks of exposed and erodible slopes to shorten slope length and spread runoff as sheet flow.

Limitations

- Degraded gravel bags may rupture when removed, spilling contents.
- Installation can be labor intensive.
- Limited durability for long term projects.
- When used to detain concentrated flows, maintenance requirements increase.

Standards and Specifications

Materials

- **Bag Material:** Bags shall be woven polypropylene, polyethylene or polyamide fabric, minimum unit weight 135 g/m² (four ounces per square yard), mullen burst strength exceeding 2,070 kPa (300 psi) in conformance with the requirements in ASTM designation D3786, and ultraviolet stability exceeding 70% in conformance with the requirements in ASTM designation D4355.
- **Bag Size:** Each gravel-filled bag shall have a length of 450 mm (18 in), width of 300 mm (12 in), thickness of 75 mm (3 in), and mass of approximately 15 kg (33 lb). Bag dimensions are nominal, and may vary based on locally available materials. Alternative bag sizes shall be submitted to the RE for approval prior to deployment.
- **Fill Material:** Gravel shall be between 10 mm and 20 mm (0.4 and 0.8 inch) in diameter, and shall be clean and free from clay balls, organic matter, and other deleterious materials. The opening of gravel-filled bags shall be between 13 kg and 22 kg (28 and 48 lb) in mass. Fill material is subject to approval by the RE.

Installation



- When used as a linear control for sediment removal:
 - Install along a level contour.
 - Turn ends of gravel bag row up slope to prevent flow around the ends.
 - Generally, gravel bag barriers shall be used in conjunction with temporary soil stabilization controls up slope to provide effective erosion and sediment

control.

- When used for concentrated flows:
 - Stack gravel bags to required height using a pyramid approach.
 - Upper rows of gravel bags shall overlap joints in lower rows.
- Construct gravel bag barriers with a set-back of at least 1m from the toe of a slope. Where it is determined to be not practicable due to specific site conditions, the gravel bag barrier may be constructed at the toe of the slope, but shall be constructed as far from the toe of the slope as practicable.
- Requires Certificate of Compliance per Standard Specifications 6-1.07.

Maintenance and Inspection

- Inspect gravel bag berms before and after each rainfall event, and weekly throughout the rainy season.
- Reshape or replace gravel bags as needed, or as directed by the RE.
- Repair washouts or other damages as needed, or as directed by the RE.
- Inspect gravel bag berms for sediment accumulations and remove sediments when accumulation reaches one-third of the berm height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.
- Remove gravel bag berms when no longer needed. Remove sediment accumulations and clean, re-grade, and stabilize the area.

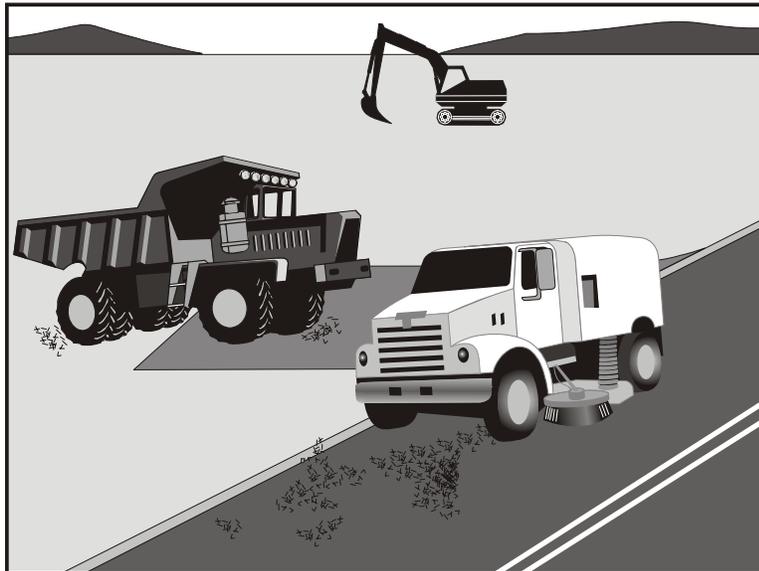

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management



Definition and Purpose Practices to remove tracked sediment to prevent the sediment from entering a storm drain or watercourse.

Appropriate Applications These practices are implemented anywhere sediment is tracked from the project site onto public or private paved roads, typically at points of ingress/egress.

Limitations Sweeping and vacuuming may not be effective when soil is wet or muddy.

- Standards and Specifications**
- Kick brooms or sweeper attachments shall not be used.
 - Inspect potential sediment tracking locations daily.
 - Visible sediment tracking shall be swept and/or vacuumed daily.
 - If not mixed with debris or trash, consider incorporating the removed sediment back into the project.

- Maintenance and Inspection**
- Inspect ingress/egress access points daily and sweep tracked sediment as needed, or as required by the Resident Engineer (RE).
 - Be careful not to sweep up any unknown substance or any object that may be potentially hazardous.
 - Adjust brooms frequently; maximize efficiency of sweeping operations.
 - After sweeping is finished, properly dispose of sweeper wastes at an approved dumpsite in conformance with the provisions in Standard Specifications Section 7-1.13 .

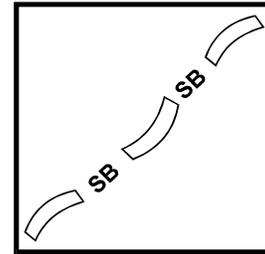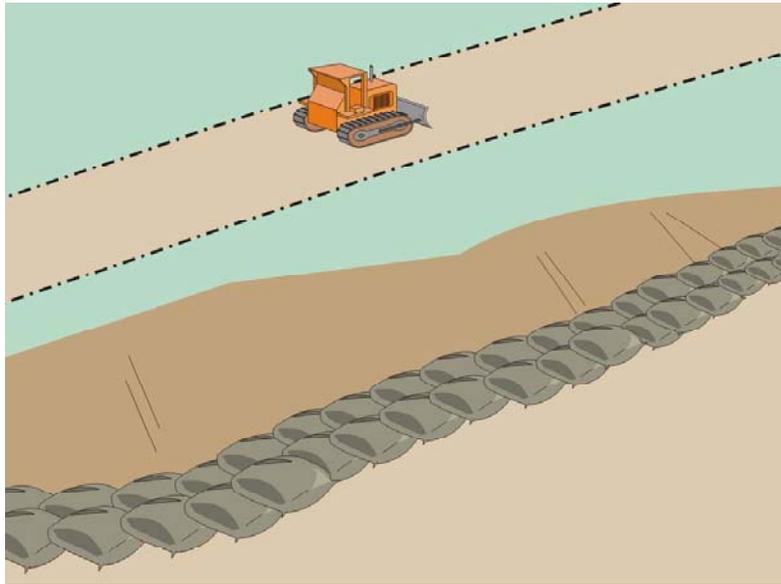

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A sandbag barrier is a temporary linear sediment barrier consisting of stacked sandbags, designed to intercept and slow the flow of sediment-laden sheet flow runoff. Sandbag barriers allow sediment to settle from runoff before water leaves the construction site.

- Appropriate Applications**
- This BMP may be implemented on a project-by-project basis in addition to other BMPs when determined necessary and feasible by the Resident Engineer (RE).
 - Along the perimeter of a site.
 - Along streams and channels.
 - Below the toe of exposed and erodible slopes.
 - Down slope of exposed soil areas.
 - Around stockpiles.
 - Across channels to serve as a barrier for utility trenches or provide a temporary channel crossing for construction equipment, to reduce stream impacts.
 - Parallel to a roadway to keep sediment off paved areas.
 - At the top of slopes to divert roadway runoff away from disturbed slopes.
 - To divert or direct flow or create a temporary sediment/desilting basin.
 - During construction activities in stream beds when the contributing drainage area is less than 2 ha (5 ac).

- Appropriate Applications
- This BMP may be implemented on a project-by-project basis in addition to other BMPs when determined necessary and feasible by the Resident Engineer (RE).
 - Along the perimeter of a site.
 - Along streams and channels.
 - Below the toe of exposed and erodible slopes.
 - Down slope of exposed soil areas.
 - Around stockpiles.
 - Across channels to serve as a barrier for utility trenches or provide a temporary channel crossing for construction equipment, to reduce stream impacts.
 - Parallel to a roadway to keep sediment off paved areas.
 - At the top of slopes to divert roadway runoff away from disturbed slopes.
 - To divert or direct flow or create a temporary sediment/desilting basin.
 - During construction activities in stream beds when the contributing drainage area is less than 2 ha (5 ac).
 - When extended construction period limits the use of either silt fences or straw bale barriers.
 - Along the perimeter of vehicle and equipment fueling and maintenance areas or chemical storage areas.
 - To capture and detain non-storm water flows until proper cleaning operations occur.
 - When site conditions or construction sequencing require adjustments or relocation of the barrier to meet changing field conditions and needs during construction.
 - To temporarily close or continue broken, damaged or incomplete curbs.
- Limitations
- Limit the drainage area upstream of the barrier to 2 ha (5 ac).
 - Degraded sandbags may rupture when removed, spilling sand.
 - Installation can be labor intensive.
 - Limited durability for long-term projects.

Standards and Specifications

- When used to detain concentrated flows, maintenance requirements increase.

Materials

- Sandbag Material: Sandbag shall be woven polypropylene, polyethylene or polyamide fabric, minimum unit weight 135 g/m² (four ounces per square yard), mullen burst strength exceeding 2,070 kPa (300 psi) in conformance with the requirements in ASTM designation D3786, and ultraviolet stability exceeding 70% in conformance with the requirements in ASTM designation D4355. Use of burlap is not acceptable.
- Sandbag Size: Each sand-filled bag shall have a length of 450 mm (18 in), width of 300 mm (12 in), thickness of 75 mm (3 in), and mass of approximately 15 kg (33 lb.). Bag dimensions are nominal, and may vary based on locally available materials. Alternative bag sizes shall be submitted to the RE for approval prior to deployment.
- Fill Material: All sandbag fill material shall be non-cohesive, Class 1 or Class 2 permeable material free from clay and deleterious material, conforming to the provisions in Standard Specifications Section 68-1.025 "Permeable Material". The requirements for the Durability Index and Sand Equivalent do not apply. Fill material is subject to approval by the RE.

Installation

- When used as a linear sediment control:
 - Install along a level contour.
 - Turn ends of sandbag row up slope to prevent flow around the ends.
 - Generally, sandbag barriers shall be used in conjunction with temporary soil stabilization controls up slope to provide effective erosion and sediment control.
 - Install as shown in Pages 4 and 5 of this BMP.
- Construct sandbag barriers with a set-back of at least 1m (3 ft) from the toe of a slope. Where it is determined to be not practical due to specific site conditions, the sandbag barrier may be constructed at the toe of the slope, but shall be constructed as far from the toe of the slope as practicable.


Maintenance and Inspection

- Inspect sandbag barriers before and after each rainfall event, and weekly throughout the rainy season.

- Reshape or replace sandbags as needed, or as directed by the RE.
- Repair washouts or other damages as needed, or as directed by the RE.
- Inspect sandbag barriers for sediment accumulations and remove sediments when accumulation reaches one-third the barrier height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.
- Remove sandbags when no longer needed. Remove sediment accumulation, and clean, re-grade, and stabilized the area.

Sandbag Barrier

SC-8

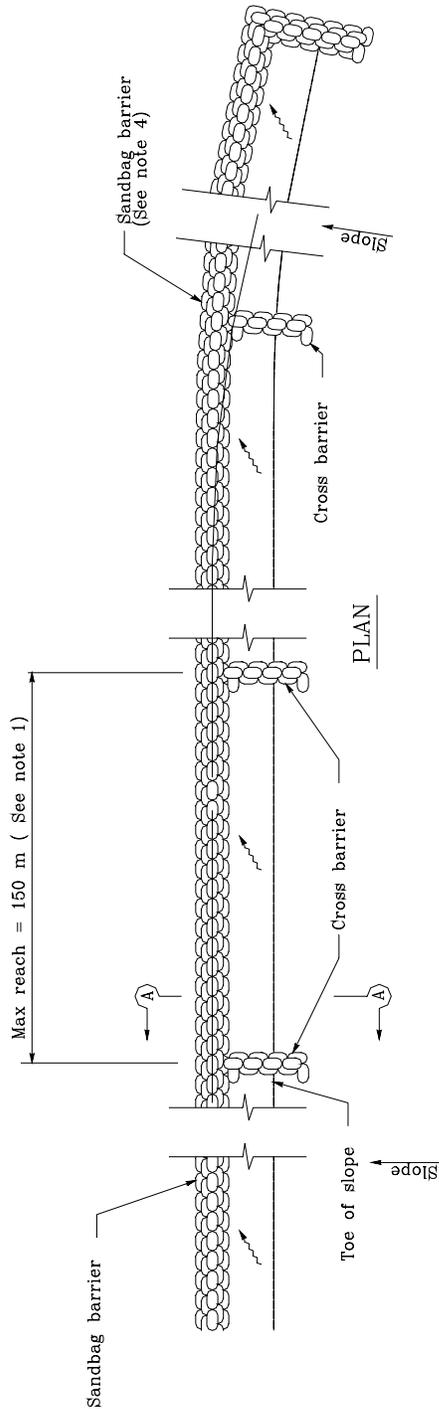

TEMPORARY LINEAR SEDIMENT BARRIER (TYPE SANDBAG)



STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

TEMPORARY LINEAR SEDIMENT BARRIER (TYPE SANDBAG)

NO SCALE


ALL DIMENSIONS ARE IN
MILLIMETERS UNLESS OTHERWISE SHOWN

NOTES

1. Construct the length of each reach so that the change in base elevation along the reach does not exceed 1/2 the height of the linear barrier. In no case shall the reach length exceed 150 m.
2. Place sandbags tightly.
3. Dimension may vary to fit field condition.
4. Sandbag barrier shall be a minimum of 3 bags high.
5. The end of the barrier shall be turned up slope.
6. Cross barriers shall be a min of 1/2 and a max of 2/3 the height of the linear barrier.
7. Sandbag rows and layers shall be staggered to eliminate gaps.

Sandbag Barrier

SC-8


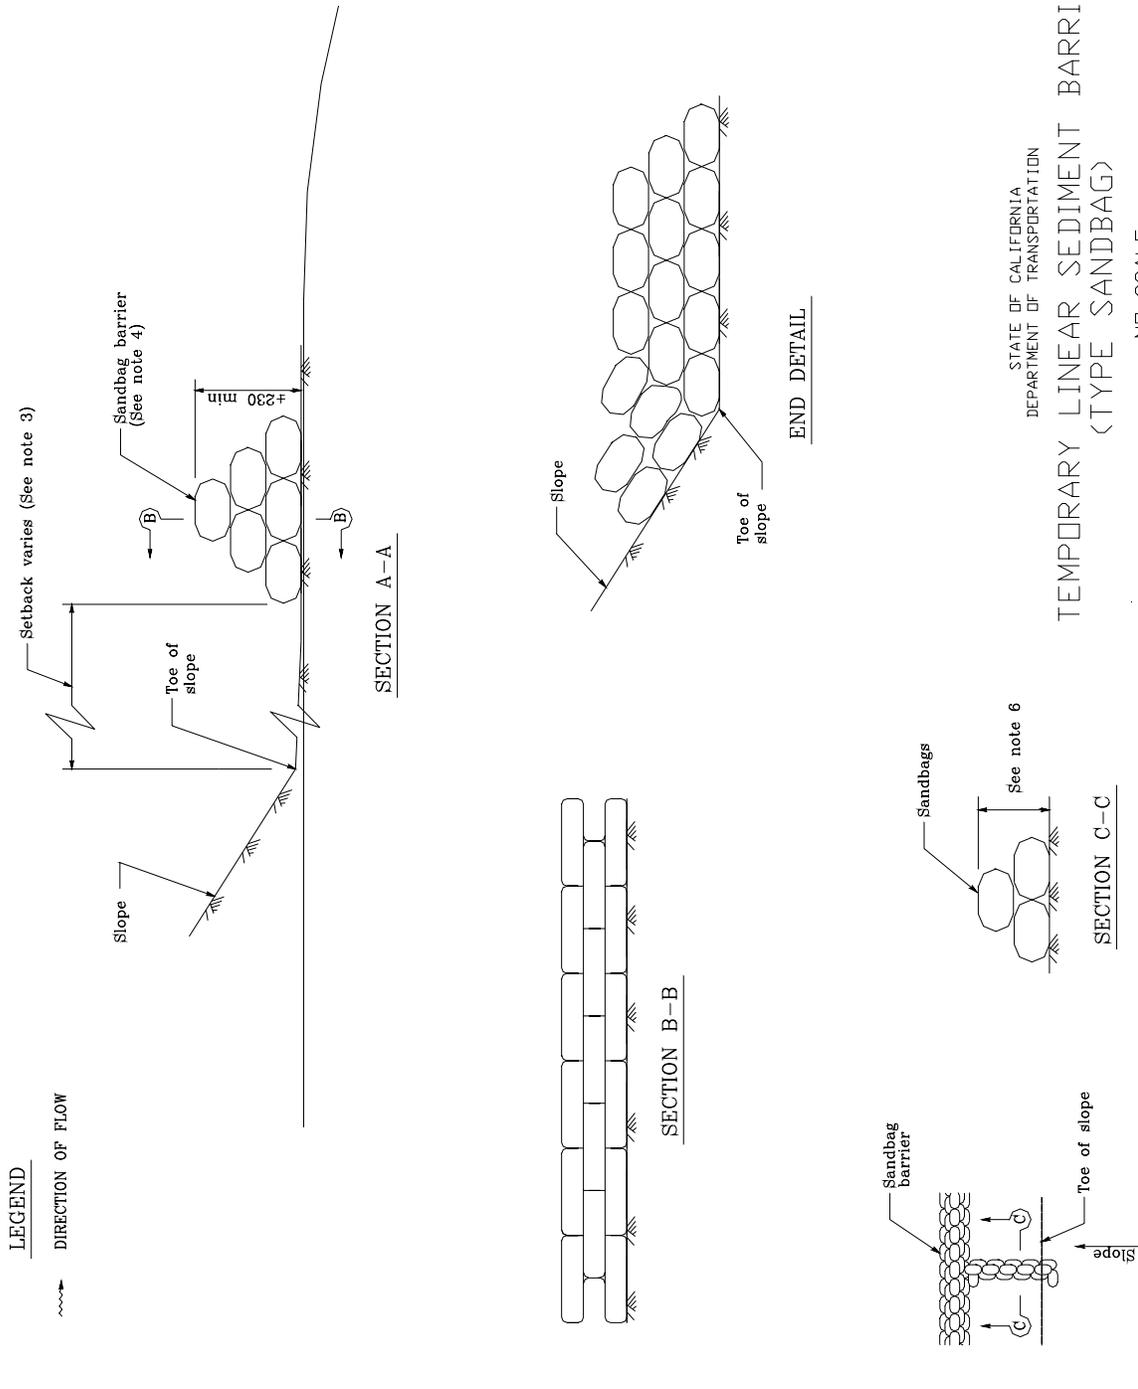


STATE OF CALIFORNIA
 DEPARTMENT OF TRANSPORTATION

TEMPORARY LINEAR SEDIMENT BARRIER
 (TYPE SANDBAG)

NO SCALE

ALL DIMENSIONS ARE IN MILLIMETERS UNLESS OTHERWISE SHOWN

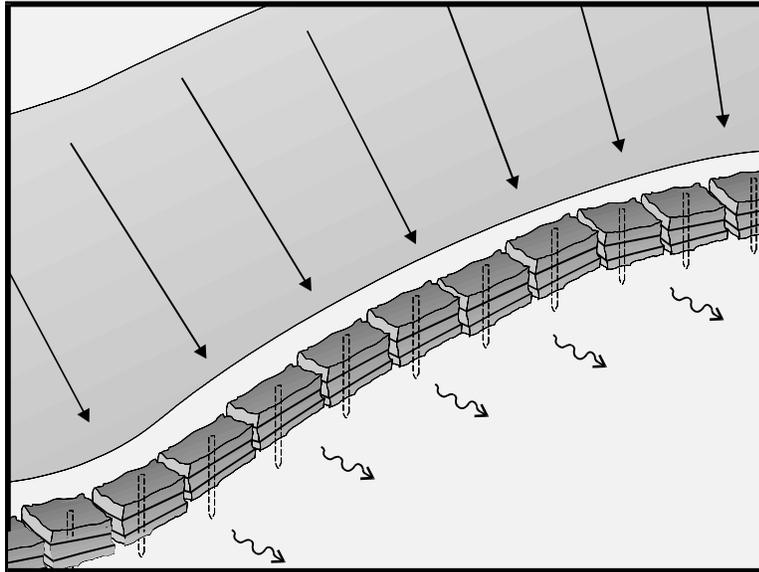

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose

A straw bale barrier is a temporary linear sediment barrier consisting of straw bales, designed to intercept and slow sediment-laden sheet flow runoff. Straw bale barriers allow sediment to settle from runoff before water leaves the construction site.

Appropriate Applications

- This BMP may be implemented on a project-by-project basis in addition to other BMPs when determined necessary and feasible by the Resident Engineer (RE).
- Along the perimeter of a site.
- Along streams and channels.
- Below the toe of exposed and erodible slopes.
- Down slope of exposed soil areas.
- Around stockpiles.
- Across minor swales or ditches with small catchments.
- Around above grade type temporary concrete washouts (See BMP WM-8, “Concrete Waste Management”).
- Parallel to a roadway to keep sediment off paved areas.

- Limitations
- Installation can be labor intensive.
 - Straw bale barriers are maintenance intensive.
 - Degraded straw bales may fall apart when removed or left in place for extended periods.
 - Can't be used on paved surfaces.
 - Not to be used for drain inlet protection.
 - Shall not be used in areas of concentrated flow.
 - Can be an attractive food source for some animals.
 - May introduce undesirable non-native plants to the area.

Standards and Specifications

Materials

- **Straw Bale Material:** Straw bale materials shall conform to the provisions in Standard Specifications Section 20-2.06, "Straw."
- **Straw Bale Size:** Each straw bale shall be a minimum of 360 mm (14 in) wide, 450 mm (18 in) in height, 900 mm (36 in) in length and shall have a minimum mass of 23 kg (51 lb.) The straw bale shall be composed entirely of vegetative matter, except for the binding material.
- **Bale Bindings:** Bales shall be bound by either steel wire, nylon or polypropylene string placed horizontally. Jute and cotton binding shall not be used. Baling wire shall be a minimum diameter of 1.57 mm (0.06 inch). Nylon or polypropylene string shall be approximately 2 mm (0.08 inch) in diameter with a breaking strength of 360 N.
- **Stakes:** Wood stakes shall be commercial quality lumber of the size and shape shown on the plans. Each stake shall be free from decay, splits or cracks longer than the thickness of the stake, or other defects that would weaken the stakes and cause the stakes to be structurally unsuitable. Steel bar reinforcement shall be equal to a number four designation or greater. End protection shall be provided for any exposed bar reinforcement.

Installation

- Limit the drainage area upstream of the barrier to 0.3 ha/100 m (0.25 ac/100ft) or barrier.
- Limit the slope length draining to the straw bale barrier to 30 m (100 ft.)


- Slopes of 2:100 (V:H) (2%) or flatter are preferred. If the slope exceeds 1:10 (V:H) (10%), the length of slope upstream of the barrier must be less than 15 m (50 ft).
- Install straw bale barriers along a level contour, with the last straw bale turned up slope.
- Straw bales must be installed in a trench and tightly abut adjacent bales.
- Construct straw bale barriers with a set-back of at least 1 m (3 ft) from the toe of a slope. Where it is determined to be not practical due to specific site conditions, the straw bale barrier may be constructed at the toe of the slope, but shall be constructed as far from the toe of the slope as practical.
- See pages 4 and 5 of this BMP for installation detail.

Maintenance and Inspection


- Inspect straw bale barriers before and after each rainfall event, and weekly throughout the rainy season.
- Inspect straw bale barriers for sediment accumulations and remove sediment when depth reaches one-third the barrier height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.
- Replace or repair damage bales as needed or as directed by the RE.
- Repair washouts or other damages as needed or as directed by the RE.
- Remove straw bales when no longer needed. Remove sediment accumulation, and clean, re-grade, and stabilized the area.

Straw Bale Barrier


SC-9

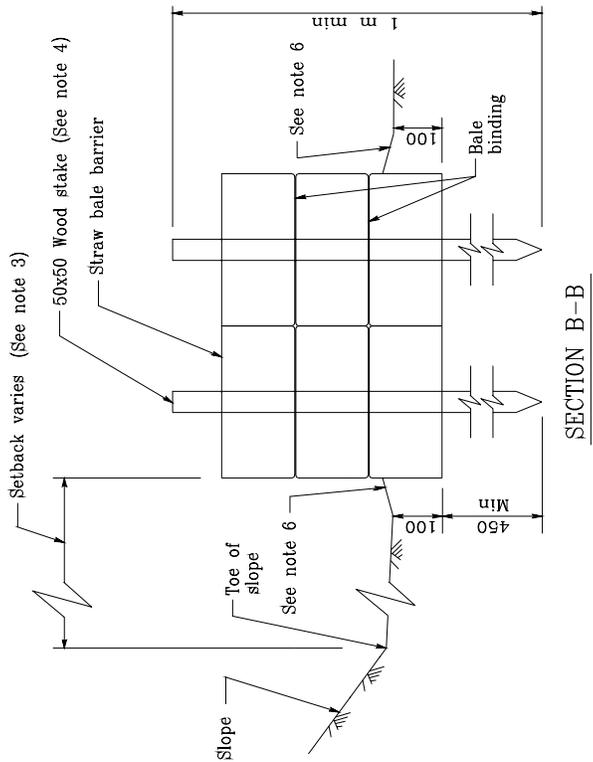

SECTION B-B

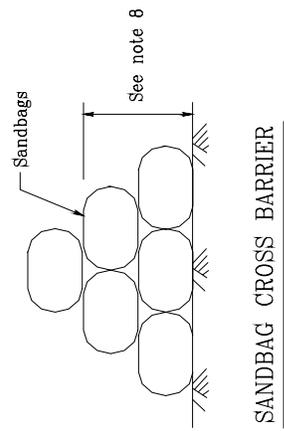

SANDBAG CROSS BARRIER

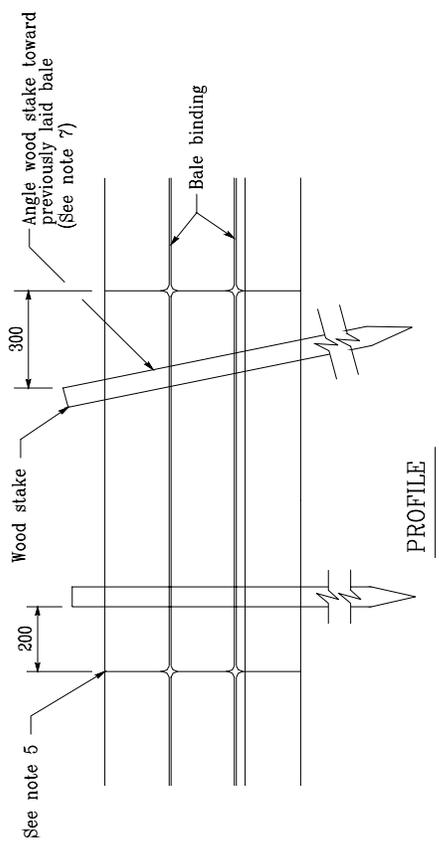


STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
TEMPORARY LINEAR SEDIMENT BARRIER
(TYPE STRAW BALE)
NO SCALE
ALL DIMENSIONS ARE IN
MILLIMETERS UNLESS OTHERWISE SHOWN

LEGEND



Straw Bale Barrier


SC-9

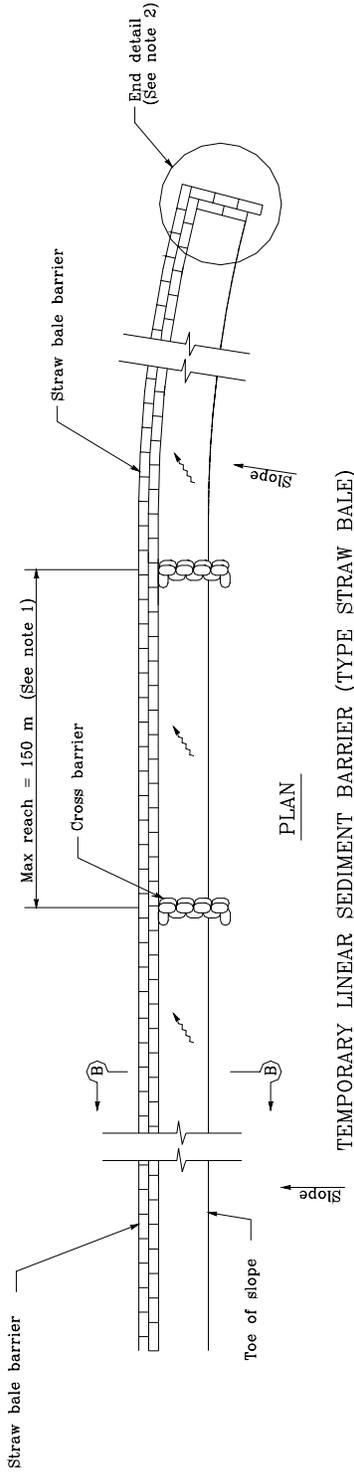

NOTES

1. Construct the length of each reach so that the change in base elevation along the reach does not exceed 1/2 the height of linear barrier. In no case shall the reach length exceed 150 m.
2. End of barrier shall be turned up slope.
3. Dimension may vary to fit field condition.

4. Place
5. Tamp
6. Cross
7. ndba





STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

TEMPORARY LINEAR SEDIMENT BARRIER
(TYPE STRAW BALE)

NO SCALE

ALL DIMENSIONS ARE IN
MILLIMETERS UNLESS OTHERWISE SHOWN



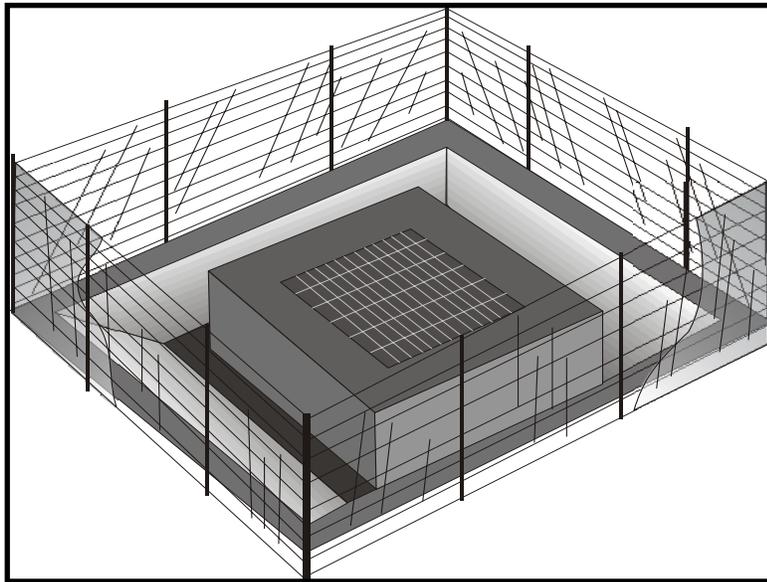

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose

Devices used at storm drain inlets that are subject to runoff from construction activities to detain and/or to filter sediment-laden runoff to allow sediment to settle and/or to filter sediment prior to discharge into storm drainage systems or watercourses.

Appropriate Applications

- Where ponding will not encroach into highway traffic.
- Where sediment laden surface runoff may enter an inlet.
- Where disturbed drainage areas have not yet been permanently stabilized.
- Where the drainage area is 0.4 ha (1 ac) or less.
- Appropriate during wet and snow-melt seasons.

Limitations

- Requires an adequate area for water to pond without encroaching upon traveled way and should not present itself to be an obstacle to oncoming traffic.
- May require other methods of temporary protection to prevent sediment-laden storm water and non-storm water discharges from entering the storm drain system.
- Sediment removal may be difficult in high flow conditions or if runoff is heavily sediment laden. If high flow conditions are expected, use other on-site sediment trapping techniques (e.g. check dams) in conjunction with inlet protection.
- Frequent maintenance is required.
- For drainage areas larger than 0.4 ha (1 ac), runoff shall be routed to a sediment trapping device designed for larger flows. See BMPs SC-2, “Sediment/Desilting Basin,” and SC-3 “Sediment Trap.”

- Filter fabric fence inlet protection is appropriate in open areas that are subject to sheet flow and for flows not exceeding 0.014 m³/s (0.5 cfs).
- Gravel bag barriers for inlet protection are applicable when sheet flows or concentrated flows exceed 0.014 m³/s (0.5 cfs), and it is necessary to allow for overtopping to prevent flooding.
- Fiber rolls and foam barriers are not appropriate for locations where they cannot be properly anchored to the surface.
- Excavated drop inlet sediment traps are appropriate where relatively heavy flows are expected and overflow capability is needed.

Standards and Specifications

Identify existing and/or planned storm drain inlets that have the potential to receive sediment-laden surface runoff. Determine if storm drain inlet protection is needed, and which method to use.

Methods and Installation

- **DI Protection Type 1 - Filter Fabric Fence** - The filter fabric fence (Type 1) protection is illustrated on Page 5. Similar to constructing a silt fence. See BMP SC-1, "Silt Fence." Do not place filter fabric underneath the inlet grate since the collected sediment may fall into the drain inlet when the fabric is removed or replaced.
- **DI Protection Type 2 - Excavated Drop Inlet Sediment Trap** - The excavated drop inlet sediment trap (Type 2) is illustrated in Page 6. Similar to constructing a temporary silt fence, See BMP SC-1, "Silt Fence." Size excavated trap to provide a minimum storage capacity calculated at the rate of 130 m³/ha (67 yd³/ac) of drainage area.
- **DI Protection Type 3 – Gravel bag** - The gravel bag barrier (Type 3) is illustrated in Page 7. Flow from a severe storm shall not overtop the curb. In areas of high clay and silts, use filter fabric and gravel as additional filter media. Construct gravel bags in accordance with BMP SC-6, "Gravel Bag Berm." Gravel bags shall be used due to their high permeability.
- **DI Protection Type 4 – Foam Barriers and Fiber Rolls** – Foam barrier or fiber roll (Type 4) is placed around the inlet and keyed and anchored to the surface. Foam barriers and fiber rolls are intended for use as inlet protection where the area around the inlet is unpaved and the foam barrier or fiber roll can be secured to the surface. RE or Construction Storm Water Coordinator approval is required.

Maintenance and Inspection

General

- Inspect all inlet protection devices before and after every rainfall event, and weekly during the rest of the rainy season. During extended rainfall events, inspect inlet protection devices at least once every 24 hours.

- Inspect the storm drain inlet after severe storms in the rainy season to check for bypassed material.
- Remove all inlet protection devices within thirty days after the site is stabilized, or when the inlet protection is no longer needed.
 - Bring the disturbed area to final grade and smooth and compact it. Appropriately stabilize all bare areas around the inlet.
 - Clean and re-grade area around the inlet and clean the inside of the storm drain inlet as it must be free of sediment and debris at the time of final inspection.

Requirements by Method

■ ***Type 1 - Filter Fabric Fence***

- This method shall be used for drain inlets requiring protection in areas where finished grade is established and erosion control seeding has been applied or is pending.
- Make sure the stakes are securely driven in the ground and are structurally sound (i.e., not bent, cracked, or splintered, and are reasonably perpendicular to the ground). Replace damaged stakes.
- Replace or clean the fabric when the fabric becomes clogged with sediment. Make sure the fabric does not have any holes or tears. Repair or replace fabric as needed or as directed by the RE.
- At a minimum, remove the sediment behind the fabric fence when accumulation reaches one-third the height of the fence or barrier height. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications Section 7-1.13.

■ ***Type 2 – Excavated Drop Inlet Sediment Trap***

- This method may be used for drain inlets requiring protection in areas that have been cleared and grubbed, and where exposed soil areas are subject to grading.
- Remove sediment from basin when the volume of the basin has been reduced by one-half.


■ ***Type 3 - Gravel Bag Barrier***

- This method may be used for drain inlets surrounded by AC or paved surfaces.
- Inspect bags for holes, gashes, and snags.


- Check gravel bags for proper arrangement and displacement. Remove the sediment behind the barrier when it reaches one-third the height of the barrier. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications Section 7-1.13.
- ***Type 4 Foam Barriers and Fiber Rolls***
 - This method may be used for drain inlets requiring protection in areas that have been cleared and grubbed, and where exposed soil areas subject to grading. RE or Construction Storm Coordinator approval is required.
 - Check foam barrier or fiber roll for proper arrangement and displacement. Remove the sediment behind the barrier when it reaches one-third the height of the barrier. Removed sediment shall be incorporated in the project at locations designated by the RE or disposed of outside the highway right-of-way in conformance with the Standard Specifications.

Storm Drain Inlet Protection

SC-10

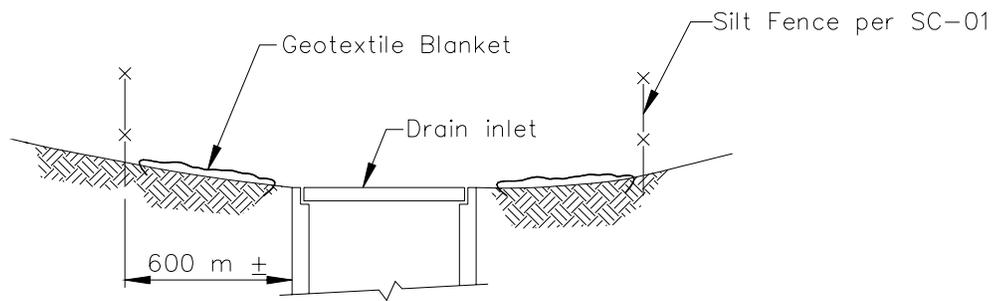

SECTION A-A

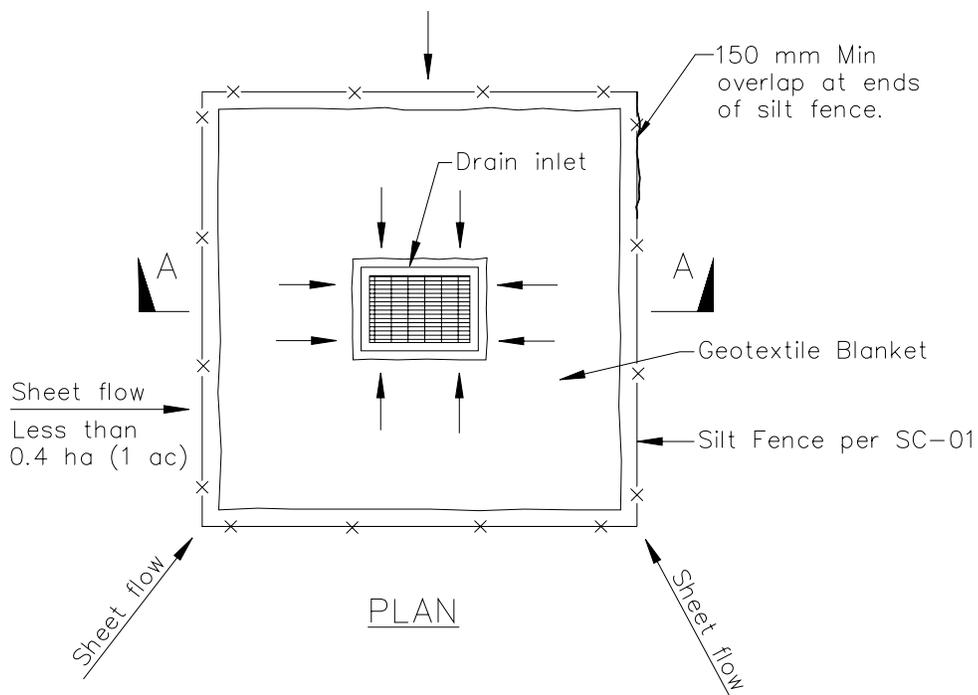

PLAN



DI PROTECTION TYPE 1
NOT TO SCALE

NOTES:

1. For use in areas where grading has been completed and final soil stabilization and seeding are pending.
2. Not applicable in paved areas.
3. Not applicable with concentrated flows.

Storm Drain Inlet Protection


SC-10

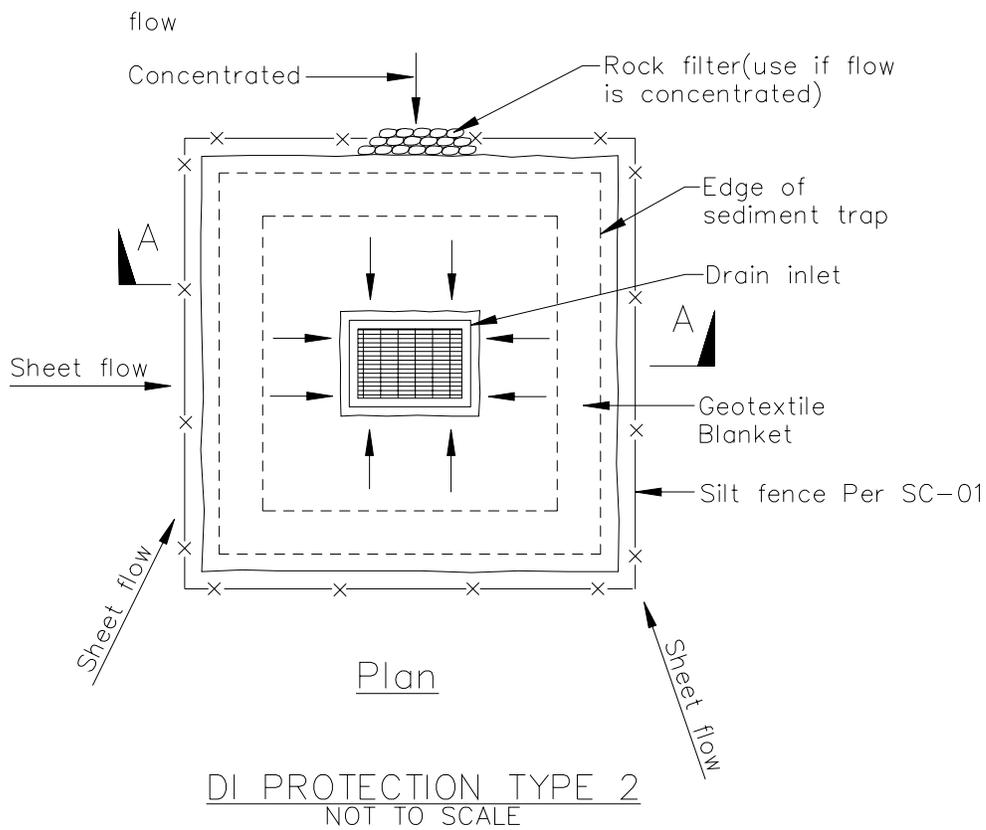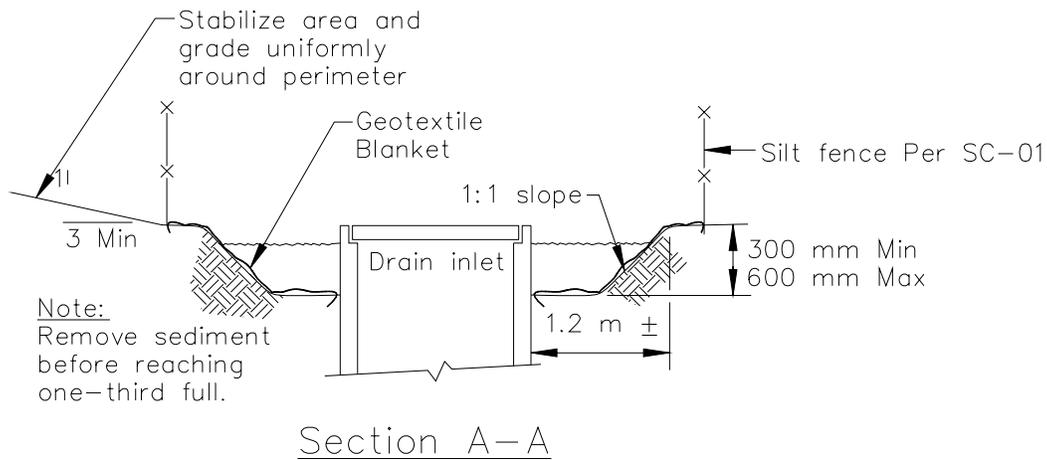


Notes

1. For use in cleared and grubbed and in graded areas.
2. Shape basin so that longest inflow area faces longest length of trap.
3. For concentrated flows, shape basin in 2:1 ratio with length oriented towards direction of flow.



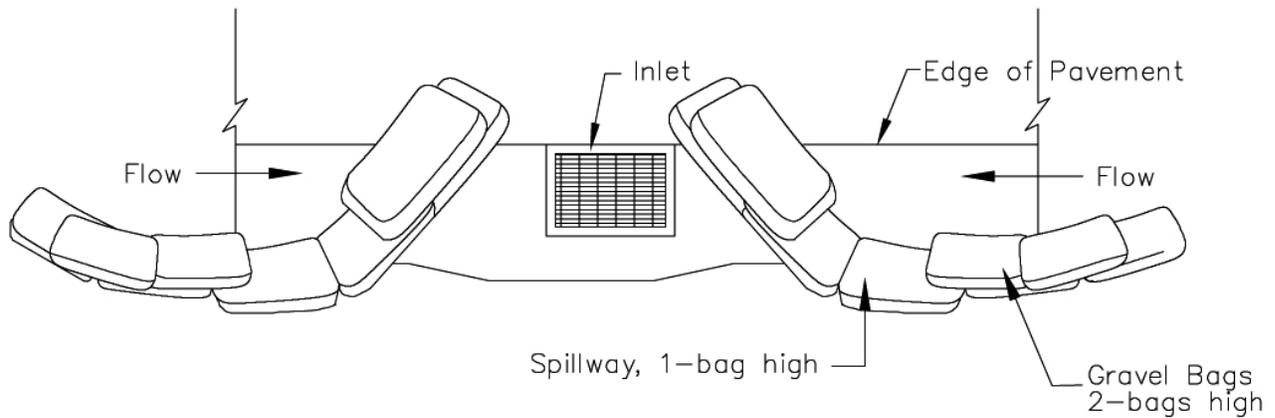



TYPICAL PROTECTION FOR INLET WITH OPPOSING FLOW DIRECTIONS

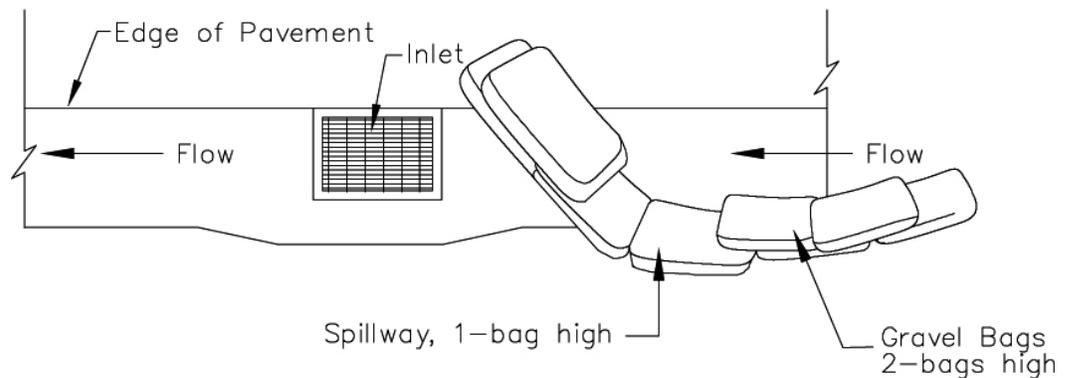

TYPICAL PROTECTION FOR INLET WITH SINGLE FLOW DIRECTION

NOTES:

1. Intended for short-term use.
2. Use to inhibit non-storm water flow.
3. Allow for proper maintenance and cleanup.
4. Bags must be removed after adjacent operation is completed
5. Not applicable in areas with high silts and clays without filter fabric.

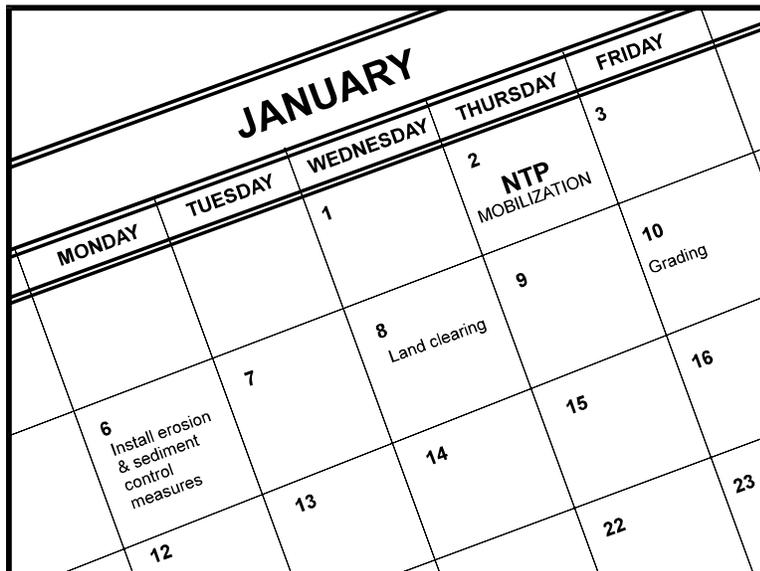

Standard Symbol

- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose This best management practice (BMP) involves developing, for every project, a schedule that includes sequencing of construction activities with the implementation of construction site BMPs such as temporary soil stabilization (erosion control) and temporary sediment controls measures. The purpose is to reduce the amount and duration of soil exposed to erosion by wind, rain, runoff and vehicle tracking, and to perform the construction activities and control practices in accordance with the planned schedule.



Appropriate Applications Construction sequencing shall be scheduled to minimize land disturbance for all projects during the rainy and non-rainy season. Appropriate BMPs shall be implemented during both rainy and non-rainy seasons.

Limitations None identified.

- Standards and Specifications**
- Developing a schedule and planning the project are the very first steps in an effective storm water program. The schedule shall clearly show how the rainy season relates to soil-disturbing and re-stabilization activities. The construction schedule shall be incorporated into the SWPPP or WPCP.
 - The schedule shall include detail on the rainy season implementation and deployment of:
 - Temporary soil stabilization BMPs.
 - Temporary sediment control BMPs.
 - Tracking control BMPs.
 - Wind erosion control BMPs.

- Non-storm water BMPs.
- Waste management and materials pollution control BMPs.
- Schedule shall also include dates for significant long-term operations or activities that may have planned non-storm water discharges such as dewatering, sawcutting, grinding, drilling, boring, crushing, blasting, painting, hydro-demolition, mortar mixing, bridge cleaning, etc.
- Schedule work to minimize soil disturbing activities during the rainy season.
- Develop the sequencing and timetable for the start and completion of each item such as site clearing and grubbing, grading, excavation, paving, pouring foundations, installing utilities, etc., to minimize the active construction area during the rainy season.
- Schedule major grading operations for the non-rainy season when practical.
- Stabilize non-active areas within 14 days from the cessation of soil-disturbing activities or one day prior to the onset of precipitation, whichever occurs first.
- Monitor the weather forecast for rainfall.
- When rainfall is predicted, adjust the construction schedule to allow the implementation of soil stabilization and sediment controls and sediment treatment controls on all disturbed areas prior to the onset of rain.
- Be prepared year-round to deploy soil stabilization and sediment control practices as required by Section 2 of this Manual. Erosion may be caused during dry seasons by unseasonal rainfall, wind, and vehicle tracking. Keep the site stabilized year-round, and retain and maintain rainy season sediment trapping devices in operational condition.
- Sequence trenching activities so that most open portions are closed before new trenching begins.
- Incorporate staged seeding and re-vegetation of graded slopes as work progresses.
- Consider scheduling when establishing permanent vegetation (appropriate planting time for specified vegetation).
- Apply permanent erosion control to areas deemed substantially complete during the project's defined seeding window.

- Maintenance and Inspection
- Verify that work is progressing in accordance with the schedule. If progress deviates, take corrective actions.
 - Amend the schedule when changes are warranted or when directed by the Resident Engineer (RE).
 - The Special Provisions require annual submittal of a rainy season implementation schedule. Amend the schedule prior to the rainy season to show updated information on the deployment and implementation of construction site BMPs.

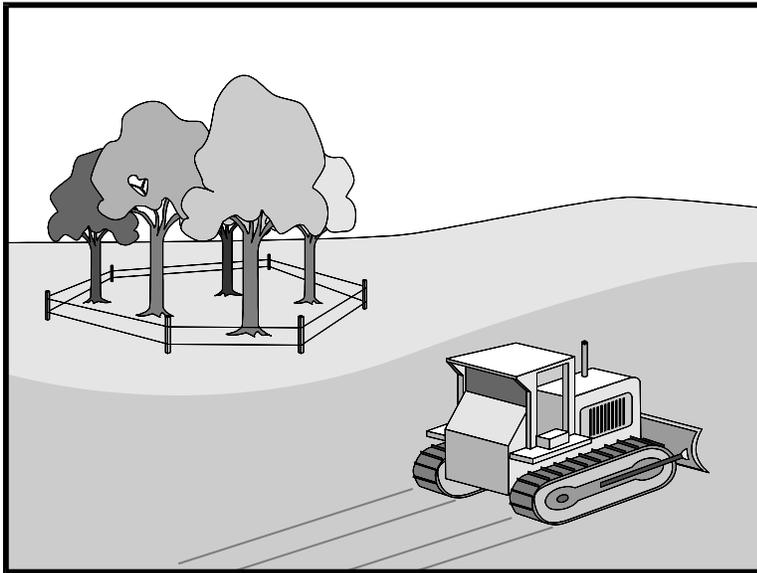

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Preservation of existing vegetation is the identification and protection of desirable vegetation that provides erosion and sediment control benefits.

- Appropriate Applications**
- Preserve existing vegetation at areas on a site where no construction activity is planned or will occur at a later date. Specifications for preservation of existing vegetation can be found in Standard Specifications, Section 7-1.11.
 - On a year-round basis, temporary fencing shall be provided prior to the commencement of clearing and grubbing operations or other soil-disturbing activities in areas.
 - Clearing and grubbing operations should be staged to preserve existing vegetation.

Limitations Protection of existing vegetation requires planning, and may limit the area available for construction activities.

Standards and Specifications *Timing*

- Preservation of existing vegetation shall be provided prior to the commencement of clearing and grubbing operations or other soil-disturbing activities in areas identified on the plans to be preserved, especially on areas designated as Environmentally Sensitive Areas (ESAs).
- Preservation of existing vegetation shall conform to scheduling requirements set forth in the special provisions.

Design and Layout

- Mark areas to be preserved with temporary fencing made of orange polypropylene that is stabilized against ultraviolet light. The temporary fencing shall be at least 1 meter (3.2. ft) tall and shall have openings not larger than 50 mm by 50 mm (2 in by 2 in).

- Fence posts shall be either wood or metal, at the Contractor's discretion, as appropriate for the intended purpose. The post spacing and depth shall be adequate to completely support the fence in an upright position.
- Minimize the disturbed areas by locating temporary roadways to avoid stands of trees and shrubs and to follow existing contours to reduce cutting and filling.
- Consider the impact of grade changes to existing vegetation and the root zone.

Installation

- Construction materials, equipment storage, and parking areas shall be located where they will not cause root compaction.
- Keep equipment away from trees to prevent trunk and root damage.
- Maintain existing irrigation systems.
- Employees and subcontractors shall be instructed to honor protective devices. No heavy equipment, vehicular traffic, or storage piles of any construction materials shall be permitted within the drip line of any tree to be retained. Removed trees shall not be felled, pushed, or pulled into any retained trees. Fires shall not be permitted within 30 m (100 ft) of the drip line of any retained trees. Any fires shall be of limited size, and shall be kept under continual surveillance. No toxic or construction materials (including paint, acid, nails, gypsum board, chemicals, fuels, and lubricants) shall be stored within 15 m (50 ft) of the drip line of any retained trees, nor disposed of in any way which would injure vegetation.

Trenching and Tunneling



- Trenching shall be as far away from tree trunks as possible, usually outside of the tree drip line or canopy. Curve trenches around trees to avoid large roots or root concentrations. If roots are encountered, consider tunneling under them. When trenching and/or tunneling near or under trees to be retained, tunnels shall be at least 450 mm (18 in) below the ground surface, and not below the tree center to minimize impact on the roots.
- Tree roots shall not be left exposed to air; they shall be covered with soil as soon as possible, protected, and kept moistened with wet burlap or peat moss until the tunnel and/or trench can be completed.
- The ends of damaged or cut roots shall be cut off smoothly.
- Trenches and tunnels shall be filled as soon as possible. Careful filling and tamping will eliminate air spaces in the soil which can damage roots.
- Remove any trees intended for retention if those trees are damaged seriously enough to affect their survival. If replacement is desired or required, the new tree shall be of similar species, and at least 50 mm (2 in) caliper, unless

otherwise required by the contract documents.

- After all other work is complete, fences and barriers shall be removed last. This is because protected trees may be destroyed by carelessness during the final cleanup and landscaping.

Maintenance and Inspection During construction, the limits of disturbance shall remain clearly marked at all times. Irrigation or maintenance of existing vegetation shall conform to the requirements in the landscaping plan. If damage to protected trees still occurs, maintenance guidelines described below shall be followed:

- Serious tree injuries shall be attended to by an arborist.
- During construction, District Environmental shall be contacted to ensure that ESAs are protected.

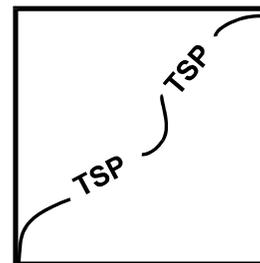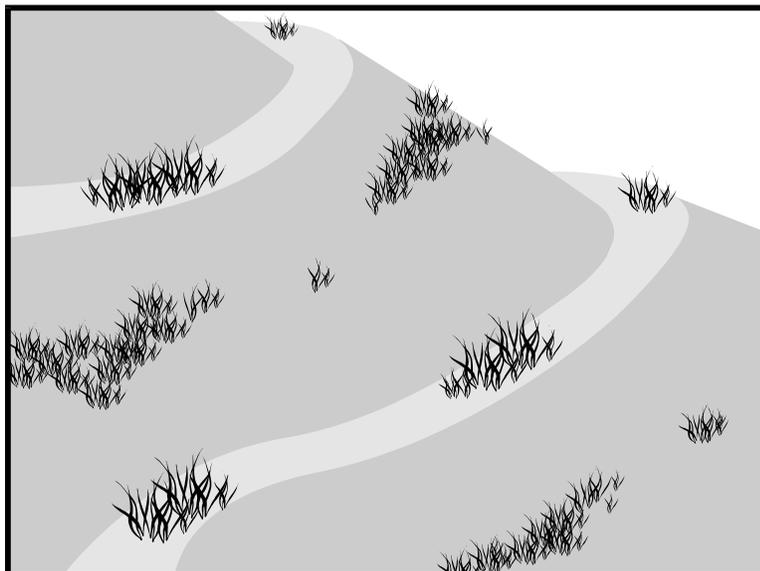

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Hydroseeding typically consists of applying a mixture of wood fiber, seed, fertilizer, and stabilizing emulsion with hydro-mulch equipment, which temporarily protects exposed soils from erosion by water and wind. This is one of five temporary soil stabilization alternatives to consider.

Appropriate Applications ■ Hydroseeding is applied on disturbed soil areas requiring temporary protection until permanent vegetation is established or disturbed soil areas that must be re-disturbed following an extended period of inactivity.

- Limitations**
- Hydroseeding may be used alone only when there is sufficient time in the season to ensure adequate vegetation establishment and erosion control. Otherwise, hydroseeding must be used in conjunction with a soil binder or mulching (i.e., straw mulch), refer to BMP SS-5, Table 1 for options.
 - Steep slopes are difficult to protect with temporary seeding.
 - Temporary seeding may not be appropriate in dry periods without supplemental irrigation.
 - Temporary vegetation may have to be removed before permanent vegetation is applied.
 - Temporary vegetation is not appropriate for short-term inactivity.

Standards and Specifications To select appropriate hydroseeding mixtures, an evaluation of site conditions shall be performed with respect to:

- Soil conditions
- Site topography
- Season and climate
- Vegetation types
- Maintenance requirements
- Sensitive adjacent areas
- Water availability
- Plans for permanent vegetation



- Selection of hydroseeding mixtures shall be approved by the District Landscape Architect and the Construction Storm Water Coordinator.

The following steps shall be followed for implementation:

- Seed mix shall comply with the Standard Specifications Section 20-2.10, and the project's special provisions.
- Hydroseeding can be accomplished using a multiple-step or one-step process; refer to the special provisions for specified process. The multiple-step process ensures maximum direct contact of the seeds to soil. When the one-step process is used to apply the mixture of fiber, seed, etc., the seed rate shall be increased to compensate for all seeds not having direct contact with the soil.
- Prior to application, roughen the slope, fill area, or area to be seeded with the furrows trending along the contours. Rolling with a crimping or punching type roller or track walking is required on all slopes prior to hydroseeding. Track walking shall only be used where other methods are impractical.
- Apply a straw mulch to keep seeds in place and to moderate soil moisture and temperature until the seeds germinate and grow, refer to Standard Specifications Sections 20-2.06 and 20-3.03.
- All seeds shall be in conformance with the California State Seed Law of the Department of Agriculture. Each seed bag shall be delivered to the site sealed and clearly marked as to species, purity, percent germination, dealer's guarantee, and dates of test; provide the Resident Engineer (RE) with such documentation. The container shall be labeled to clearly reflect the amount of Pure Live Seed (PLS) contained. All legume seed shall be pellet-inoculated. Inoculant sources shall be species-specific and shall be applied at a rate of 2 kg of inoculant per 100 kg of seed (2-lb inoculant per 100-lb seed), refer to Standard Specifications Section 20-2.10.
- Commercial fertilizer shall conform to the requirements of the California Food and Agricultural Code. Fertilizer shall be pelleted or granular form.

Maintenance and Inspection

- Follow-up applications shall be made as needed to cover weak spots, and to maintain adequate soil protection.
- Avoid over-spray onto the traveled way, sidewalks, lined drainage channels, and existing vegetation.
- All seeded areas shall be inspected for failures and re-seeded, fertilized, and mulched within the planting season, using not less than half the original application rates. Any temporary revegetation efforts that do not provide adequate cover must be reapplied at a scheduled recommended by the Caltrans Landscape Architect or RE.
- After any rainfall event, the Contractor is responsible for maintaining all slopes to prevent erosion.

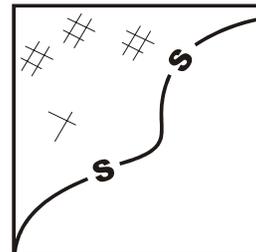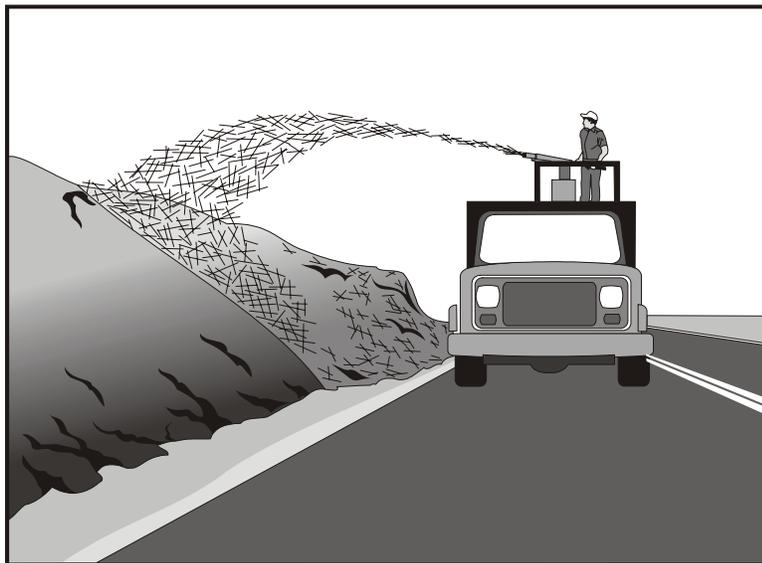

Standard Symbol

- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose Straw mulch consists of placing a uniform layer of straw and incorporating it into the soil with a studded roller or anchoring it with a stabilizing emulsion. This is one of five temporary soil stabilization alternatives to consider.

- Appropriate Applications**
- Straw mulch is typically used for soil stabilization as a temporary surface cover on disturbed areas until soils can be prepared for revegetation and permanent vegetation is established.
 - Also typically used in combination with temporary and/or permanent seeding strategies to enhance plant establishment.

- Limitations**
- Availability of erosion control contractors and straw may be limited prior to the rainy season due to high demand.
 - There is a potential for introduction of weed-seed and unwanted plant material.
 - When straw blowers are used to apply straw mulch, the treatment areas must be within 45 m (150 ft) of a road or surface capable of supporting trucks.
 - Straw mulch applied by hand is more time intensive and potentially costly.
 - May have to be removed prior to permanent seeding or soil stabilization.
 - “Punching” of straw does not work in sandy soils.

Standards and Specifications

- Straw shall be derived from wheat, rice, or barley.
- All materials shall conform to Standard Specifications Sections 20-2.06, 20-2.07 and 20-2.11.
- A tackifier is the preferred method for anchoring straw mulch to the soil on slopes.
- Crimping, punch roller-type rollers, or track-walking may also be used to incorporate straw mulch into the soil on slopes. Track walking shall only be used where other methods are impractical.
- Avoid placing straw onto the traveled way, sidewalks, lined drainage channels, sound walls, and existing vegetation.
- Straw mulch with tackifier shall not be applied during or immediately before rainfall.

Application Procedures

- Apply loose straw at a minimum rate of 3,570 kg/ha (4,000 lb/ac), or as indicated in the project's special provisions, either by machine or by hand distribution.
- If stabilizing emulsion will be used to anchor the straw mulch in lieu of incorporation, roughen embankment or fill areas by rolling with a crimping or punching-type roller or by track walking before placing the straw mulch. Track walking should only be used where rolling is impractical.
- The straw mulch must be evenly distributed on the soil surface.
- Anchor the mulch in place by using a tackifier or by "punching" it into the soil mechanically (incorporating).
- A tackifier acts to glue the straw fibers together and to the soil surface. The tackifier shall be selected based on longevity and ability to hold the fibers in place.
- A tackifier is typically applied at a rate of 140 kg/ha (125 lb/ac). In windy conditions, the rates are typically 200 kg/ha (178 lb/ac).
- Methods for holding the straw mulch in place depend upon the slope steepness, accessibility, soil conditions and longevity. If the selected method is incorporation of straw mulch into the soil, then do as follows:
 - Applying and incorporating straw shall follow the requirements in Standard Specifications Section 20-3.03.
 - On small areas, a spade or shovel can be used.



- On slopes with soils, which are stable enough and of sufficient gradient to safely support construction equipment without contributing to compaction and instability problems, straw can be “punched” into the ground using a knife-blade roller or a straight bladed coulter, known commercially as a “crimper.”
- On small areas and/or steep slopes, straw can also be held in place using plastic netting or jute. The netting shall be held in place using 11 gauge wire staples, geotextile pins or wooden stakes. Refer to BMP SS-7, “Geotextiles, Plastic Covers and Erosion Control Blankets/Mats.”

Maintenance and Inspections

- The key consideration in Maintenance and Inspection is that the straw needs to last long enough to achieve erosion control objectives.
- Maintain an unbroken, temporary mulched ground cover while DSAs are non-active. Repair any damaged ground cover and re-mulch exposed areas.
- Reapplication of straw mulch and tackifier may be required by the Resident Engineer (RE) to maintain effective soil stabilization over disturbed areas and slopes.
- After any rainfall event, the Contractor is responsible for maintaining all slopes to prevent erosion.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

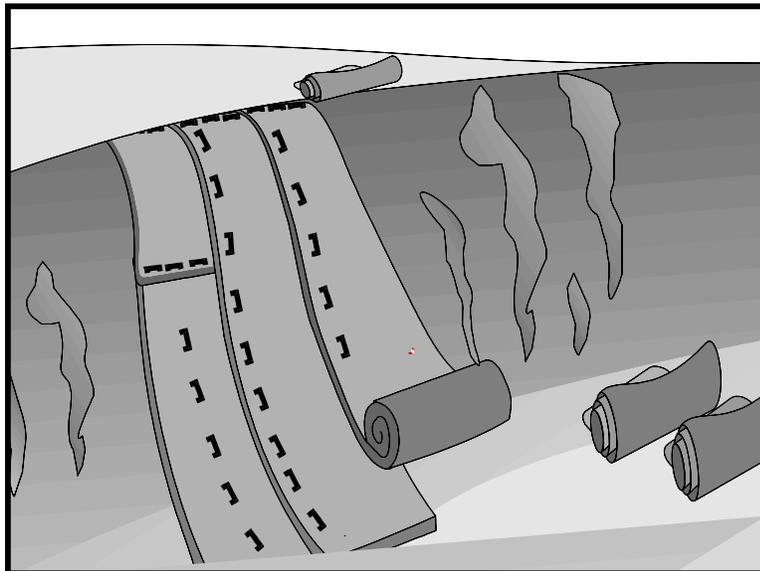

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose This Best Management Practice (BMP) involves the placement of geotextiles, mats, plastic covers, or erosion control blankets to stabilize disturbed soil areas and protect soils from erosion by wind or water. This is one of five temporary soil stabilization alternatives to consider.

Appropriate Applications These measures are used when disturbed soils may be particularly difficult to stabilize, including the following situations:

- Steep slopes, generally steeper than 1:3 (V:H).
- Slopes where the erosion potential is high.
- Slopes and disturbed soils where mulch must be anchored.
- Disturbed areas where plants are slow to develop.
- Channels with flows exceeding 1.0 m/s (3.3 ft/s).
- Channels to be vegetated.
- Stockpiles.
- Slopes adjacent to water bodies of Environmentally Sensitive Areas (ESAs).

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

- Limitations
- Blankets and mats are more expensive than other erosion control measures, due to labor and material costs. This usually limits their application to areas inaccessible to hydraulic equipment, or where other measures are not applicable, such as channels.
 - Blankets and mats are generally not suitable for excessively rocky sites, or areas where the final vegetation will be mowed (since staples and netting can catch in mowers).
 - Blankets and mats must be removed and disposed of prior to application of permanent soil stabilization measures.
 - Plastic sheeting is easily vandalized, easily torn, photodegradable, and must be disposed of at a landfill.
 - Plastic results in 100% runoff, which may cause serious erosion problems in the areas receiving the increased flow.
 - The use of plastic shall be limited to covering stockpiles, or very small graded areas for short periods of time (such as through one imminent storm event), until alternative measures, such as seeding and mulching, may be installed.
 - Geotextiles, mats, plastic covers, and erosion control covers have maximum flow rate limitations; consult the manufacturer for proper selection.

Standards and Specifications **Material Selection**

There are many types of erosion control blankets and mats, and selection of the appropriate type shall be based on the specific type of application and site conditions. Selection(s) made by the Contractor must be approved by the Resident Engineer (RE); certification of compliance shall be in accordance with Standard Specifications Section 6-1.07.

Geotextiles

- Material shall be a woven polypropylene fabric with minimum thickness of 1.5 mm (0.06 inch), minimum width of 3.7 m (12 ft) and shall have minimum tensile strength of 0.67 kN (warp) 0.36 kN (fill) in conformance with the requirements in ASTM Designation: D 4632. The permittivity of the fabric shall be approximately 0.07 sec⁻¹ in conformance with the requirements in ASTM Designation: D4491. The fabric shall have an ultraviolet (UV) stability of 70 percent in conformance with the requirements in ASTM designation: D4355. Geotextile blankets shall be secured in place with wire staples or sandbags and by keying into tops of slopes and edges to prevent infiltration of surface waters under Geotextile. Staples shall be made of 3.05-mm (0.12-inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.
- Geotextiles may be reused if, in the opinion of the RE, they are suitable for the use intended.

Plastic Covers

- Plastic sheeting shall have a minimum thickness of 6 mil, and shall be keyed in at the top of slope and firmly held in place with sandbags or other weights placed no more than 3 m (10 ft) apart. Seams are typically taped or weighted down their entire length, and there shall be at least a 300 mm to 600 mm (12 to 24 inches) overlap of all seams. Edges shall be embedded a minimum of 150 mm (6 inches) in soil.
- All sheeting shall be inspected periodically after installation and after significant rainstorms to check for erosion, undermining, and anchorage failure. Any failures shall be repaired immediately. If washout or breakages occurs, the material shall be re-installed after repairing the damage to the slope.

Erosion Control Blankets/Mats

- Biodegradable rolled erosion control products (RECPs) are typically composed of jute fibers, curled wood fibers, straw, coconut fiber, or a combination of these materials. For an RECP to be considered 100% biodegradable, the netting, sewing or adhesive system that holds the biodegradable mulch fibers together must also be biodegradable.
 - **Jute** is a natural fiber that is made into a yarn, which is loosely woven into a biodegradable mesh. It is designed to be used in conjunction with vegetation and has longevity of approximately one year. The material is supplied in rolled strips, which shall be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Excelsior (curled wood fiber)** blanket material shall consist of machine produced mats of curled wood excelsior with 80 percent of the fiber 150 mm (6 inches) or longer. The excelsior blanket shall be of consistent thickness. The wood fiber shall be evenly distributed over the entire area of the blanket. The top surface of the blanket shall be covered with a photodegradable extruded plastic mesh. The blanket shall be smolder resistant without the use of chemical additives and shall be non-toxic and non-injurious to plant and animal life. Excelsior blanket shall be furnished in rolled strips, a minimum of 1220 mm (48 inches) wide, and shall have an average weight of 0.5 kg/m² (12 lb/ft²), ±10 percent, at the time of manufacture. Excelsior blankets shall be secured in place with wire staples. Staples shall be made of 3.05-mm (0.12 inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

- **Straw blanket** shall be machine-produced mats of straw with a lightweight biodegradable netting top layer. The straw shall be attached to the netting with biodegradable thread or glue strips. The straw blanket shall be of consistent thickness. The straw shall be evenly distributed over the entire area of the blanket. Straw blanket shall be furnished in rolled strips a minimum of 2 m (6.5 ft) wide, a minimum of 25 m (80 ft) long and a minimum of 0.27 kg/m² (6.4 lb/ft²). Straw blankets shall be secured in place with wire staples. Staples shall be made of 3.05-mm (0.12 inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.
- **Wood fiber blanket** is composed of biodegradable fiber mulch with extruded plastic netting held together with adhesives. The material is designed to enhance revegetation. The material is furnished in rolled strips, which shall be secured to the ground with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Coconut fiber blanket** shall be machine-produced mats of 100% coconut fiber with biodegradable netting on the top and bottom. The coconut fiber shall be attached to the netting with biodegradable thread or glue strips. The coconut fiber blanket shall be of consistent thickness. The coconut fiber shall be evenly distributed over the entire area of the blanket. Coconut fiber blanket shall be furnished in rolled strips with a minimum of 2 m (6.5 ft) wide, a minimum of 25 m (80 ft) long and a minimum of 0.27-kg/m² (6.4 lb/ft²). Coconut fiber blankets shall be secured in place with wire staples. Staples shall be made of 3.05-mm (0.12 inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.
- **Coconut fiber mesh** is a thin permeable membrane made from coconut or corn fiber that is spun into a yarn and woven into a biodegradable mat. It is designed to be used in conjunction with vegetation and typically has longevity of several years. The material is supplied in rolled strips, which shall be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
- **Straw coconut fiber blanket** shall be machine-produced mats of 70% straw and 30% coconut fiber with a biodegradable netting top layer and a biodegradable bottom net. The straw and coconut fiber shall be attached to the netting with biodegradable thread or glue strips. The straw coconut fiber blanket shall be of consistent thickness. The straw and coconut fiber shall be evenly distributed over the entire area of the blanket. Straw coconut fiber blanket shall be furnished in rolled strips a minimum of 2 m (6.5 ft) wide, a minimum of 25 m (80 ft) long and a minimum of 0.27 kg/m² (6.4 lb/ft²). Straw coconut fiber blankets shall be secured in place with wire staples. Staples shall be made of 3.05-mm (0.12-inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

- Non-biodegradable RECPs are typically composed of polypropylene, polyethylene, nylon or other synthetic fibers. In some cases, a combination of biodegradable and synthetic fibers is used to construct the RECP. Netting used to hold these fibers together is typically non-biodegradable as well.
 - **Plastic netting** is a lightweight biaxially-oriented netting designed for securing loose mulches like straw to soil surfaces to establish vegetation. The netting is photodegradable. The netting is supplied in rolled strips, which shall be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Plastic mesh** is an open-weave geotextile that is composed of an extruded synthetic fiber woven into a mesh with an opening size of less than 0.5 cm (0.2 inch). It is used with revegetation or may be used to secure loose fiber such as straw to the ground. The material is supplied in rolled strips, which shall be secured to the soil with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Synthetic fiber with netting** is a mat that is composed of durable synthetic fibers treated to resist chemicals and ultraviolet light. The mat is a dense, three-dimensional mesh of synthetic (typically polyolefin) fibers stitched between two polypropylene nets. The mats are designed to be revegetated and provide a permanent composite system of soil, roots, and geomatrix. The material is furnished in rolled strips, which shall be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Bonded synthetic fibers** consist of a three-dimensional geomatrix nylon (or other synthetic) matting. Typically it has more than 90% open area, which facilitates root growth. Its tough root-reinforcing system anchors vegetation and protects against hydraulic lift and shear forces created by high volume discharges. It can be installed over prepared soil, followed by seeding into the mat. Once vegetated, it becomes an invisible composite system of soil, roots, and geomatrix. The material is furnished in rolled strips that shall be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.
 - **Combination synthetic and biodegradable RECPs** consist of biodegradable fibers, such as wood fiber or coconut fiber, with a heavy polypropylene net stitched to the top and a high-strength continuous-filament geomatrix or net stitched to the bottom. The material is designed to enhance revegetation. The material is furnished in rolled strips, which shall be secured with U-shaped staples or stakes in accordance with manufacturers' recommendations.

Site Preparation

- Proper site preparation is essential to ensure complete contact of the blanket or matting with the soil.
- Grade and shape the area of installation.
- Remove all rocks, clods, vegetation or other obstructions so that the installed blankets or mats will have complete, direct contact with the soil.
- Prepare seedbed by loosening 50 mm (2 in) to 75 mm (3 in) of topsoil.

Seeding

Seed the area before blanket installation for erosion control and revegetation. Seeding after mat installation is often specified for turf reinforcement application. When seeding prior to blanket installation, all check slots and other areas disturbed during installation must be re-seeded. Where soil filling is specified, seed the matting and the entire disturbed area after installation and prior to filling the mat with soil.

Anchoring

- U-shaped wire staples, metal geotextile stake pins or triangular wooden stakes can be used to anchor mats and blankets to the ground surface.
- Staples shall be made of 3.05 mm (0.12 inch) steel wire and shall be U-shaped with 200-mm (8-inch) legs and 50-mm (2-inch) crown.
- Metal stake pins shall be 5 mm (0.188 in) diameter steel with a 40 mm (1.5 in) steel washer at the head of the pin.
- Wire staples and metal stakes shall be driven flush to the soil surface.
- All anchors shall be 150 mm (6 in) to 450 mm (18 in) long and have sufficient ground penetration to resist pullout. Longer anchors may be required for loose soils.

Installation on Slopes

Installation shall be in accordance with the manufacturer's recommendations. In general, these will be as follows:

- Begin at the top of the slope and anchor the blanket in a 150 mm (6 in) deep by 150 mm (6 in) wide trench. Backfill trench and tamp earth firmly.
- Unroll blanket downslope in the direction of water flow.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

- Overlap the edges of adjacent parallel rolls 50 mm (2 in) to 75 mm (3 in) and staple every 1 m (3 ft).
- When blankets must be spliced, place blankets end over end (shingle style) with 150 mm (6 in) overlap. Staple through overlapped area, approximately 300 mm (12 in) apart.
- Lay blankets loosely and maintain direct contact with the soil. Do not stretch.
- Staple blankets sufficiently to anchor blanket and maintain contact with the soil. Staples shall be placed down the center and staggered with the staples placed along the edges. Steep slopes, 1:1 (V:H) to 1:2 (V:H), require a minimum of 2 staples/m² (2 staples/yd²). Moderate slopes, 1:2 (V:H) to 1:3 (V:H), require a minimum of 1½ staples/m² (1½ staples/yd²), placing 1 staple/m (1 staple/yd) on centers. Gentle slopes require a minimum of 1 staple/m² (1 staple/yd²).

Installation in Channels

Installation shall be in accordance with the manufacturer's recommendations. In general, these will be as follows:

- Dig initial anchor trench 300 mm (12 in) deep and 150 mm (6 in) wide across the channel at the lower end of the project area.
- Excavate intermittent check slots, 150 mm (6 in) deep and 150 mm (6 in) wide across the channel at 8 m to 10 m (25 ft to 30 ft) intervals along the channels.
- Cut longitudinal channel anchor slots 100 mm (4 in) deep and 100 mm (4 in) wide along each side of the installation to bury edges of matting, whenever possible extend matting 50 mm (2 in) to 75 mm (3 in) above the crest of the channel side slopes.
- Beginning at the downstream end and in the center of the channel, place the initial end of the first roll in the anchor trench and secure with fastening devices at 300 mm (12 in) intervals. Note: matting will initially be upside down in anchor trench.
- In the same manner, position adjacent rolls in anchor trench, overlapping the preceding roll a minimum of 75 mm (3 in).
- Secure these initial ends of mats with anchors at 300 mm (12 in) intervals, backfill and compact soil.
- Unroll center strip of matting upstream. Stop at next check slot or terminal anchor trench. Unroll adjacent mats upstream in similar fashion, maintaining a 75 mm (3 in) overlap.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

- Fold and secure all rolls of matting snugly into all transverse check slots. Lay mat in the bottom of the slot then fold back against itself. Anchor through both layers of mat at 300 mm (12 in) intervals, then backfill and compact soil. Continue rolling all mat widths upstream to the next check slot or terminal anchor trench.
- Alternate method for non-critical installations: Place two rows of anchors on 150 mm (6 in) centers at 8 m (25 ft) to 10 m (30 ft) intervals in lieu of excavated check slots.
- Shingle-lap spliced ends by a minimum of 300 mm (12 in) apart on 300 mm (12 in) intervals.
- Place edges of outside mats in previously excavated longitudinal slots, anchor using prescribed staple pattern, backfill and compact soil.
- Anchor, fill and compact upstream end of mat in a 300 mm (12 in) by 150 mm (6 in) terminal trench.
- Secure mat to ground surface using U-shaped wire staples, geotextile pins, or wooden stakes.
- Seed and fill turf reinforcement matting with soil, if specified.

Soil Filling (if specified for turf reinforcement)

- Always consult the manufacturer's recommendations for installation.
- Do not drive tracked or heavy equipment over mat.
- Avoid any traffic over matting if loose or wet soil conditions exist.
- Use shovels, rakes or brooms for fine grading and touch up.
- Smooth out soil filling, just exposing top netting of mat.

Temporary Soil Stabilization Removal

- When no longer required for the work, temporary soil stabilization shall become the property of the Contractor. Temporary soil stabilization removed from the site of the work shall be disposed of outside the highway right-of-way in conformance with the provisions in Standard Specifications Section 7-1.13. If approved by the RE, the contractor may leave the temporary soil stabilizer in place.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7


Maintenance and Inspection Areas treated with temporary soil stabilization shall be inspected as specified in the special provisions. Areas treated with temporary soil stabilization shall be maintained to provide adequate erosion control. Temporary soil stabilization shall be reapplied or replaced on exposed soils when area becomes exposed or exhibits visible erosion.

- All blankets and mats shall be inspected periodically after installation.
- Installation shall be inspected after significant rain storms to check for erosion and undermining. Any failures shall be repaired immediately.
- If washout or breakage occurs, re-install the material after repairing the damage to the slope or channel.

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

Typical Installation Detail

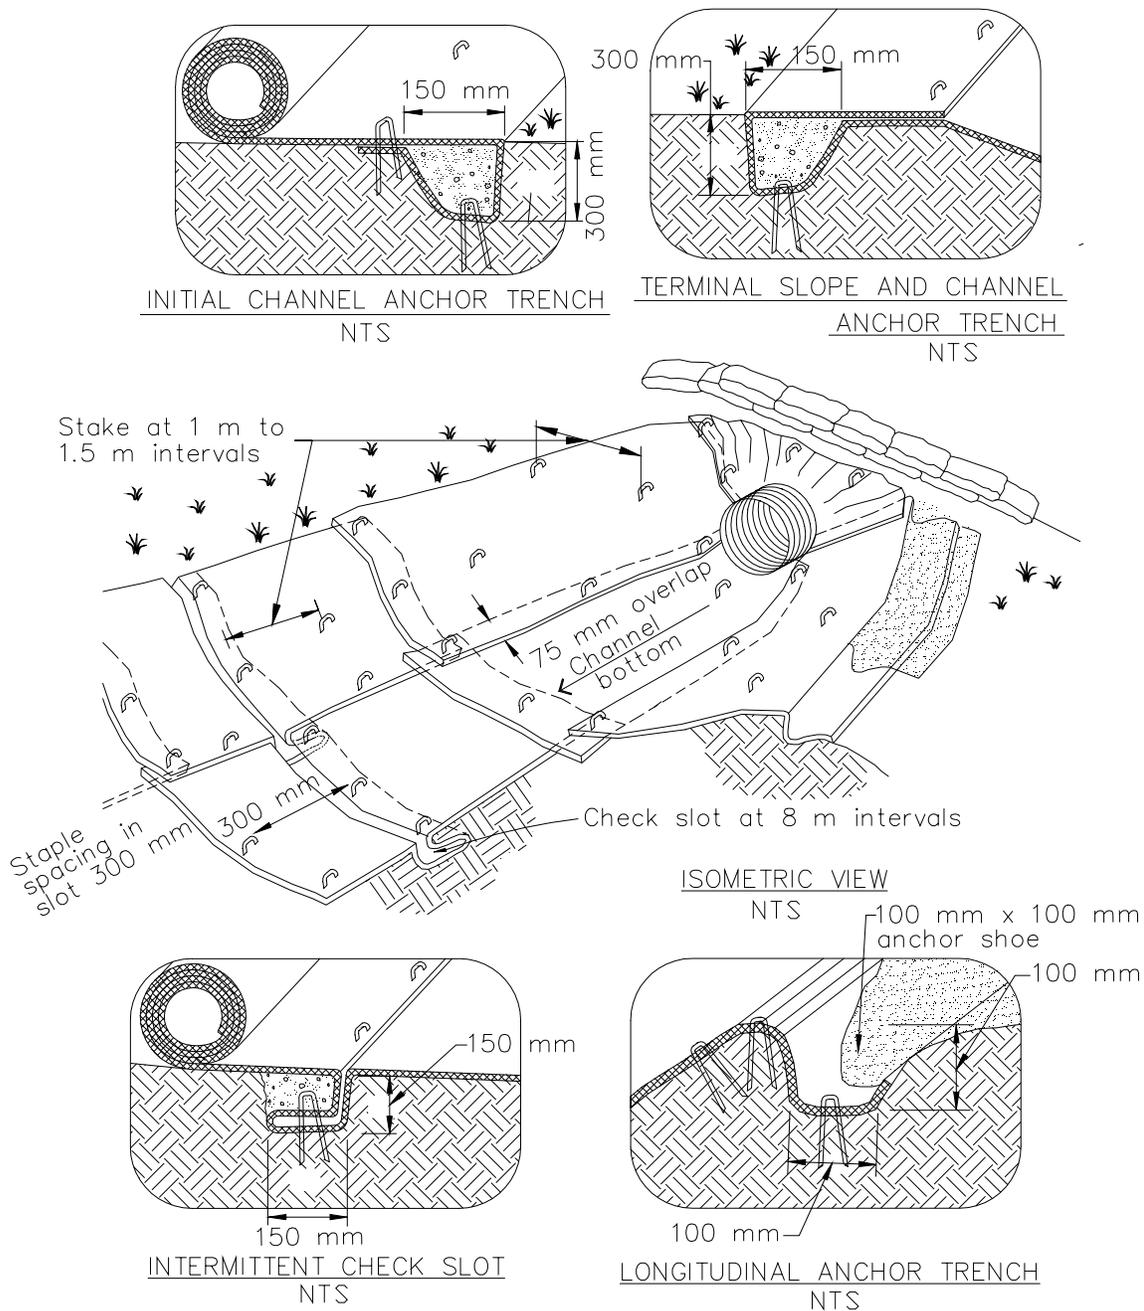


NOTES:

1. Check slots to be constructed per manufacturers specifications.
2. Staking or stapling layout per manufacturers specifications.
3. Install per manufacturer's recommendations

Geotextiles, Mats, Plastic Covers and Erosion Control Blankets

SS-7

Typical Installation Detail


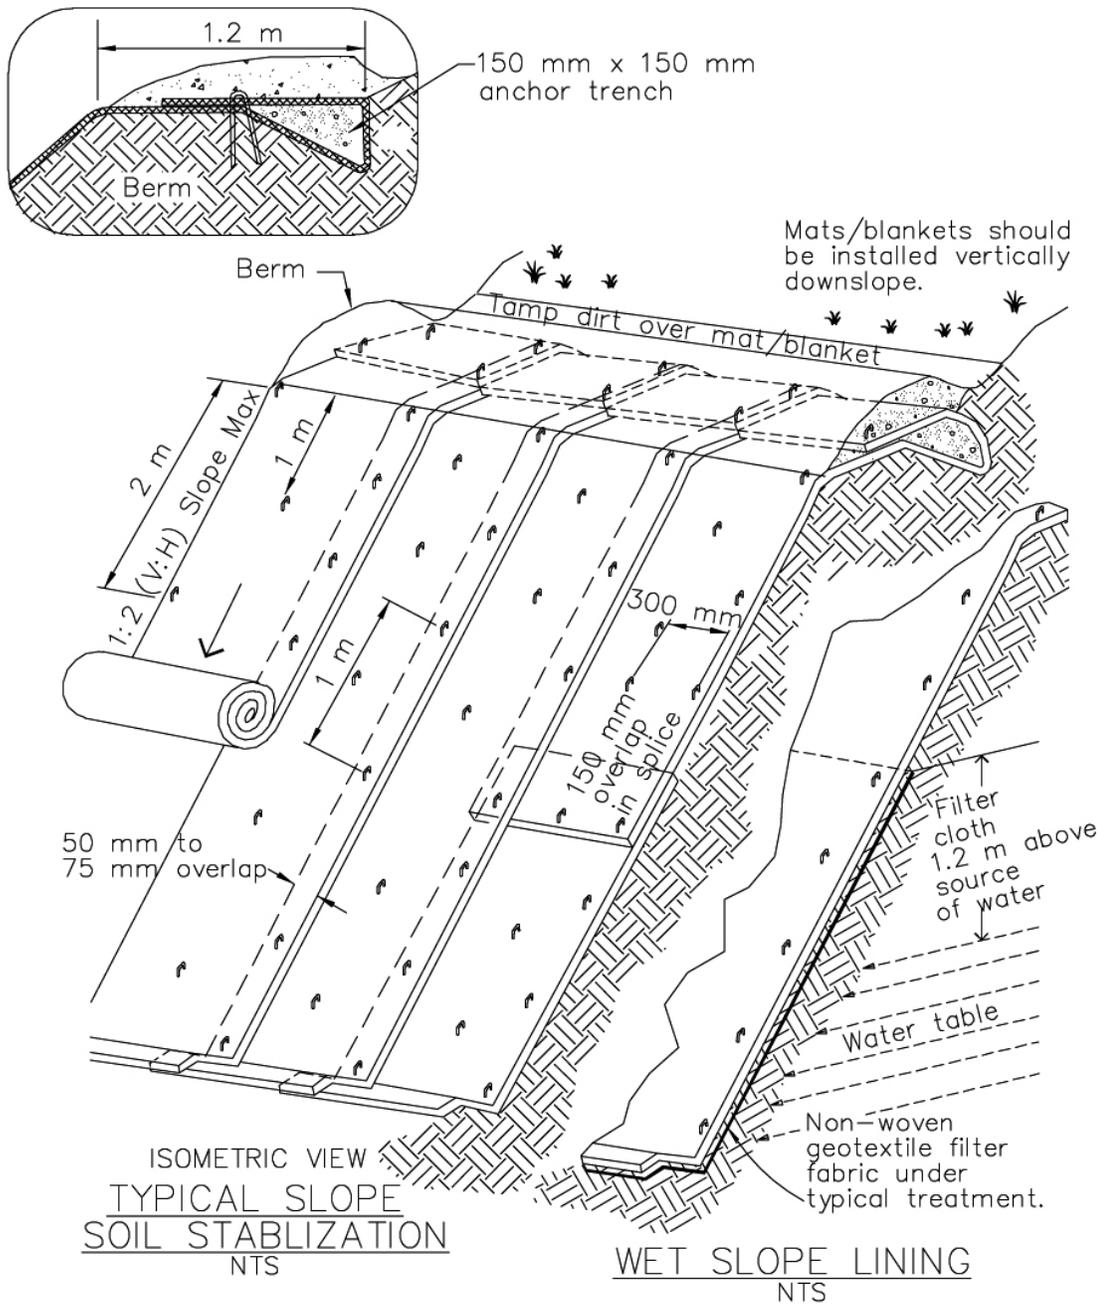


NOTES:

1. Slope surface shall be free of rocks, clods, sticks and grass. Mats/blankets shall have good soil contact.
2. Lay blankets loosely and stake or staple to maintain direct contact with the soil. Do not stretch.
3. Install per manufacturer's recommendations



Earth Dikes/Drainage Swales and Lined Ditches

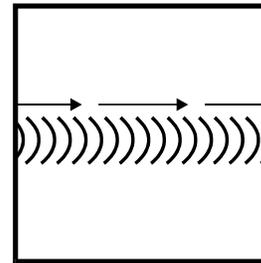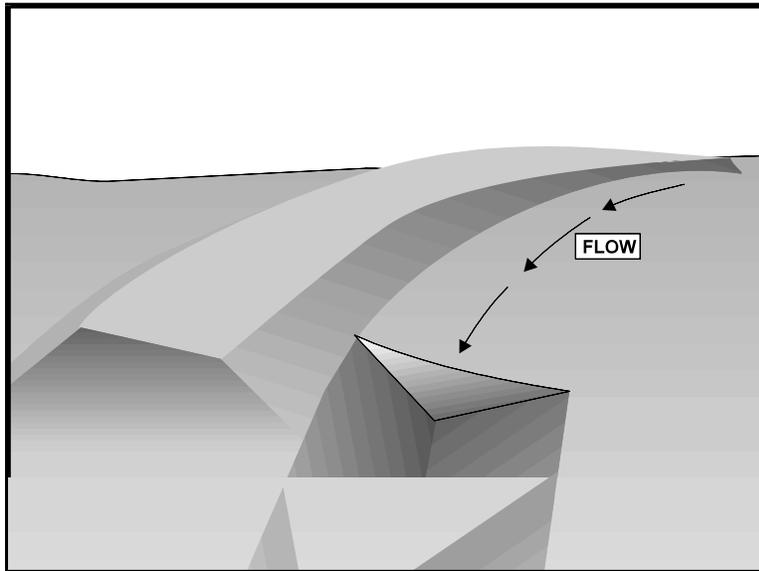

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose

These are structures that intercept, divert and convey surface run-on, generally sheet flow, to prevent erosion.

Appropriate Applications

- Earth dikes/drainage swales and lined ditches may be used to:
 - Convey surface runoff down sloping land.
 - Intercept and divert runoff to avoid sheet flow over sloped surfaces.
 - Divert and direct runoff towards a stabilized watercourse, drainage pipe or channel.
 - Intercept runoff from paved surfaces.
- Earth dikes/drainage swales and lined ditches also may be used:
 - Below steep grades where runoff begins to concentrate.
 - Along roadways and facility improvements subject to flood drainage.
 - At the top of slopes to divert run-on from adjacent or undisturbed slopes.
 - At bottom and mid-slope locations to intercept sheet flow and convey concentrated flows.
- This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the Resident Engineer (RE).


Earth Dikes/Drainage Swales and Lined Ditches

SS-9

- Limitations**
- Earth dikes/drainage swales and lined ditches are not suitable as sediment trapping devices.
 - May be necessary to use other soil stabilization and sediment controls, such as check dams, plastics, and blankets, to prevent scour and erosion in newly graded dikes, swales and ditches.
- Standards and Specifications**
- Care must be applied to correctly size and locate earth dikes, drainage swales and lined ditches. Excessively steep, unlined dikes and swales are subject to erosion and gully formation.
 - Conveyances shall be stabilized.
 - Use a lined ditch for high flow velocities.
 - Select flow velocity based on careful evaluation of the risks due to erosion of the measure, soil types, over topping, flow backups, washout, and drainage flow patterns for each project site.
 - Compact any fills to prevent unequal settlement.
 - Do not divert runoff from the highway right-of-way onto other property.
 - When possible, install and utilize permanent dikes, swales and ditches early in the construction process.
 - Provide stabilized outlets. Refer to SS-10, “Outlet Protection/Velocity/Dissipation Devices.”
- Maintenance and Inspections**
- Inspect temporary measures prior to the rainy season, after rainfall events, and regularly (approximately once per week) during the rainy season.
 - Inspect ditches and berms for washouts. Replace lost riprap, damaged linings or soil stabilizers as needed.
 - Inspect channel linings, embankments, and beds of ditches and berms for erosion and accumulation of debris and sediment. Remove debris and sediment, and repair linings and embankments as needed or as directed by the RE.
 - Temporary conveyances shall be completely removed as soon as the surrounding drainage area has been stabilized, or at the completion of construction.


Earth Dikes/Drainage Swales and Lined Ditches

SS-9

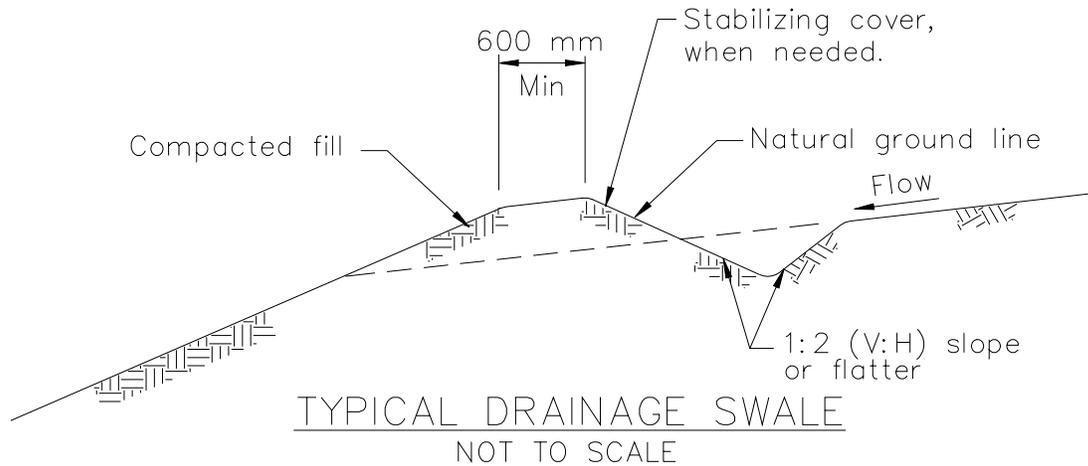



NOTES:

1. Stabilize inlet, outlets and slopes.
2. Properly compact the subgrade, in conformance with Section 19-5 of the Caltrans Standard Specifications.

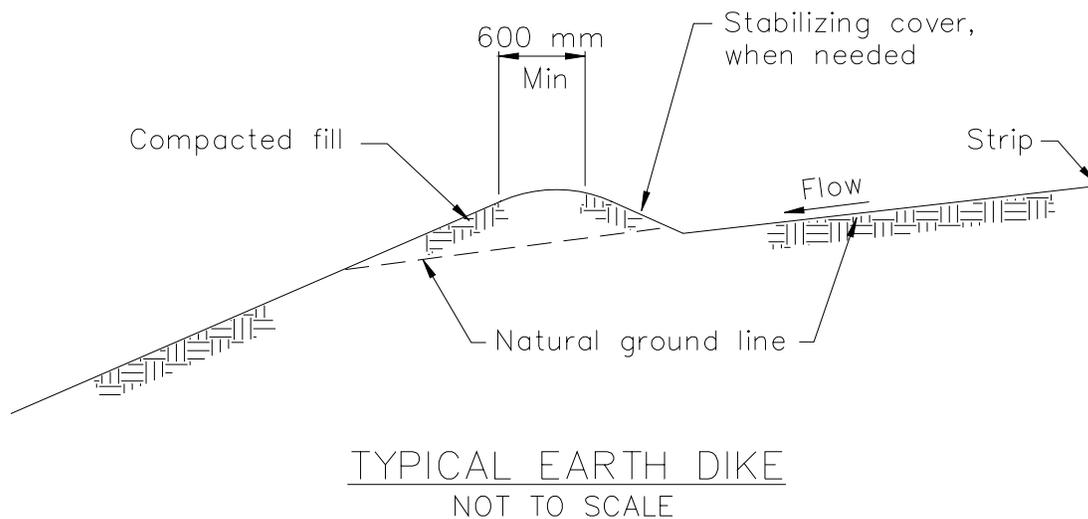

Outlet Protection/Velocity Dissipation Devices

SS-10

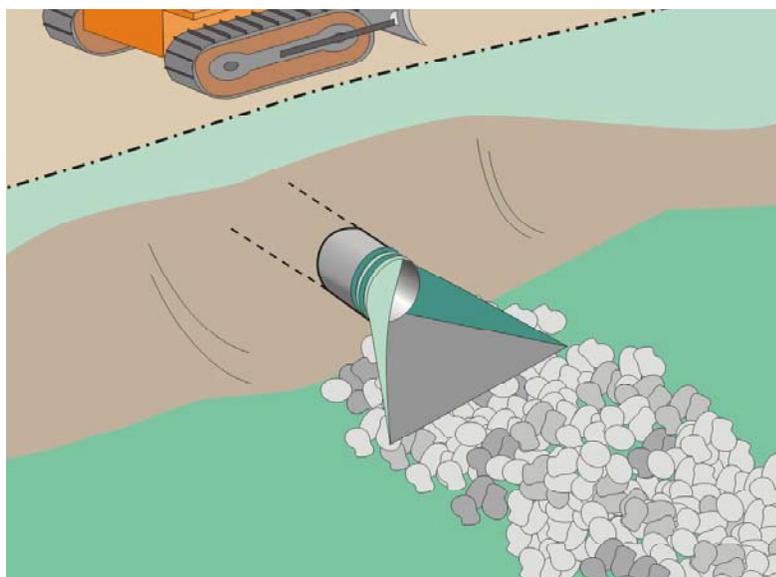

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose These devices are placed at pipe outlets to prevent scour and reduce the velocity and/or energy of storm water flows.

Appropriate Applications

- These devices may be used at the following locations:
 - Outlets of pipes, drains, culverts, slope drains, diversion ditches, swales, conduits or channels.
 - Outlets located at the bottom of mild to steep slopes.
 - Discharge outlets that carry continuous flows of water.
 - Outlets subject to short, intense flows of water, such as flash floods.
 - Points where lined conveyances discharge to unlined conveyances.
- This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the Resident Engineer (RE).

Limitations

- Loose rock may have stones washed away during high flows.
- Grouted riprap may break up in areas of freeze and thaw.
- If there is not adequate drainage, and water builds up behind grouted riprap, it may cause the grouted riprap to break up due to the resulting hydrostatic pressure.


Outlet Protection/Velocity Dissipation Devices

SS-10

- Standards and Specifications**
- There are many types of energy dissipaters, with rock being the one that is represented in the figure on Page 3. Please note that this is only one example and the RE may approve other types of devices proposed by the contractor.
 - Install riprap, grouted riprap, or concrete apron at selected outlet. Riprap aprons are best suited for temporary use during construction.
 - Carefully place riprap to avoid damaging the filter fabric.
 - For proper operation of apron:
 - Align apron with receiving stream and keep straight throughout its length. If a curve is needed to fit site conditions, place it in upper section of apron.
 - If size of apron riprap is large, protect underlying filter fabric with a gravel blanket.
 - Outlets on slopes steeper than 10% shall have additional protection.
- Maintenance and Inspection**
- Inspect temporary measures prior to the rainy season, after rainfall events, and regularly (approximately once per week) during the rainy season.
 - Inspect apron for displacement of the riprap and/or damage to the underlying fabric. Repair fabric and replace riprap that has washed away.
 - Inspect for scour beneath the riprap and around the outlet. Repair damage to slopes or underlying filter fabric immediately.
 - Temporary devices shall be completely removed as soon as the surrounding drainage area has been stabilized, or at the completion of construction.

Outlet Protection/Velocity Dissipation Devices

SS-10


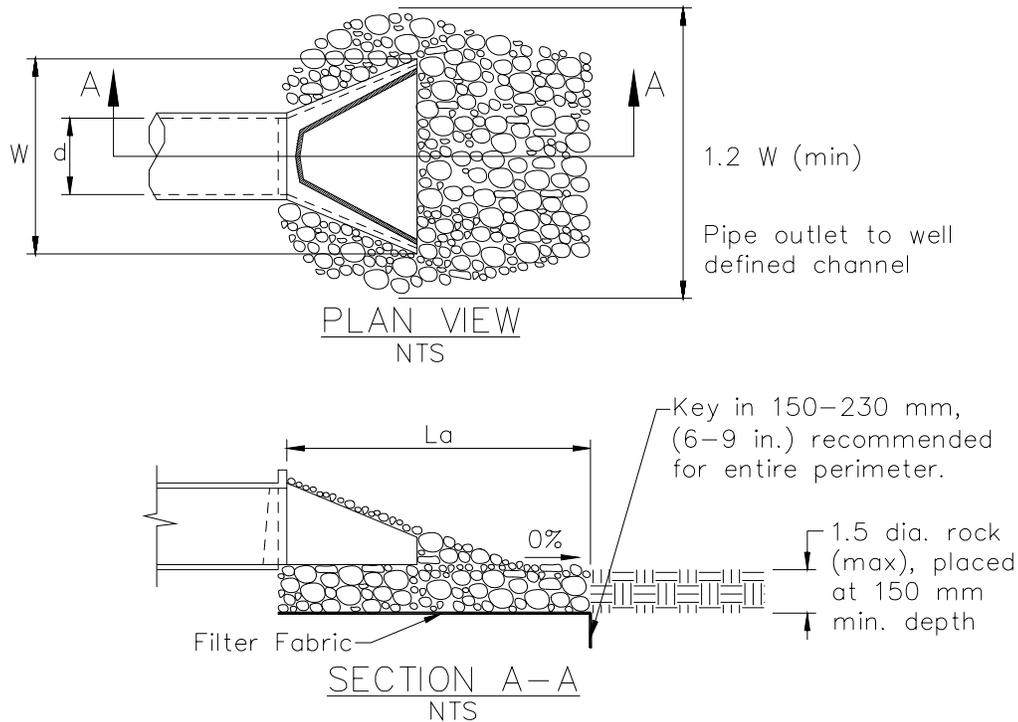


Pipe Diameter mm	Discharge m ³ /s	Apron Length, La m	Rip Rap D ₅₀ Diameter Min mm
300	0.14	3	100
	0.28	4	150
450	0.28	3	150
	0.57	5	200
	0.85	7	300
	1.13	8	400
600	0.85	5	200
	1.13	8	200
	1.42	8	300
	1.70	9	400

For larger or higher flows, consult a Registered Civil Engineer

Source: USDA – SCS



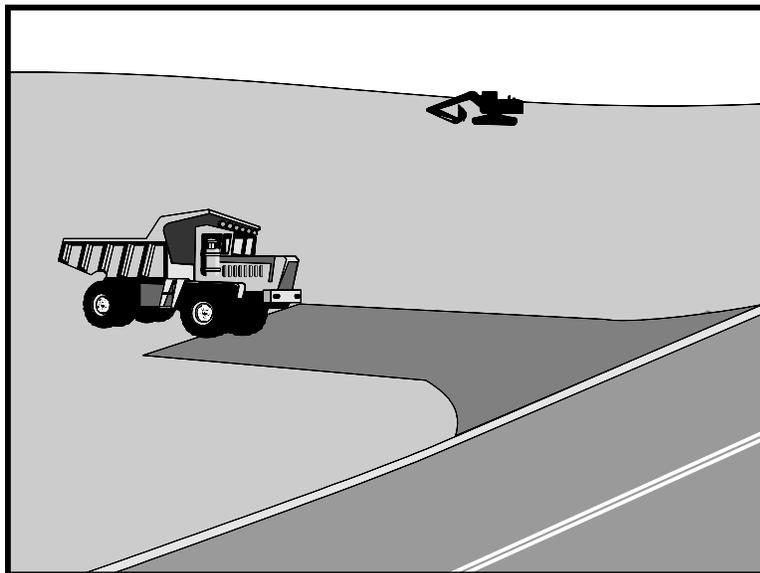

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A stabilized construction access is defined by a point of entrance/exit to a construction site that is stabilized to reduce the tracking of mud and dirt onto public roads by construction vehicles.

Appropriate Applications

- Use at construction sites:
 - Where dirt or mud can be tracked onto public roads.
 - Adjacent to water bodies.
 - Where poor soils are encountered.
 - Where dust is a problem during dry weather conditions.
- This BMP may be implemented on a project-by-project basis in addition to other BMPs when determined necessary and feasible by the Resident Engineer (RE).

Limitations

- Site conditions will dictate design and need.


Standards and Specifications

- Limit the points of entrance/exit to the construction site.
- Limit speed of vehicles to control dust.
- Properly grade each construction entrance/exit to prevent runoff from leaving the construction site.
- Route runoff from stabilized entrances/exits through a sediment-trapping device before discharge.
- Design stabilized entrance/exit to support the heaviest vehicles and equipment that will use it.


- Select construction access stabilization (aggregate, asphaltic concrete, concrete) based on longevity, required performance, and site conditions. The use of asphalt concrete (AC) grindings for stabilized construction access/roadway is not allowed.
 - Use of constructed/manufactured steel plates with ribs for entrance/exit access is allowed with written approval from the RE.
 - If aggregate is selected, place crushed aggregate over geotextile fabric to at least 300 mm (12 in) depth, or place aggregate to a depth recommended by the RE. Crushed aggregate greater than 75 mm (3 inches) and smaller than 150 mm (6 inches) shall be used.
 - Designate combination or single purpose entrances and exits to the construction site.
 - Implement BMP SC-7, “Street Sweeping and Vacuuming” as needed and as required.
 - Require all employees, subcontractors, and suppliers to utilize the stabilized construction access.
 - All exit locations intended to be used continuously and for a period of time shall have stabilized construction entrance/exit BMPs (TC-1 “Stabilized Construction Entrance/Exit” or TC-3 “Entrance/Outlet Tire Wash”).
- Maintenance and Inspection
- Inspect routinely for damage and assess effectiveness of the BMP. Remove aggregate, separate and dispose of sediment if construction entrance/exit is clogged with sediment or as directed by the RE.
 - Keep all temporary roadway ditches clear.
 - Inspect for damage and repair as needed.

Stabilized Construction Entrance/Exit

TC-1

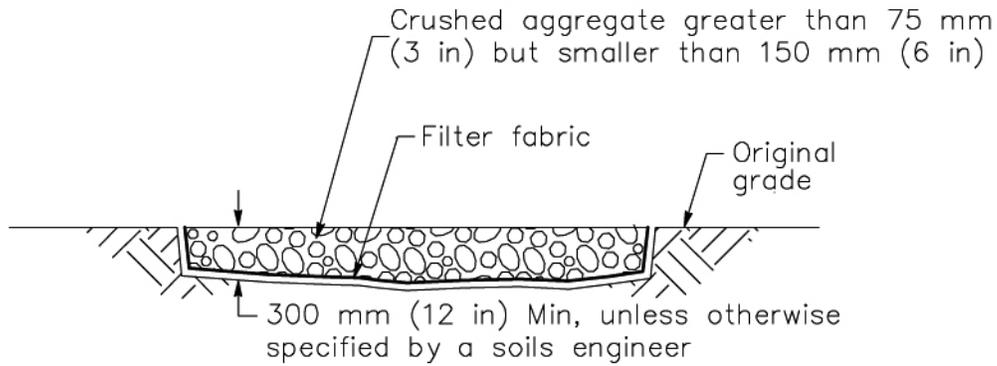

SECTION B-B
NTS

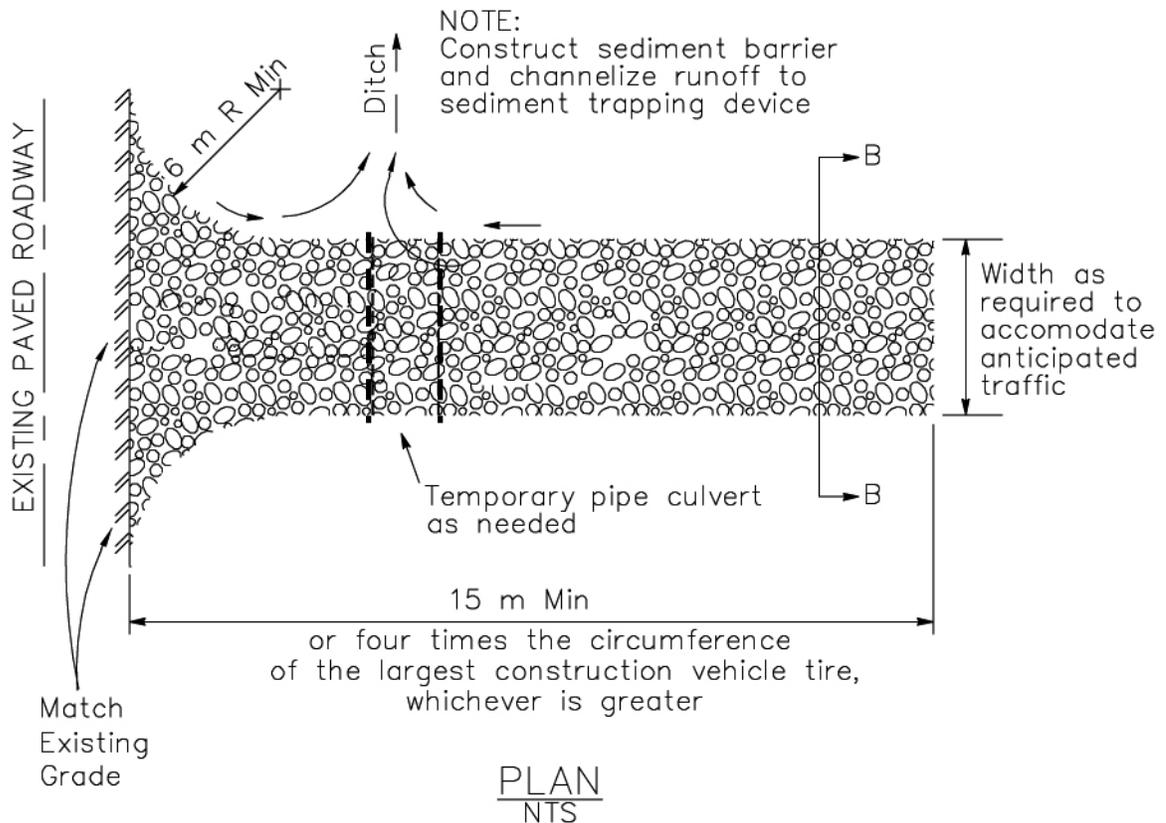


Stabilized Construction Entrance/Exit (Type 1)




Stabilized Construction Entrance/Exit

TC-1




SECTION B-B
NTS

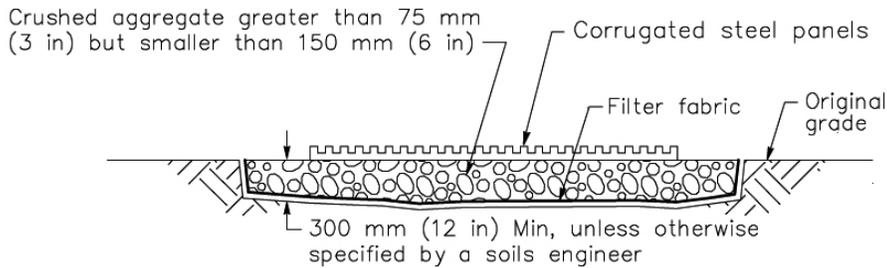


SECTION A-A
NOT TO SCALE

NOTE:
Construct sediment barrier
and channelize runoff to
sediment trapping device





Sediment trapping
device

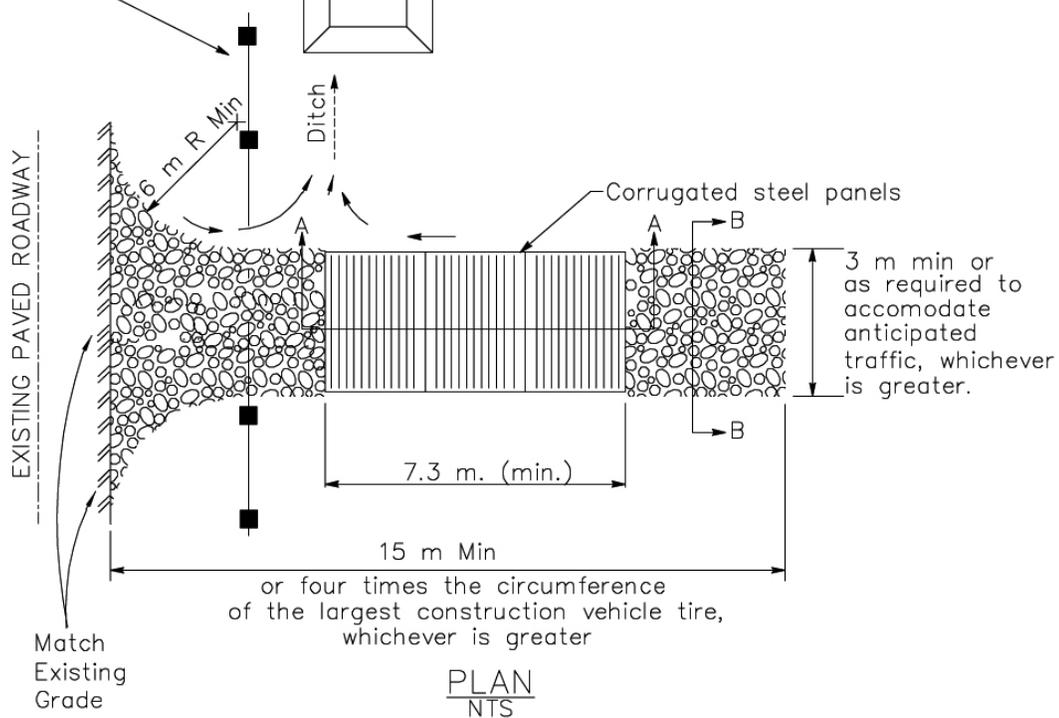

PLAN
NTS

Stabilized Construction Entrance/Exit (Type 2)



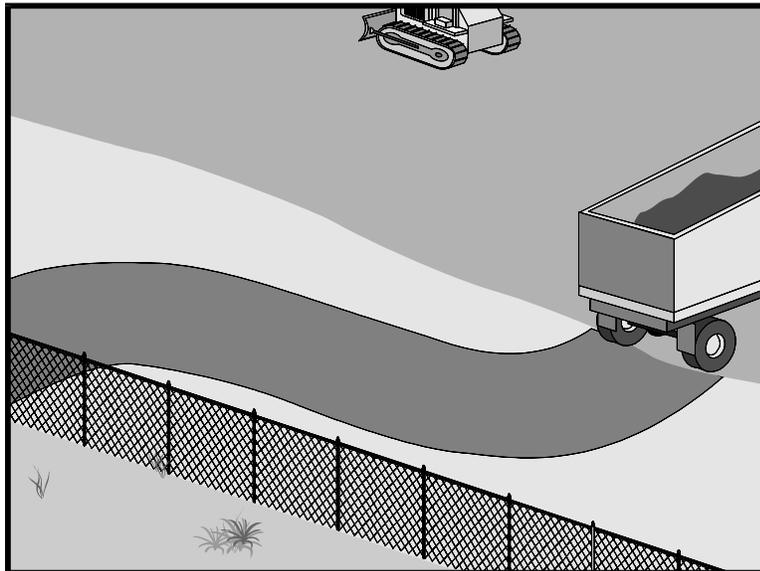

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A stabilized construction roadway is a temporary access road. It is designed for the control of dust and erosion created by vehicular tracking.

Appropriate Applications

- Construction roadways and short-term detour roads:
 - Where mud tracking is a problem during wet weather.
 - Where dust is a problem during dry weather.
 - Adjacent to water bodies.
 - Where poor soils are encountered.
 - Where there are steep grades and additional traction is needed.
- This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the Resident Engineer (RE).

Limitations



- Materials will likely need to be removed prior to final project grading and stabilization.
- Site conditions will dictate design and need.
- May not be applicable to very short duration projects.
- Limit speed of vehicles to control dust.

Standards and Specifications

- Properly grade roadway to prevent runoff from leaving the construction site.
- Design stabilized access to support the heaviest vehicles and equipment that will use it.
- Stabilize roadway using aggregate, asphalt concrete, or concrete based on longevity, required performance, and site conditions. The use of cold mix asphalt or asphalt concrete (AC) grindings for stabilized construction roadway is not allowed.
- Coordinate materials with those used for stabilized construction entrance/exit points.
- If aggregate is selected, place crushed aggregate over geotextile fabric to at least 300 mm (12 in) depth, or place aggregate to a depth recommended by the RE or Construction Storm Water Coordinator. Crushed aggregate greater than 75 mm (3 inches) and smaller than 150 mm (6 inches) shall be used.

Maintenance and Inspection

- Inspect routinely for damage and repair as needed, or as directed by the RE.
- Keep all temporary roadway ditches clear.
- When no longer required, remove stabilized construction roadway and re-grade and repair slopes.

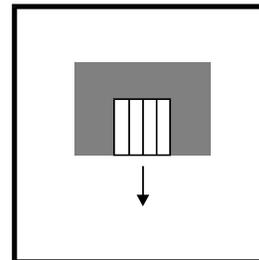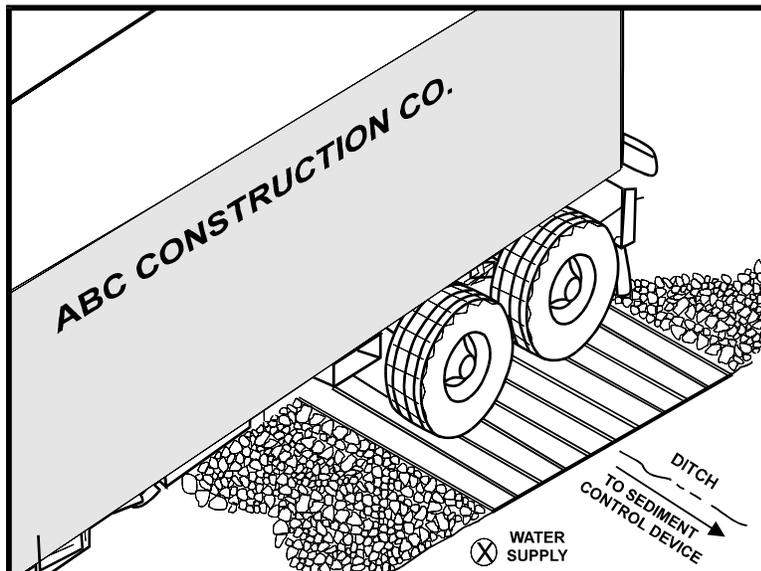

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose A tire wash is an area located at stabilized construction access points to remove sediment from tires and undercarriages, and to prevent sediment from being transported onto public roadways.

Appropriate Applications

- Tire washes may be used on construction sites where dirt and mud tracking onto public roads by construction vehicles may occur.
- This BMP may be implemented on a project-by-project basis with other BMPs when determined necessary and feasible by the Resident Engineer (RE).

Limitations

- Requires a supply of wash water.
- Requires a turnout or doublewide exit to avoid having entering vehicles drive through the wash area.


Standards and Specifications

- Incorporate with a stabilized construction entrance/exit. See BMP TC-1, “Stabilized Construction Entrance/Exit.”
- Construct on level ground when possible, on a pad of coarse aggregate, greater than 75 mm (3 inches) and smaller than 150 mm (6 inches). A geotextile fabric shall be placed below the aggregate.
- Wash rack shall be designed and constructed/manufactured for anticipated traffic loads.
- Provide a drainage ditch that will convey the runoff from the wash area to a sediment trapping device. The drainage ditch shall be of sufficient grade, width, and depth to carry the wash runoff.


- Require all employees, subcontractors, and others that leave the site with mud-caked tires and/or undercarriages to use the wash facility.
 - Implement BMP SC-7, “Street Sweeping and Vacuuming” as needed.
 - Use of constructed or prefabricated steel plate with ribs for entrance/exit access is allowed with written approval of RE.
- Maintenance and Inspection
- Remove accumulated sediment in wash rack and/or sediment trap to maintain system performance.
 - Inspect routinely for damage and repair as needed.

Entrance/Outlet Tire Wash


TC-3

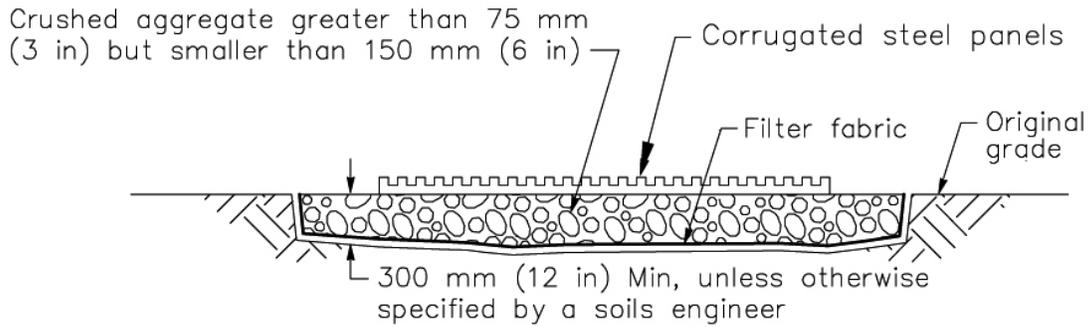

SECTION A-A
NOT TO SCALE


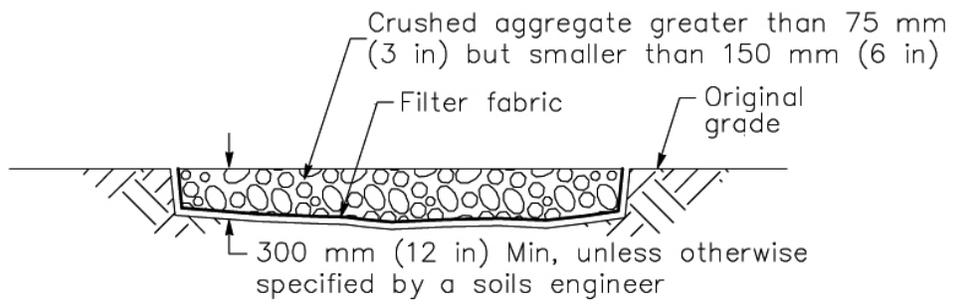


SECTION B-B
NTS

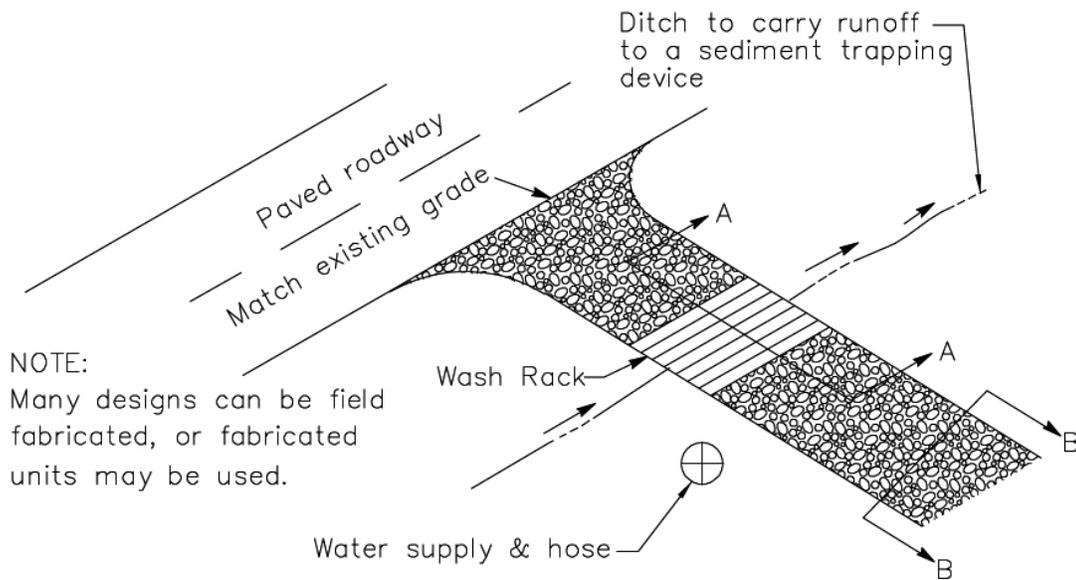

TYPICAL TIRE WASH
NOT TO SCALE



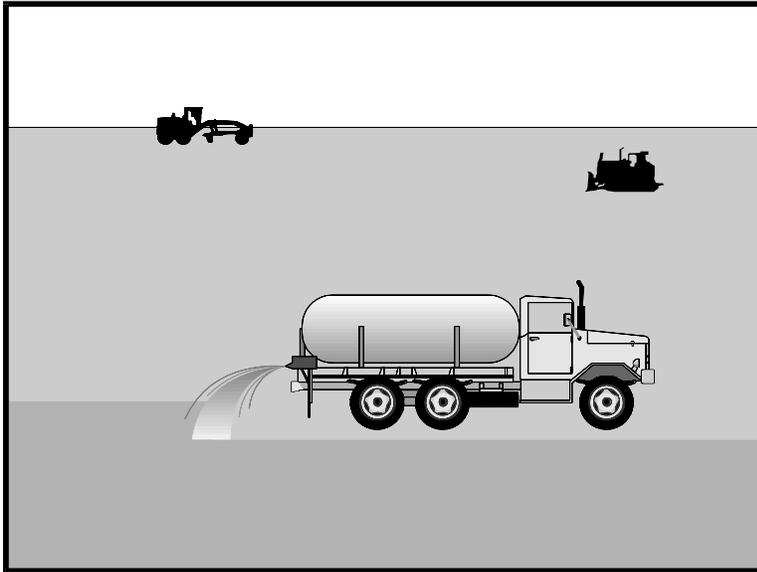

Standard Symbol



- BMP Objectives**
- Soil Stabilization
 - Sediment Control
 - Tracking Control
 - Wind Erosion Control
 - Non-Storm Water Management
 - Materials and Waste Management

Definition and Purpose Wind erosion control consists of applying water and/or other dust palliatives as necessary to prevent or alleviate erosion by the forces of wind. Dust control shall be applied in accordance with Caltrans standard practices. Covering of small stockpiles or areas is an alternative to applying water or other dust palliatives.

- Appropriate Applications**
- This practice is implemented on all exposed soils subject to wind erosion.
- Limitations**
- Effectiveness depends on soil, temperature, humidity and wind velocity.

- Standards and Specifications**
- Water shall be applied by means of pressure-type distributors or pipelines equipped with a spray system or hoses and nozzles that will ensure even distribution.
 - All distribution equipment shall be equipped with a positive means of shutoff.
 - Unless water is applied by means of pipelines, at least one mobile unit shall be available at all times to apply water or dust palliative to the project.
 - If reclaimed water is used, the sources and discharge must meet California Department of Health Services water reclamation criteria and the Regional Water Quality Control Board requirements. Non-potable water shall not be conveyed in tanks or drain pipes that will be used to convey potable water and there shall be no connection between potable and non-potable supplies. Non-potable tanks, pipes and other conveyances shall be marked “NON-POTABLE WATER - DO NOT DRINK.”
 - Materials applied as temporary soil stabilizers and soil binders will also provide wind erosion control benefits.

- Maintenance and Inspection**
- Check areas that have been protected to ensure coverage.

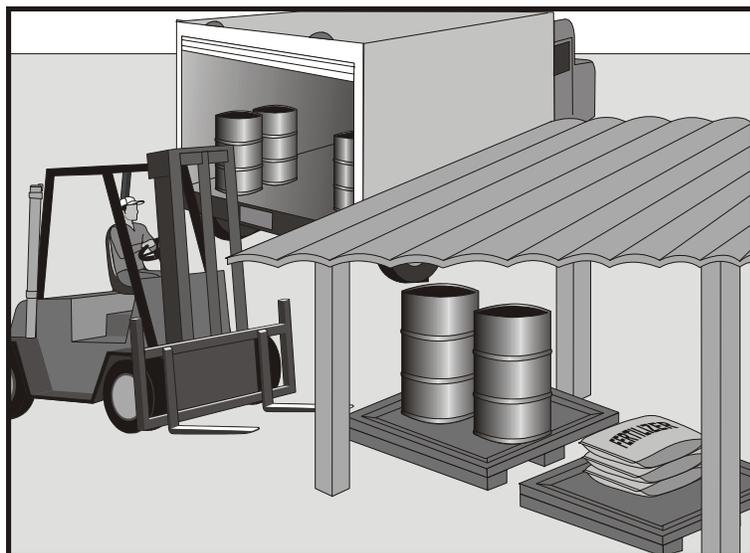

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Procedures and practices for the proper handling and storage of materials in a manner that minimizes or eliminates the discharge of these materials to the storm drain system or to watercourses.

Appropriate Applications These procedures are implemented at all construction sites with delivery and storage of the following:

- Hazardous chemicals such as:
 - Acids,
 - lime,
 - glues,
 - adhesives,
 - paints,
 - solvents, and
 - curing compounds.
- Soil stabilizers and binders.
- Fertilizers.
- Detergents.
- Plaster.
- Petroleum products such as fuel, oil, and grease.
- Asphalt and concrete components.
- Pesticides and herbicides.

- Other materials that may be detrimental if released to the environment.
- Limitations
- Space limitation may preclude indoor storage.
 - Storage sheds must meet building & fire code requirements.

Standards and Specifications

General

- Train employees and subcontractors on the proper material delivery and storage practices.
- Temporary storage area shall be located away from vehicular traffic.
- Material Safety Data Sheets (MSDS) shall be supplied to the Resident Engineer (RE) for all materials stored.

Material Storage Areas and Practices

- Liquids, petroleum products, and substances listed in 40 CFR Parts 110, 117, or 302 shall be stored in approved containers and drums and shall be placed in temporary containment facilities for storage.
- Throughout the rainy season, each temporary containment facility shall have a permanent cover and side wind protection or be covered during non-working days and prior to and during rain events.
- A temporary containment facility shall provide for a spill containment volume able to contain precipitation from a 24-hour, 25-year storm event, plus the greater of 10% of the aggregate volume of all containers or 100% of the capacity of the largest container within its boundary, whichever is greater.
- A temporary containment facility shall be impervious to the materials stored therein for a minimum contact time of 72 hours.
- A temporary containment facility shall be maintained free of accumulated rainwater and spills. In the event of spills or leaks, accumulated rainwater and spills shall be collected and placed into drums. These liquids shall be handled as a hazardous waste unless testing determines them to be non-hazardous. All collected liquids or non-hazardous liquids shall be sent to an approved disposal site.
- Sufficient separation shall be provided between stored containers to allow for spill cleanup and emergency response access.
- Incompatible materials, such as chlorine and ammonia, shall not be stored in the same temporary containment facility.
- Materials shall be stored in their original containers and the original product labels shall be maintained in place in a legible condition. Damaged or otherwise illegible labels shall be replaced immediately.

-
- Bagged and boxed materials shall be stored on pallets and shall not be allowed to accumulate on the ground. To provide protection from wind and rain, throughout the rainy season, bagged and boxed materials shall be covered during non-working days and prior to rain events.
- Stockpiles shall be protected in accordance with BMP WM-3, “Stockpile Management.”
- Minimize the material inventory stored on-site (e.g., only a few days supply).
- Have proper storage instructions posted at all times in an open and conspicuous location.
- Do not store hazardous chemicals, drums, or bagged materials directly on the ground. Place these items on a pallet and when possible, under cover in secondary containment.
- Keep hazardous chemicals well labeled and in their original containers.
- Keep ample supply of appropriate spill clean up material near storage areas.
- Also see BMP WM-6, “Hazardous Waste Management”, for storing of hazardous materials.



Material Delivery Practices

- Keep an accurate, up-to-date inventory of material delivered and stored on-site.
- Employees trained in emergency spill clean-up procedures shall be present when dangerous materials or liquid chemicals are unloaded.

Spill Clean-up

- Contain and clean up any spill immediately.
- If significant residual materials remain on the ground after construction is complete, properly remove and dispose any hazardous materials or contaminated soil.
- See BMP WM-4, “Spill Prevention and Control”, for spills of chemicals and/or hazardous materials.

- Maintenance and Inspection
- Storage areas shall be kept clean, well organized, and equipped with ample clean-up supplies as appropriate for the materials being stored.
 - Perimeter controls, containment structures, covers, and liners shall be repaired or replaced as needed to maintain proper function.
 - Inspect storage areas before and after rainfall events, and at least weekly during other times. Collect and place into drums any spills or accumulated rainwater.

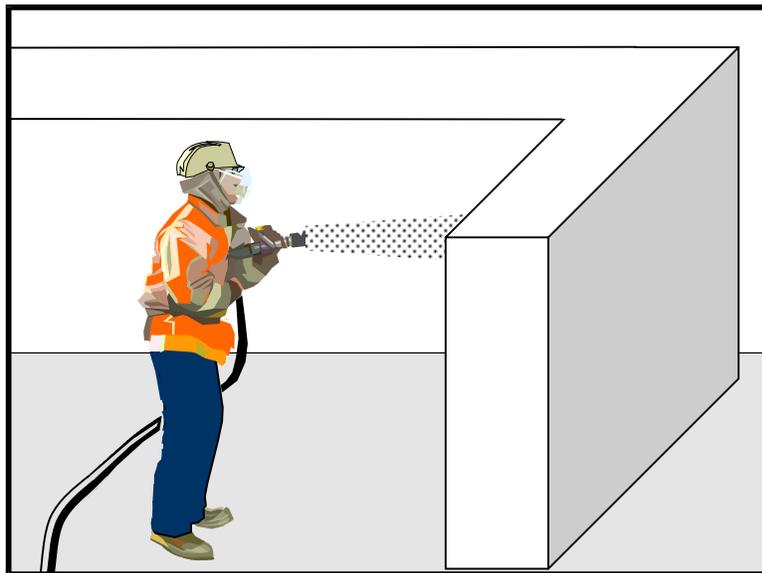

Standard Symbol

BMP Objectives


- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose These are procedures and practices for use of construction material in a manner that minimizes or eliminates the discharge of these materials to the storm drain system or to watercourses.

Appropriate Applications This BMP applies to all construction projects. These procedures apply when the following materials are used or prepared on site:

- Hazardous chemicals such as:
 - Acids,
 - lime,
 - glues,
 - adhesives,
 - paints,
 - solvents, and
 - curing compounds.
- Soil stabilizers and binders.
- Fertilizers.
- Detergents.
- Plaster.
- Petroleum products such as fuel, oil, and grease.
- Asphalt and concrete components.
- Pesticides and herbicides.
- Other materials that may be detrimental if released to the environment.

- Limitations** ■ Safer alternative building and construction products may not be available or suitable in every instance.
- Standards and Specifications** ■ Material Safety Data Sheets (MSDS) shall be supplied to the Resident Engineer (RE) for all materials.
- Latex paint and paint cans, used brushes, rags, absorbent materials, and drop cloths, when thoroughly dry and are no longer hazardous, may be disposed of with other construction debris.
 - Do not remove the original product label, it contains important safety and disposal information. Use the entire product before disposing of the container.
 - Mix paint indoors, or in a containment area. Never clean paintbrushes or rinse paint containers into a street, gutter, storm drain or watercourse. Dispose of any paint thinners, residue and sludge(s), that cannot be recycled, as hazardous waste.
 - For water-based paint, clean brushes to the extent practical, and rinse to a drain leading to a sanitary sewer where permitted, or into a concrete washout pit. For oil-based paints, clean brushes to the extent practical and filter and reuse thinners and solvents.
 - Use recycled and less hazardous products when practical. Recycle residual paints, solvents, non-treated lumber, and other materials.
 - Use materials only where and when needed to complete the construction activity. Use safer alternative materials as much as possible. Reduce or eliminate use of hazardous materials on-site when practical.
 - Do not over-apply fertilizers and pesticides. Prepare only the amount needed. Strictly follow the recommended usage instructions. Apply surface dressings in smaller applications, as opposed to large applications, to allow time for it to work in and to avoid excess materials being carried off-site by runoff.
 - Application of herbicides and pesticides shall be performed by a licensed applicator.
 - Contractors are required to complete the “Report of Chemical Spray Forms” when spraying herbicides and pesticides.
 - Keep an ample supply of spill clean up material near use areas. Train employees in spill clean up procedures.
 - Avoid exposing applied materials to rainfall and runoff unless sufficient time has been allowed for them to dry.
- Maintenance and Inspections** ■ Spot check employees and subcontractors monthly throughout the job to ensure appropriate practices are being employed.

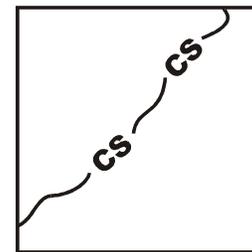

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose	Stockpile management procedures and practices are designed to reduce or eliminate air and storm water pollution from stockpiles of soil, and paving materials such as portland cement concrete (PCC) rubble, asphalt concrete (AC), asphalt concrete rubble, aggregate base, aggregate subbase or pre-mixed aggregate, asphalt binder (so called “cold mix” asphalt) and pressure treated wood.
Appropriate Applications	Implemented in all projects that stockpile soil and other materials.
Limitations	<ul style="list-style-type: none"> ■ None identified
Standards and Specifications	<ul style="list-style-type: none"> ■ Protection of stockpiles is a year-round requirement. ■ Locate stockpiles a minimum of 15 m (50 ft) away from concentrated flows of storm water, drainage courses, and inlets. ■ Implement wind erosion control practices as appropriate on all stockpiled material. For specific information see BMP WE-1, “Wind Erosion Control.” ■ Stockpiles of contaminated soil shall be managed in accordance with BMP WM-7, “Contaminated Soil Management.” ■ Bagged materials should be placed on pallets and under cover.

Protection of Non-Active Stockpiles

Non-active stockpiles of the identified materials shall be protected further as follows:

- ***Soil stockpiles:***

- During the rainy seasons, soil stockpiles shall be covered or protected with soil stabilization measures and a temporary perimeter sediment barrier at all times.
- During the non-rainy season, soil stockpiles shall be covered and protected with a temporary perimeter sediment barrier prior to the onset of precipitation.

- ***Stockpiles of portland cement concrete rubble, asphalt concrete, asphalt concrete rubble, aggregate base, or aggregate subbase:***

- During the rainy season, the stockpiles shall be covered or protected with a temporary perimeter sediment barrier at all times.
- During the non-rainy season, the stockpiles shall be covered or protected with a temporary perimeter sediment barrier prior to the onset of precipitation.

- ***Stockpiles of “cold mix”:***

- During the rainy season, cold mix stockpiles shall be placed on and covered with plastic or comparable material at all times.
- During the non-rainy season, cold mix stockpiles shall be placed on and covered with plastic or comparable material prior to the onset of precipitation.

- ***Stockpiles/Storage of pressure treated wood with copper, chromium, and arsenic or ammonical, copper, zinc, and arsenate:***


- During the rainy season, treated wood shall be covered with plastic or comparable material at all times.
- During the non-rainy season, treated wood shall be covered with plastic or comparable material and shall be placed on pallets prior to the onset of precipitation.

Protection of Active Stockpiles

Active stockpiles of the identified materials shall be protected further as follows:

- All stockpiles shall be covered, stabilized, or protected with a temporary linear sediment barrier prior to the onset of precipitation.
- Stockpiles of “cold mix” shall be placed on and covered with plastic or comparable material prior to the onset of precipitation.

- Maintenance and Inspections
- Repair and/or replace perimeter controls and covers as needed, or as directed by the RE, to keep them functioning properly. Sediment shall be removed when sediment accumulation reaches one-third (1/3) of the barrier height.

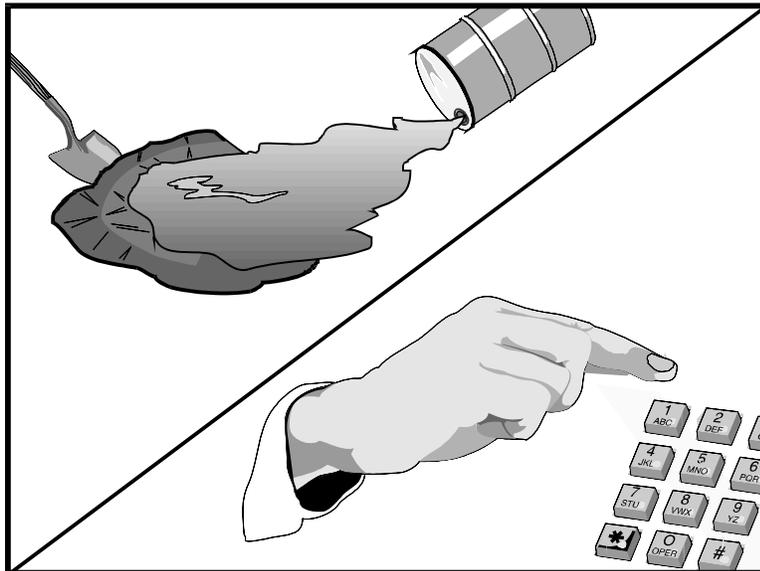

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose These procedures and practices are implemented to prevent and control spills in a manner that minimizes or prevents the discharge of spilled material to the drainage system or watercourses.

Appropriate Application This best management practice (BMP) applies to all construction projects. Spill control procedures are implemented anytime chemicals and/or hazardous substances are stored. Substances may include, but are not limited to:

- Soil stabilizers/binders.
- Dust Palliatives.
- Herbicides.
- Growth inhibitors.
- Fertilizers.
- Deicing/anti-icing chemicals.
- Fuels.
- Lubricants.
- Other petroleum distillates.

To the extent that the work can be accomplished safely, spills of oil, petroleum products, substances listed under 40 CFR parts 110, 117, and 302, and sanitary and septic wastes shall be contained and cleaned up immediately.

Limitations ■ This BMP only applies to spills caused by the contractor.

■ Procedures and practices presented in this BMP are general. Contractor shall identify appropriate practices for the specific materials used or stored on-site.

Standards and Specifications

■ To the extent that it doesn't compromise clean up activities, spills shall be covered and protected from storm water run-on during rainfall.

■ Spills shall not be buried or washed with water.

■ Used clean up materials, contaminated materials, and recovered spill material that is no longer suitable for the intended purpose shall be stored and disposed of in conformance with the special provisions.

■ Water used for cleaning and decontamination shall not be allowed to enter storm drains or watercourses and shall be collected and disposed of in accordance with BMP WM-10, "Liquid Waste Management."

■ Water overflow or minor water spillage shall be contained and shall not be allowed to discharge into drainage facilities or watercourses.

■ Proper storage, clean-up and spill reporting instruction for hazardous materials stored or used on the project site shall be posted at all times in an open, conspicuous and accessible location.

■ Waste storage areas shall be kept clean, well organized and equipped with ample clean-up supplies as appropriate for the materials being stored. Perimeter controls, containment structures, covers and liners shall be repaired or replaced as needed to maintain proper function.

Education

■ Educate employees and subcontractors on what a "significant spill" is for each material they use, and what is the appropriate response for "significant" and "insignificant" spills.

■ Educate employees and subcontractors on potential dangers to humans and the environment from spills and leaks.

■ Hold regular meetings to discuss and reinforce appropriate disposal procedures (incorporate into regular safety meetings).

■ Establish a continuing education program to indoctrinate new employees.

■ The Contractor's Water Pollution Control Manager (WPCM) shall oversee and enforce proper spill prevention and control measures.

Cleanup and Storage Procedures



- Minor Spills
 - Minor spills typically involve small quantities of oil, gasoline, paint, etc., which can be controlled by the first responder at the discovery of the spill.
 - Use absorbent materials on small spills rather than hosing down or burying the spill.
 - Remove the absorbent materials promptly and dispose of properly.
 - The practice commonly followed for a minor spill is:
 - Contain the spread of the spill.
 - Recover spilled materials.
 - Clean the contaminated area and/or properly dispose of contaminated materials.
- Semi-Significant Spills
 - Semi-significant spills still can be controlled by the first responder along with the aid of other personnel such as laborers and the foreman, etc. This response may require the cessation of all other activities.
 - Clean up spills immediately:
 - Notify the project foreman immediately. The foreman shall notify the Resident Engineer (RE).
 - Contain spread of the spill.
 - If the spill occurs on paved or impermeable surfaces, clean up using "dry" methods (absorbent materials, cat litter and/or rags). Contain the spill by encircling with absorbent materials and do not let the spill spread widely.
 - If the spill occurs in dirt areas, immediately contain the spill by constructing an earthen dike. Dig up and properly dispose of contaminated soil.
 - If the spill occurs during rain, cover spill with tarps or other material to prevent contaminating runoff.

■ Significant/Hazardous Spills

- For significant or hazardous spills that cannot be controlled by personnel in the immediate vicinity, the following steps shall be taken:
 - Notify the RE immediately and follow up with a written report.
 - Notify the local emergency response by dialing 911. In addition to 911, the contractor will notify the proper county officials. It is the contractor's responsibility to have all emergency phone numbers at the construction site.
 - Notify the Governor's Office of Emergency Services Warning Center, (805) 852-7550.
 - For spills of federal reportable quantities, in conformance with the requirements in 40 CFR parts 110,119, and 302, the contractor shall notify the National Response Center at (800) 424-8802.
 - Notification shall first be made by telephone and followed up with a written report.
 - The services of a spills contractor or a Haz-Mat team shall be obtained immediately. Construction personnel shall not attempt to clean up the spill until the appropriate and qualified staff have arrived at the job site.
 - Other agencies which may need to be consulted include, but are not limited to, the Fire Department, the Public Works Department, the Coast Guard, the Highway Patrol, the City/County Police Department, Department of Toxic Substances, California Division of Oil and Gas, Cal/OSHA, RWQCB, etc.

Maintenance and Inspection

- Verify weekly that spill control clean up materials are located near material storage, unloading, and use areas.
- Update spill prevention and control plans and stock appropriate clean-up materials whenever changes occur in the types of chemicals used or stored onsite.

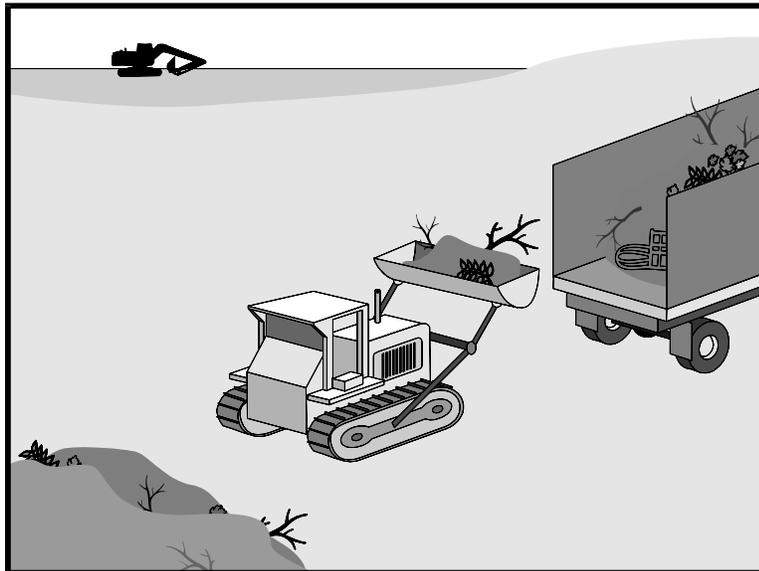

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Solid waste management procedures and practices are designed to minimize or eliminate the discharge of pollutants to the drainage system or to watercourses as a result of the creation, stockpiling, or removal of construction site wastes.

Appropriate Applications Solid waste management procedures and practices are implemented on all construction projects that generate solid wastes.

Solid wastes include but are not limited to:

- Construction wastes including brick, mortar, timber, steel and metal scraps, sawdust, pipe and electrical cuttings, non-hazardous equipment parts, styrofoam and other materials used to transport and package construction materials.
- Highway planting wastes, including vegetative material, plant containers, and packaging materials.
- Litter, including food containers, beverage cans, coffee cups, paper bags, plastic wrappers, and smoking materials, including litter generated by the public.

Limitations ■ Temporary stockpiling of certain construction wastes may not necessitate stringent drainage related controls during the non-rainy season or in desert areas with low rainfall.

Standards and Specifications

Education



- The Contractor's Water Pollution Control Manager (WPCM) shall oversee and enforce proper solid waste procedures and practices.
- Instruct employees and subcontractors on identification of solid waste and hazardous waste.
- Educate employees and subcontractors on solid waste storage and disposal procedures.
- Hold regular meetings to discuss and reinforce disposal procedures (incorporate into regular safety meetings).
- Require that employees and subcontractors follow solid waste handling and storage procedures.
- Prohibit littering by employees, subcontractors, and visitors.
- Wherever possible, minimize production of solid waste materials.

Collection, Storage, and Disposal

- Dumpsters of sufficient size and number shall be provided to contain the solid waste generated by the project and properly serviced.
- Littering on the project site shall be prohibited.
- To prevent clogging of the storm drainage system litter and debris removal from drainage grates, trash racks, and ditch lines shall be a priority.
- Trash receptacles shall be provided in the Contractor's yard, field trailer areas, and at locations where workers congregate for lunch and break periods.
- Construction debris and litter from work areas within the construction limits of the project site shall be collected and placed in watertight dumpsters at least weekly regardless of whether the litter was generated by the Contractor, the public, or others. Collected litter and debris shall not be placed in or next to drain inlets, storm water drainage systems or watercourses.
- Full dumpsters shall be removed from the project site and the contents shall be disposed of outside the highway right-of-way in conformance with the provisions in the Standard Specifications Section 7-1.13.
- Litter stored in collection areas and containers shall be handled and disposed of by trash hauling contractors.
- Construction debris and waste shall be removed from the site every two weeks or as directed by the RE.

- Construction material visible to the public shall be stored or stacked in an orderly manner to the satisfaction of the RE.
- Storm water run-on shall be prevented from contacting stored solid waste through the use of berms, dikes, or other temporary diversion structures or through the use of measures to elevate waste from site surfaces.
- Solid waste storage areas shall be located at least 15 m (50 ft) from drainage facilities and watercourses and shall not be located in areas prone to flooding or ponding.
- Except during fair weather, construction and highway planting waste not stored in watertight dumpsters shall be securely covered from wind and rain by covering the waste with tarps or plastic sheeting or protected in conformance with the applicable Disturbed Soil Area protection section.
- Dumpster washout on the project site is not allowed.
- Notify trash hauling contractors that only watertight dumpsters are acceptable for use on-site.
- Plan for additional containers during the demolition phase of construction.
- Plan for more frequent pickup during the demolition phase of construction.
- Construction waste shall be stored in a designated area approved by the RE.
- Segregate potentially hazardous waste from non-hazardous construction site waste.
- Keep the site clean of litter debris.
- Make sure that toxic liquid wastes (e.g., used oils, solvents, and paints) and chemicals (e.g., acids, pesticides, additives, curing compounds) are not disposed of in dumpsters designated for construction debris.
- Dispose of non-hazardous waste in accordance with Standard Specification 7-1.13, Disposal of Material Outside the Highway Right of Way.
- For disposal of hazardous waste, see BMP WM-6, “Hazardous Waste Management.” Have hazardous waste hauled to an appropriate disposal and/or recycling facility.
- Salvage or recycle useful vegetation debris, packaging and/or surplus building materials when practical. For example, trees and shrubs from land clearing can be converted into wood chips, then used as mulch on graded areas. Wood pallets, cardboard boxes, and construction scraps can also be recycled.

- Maintenance and Inspection
- The WPCM shall monitor onsite solid waste storage and disposal procedures.
 - Police site for litter and debris.

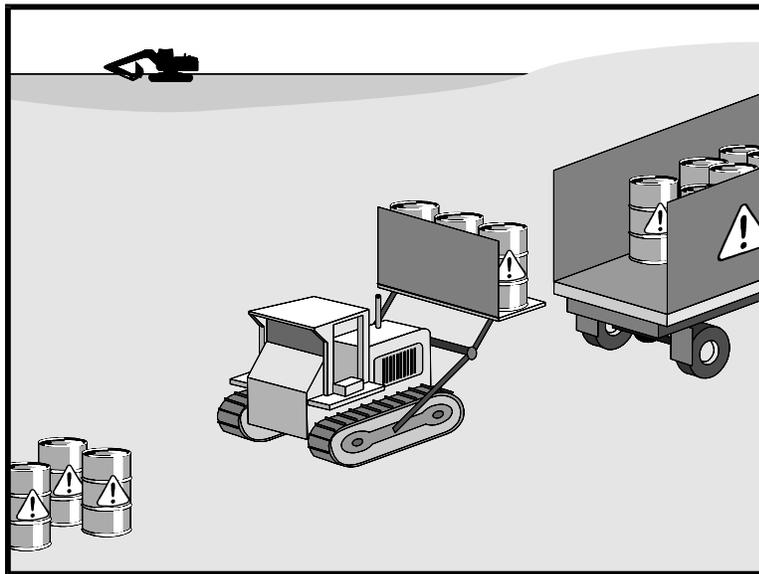

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose These are procedures and practices to minimize or eliminate the discharge of pollutants from construction site hazardous waste to the storm drain systems or to watercourses.

- Appropriate Applications**
- This best management practice (BMP) applies to all construction projects.
 - Hazardous waste management practices are implemented on construction projects that generate waste from the use of:
 - Petroleum Products,
 - Asphalt Products,
 - Concrete Curing Compounds,
 - Pesticides,
 - Acids,
 - Paints,
 - Stains,
 - Solvents,
 - Wood Preservatives,
 - Roofing Tar, or
 - Any materials deemed a hazardous waste in California, Title 22 Division 4.5, or listed in 40 CFR Parts 110, 117, 261, or 302.

- Limitations**
- Nothing in this BMP relieves the Contractor from responsibility for compliance with federal, state, and local laws regarding storage, handling, transportation, and disposal of hazardous wastes.
 - This BMP does not cover aerially deposited lead (ADL) soils. For ADL soils refer to BMP WM-7, “Contaminated Soil Management,” and the project special provisions.

Standards and Specifications

Education

- Educate employees and subcontractors on hazardous waste storage and disposal procedures.
- Educate employees and subcontractors on potential dangers to humans and the environment from hazardous wastes.
- Instruct employees and subcontractors on safety procedures for common construction site hazardous wastes.
- Instruct employees and subcontractors in identification of hazardous and solid waste.
- Hold regular meetings to discuss and reinforce hazardous waste management procedures (incorporate into regular safety meetings).
- The Contractor’s Water Pollution Control Manager (WPCM) shall oversee and enforce proper hazardous waste management procedures and practices.
- Make sure that hazardous waste is collected, removed, and disposed of only at authorized disposal areas.

Storage Procedures

- Wastes shall be stored in sealed containers constructed of a suitable material and shall be labeled as required by Title 22 CCR, Division 4.5 and 49 CFR Parts 172,173, 178, and 179.
- All hazardous waste shall be stored, transported, and disposed as required in Title 22 CCR, Division 4.5 and 49 CFR 261-263.
- Waste containers shall be stored in temporary containment facilities that shall comply with the following requirements:
 - Temporary containment facility shall provide for a spill containment volume able to contain precipitation from a 24-hour, 25 year storm event, plus the greater of 10% of the aggregate volume of all containers or 100% of the capacity of the largest tank within its boundary, whichever is greater.

- Temporary containment facility shall be impervious to the materials stored there for a minimum contact time of 72 hours.
 - Temporary containment facilities shall be maintained free of accumulated rainwater and spills. In the event of spills or leaks accumulated rainwater and spills shall be placed into drums after each rainfall. These liquids shall be handled as a hazardous waste unless testing determines them to be non-hazardous. Non-hazardous liquids shall be sent to an approved disposal site.
 - Sufficient separation shall be provided between stored containers to allow for spill cleanup and emergency response access.
 - Incompatible materials, such as chlorine and ammonia, shall not be stored in the same temporary containment facility.
 - Throughout the rainy season, temporary containment facilities shall be covered during non-working days, and prior to rain events. Covered facilities may include use of plastic tarps for small facilities or constructed roofs with overhangs. A storage facility having a solid cover and sides is preferred to a temporary tarp. Storage facilities shall be equipped with adequate ventilation.
- Drums shall not be overfilled and wastes shall not be mixed.
 - Unless watertight, containers of dry waste shall be stored on pallets.
 - Paint brushes and equipment for water and oil based paints shall be cleaned within a contained area and shall not be allowed to contaminate site soils, watercourses or drainage systems. Waste paints, thinners, solvents, residues, and sludges that cannot be recycled or reused shall be disposed of as hazardous waste. When thoroughly dry, latex paint and paint cans, used brushes, rags, absorbent materials, and drop cloths shall be disposed of as solid waste.
 - Ensure that adequate hazardous waste storage volume is available.
 - Ensure that hazardous waste collection containers are conveniently located.
 - Designate hazardous waste storage areas on site away from storm drains or watercourses and away from moving vehicles and equipment to prevent accidental spills.
 - Minimize production or generation of hazardous materials and hazardous waste on the job site.
 - Use containment berms in fueling and maintenance areas and where the potential for spills is high.



- Segregate potentially hazardous waste from non-hazardous construction site debris.
- Keep liquid or semi-liquid hazardous waste in appropriate containers (closed drums or similar) and under cover.
- Clearly label all hazardous waste containers with the waste being stored and the date of accumulation.
- Place hazardous waste containers in secondary containment.
- Do not allow potentially hazardous waste materials to accumulate on the ground.
- Do not mix wastes.

Disposal Procedures

- Waste shall be disposed of outside the highway right-of-way within 90 days of being generated, or as directed by the Resident Engineer (RE). In no case shall hazardous waste storage exceed requirements in Title 22 CCR, Section 66262.34.
- Waste shall be disposed of by a licensed hazardous waste transporter at an authorized and licensed disposal facility or recycling facility utilizing properly completed Uniform Hazardous Waste Manifest forms.
- A Department of Health Services (DHS) certified laboratory shall sample waste and classify it to determine the appropriate disposal facility.
- Make sure that toxic liquid wastes (e.g., used oils, solvents, and paints) and chemicals (e.g., acids, pesticides, additives, curing compounds) are not disposed of in dumpsters designated for solid waste construction debris.
- Properly dispose of rainwater in secondary containment that may have mixed with hazardous waste.
- Recycle any useful material such as used oil or water-based paint when practical.
- Attention is directed to "Hazardous Material", "Contaminated Material", and "Aerially Deposited Lead" of the contract documents regarding the handling and disposal of hazardous materials.

Maintenance and Inspection

- A foreman and/or construction supervisor shall monitor on-site hazardous waste storage and disposal procedures.
- Waste storage areas shall be kept clean, well organized, and equipped with ample clean-up supplies as appropriate for the materials being stored.
- Storage areas shall be inspected in conformance with the provisions in the contract documents.
- Perimeter controls, containment structures, covers, and liners shall be repaired or replaced as needed to maintain proper function.
- Hazardous spills shall be cleaned up and reported in conformance with the applicable Material Safety Data Sheet (MSDS) and the instructions posted at the project site.
- The National Response Center, at (800) 424-8802, shall be notified of spills of Federal reportable quantities in conformance with the requirements in 40 CFR parts 110, 117, and 302.
- Copy of the hazardous waste manifests shall be provided to the RE.

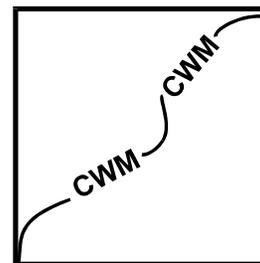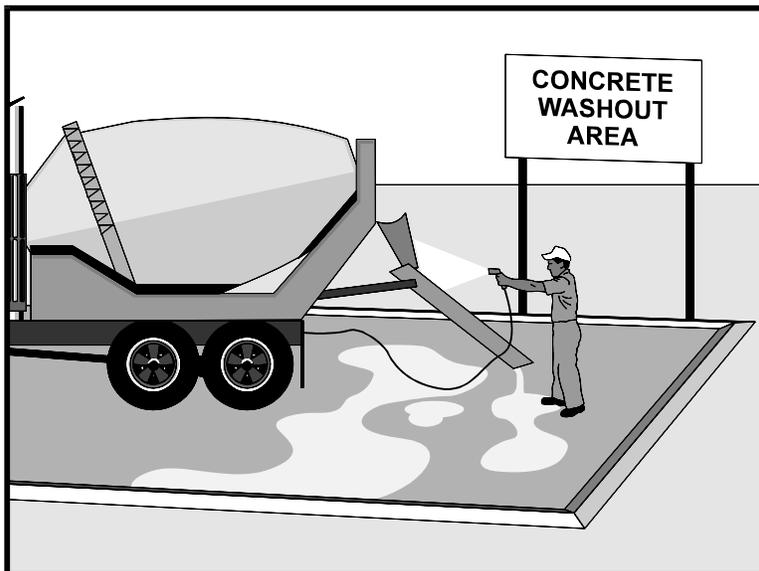

Standard Symbol

BMP Objectives	
<input type="radio"/>	Soil Stabilization
<input type="radio"/>	Sediment Control
<input type="radio"/>	Tracking Control
<input type="radio"/>	Wind Erosion Control
<input checked="" type="radio"/>	Non-Storm Water Management
<input checked="" type="radio"/>	Materials and Waste Management

Definition and Purpose These are procedures and practices that are designed to minimize or eliminate the discharge of concrete waste materials to the storm drain systems or watercourses.

- Appropriate Applications**
- Concrete waste management procedures and practices are implemented on construction projects where concrete is used as a construction material or where concrete dust and debris result from demolition activities.
 - Where slurries containing portland cement concrete (PCC) or asphalt concrete (AC) are generated, such as from sawcutting, coring, grinding, grooving, and hydro-concrete demolition.
 - Where concrete trucks and other concrete-coated equipment are washed on site, when approved by the Resident Engineer (RE). See also NS-8, "Vehicle and Equipment Cleaning."
 - Where mortar-mixing stations exist.

Limitations ■ None identified.

- Standards and Specifications**
- Education**
- Educate employees, subcontractors, and suppliers on the concrete waste management techniques described herein.
 - The Contractor's Water Pollution Control Manager (WPCM) shall oversee and enforce concrete waste management procedures.

Concrete Slurry Wastes

- PCC and AC waste shall not be allowed to enter storm drains or watercourses.

- PCC and AC waste shall be collected and properly disposed of outside the highway right-of-way in conformance with Standard Specifications Section 7-1.13 or placed in a temporary concrete washout facility as shown in the figures on Pages 5 and 6.
- Disposal of hardened PCC and AC waste shall be in conformance with Standard Specifications Section 15-3.02.
- A sign shall be installed adjacent to each temporary concrete washout facility to inform concrete equipment operators to utilize the proper facilities as shown on Page 6.
- A foreman and/or construction supervisor shall monitor onsite concrete working tasks, such as saw cutting, coring, grinding and grooving to ensure proper methods are implemented.
- Do not allow saw-cut PCC slurry to enter storm drains or watercourses. See also BMP NS-3, "Paving and Grinding Operations;" and BMP WM-10, "Liquid Waste Management." Residue from grinding operations shall be picked up by means of a vacuum attachment to the grinding machine. Saw cutting residue shall not be allowed to flow across the pavement, and shall not be left on the surface of the pavement.
- Vacuum slurry residue and dispose in a temporary facility (as described in Onsite Temporary Concrete Washout Facility, Concrete Transit Truck Washout Procedures, below) and allow slurry to dry. Dispose of dry slurry residue in accordance with BMP WM-5, "Solid Waste Management", or, for on-site disposal, in accordance with Standard Specification 15-3.02, Removal Methods.
- Collect and dispose of residue from grooving and grinding operations in accordance with Standard Specifications Section 42-1.02 and 42-2.02.

Onsite Temporary Concrete Washout Facility, Concrete Transit Truck Washout Procedures

- Temporary concrete washout facilities shall be located a minimum of 15 m (50 ft) from storm drain inlets, open drainage facilities, and watercourses, unless determined infeasible by the RE. Each facility shall be located away from construction traffic or access areas to prevent disturbance or tracking.
- A sign shall be installed adjacent to each washout facility to inform concrete equipment operators to utilize the proper facilities. The sign shall be installed as shown on the plans and in conformance with the provisions in Standard Specifications Section 56-2, Roadside Signs.

- Temporary concrete washout facilities shall be constructed above grade or below grade at the option of the Contractor. Temporary concrete washout facilities shall be constructed and maintained in sufficient quantity and size to contain all liquid and concrete waste generated by washout operations.
- Temporary washout facilities shall have a temporary pit or bermed areas of sufficient volume to completely contain all liquid and waste concrete materials generated during washout procedures.
- Perform washout of concrete mixer trucks in designated areas only.
- Wash concrete only from mixer truck chutes into approved concrete washout facility. Washout may be collected in an impermeable bag for disposal.
- Pump excess concrete in concrete pump bin back into concrete mixer truck.
- Concrete washout from concrete pumper bins can be washed into concrete pumper trucks and discharged into designated washout area or properly disposed offsite.
- Once concrete wastes are washed into the designated area and allowed to harden, the concrete shall be broken up, removed, and disposed of per BMP WM-5, "Solid Waste Management", and in conformance with the provisions in Standard Specifications Section 15-3.02, "Removal Methods."

Temporary Concrete Washout Facility Type "Above Grade"

- Temporary concrete washout facility Type "Above Grade" shall be constructed as shown on Page 5 or 6, with a recommended minimum length and minimum width of 3 m (10 ft), but with sufficient quantity and volume to contain all liquid and concrete waste generated by washout operations. The length and width of a facility may be increased, at the Contractor's expense, upon approval from the RE.
- Straw bales, wood stakes, and sandbag materials shall conform to the provisions in BMP SC-9, "Straw Bale Barrier."
- Plastic lining material shall be a minimum of 10-mil polyethylene sheeting and shall be free of holes, tears or other defects that compromise the impermeability of the material.
- Portable delineators shall conform to the provisions in Standard Specifications Section 12-3.04, "Portable Delineators.". The delineator bases shall be cemented to the pavement in the same manner as provided for cementing pavement markers to pavement in Standard Specifications Section 85-1.06, "Placement." Portable delineators shall be applied only to a clean, dry surface.

Temporary Concrete Washout Facility (Type Below Grade)

- Temporary concrete washout facility Type “Below Grade” shall be constructed as shown on page 6, with a recommended minimum length and minimum width of 3m (10 ft). The quantity and volume shall be sufficient to contain all liquid and concrete waste generated by washout operations. The length and width of a facility may be increased, at the Contractor’s expense, upon approval of the RE. Lath and flagging shall be commercial type.
- Plastic lining material shall be a minimum of 10-mil polyethylene sheeting and shall be free of holes, tears or other defects that compromise the impermeability of the material.
- The soil base shall be prepared free of rocks or other debris that may cause tears or holes in the plastic lining material.

Removal of Temporary Concrete Washout Facilities





- When temporary concrete washout facilities are no longer required for the work, as determined by the RE, the hardened concrete shall be removed and disposed of in conformance with the provisions in Standard Specifications Section 15-3.02. Disposal of PCC slurries or liquid waste shall be disposed of outside the highway right-of-way in conformance with provisions of Standard Specifications Section 7-1-13. Materials used to construct temporary concrete washout facilities shall become the property of the Contractor, shall be removed from the site of the work, and shall be disposed of outside the highway right-of-way in conformance with the provisions of the Standard Specifications, Section 7-1.13.
- Holes, depressions or other ground disturbance caused by the removal of the temporary concrete washout facilities shall be backfilled and repaired in conformance with the provisions in Standard Specifications Section 15-1.02, "Preservation of Property."

Maintenance and Inspection

- The Contractor’s Water Pollution Control Manager (WPCM) shall monitor on site concrete waste storage and disposal procedures at least weekly or as directed by the RE.
- The WPCM shall monitor concrete working tasks, such as saw cutting, coring, grinding and grooving daily to ensure proper methods are employed or as directed by the RE.

- Temporary concrete washout facilities shall be maintained to provide adequate holding capacity with a minimum freeboard of 100 mm (4 inches) for above grade facilities and 300 mm (12 inches) for below grade facilities. Maintaining temporary concrete washout facilities shall include removing and disposing of hardened concrete and returning the facilities to a functional condition. Hardened concrete materials shall be removed and disposed of in conformance with the provisions in Standard Specifications Section 15-3.02, "Removal Methods."
- Existing facilities must be cleaned, or new facilities must be constructed and ready for use once the washout is 75% full.
- Temporary concrete washout facilities shall be inspected for damage (i.e. tears in PVC liner, missing sand bags, etc.). Damaged facilities shall be repaired.





Concrete Waste Management

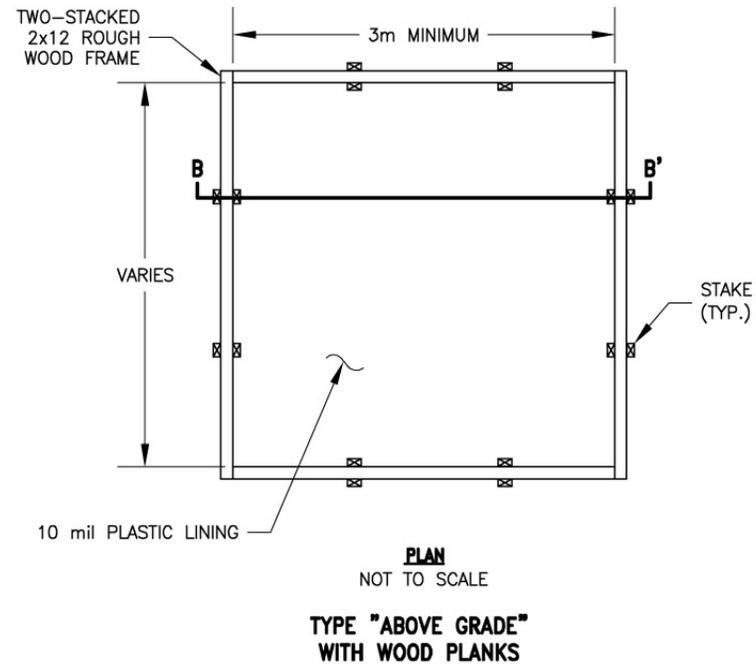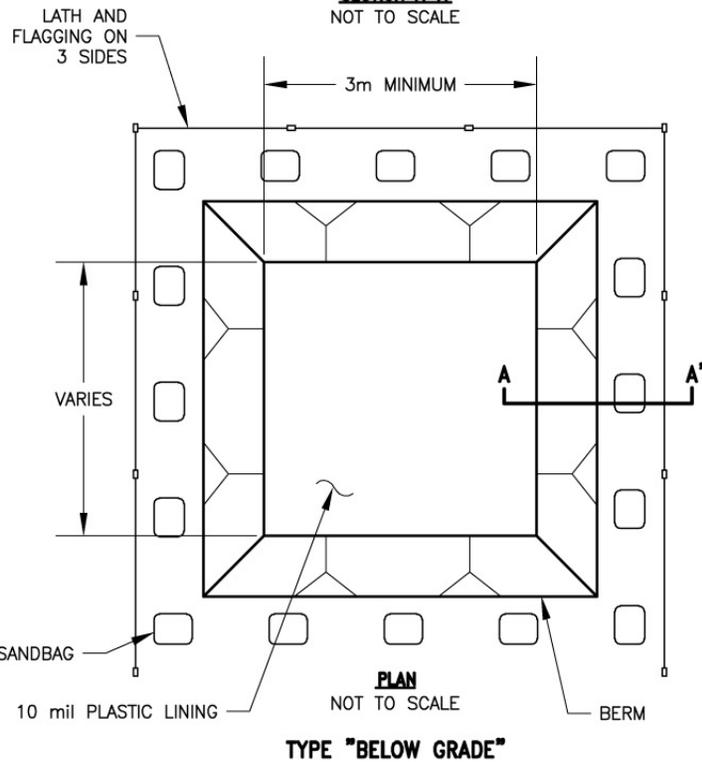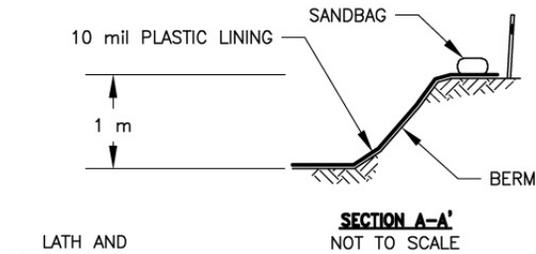

NOTES:

1. ACTUAL LAYOUT DETERMINED IN THE FIELD.
2. THE CONCRETE WASHOUT SIGN (SEE PAGE 6) SHALL BE INSTALLED WITHIN 10 m OF THE TEMPORARY CONCRETE WASHOUT FACILITY.

Concrete Waste Management

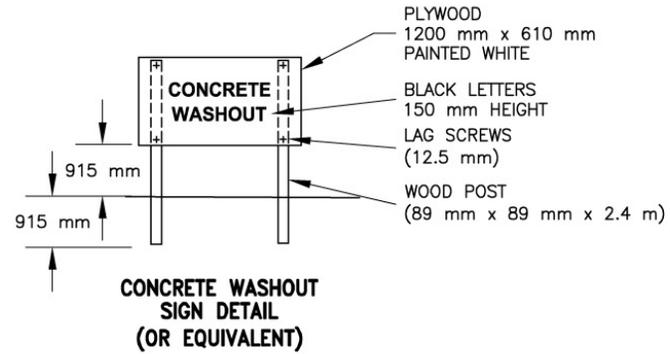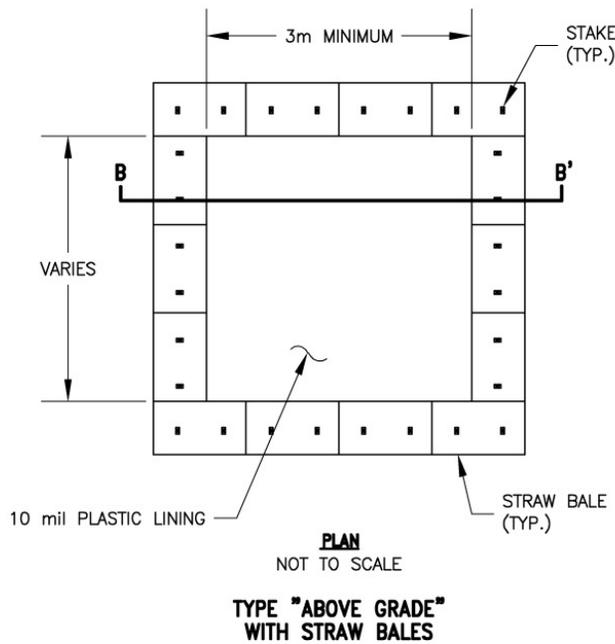



NOTES:

1. ACTUAL LAYOUT DETERMINED IN THE FIELD.
2. THE CONCRETE WASHOUT SIGN (SEE FIG. 4-15) SHALL BE INSTALLED WITHIN 10 m OF THE TEMPORARY CONCRETE WASHOUT FACILITY.

CALTRANS/FIG4-14.DWG SAC 8-14-02



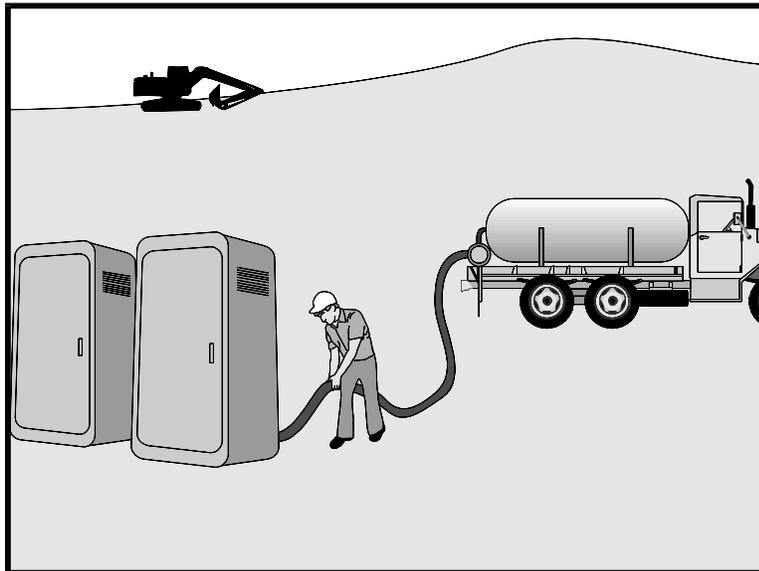

Standard Symbol

BMP Objectives

- Soil Stabilization
- Sediment Control
- Tracking Control
- Wind Erosion Control
- Non-Storm Water Management
- Materials and Waste Management

Definition and Purpose Procedures and practices to minimize or eliminate the discharge of construction site sanitary/septic waste materials to the storm drain system or to watercourses.

Appropriate Applications Sanitary/septic waste management practices are implemented on all construction sites that use temporary or portable sanitary/septic waste systems.

Limitations ■ None identified.

Standards and Specifications *Education*

- Educate employees, subcontractors, and suppliers on sanitary/septic waste storage and disposal procedures.
- Educate employees, subcontractors, and suppliers of potential dangers to humans and the environment from sanitary/septic wastes.
- Instruct employees, subcontractors, and suppliers in identification of sanitary/septic waste.
- Hold regular meetings to discuss and reinforce disposal procedures (incorporate into regular safety meetings).
- Establish a continuing education program to indoctrinate new employees.

Storage and Disposal Procedures

- Temporary sanitary facilities shall be located away from drainage facilities, watercourses, and from traffic circulation. When subjected to high winds or risk.

- Wastewater shall not be discharged or buried within the highway right-of-way.
 - Sanitary and septic systems that discharge directly into sanitary sewer systems, where permissible, shall comply with the local health agency, city, county, and sewer district requirements.
 - If using an on site disposal system, such as a septic system, comply with local health agency requirements.
 - Properly connect temporary sanitary facilities that discharge to the sanitary sewer system to avoid illicit discharges.
 - Ensure that sanitary/septic facilities are maintained in good working order by a licensed service.
 - Use only reputable, licensed sanitary/septic waste haulers.
- Maintenance and Inspection
- The Contractor's Water Pollution Control Manager (WPCM) shall monitor onsite sanitary/septic waste storage and disposal procedures at least weekly.
