OCCIDENTAL OF ELK HILLS INC

311-2G

Event: WELL MAINT - RIG
Event End:
Sec. Reason:

Ground Elev: 853.0ft
KB to Ground: 17.0ft
Datum: ORIGINAL KB @ 870.00ft (default)
API No.: 0402958720

Wellbore: ORIGINAL HOLE
Top TMD: 17.0ft
PBMD: 7,417.0ft
Btm TMD: 7,635.0ft
Spud Date: 2/1/1983 00:00
BH Coord X: 6,151,113.24uss ftBH Coord Y: 2,286,489.95uss

Casing Shoes (ft) | Schematic (7/30/2009) | Openings Top/Btm/Type/Status

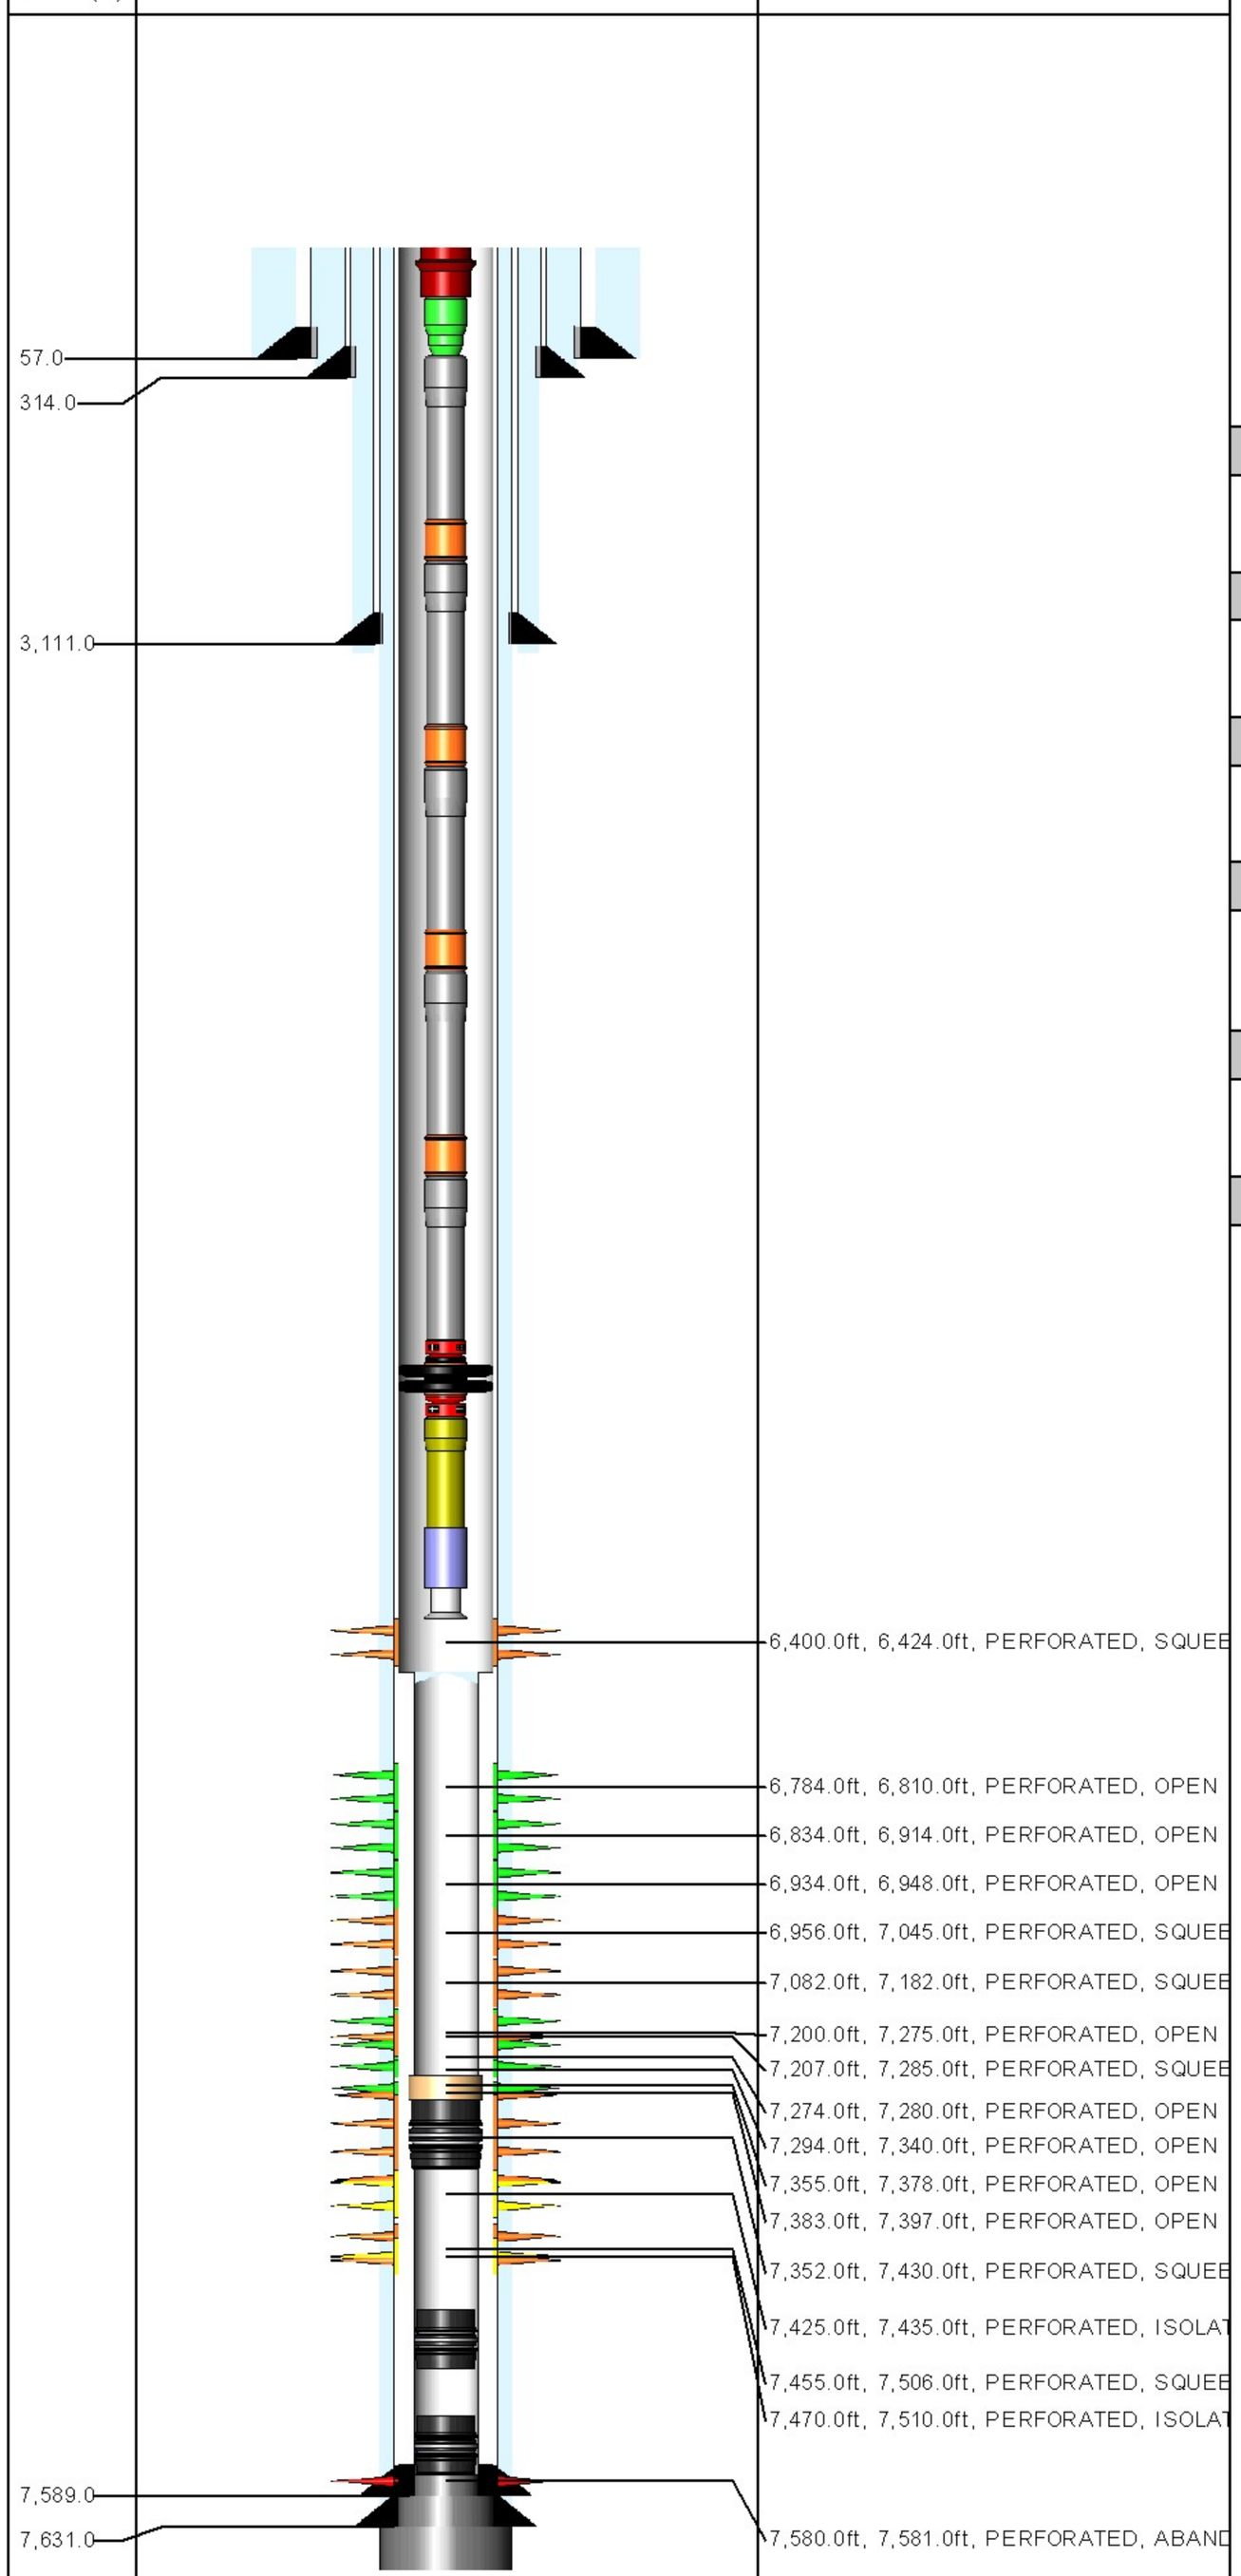

TUBING STRING Report Date: 5/22/2008 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	17.0	17.7
FATNIP	17.7	18.4
CAS	18.4	2,208.4
GLM-V	2,208.4	2,217.1
CAS	2,217.1	3,970.1
GLM-V	3,970.1	3,978.8
CAS	3,978.8	5,355.9
GLM-V	5,355.9	5,364.5
CAS	5,364.5	6,302.8
GLM-V	6,302.8	6,311.4
CAS	6,311.4	6,374.0
PKR	6,374.0	6,378.1
PUPJNT	6,378.1	6,384.2
NOGO	6,384.2	6,385.5
BELCOL	6,385.5	6,385.9

PLUG BACK Report Date: 1/19/2005 00:00

Component	Top MD (ft)	Btm MD (ft)
FILL	7,333.0	7,417.0

PLUG BACK Report Date: 2/2/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-RET	7,417.0	7,419.5

PLUG BACK Report Date: 5/7/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-DR	7,567.0	7,569.0

PLUG BACK Report Date: 10/19/1996 00:00

Component	Top MD (ft)	Btm MD (ft)
CR-PRM	7,575.0	7,577.0
CEMENT	7,577.0	7,589.0

PLUG BACK Report Date: 3/11/1983 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,589.0	7,631.0

PLUG BACK Report Date: 3/11/1983 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,631.0	7,635.0

CONDUCTOR CASING Report Date: 2/10/1983 00:00

Item Description	Btm MD(ft)
CASING JOINT(S) 20 in,	57.0

SURFACE CASING Report Date: 2/17/1983 00:00

Item Description	Btm MD(ft)
CASING JOINT(S) 13.375 in, , H-40, 48	314.0

INTERMEDIATE CASING Report Date: 2/21/1983 00:00

Item Description	Btm MD (ft)
CASING JOINT(S) 9.625 in, , K-55, 40	3,111.0

PRODUCTION CASING Report Date: 3/11/1983 00:00

Item Description	Btm MD (ft)
CASING JOINT(S) 7 in, , N-80, 26	83.0
CASING JOINT(S) 7 in, , K-55, 23	5,036.0
CASING JOINT(S) 7 in, , K-55, 26	6,654.0
CASING JOINT(S) 7 in, , N-80, 26	7,631.0

LINER Report Date: 10/16/1996 00:00

Item Description	Btm MD (ft)
LINER HANGER 6.276 in, , P-110, 18	6,529.0
CASING JOINT(S) 5 in, , P-110, 18	7,589.0

S/T/R: 2G/31S/24E (WELL: 311-2G)

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 475cf
Hole Size: 17-1/2"
Top Job:
Rtns to Sfc: YES
TOC:
- - -
Int. Csg. Cmt Vol.: 1430cf
Hole Size: 12-1/4"
Top Job:
Rtns to Sfc: YES
TOC:
- - -
Prod Csg. Cmt Vol.: 1880cf
Hole Size: 8-3/4"
Rtns to Sfc: YES
TOC:
- - -
Liner Cmt Vol.: landed
Hole Size:

Top of Formation:
UBA 6932'
BLW: 7510'

Volume Behind Pipe
1.3 Yield Assumed on
Theoretical Calculations
