OCCIDENTAL OF ELK HILLS INC

316X-34S

Event: WELL MAINT - RIGLESS
Event End:
Sec. Reason:

Ground Level: 927.8ft
Datum: ORIGINAL KB @ 947.80ft (default)
API No.: 0403017149

Wellbore: ORIGINAL HOLE
PBMD: 7,349.0ft
Btm TMD: 7,450.0ft
Spud Date: 12/20/2000 00:00
BH Coord X: 6,145,515.32uss ft
BH Coord Y: 2,287,928.30uss ft

Casing Shoes (ft) | Schematic (7/30/2009) | Openings Top/Btm/Type/Status

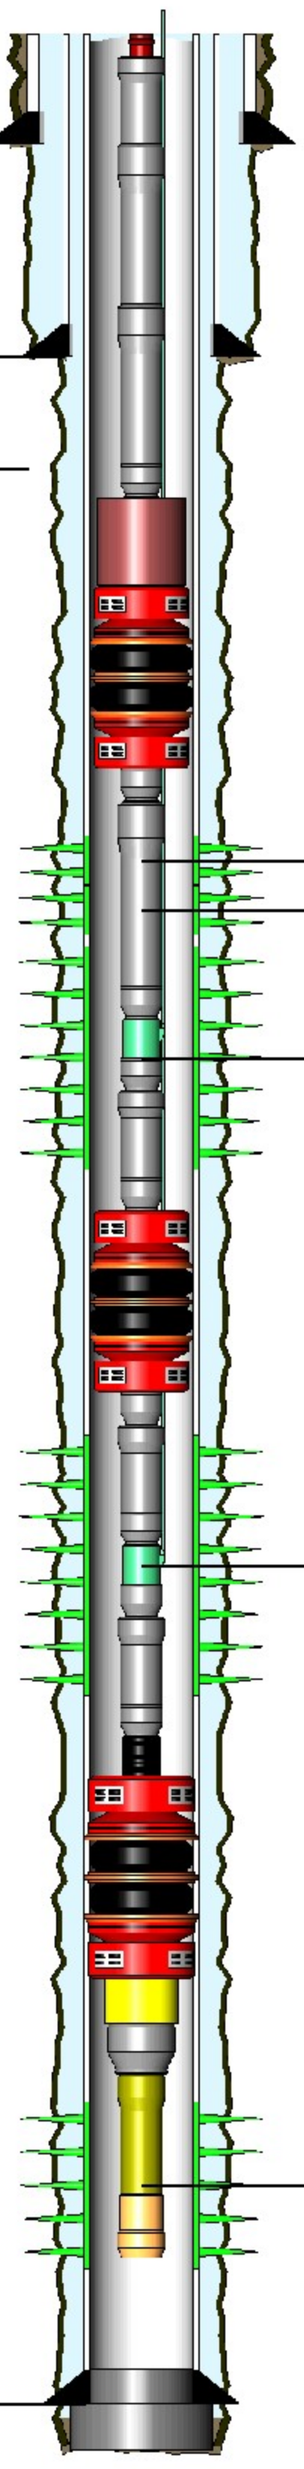

965.0
80.0
7,438.0

6,800.0ft, 6,810.0ft, PERFORATED, OPEN
6,813.0ft, 6,902.0ft, PERFORATED, OPEN
6,913.0ft, 6,990.0ft, PERFORATED, OPEN
7,016.0ft, 7,160.0ft, PERFORATED, OPEN
7,176.0ft, 7,254.0ft, PERFORATED, OPEN

TUBING STRING Report Date: 3/12/2001 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	20.0	21.0
TBGJNT	21.0	39.2
TBGJNT	39.2	6,694.8
XO	6,694.8	6,695.1
ON-OFF	6,695.1	6,696.7
PKR-S	6,696.7	6,700.7
XO	6,700.7	6,701.5
TBGJNT	6,701.5	6,951.4
XO	6,951.4	6,952.2
INJM-V	6,952.2	6,961.2
XO	6,961.2	6,961.6
TBGJNT	6,961.6	6,993.3
XO	6,993.3	6,994.1
PKR-S	6,994.1	7,001.4
XO	7,001.4	7,002.2
TBGJNT	7,002.2	7,121.3
XO	7,121.3	7,122.1
INJM-V	7,122.1	7,131.7
XO	7,131.7	7,132.0
TBGJNT	7,132.0	7,163.2
XO	7,163.2	7,164.0
SA	7,164.0	7,165.0

PACKER ASSEMBLY (PERMANENT) Report Date: 3/16/2001 00:00

Component	Top MD (ft)	Btm MD (ft)
PKR-S	7,165.0	7,168.9
MOEXT	7,168.9	7,174.5
XO	7,174.5	7,175.5
PUPJNT	7,175.5	7,177.6
WLREG	7,177.6	7,178.1

PLUG BACK Report Date: 1/7/2001 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,349.0	7,438.0

PLUG BACK Report Date: 1/6/2001 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,438.0	7,450.0

CONDUCTOR CASING Report Date: 12/19/2000 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	14.000			20.0	60.0

SURFACE CASING Report Date: 12/22/2000 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	36.00	20.0	916.9
	9.625	K-55	36.00	916.9	916.9
CASING JOINT(S)	9.625	K-55	36.00	916.9	963.9
FLOAT SHOE	9.625	K-55	36.00	963.9	965.0

PRODUCTION CASING Report Date: 1/6/2001 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	20.0	6,655.0
FLAG JOINT	7.000	N-80	26.00	6,655.0	6,677.3
CASING JOINT(S)	7.000	N-80	26.00	6,677.3	7,346.1
FLOAT COLLAR	7.000		26.00	7,346.1	7,348.0
CASING JOINT(S)	7.000	N-80	26.00	7,348.0	7,436.2
FLOAT SHOE	7.000		26.00	7,436.2	7,438.0

Well: 316X-34S S/T/R: 34S/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 532 cf
Hole Size: 12.25"
Top Job: No
Rtns to Sfc: 79 cf
TOC: Sfc
- - -

Interm Csg. Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -

Prod. Csg. Cmt Vol.: 1718 cf
Hole Size: 8.75"
Top Job: No
Rtns to Sfc: 128 cf
TOC: Sfc

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TTOC:
- - -
Top of Formation:
UBA: 6797'
BLW: 7344'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
