OCCIDENTAL OF ELK HILLS INC

342-2G

Event: WELL MAINT - RIG
Event End: 10/4/2008 00:00
Sec. Reason:
End Status: FINISHED - SUCCESS
Well Classification: DEVELOPMENT

Ground Level: 882.5ft
Datum: ORIGINAL KB @ 891.51ft (default)
API No.: 0402927982

Wellbore: ORIGINAL HOLE
PBMD: 7,140.0ft
Btm TMD: 7,959.0ft
Spud Date: 8/1/1949 00:00
BH Coord X: 6,153,068.19uss ft
BH Coord Y: 2,285,612.93uss ft

Casing Shoes (ft) | Schematic (10/1/2008) | Openings Top/Btm/Type/Status

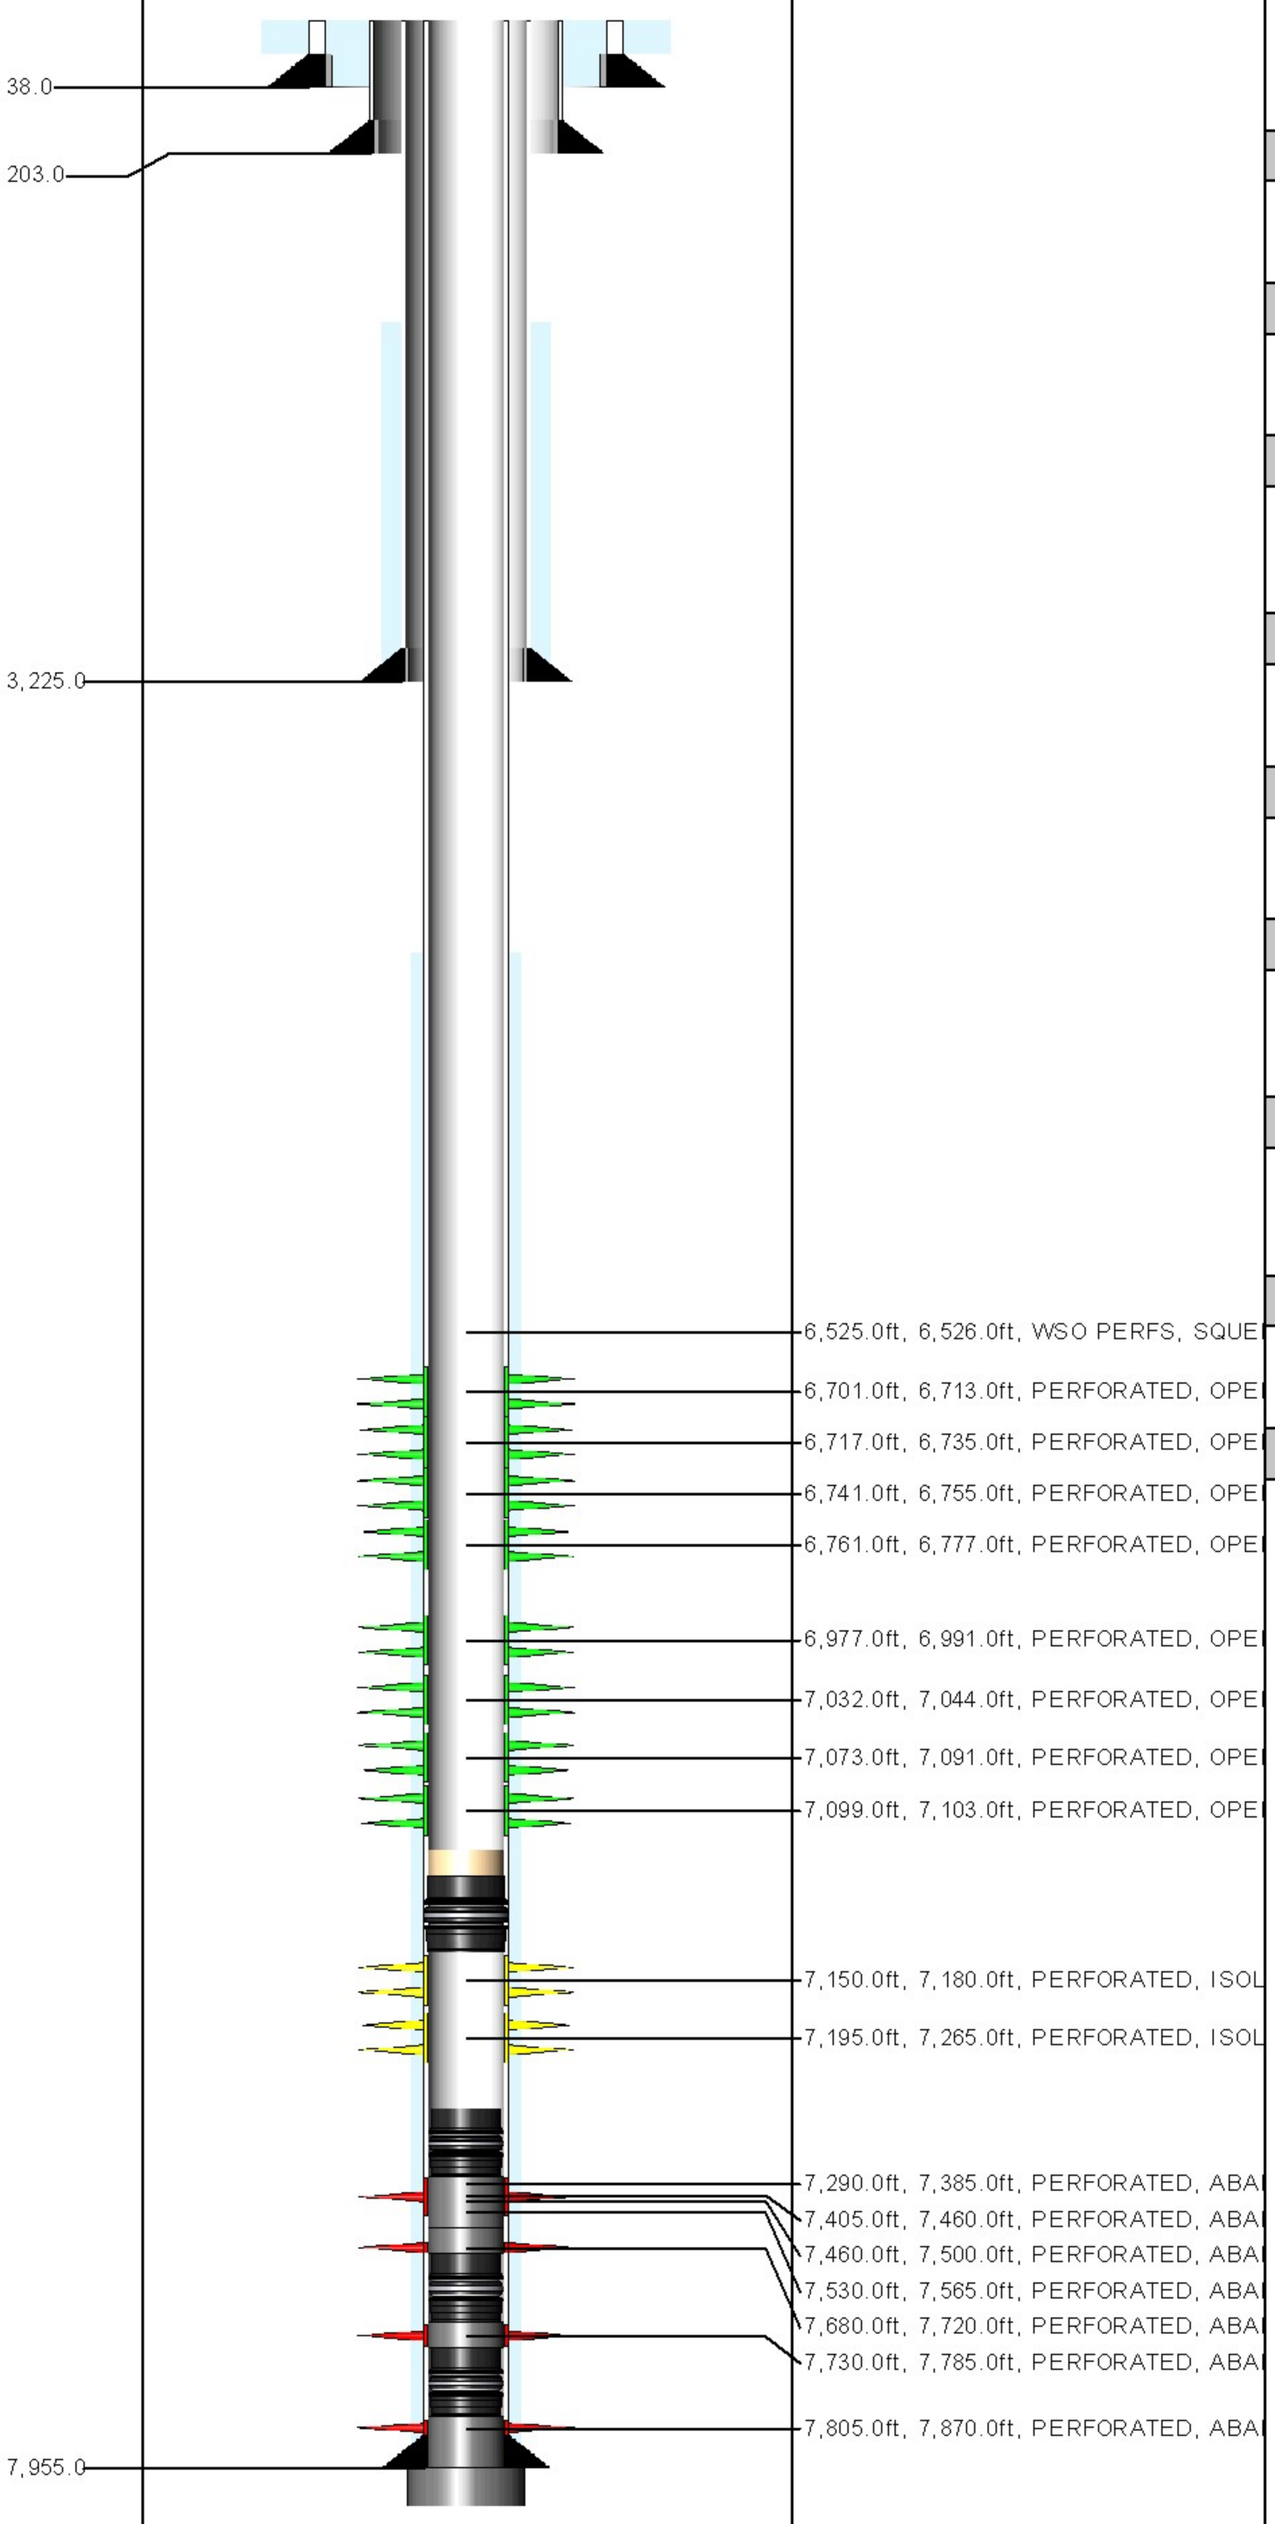

ESP ASSEMBLY Report Date: 5/16/2008 00:00

Component	Top MD (ft)	Btm MD (ft)
TH	9.0	9.6
PUPJNT	9.6	11.6
TBGJNT	11.6	6,578.7
ESPPMP	6,578.7	6,587.0
ESPPMP	6,587.0	6,596.1
ESPINT	6,596.1	6,599.7
ESPPRT	6,599.7	6,607.9
ESPMTR	6,607.9	6,631.7
ESPSEN	6,631.7	6,633.6
XO	6,633.6	6,634.3
ACH	6,634.3	6,665.7
BULPLG	6,665.7	6,666.2

PLUG BACK Report Date: 4/19/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
SAND	7,135.0	7,140.0

PLUG BACK Report Date: 4/17/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-RET	7,140.0	7,144.5

PLUG BACK Report Date: 8/6/1989 00:00

Component	Top MD (ft)	Btm MD (ft)
CR-PRM	7,282.0	7,284.0
CEMENT	7,284.0	7,502.0

PLUG BACK Report Date: 1/3/1950 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,502.0	7,627.0

PLUG BACK Report Date: 12/27/1949 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,627.0	7,722.0

PLUG BACK Report Date: 12/24/1949 00:00

Component	Top MD (ft)	Btm MD (ft)
CR-PRM	7,722.0	7,724.0
CEMENT	7,724.0	7,789.0

PLUG BACK Report Date: 12/19/1949 00:00

Component	Top MD (ft)	Btm MD (ft)
CR-PRM	7,789.0	7,791.0
CEMENT	7,791.0	7,900.0

PLUG BACK Report Date: 12/17/1949 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,900.0	7,955.0

PLUG BACK Report Date: 12/14/1949 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,955.0	7,959.0

CONDUCTOR CASING Report Date: 8/1/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	26.000			9.0	38.0

SURFACE CASING Report Date: 10/13/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	16.000	H-40	65.00	9.0	203.0

INTERMEDIATE CASING Report Date: 10/19/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	10.750	J-55	45.50	9.0	75.0
CASING JOINT(S)	10.750	J-55	40.50	75.0	1,923.0
CASING JOINT(S)	10.750	J-55	45.50	1,923.0	3,225.0

PRODUCTION CASING Report Date: 12/14/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	9.0	63.0
CASING JOINT(S)	7.000	N-80	23.00	63.0	5,849.0
CASING JOINT(S)	7.000	N-80	26.00	5,849.0	7,955.0

Well: 342-2G S/T/R: 2G/31S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 400 sx
Hole Size: 22"
Top Job: No
Rtns to Sfc: Good
TOC: Sfc
- - -

Interm Csg. Cmt Vol.: 600 sx
Hole Size: 15"
Top Job: No
Rtns to Sfc:
TTOC: 1400'
- - -

Prod. Csg. Cmt Vol.: 650 sx
Hole Size: 9.625"
Top Job: No
Rtns to Sfc:
TTOC: 4600'
- - -

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TTOC:
- - -
Top of Formation:
UBA: 7290'
BLW: 7899'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
