OCCIDENTAL OF ELK HILLS INC

355-35S

Event: WELL MAINT - RIGLESS
Event End: 12/1/2005 00:00
Sec. Reason:

Ground Level: 693.7ft
Datum: ORIGINAL KB @ 708.72ft (default)
API No.: 0402955740

Wellbore: ORIGINAL HOLE
PBMD: 7,240.0ft
Btm TMD: 7,725.0ft
Spud Date: 6/1/1977 00:00
BH Coord X: 6,153,369.23uss ft
BH Coord Y: 2,288,768.60uss ft

Casing Shoes (ft) | Schematic (1/1/2006) | Openings Top/Btm/Type/Status

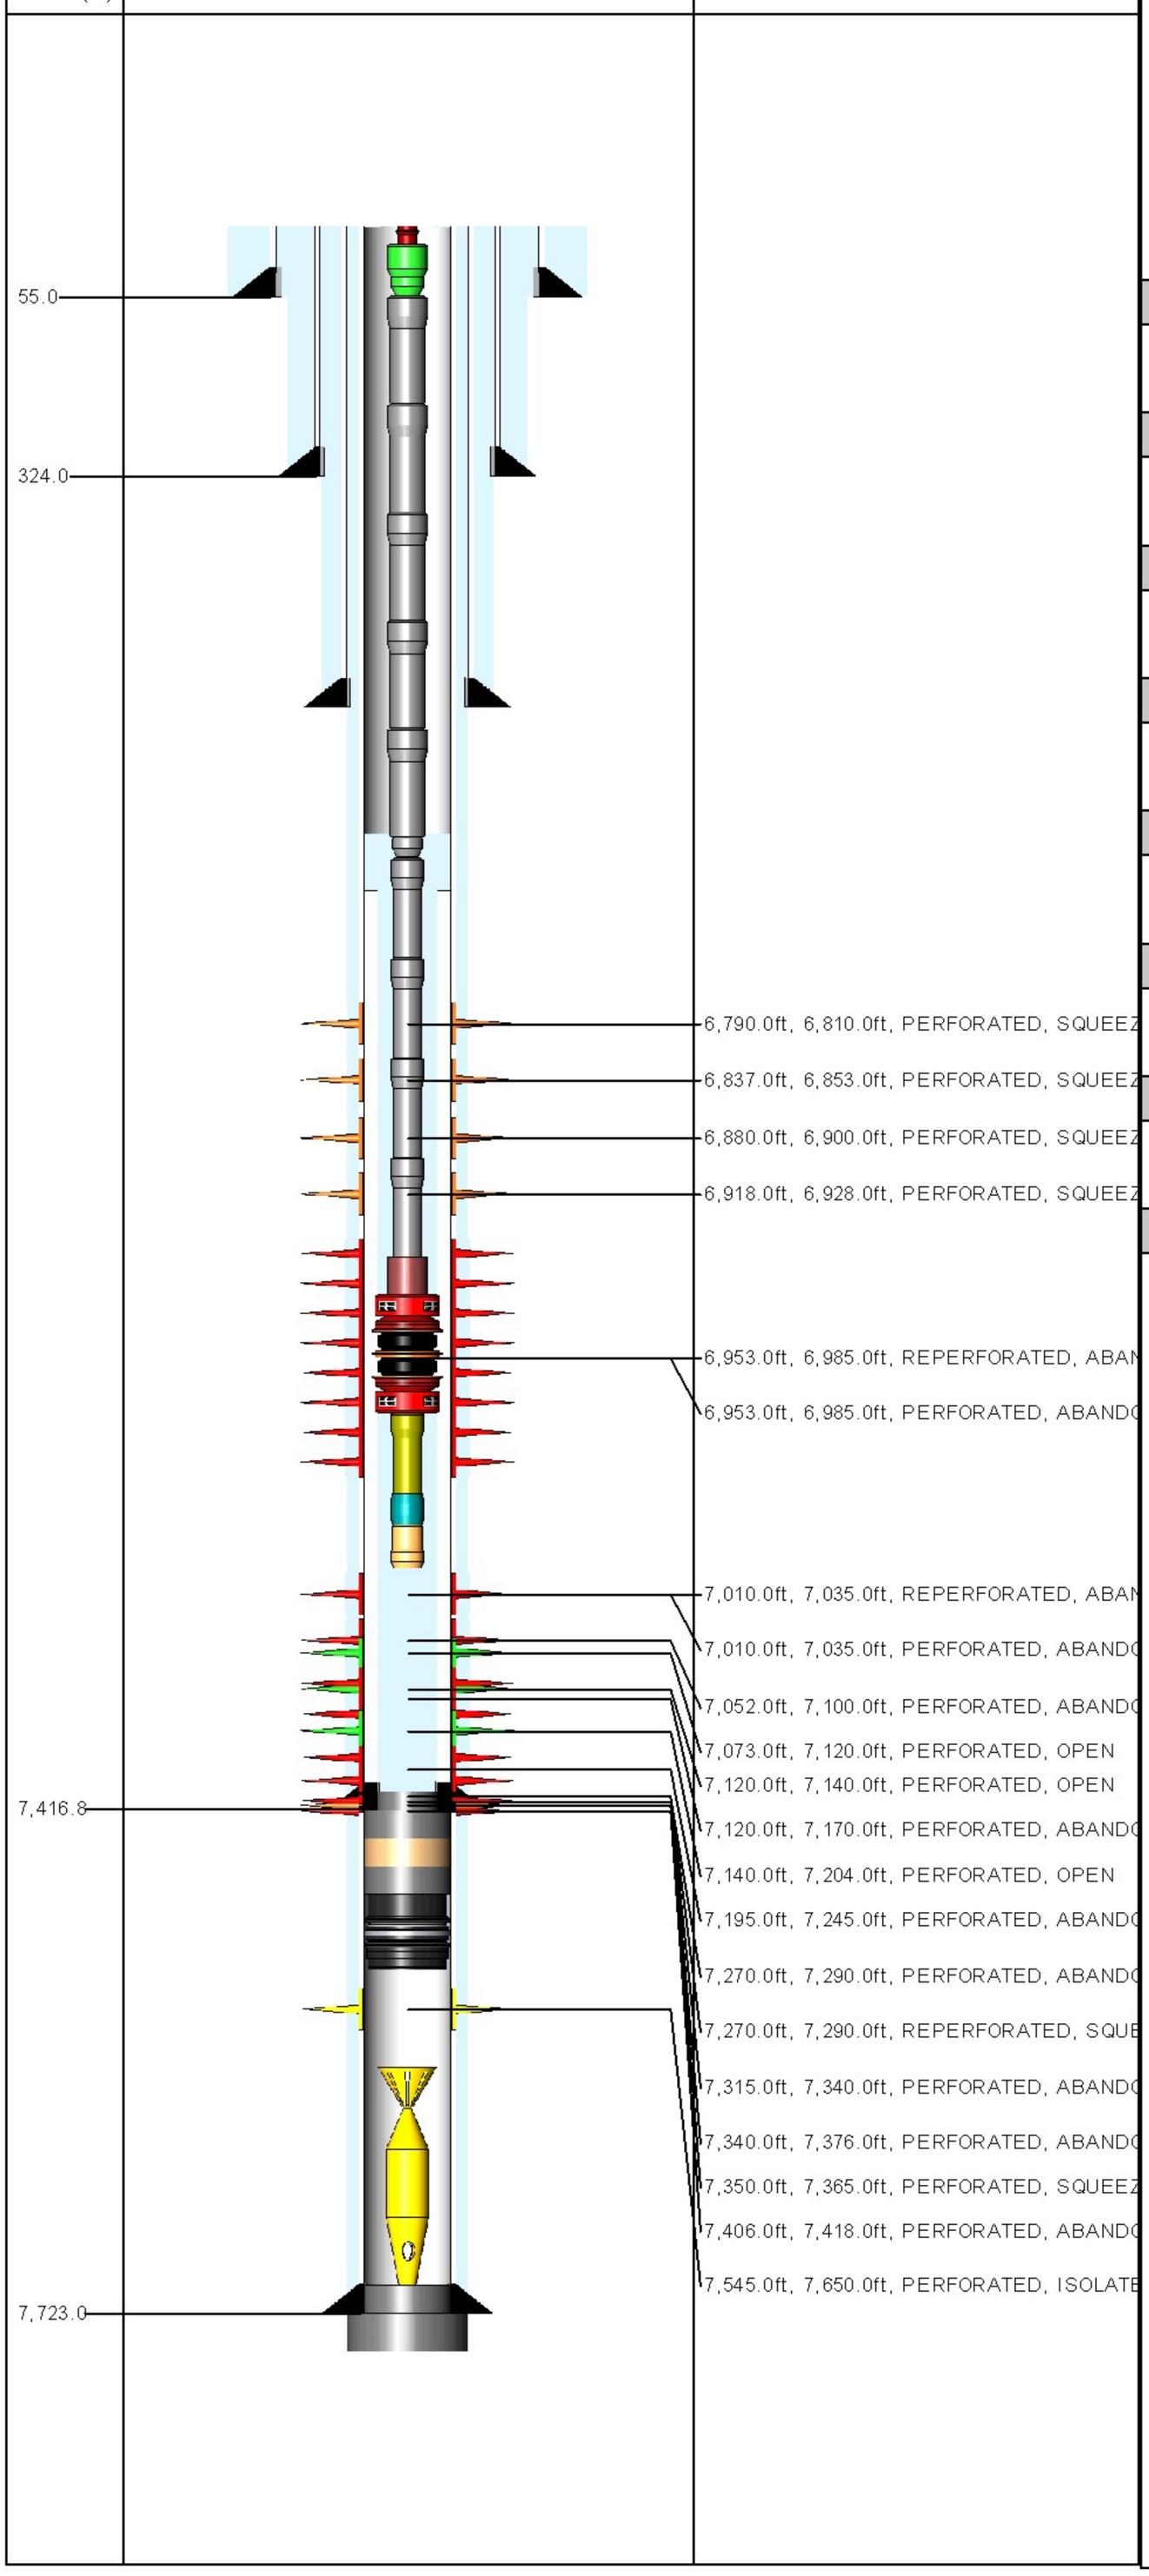

TUBING STRING Report Date: 5/5/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	15.0	15.5
FATNIP	15.5	16.2
TBGJNT	16.2	6,620.8
XO	6,620.8	6,621.9
TBGJNT	6,621.9	6,971.7
ON-OFF	6,971.7	6,973.1
PKR-S	6,973.1	6,976.8
PUPJNT	6,976.8	6,987.1
PNIP-O	6,987.1	6,988.2
WLREG	6,988.2	6,988.6

PLUG BACK Report Date: 5/1/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,240.0	7,417.0

PLUG BACK Report Date: 12/1/1997 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,417.0	7,476.0

PLUG BACK Report Date: 10/25/1983 00:00

Component	Top MD (ft)	Btm MD (ft)
FILL	7,476.0	7,479.0

PLUG BACK Report Date: 1/6/1980 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,479.0	7,480.0

PLUG BACK Report Date: 1/6/1980 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-DR	7,480.0	7,482.0

PLUG BACK Report Date: 1/5/1980 00:00

Component	Top MD (ft)	Btm MD (ft)
JUNK	7,674.0	7,676.0

PLUG BACK Report Date: 7/21/1977 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,676.0	7,723.0

PLUG BACK Report Date: 7/20/1977 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,723.0	7,725.0

CONDUCTOR CASING Report Date: 6/1/1977 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			15.0	55.0

SURFACE CASING Report Date: 6/27/1977 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	H-40	48.00	15.0	282.5
FLOAT COLLAR	13.375	H-40	48.00	282.5	282.6
CASING JOINT(S)	13.375	H-40	48.00	282.6	322.8
FLOAT SHOE	13.375	H-40	48.00	322.8	324.0

INTERMEDIATE CASING Report Date: 7/1/1977 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	N-80	40.00	15.0	3,163.4
FLOAT COLLAR	9.625	N-80	40.00	3,163.4	3,163.4
CASING JOINT(S)	9.625	N-80	40.00	3,163.4	3,205.8
FLOAT SHOE	9.625	N-80	40.00	3,205.8	3,207.0

PRODUCTION CASING Report Date: 7/20/1977 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	K-55	26.00	15.0	78.8
CASING JOINT(S)	7.000	K-55	23.00	78.8	5,183.6
CASING JOINT(S)	7.000	K-55	26.00	5,183.6	6,377.4
FLAG JOINT	7.000	K-55	26.00	6,377.4	6,392.8
CASING JOINT(S)	7.000	K-55	26.00	6,392.8	7,677.2
FLOAT COLLAR	7.000	K-55	26.00	7,677.2	7,678.6
CASING JOINT(S)	7.000	K-55	26.00	7,678.6	7,720.7
FLOAT SHOE	7.000	K-55	26.00	7,720.7	7,723.0

LINER Report Date: 11/29/1997 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
LINER HANGER	6.276	N-80	18.00	6,692.0	6,700.0
CASING JOINT(S)	5.000	N-80	18.00	6,700.0	7,335.5
	5.000	N-80	18.00	7,335.5	7,336.2
FLOAT COLLAR	5.000	N-80	18.00	7,336.2	7,336.8
CASING JOINT(S)	5.000	N-80	18.00	7,336.8	7,416.0
FLOAT SHOE	5.000	N-80	18.00	7,416.0	7,417.0

Well: 355-35S S/T/R: 36/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 400 cf
Hole Size: 17.5
Top Job: no
Rtns to Sfc: 37 cf
TOC: sfc
- - -

Interm Csg. Cmt Vol.: 1605 cf
Hole Size: 12.25
Top Job: no
Rtns to Sfc: 180 cf
TOC: sfc
- - -

Prod. Csg. Cmt Vol.: 1800 cf
Hole Size: 8.75
Top Job: no
Rtns to Sfc: no
TOC: sfc
- - -

Liner Cmt Vol.: 101 cf
Hole Size: 6.0
Top Job: no
Rtns to Sfc: no
TOC: below top of liner
- - -
Top of Formation:
UBA: 6947'
BLW: 7417'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
JEP
