OCCIDENTAL OF ELK HILLS INC

374X-35S

Event: WELL MAINT - RIGLESS
Event End:
Sec. Reason:

Ground Level: 593.0ft
Datum: ORIGINAL KB @ 607.00ft (default)
API No.: 0402960699

Wellbore: ORIGINAL HOLE
PBMD: 7,250.0ft
Btm TMD: 7,948.0ft
Spud Date: 12/20/1979 00:00
BH Coord X: 6,155,210.26uss ft
BH Coord Y: 2,289,120.46uss ft

Casing Shoes (ft)	Schematic (8/4/2009)	Openings Top/Btm/Type/Status

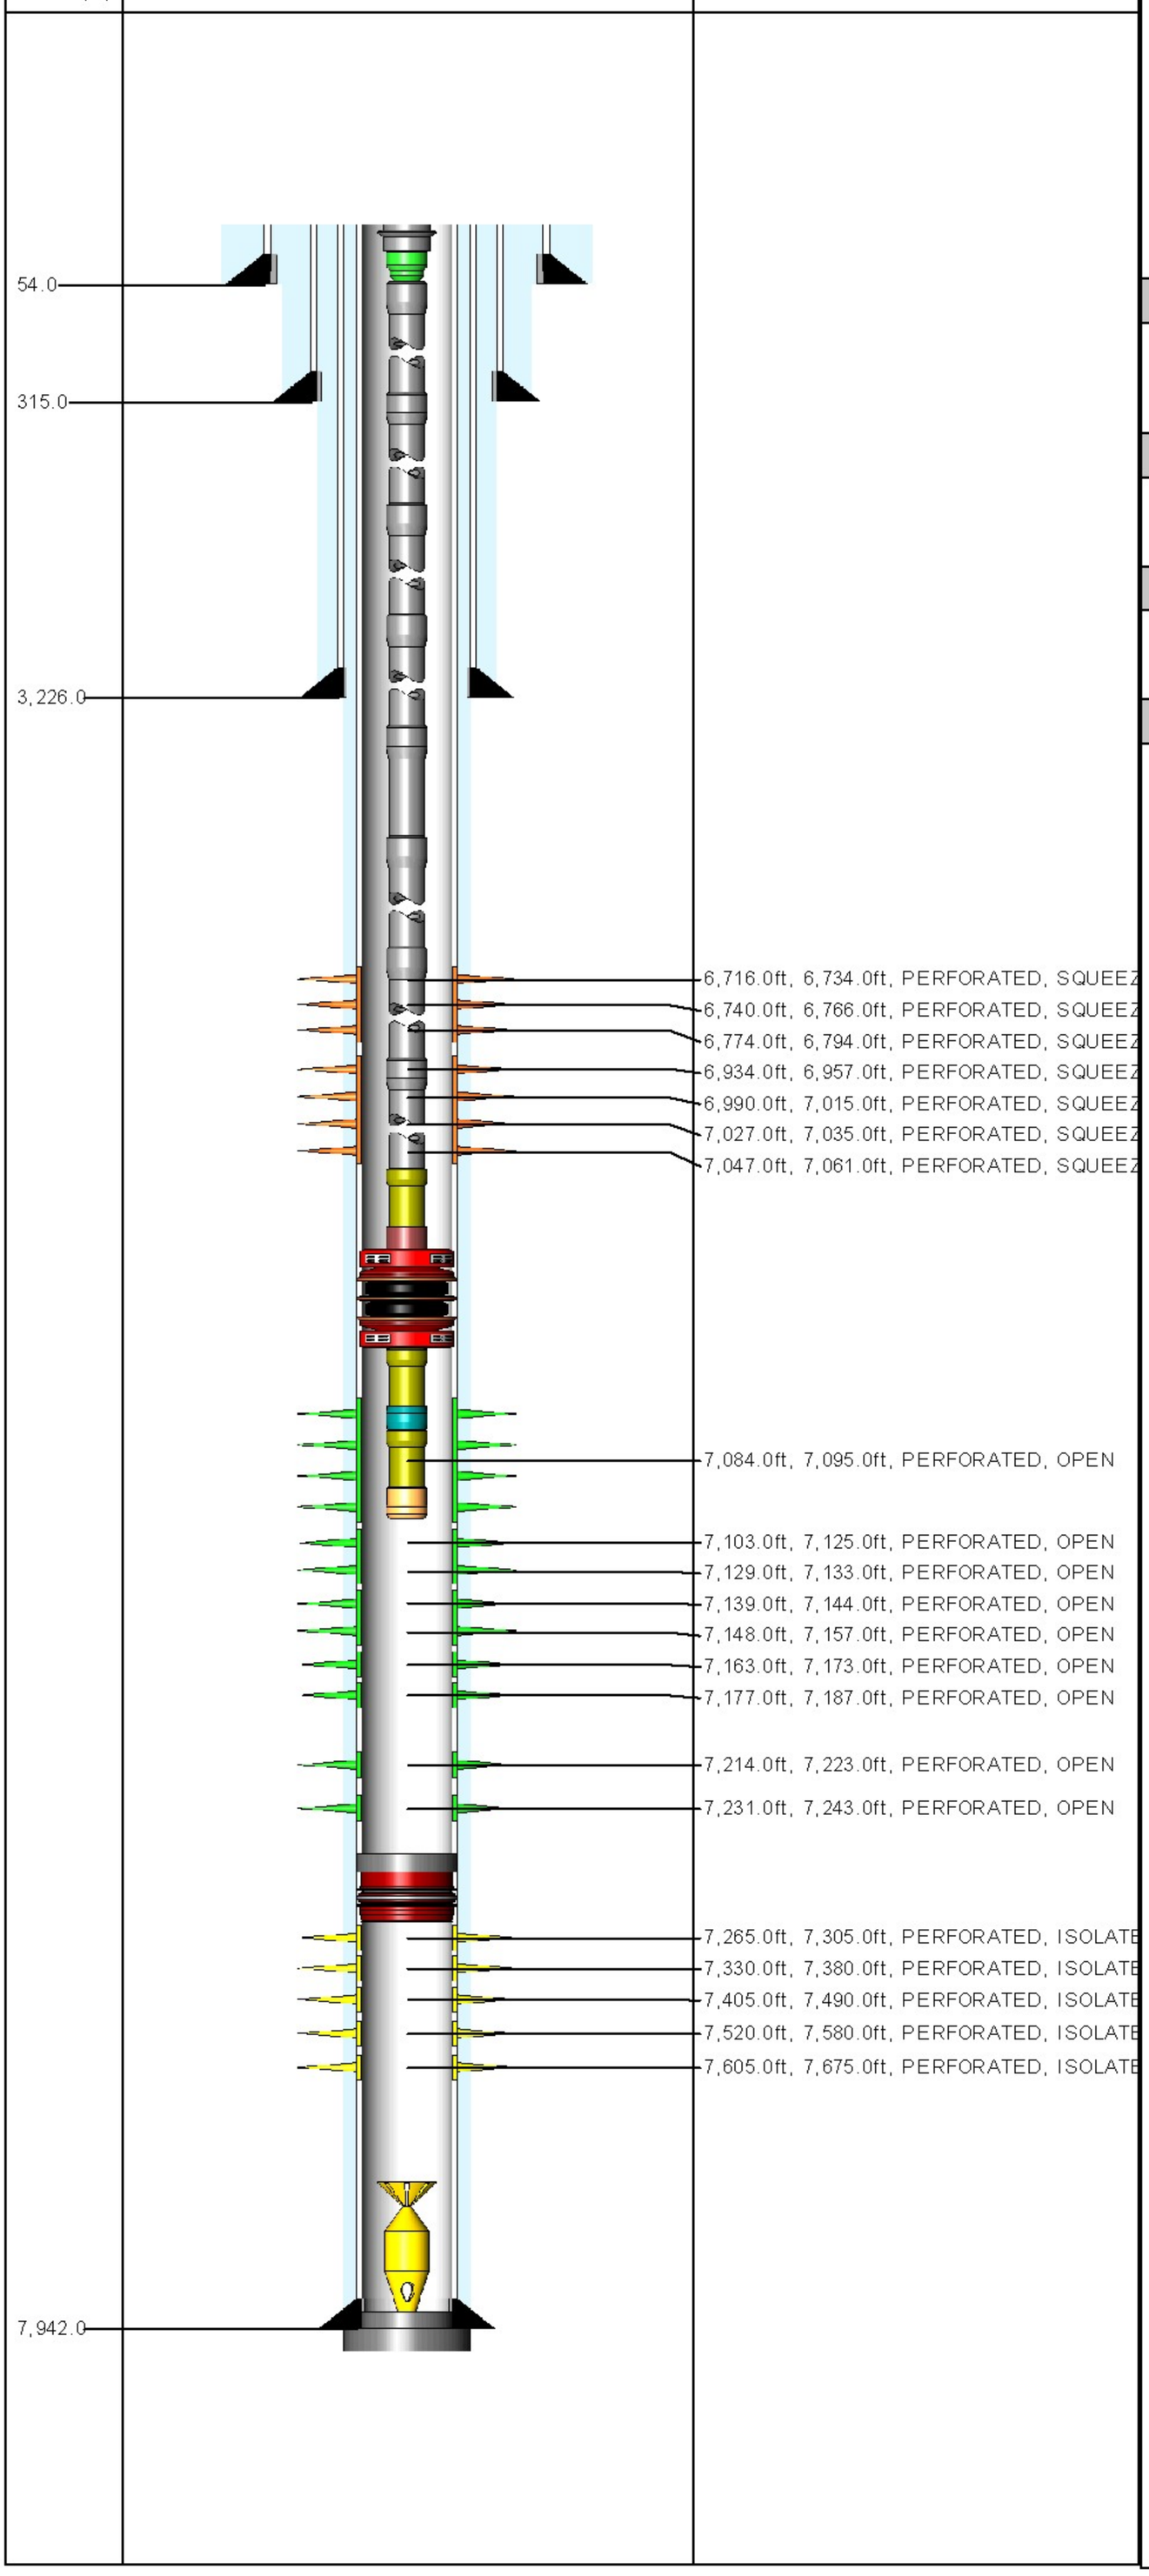

TUBING STRING Report Date: 10/30/2008 00:00

Component	Top MD (ft)	Btm MD (ft)
TH	14.0	14.6
FATNIP	14.6	15.3
CAS	15.3	7,064.7
PUPJNT	7,064.7	7,068.9
ON-OFF	7,068.9	7,070.7
PKR	7,070.7	7,078.7
PUPJNT	7,078.7	7,084.9
PRONIP	7,084.9	7,086.0
PUPJNT	7,086.0	7,090.2
WLREG	7,090.2	7,090.8

PLUG BACK Report Date: 11/21/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,245.0	7,250.0
BRP	7,250.0	7,252.0

PLUG BACK Report Date: 6/18/1986 00:00

Component	Top MD (ft)	Btm MD (ft)
JUNK	7,892.0	7,897.0

PLUG BACK Report Date: 6/13/1980 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,897.0	7,942.0

PLUG BACK Report Date: 3/30/1980 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,942.0	7,950.0

CONDUCTOR CASING Report Date: 12/20/1979 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			14.0	54.0

SURFACE CASING Report Date: 2/24/1980 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	K-55	54.50	14.0	273.5
FLOAT COLLAR	13.375	K-55	54.50	273.5	273.5
CASING JOINT(S)	13.375	K-55	54.50	273.5	314.0
FLOAT SHOE	13.375	K-55	54.50	314.0	315.0

INTERMEDIATE CASING Report Date: 3/1/1980 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	40.00	14.0	3,182.2
FLOAT COLLAR	9.625	K-55	40.00	3,182.2	3,182.3
CASING JOINT(S)	9.625	K-55	40.00	3,182.3	3,225.0
FLOAT SHOE	9.625	K-55	40.00	3,225.0	3,226.0

PRODUCTION CASING Report Date: 3/30/1980 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	14.0	45.9
CASING JOINT(S)	7.000	N-80	23.00	45.9	6,574.8
CROSSOVER	7.000	N-80	26.00	6,574.8	6,613.5
FLAG JOINT	7.000	N-80	26.00	6,613.5	6,632.2
CASING JOINT(S)	7.000	N-80	26.00	6,632.2	7,897.4
FLOAT COLLAR	7.000	N-80	26.00	7,897.4	7,898.7
CASING JOINT(S)	7.000	N-80	26.00	7,898.7	7,939.8
FLOAT SHOE	7.000	N-80	26.00	7,939.8	7,942.0

Well: 374X-35S S/T/R: 36/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 450 cf
Hole Size: 17.5
Top Job: no
Rtns to Sfc: 20 cf
TOC: sfc
- - -

Interm Csg. Cmt Vol.: 1550 cf
Hole Size: 12.25
Top Job: no
Rtns to Sfc: 56 cf
TOC: sfc
- - -

Prod. Csg. Cmt Vol.: 1900 cf
Hole Size: 8.75
Top Job: no
Rtns to Sfc: 0
TTOC: sfc
- - -

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -
Top of Formation:
UBA: 7234'
BLW: 7698'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
JEP
