OCCIDENTAL OF ELK HILLS INC

375-35S

Event: WELL MAINT - RIG
Event End: 4/10/2007 00:00
Sec. Reason: SANDED

Ground Level: 666.0ft
Datum: ORIGINAL KB @ 681.00ft (default)
API No.: 0402957941

Wellbore: ORIGINAL HOLE
PBMD: 7,180.0ft
Btm TMD: 7,910.0ft
Spud Date: 5/9/1978 00:00
BH Coord X: 6,155,004.38uss ft
BH Coord Y: 2,288,606.96uss ft

Casing Shoes (ft) | Schematic (5/1/2007) | Openings Top/Btm/Type/Status

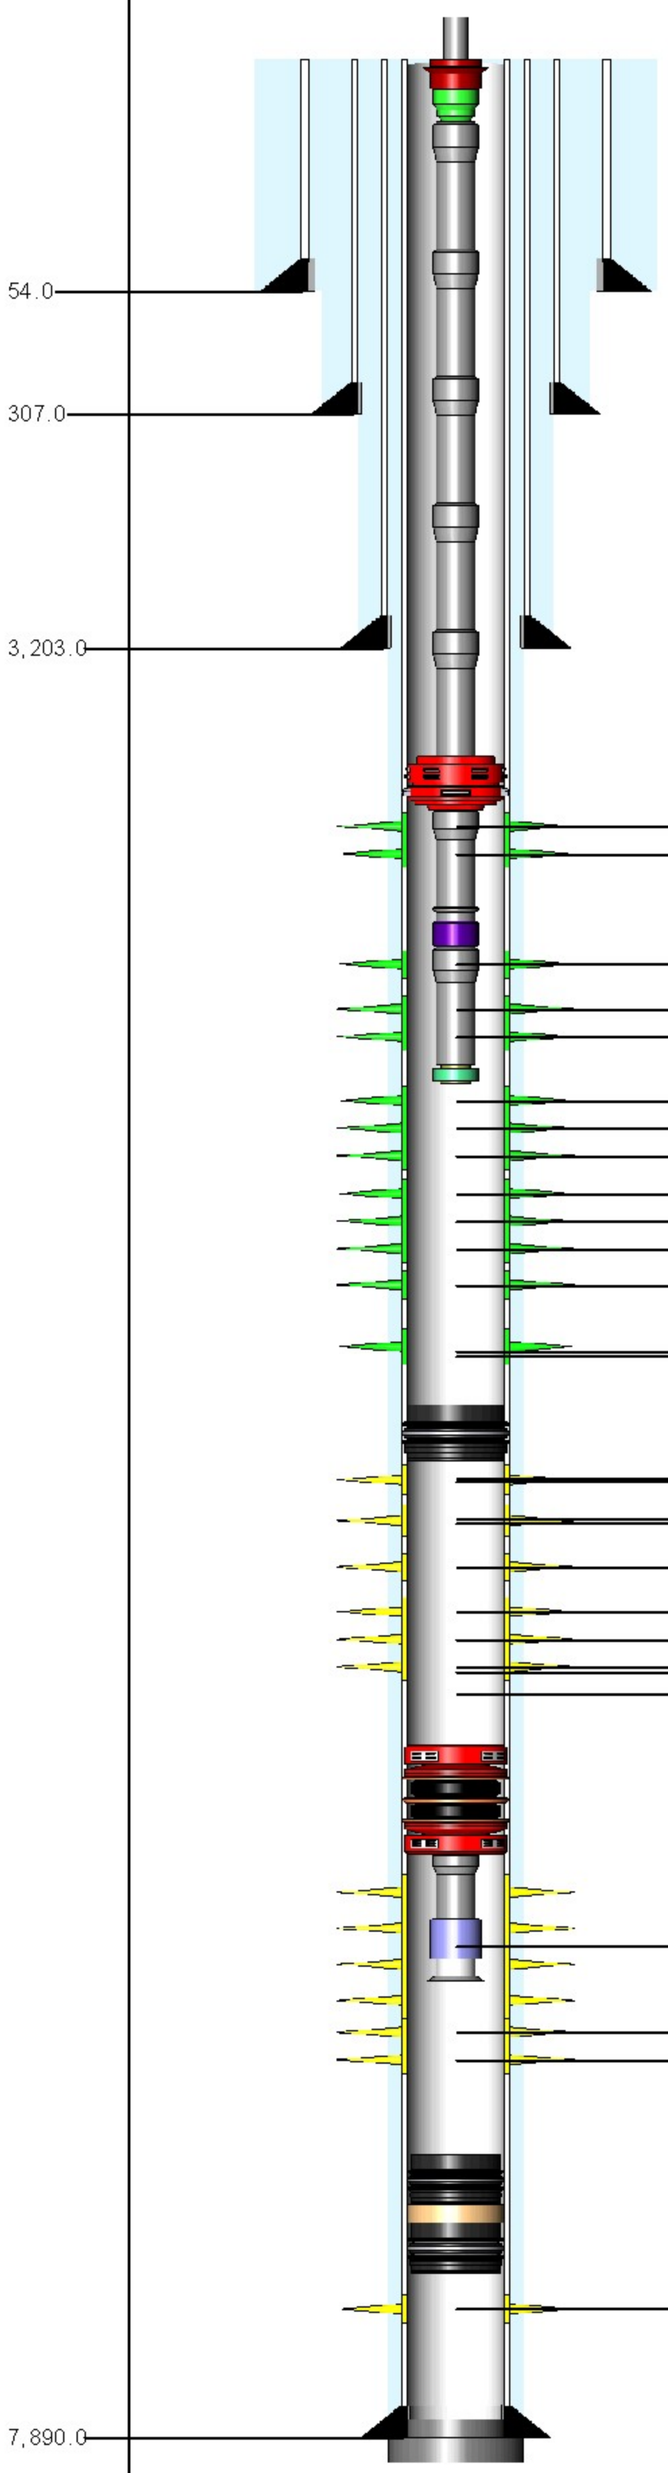

PACKER

6,670.0ft, 6,739.0ft, PERFORATED, OPEN
6,739.0ft, 6,760.0ft, PERFORATED, OPEN
6,902.0ft, 6,918.0ft, PERFORATED, OPEN
6,955.0ft, 6,967.0ft, PERFORATED, OPEN
6,967.0ft, 6,978.0ft, PERFORATED, OPEN
6,995.0ft, 7,008.0ft, PERFORATED, OPEN
7,008.0ft, 7,022.0ft, PERFORATED, OPEN
7,022.0ft, 7,030.0ft, PERFORATED, OPEN
7,052.0ft, 7,056.0ft, PERFORATED, OPEN
7,056.0ft, 7,066.0ft, PERFORATED, OPEN
7,066.0ft, 7,074.0ft, PERFORATED, OPEN
7,089.0ft, 7,108.0ft, PERFORATED, OPEN
7,155.0ft, 7,162.0ft, PERFORATED, OPEN
7,150.0ft, 7,166.0ft, PERFORATED, OPEN
7,199.0ft, 7,239.0ft, PERFORATED, ISOLATE
7,204.0ft, 7,245.0ft, PERFORATED, ISOLATE
7,264.0ft, 7,294.0ft, PERFORATED, ISOLATE
7,270.0ft, 7,300.0ft, PERFORATED, ISOLATE
7,328.0ft, 7,353.0ft, PERFORATED, ISOLATE
7,376.0ft, 7,398.0ft, PERFORATED, ISOLATE
7,398.0ft, 7,423.0ft, PERFORATED, ISOLATE
7,423.0ft, 7,453.0ft, PERFORATED, ISOLATE
7,437.0ft, 7,450.0ft, CASING HOLE, ISOLATE
7,438.0ft, 7,459.0ft, CASING HOLE, ISOLATE
7,473.0ft, 7,538.0ft, PERFORATED, ISOLATE
7,538.0ft, 7,563.0ft, PERFORATED, ISOLATE
7,563.0ft, 7,658.0ft, PERFORATED, ISOLATE
7,730.0ft, 7,750.0ft, PERFORATED, ISOLATE

ROD STRING Report Date: 4/10/2007 00:00

Component	Top MD (ft)	Btm MD (ft)
POLROD	0.0	30.0
PNYROD	30.0	54.0
ROD	54.0	2,874.0
ROD	2,874.0	6,834.0
RSTBAR	6,834.0	6,838.0
INSPMP	6,838.0	6,862.0

TUBING STRING Report Date: 4/10/2007 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	15.0	15.6
FATNIP	15.6	16.8
TBGJNT	16.8	6,572.3
AC	6,572.3	6,574.6
TBGJNT	6,574.6	6,857.3
STNIP	6,857.3	6,858.4
TBGJNT	6,858.4	6,889.6
DESAND	6,889.6	6,892.5
TBGJNT	6,892.5	6,986.1
PRGVLV	6,986.1	6,986.5

PLUG BACK Report Date: 5/16/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-RET	7,180.0	7,190.3

PACKER ASSEMBLY (PERMANENT) Report Date: 1/27/1987 00:00

Component	Top MD (ft)	Btm MD (ft)
PKR-S	7,462.6	7,470.5
TBGJNT	7,470.5	7,478.6
NOGO-O	7,478.6	7,479.7
BELCOL	7,479.7	7,480.3

PLUG BACK Report Date: 1/25/1987 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-RET	7,662.0	7,665.0
FILL	7,665.0	7,700.0

PLUG BACK Report Date: 12/20/1978 00:00

Component	Top MD (ft)	Btm MD (ft)
BP-DR	7,700.0	7,703.0

PLUG BACK Report Date: 8/27/1978 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,846.0	7,890.0

PLUG BACK Report Date: 8/26/1978 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,890.0	7,910.0

CONDUCTOR CASING Report Date: 5/9/1978 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			15.0	54.0

SURFACE CASING Report Date: 7/25/1978 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	H-40	48.00	15.0	266.0
FLOAT COLLAR	13.375	H-40	48.00	266.0	266.0
CASING JOINT(S)	13.375	H-40	48.00	266.0	306.0
FLOAT SHOE	13.375	H-40	48.00	306.0	307.0

INTERMEDIATE CASING Report Date: 7/29/1978 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	N-80	40.00	15.0	3,161.0
FLOAT COLLAR	9.625	N-80	40.00	3,161.0	3,161.0
CASING JOINT(S)	9.625	N-80	40.00	3,161.0	3,202.0
FLOAT SHOE	9.625	N-80	40.00	3,202.0	3,203.0

PRODUCTION CASING Report Date: 8/26/1978 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	K-55	26.00	15.0	74.4
CASING JOINT(S)	7.000	K-55	23.00	74.4	5,154.6
CASING JOINT(S)	7.000	K-55	26.00	5,154.6	6,548.7
FLAG JOINT	7.000	K-55	26.00	6,548.7	6,567.4
CASING JOINT(S)	7.000	K-55	26.00	6,567.4	7,846.2
FLOAT COLLAR	7.000	K-55	26.00	7,846.2	7,847.5
CASING JOINT(S)	7.000	K-55	26.00	7,847.5	7,887.9
FLOAT SHOE	7.000	K-55	26.00	7,887.9	7,890.0

Well: 375-35S S/T/R: 36/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 450 cf
Hole Size: 17.5
Top Job: no
Rtns to Sfc: 59 cf
TOC: sfc
- - -

Interm Csg. Cmt Vol.: 1606 cf
Hole Size: 12.25
Top Job: no
Rtns to Sfc: 110 cf
TOC: sfc
- - -

Prod. Csg. Cmt Vol.: 2000 cf
Hole Size: 8.75
Top Job: no
Rtns to Sfc: 0
TTOC: sfc
- - -

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -
Top of Formation:
UBA: 7177'
BLW: 7660'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
JEP
