OCCIDENTAL OF ELK HILLS INC

376-34S

Event: WELL MAINT - RIGLESS
Event End: 5/10/2007 00:00
Sec. Reason:

Ground Elev: 833.0ft
KB to Ground: 14.0ft
Datum: ORIGINAL KB @ 847.00ft (default)
API No.: 0402967232

Wellbore: ORIGINAL HOLE
Top TMD: 14.0ft
PBMD: 7,172.0ft
Btm TMD: 7,325.0ft
Spud Date: 7/16/1982 00:00
BH Coord X: 6,149,684.74uss ft BH Coord Y: 2,288,161.68uss

Casing Shoes (ft) | Schematic (6/1/2007) | Openings Top/Btm/Type/Status

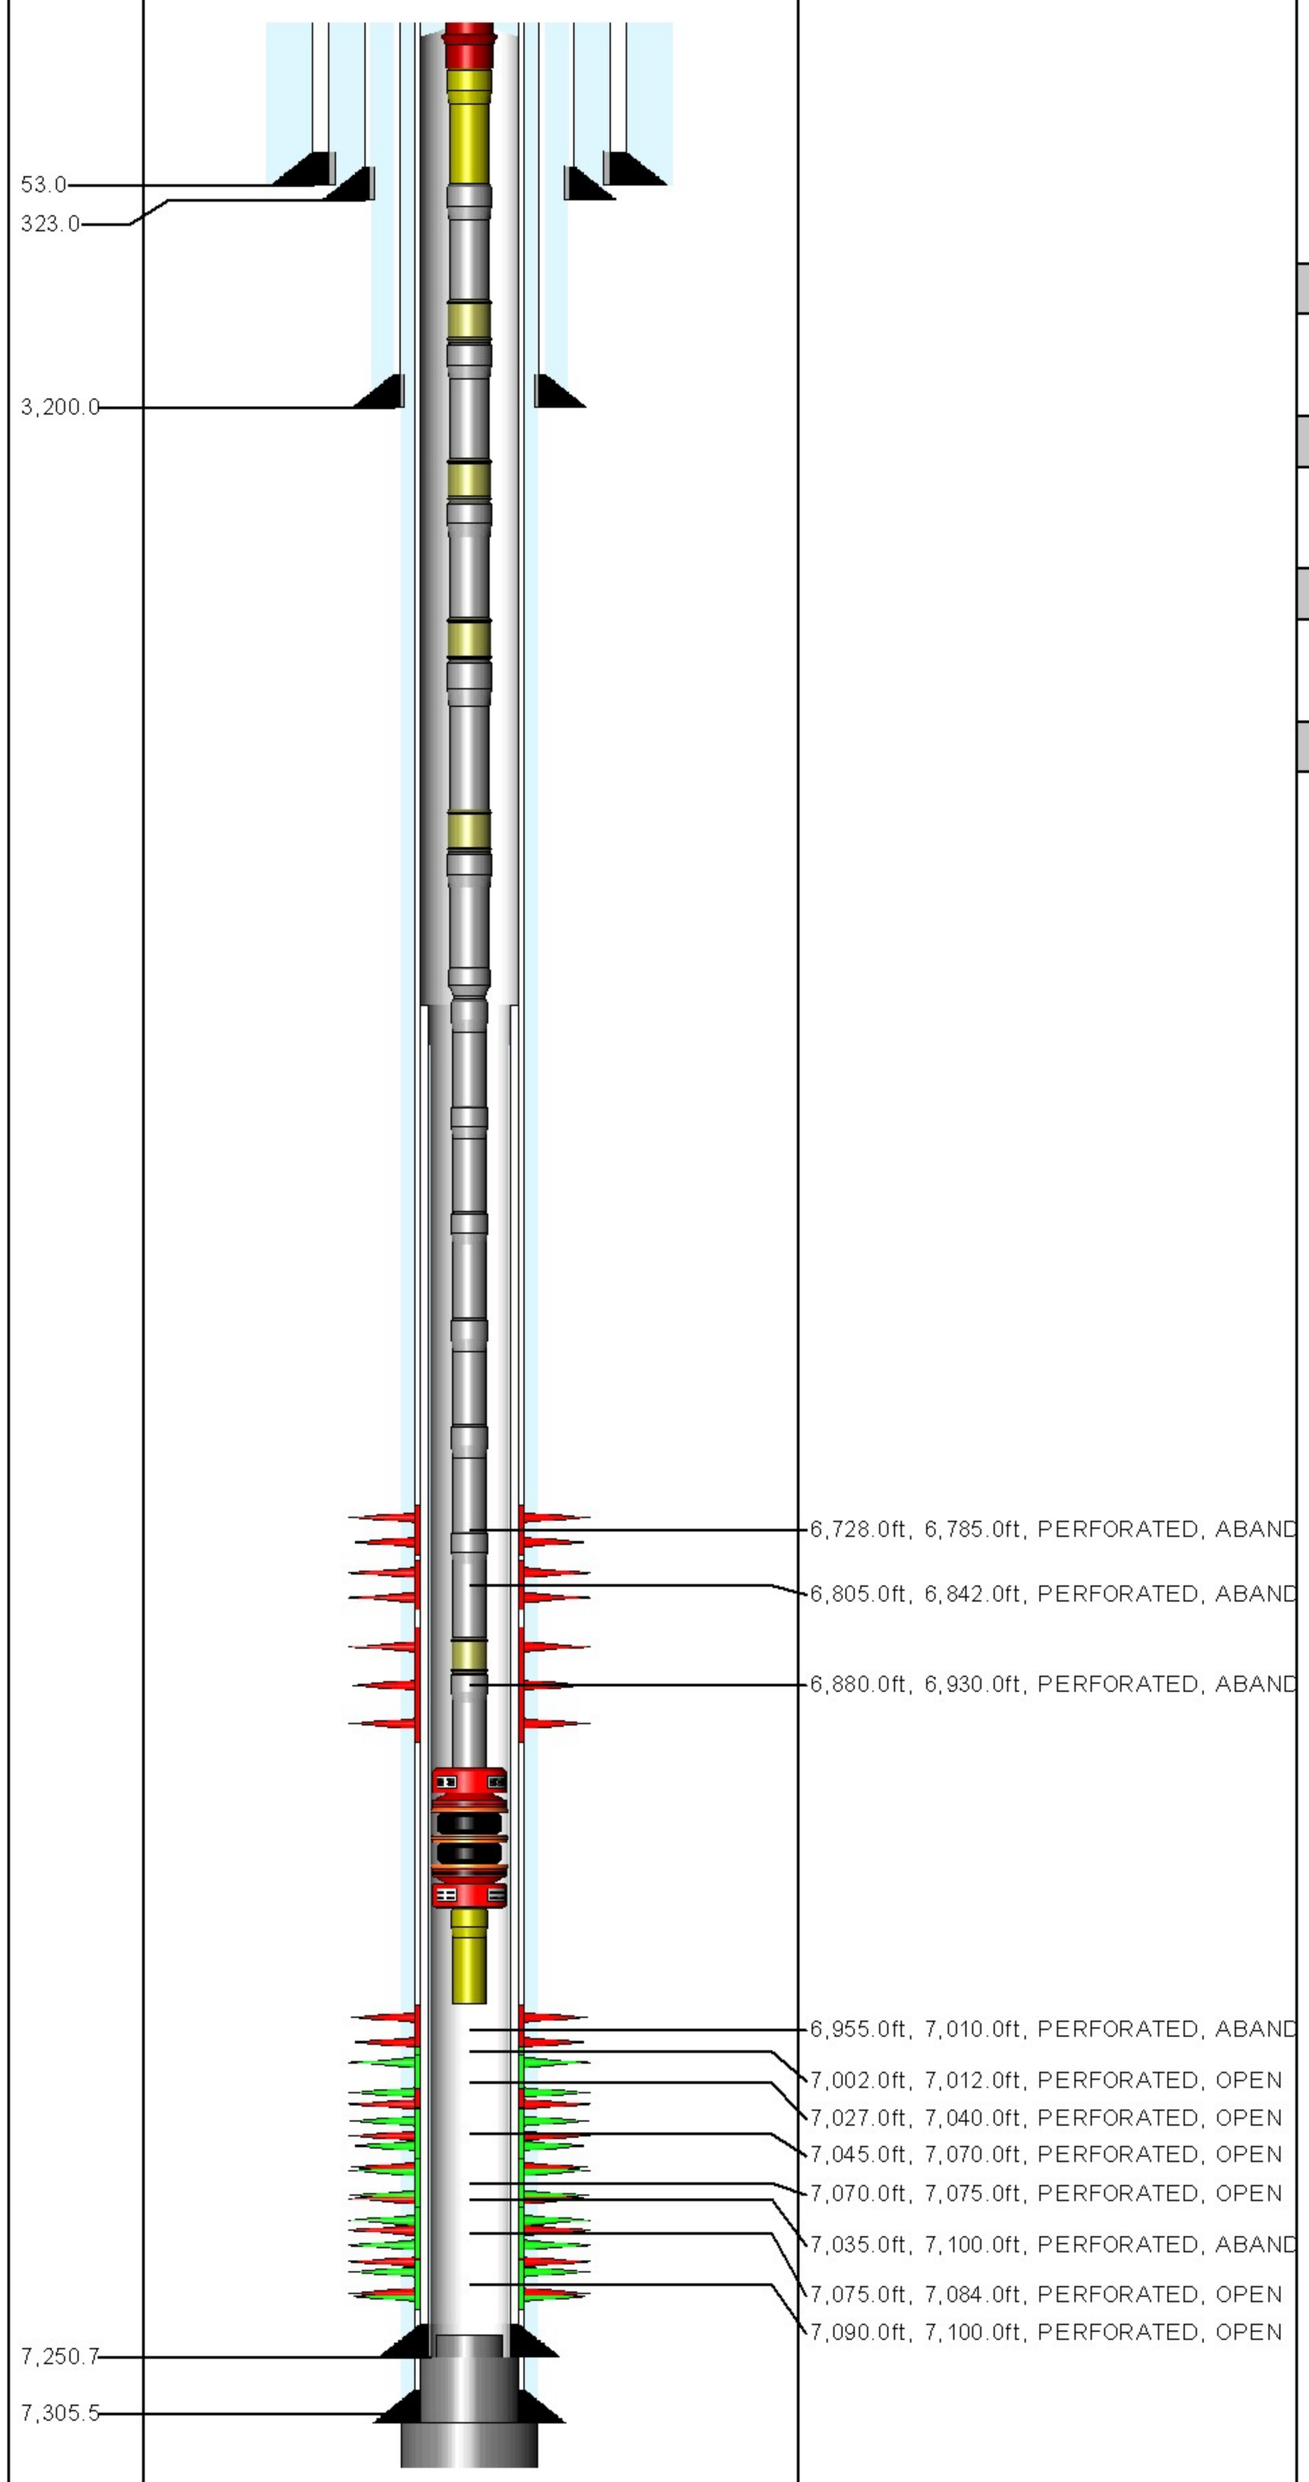

TUBING STRING Report Date: 3/1/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	14.0	14.6
PUPJNT	14.6	31.3
TBGJNT	31.3	2,189.5
GLM-D	2,189.5	2,198.0
TBGJNT	2,198.0	3,992.0
GLM-D	3,992.0	4,000.9
TBGJNT	4,000.9	5,192.2
GLM-D	5,192.2	5,201.0
TBGJNT	5,201.0	6,205.0
GLM-D	6,205.0	6,213.5
TBGJNT	6,213.5	6,371.7
XO	6,371.7	6,372.8
TBGJNT	6,372.8	6,901.0
GLM-D	6,901.0	6,907.7
TBGJNT	6,907.7	6,938.1
PKR-S	6,938.1	6,942.1
PUPJNT	6,942.1	6,946.2

PLUG BACK Report Date: 5/12/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,172.0	7,250.7

PLUG BACK Report Date: 5/8/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,250.7	7,264.0

PLUG BACK Report Date: 10/5/1982 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,264.0	7,306.0

PLUG BACK Report Date: 8/9/1982 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,306.0	7,325.0

CONDUCTOR CASING Report Date: 7/16/1982 00:00

Item Description	Btm MD(ft)
CASING JOINT(S) 20 in,	53.0

SURFACE CASING Report Date: 7/22/1982 00:00

Item Description	Btm MD(ft)
CASING JOINT(S) 13.375 in, , H-40, 48	323.0

INTERMEDIATE CASING Report Date: 7/28/1982 00:00

Item Description	Btm MD (ft)
CASING JOINT(S) 9.625 in, , K-55, 40	3,200.0

PRODUCTION CASING Report Date: 8/9/1982 00:00

Item Description	Btm MD (ft)
CASING JOINT(S) 7 in, , K-55, 26	80.5
CASING JOINT(S) 7 in, , K-55, 23	5,004.4
CASING JOINT(S) 7 in, , K-55, 26	6,160.9
FLAG JOINT 7 in, , K-55, 26	6,175.0
CASING JOINT(S) 7 in, , K-55, 26	7,263.8
FLOAT COLLAR 7 in, , K-55, 26	7,265.9
CASING JOINT(S) 7 in, , K-55, 26	7,305.0
GUIDE SHOE 7 in, , K-55, 26	7,306.0

INNER LINER Report Date: 5/8/2002 00:00

Item Description	Btm MD (ft)
LINER HANGER 6.276 in, , L-80	6,413.4
LINER HANGER PACKER 6.276 in, , L-80, 26	6,420.1
PBR 6.276 in, , L-80	6,423.0
LINER HANGER 6.276 in, , L-80	6,429.5
CASING JOINT(S) 5 in, , P-110, 18	7,188.7
LANDING COLLAR 5 in, , L-80	7,190.1
PUP JOINT 5 in, , P-110, 18	7,206.8
FLOAT COLLAR 5 in, , L-80	7,207.8
CASING JOINT(S) 5 in, , P-110, 18	7,248.8
FLOAT SHOE 5 in, , L-80	7,250.7

S/T/R: 376-34S 34S/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 550cf
Hole Size: 17-1/2"
Top Job:
Rtns to Sfc: Yes
TOC:
- - -
Int. Csg. Cmt Vol.: 1930cf
Hole Size: 12-1/4"
Top Job:
Rtns to Sfc: Yes
TOC:
- - -
Prod Csg. Cmt Vol.: 1470cf
Hole Size: 8-3/4"
Rtns to Sfc: none
TOC: TTOC at surface
- - -
Liner Cmt Vol.: 125 cf
Hole Size: 6"
Rtns to Sfc: none
TOC: TTOC at surface

Top of Formation:
UBA: 6729'
BLW: 7119'

Volume Behind Pipe
1.3 Yield Assumed on
Theoretical Calculations
