OCCIDENTAL OF ELK HILLS INC

377X-34S-RD2

Event: WELL MAINT - RIGLESS
Event End: 10/23/2009 00:00
Sec. Reason:

Water Depth: 892.0ft
Datum: ORIGINAL KB @ 914.00ft (default)
API No.: 0403028943

Wellbore: MAIN WELLBORE (REENTERED)
PBMD: 7,420.0ft
Btm TMD: 7,480.0ft
Spud Date: 2/2/2006 02:00
BH Coord X: 6,150,059.32uss ft
BH Coord Y: 2,287,554.63uss ft

Casing Shoes (ft) | Schematic (7/1/2009) | Openings Top/Btm/Type/Status

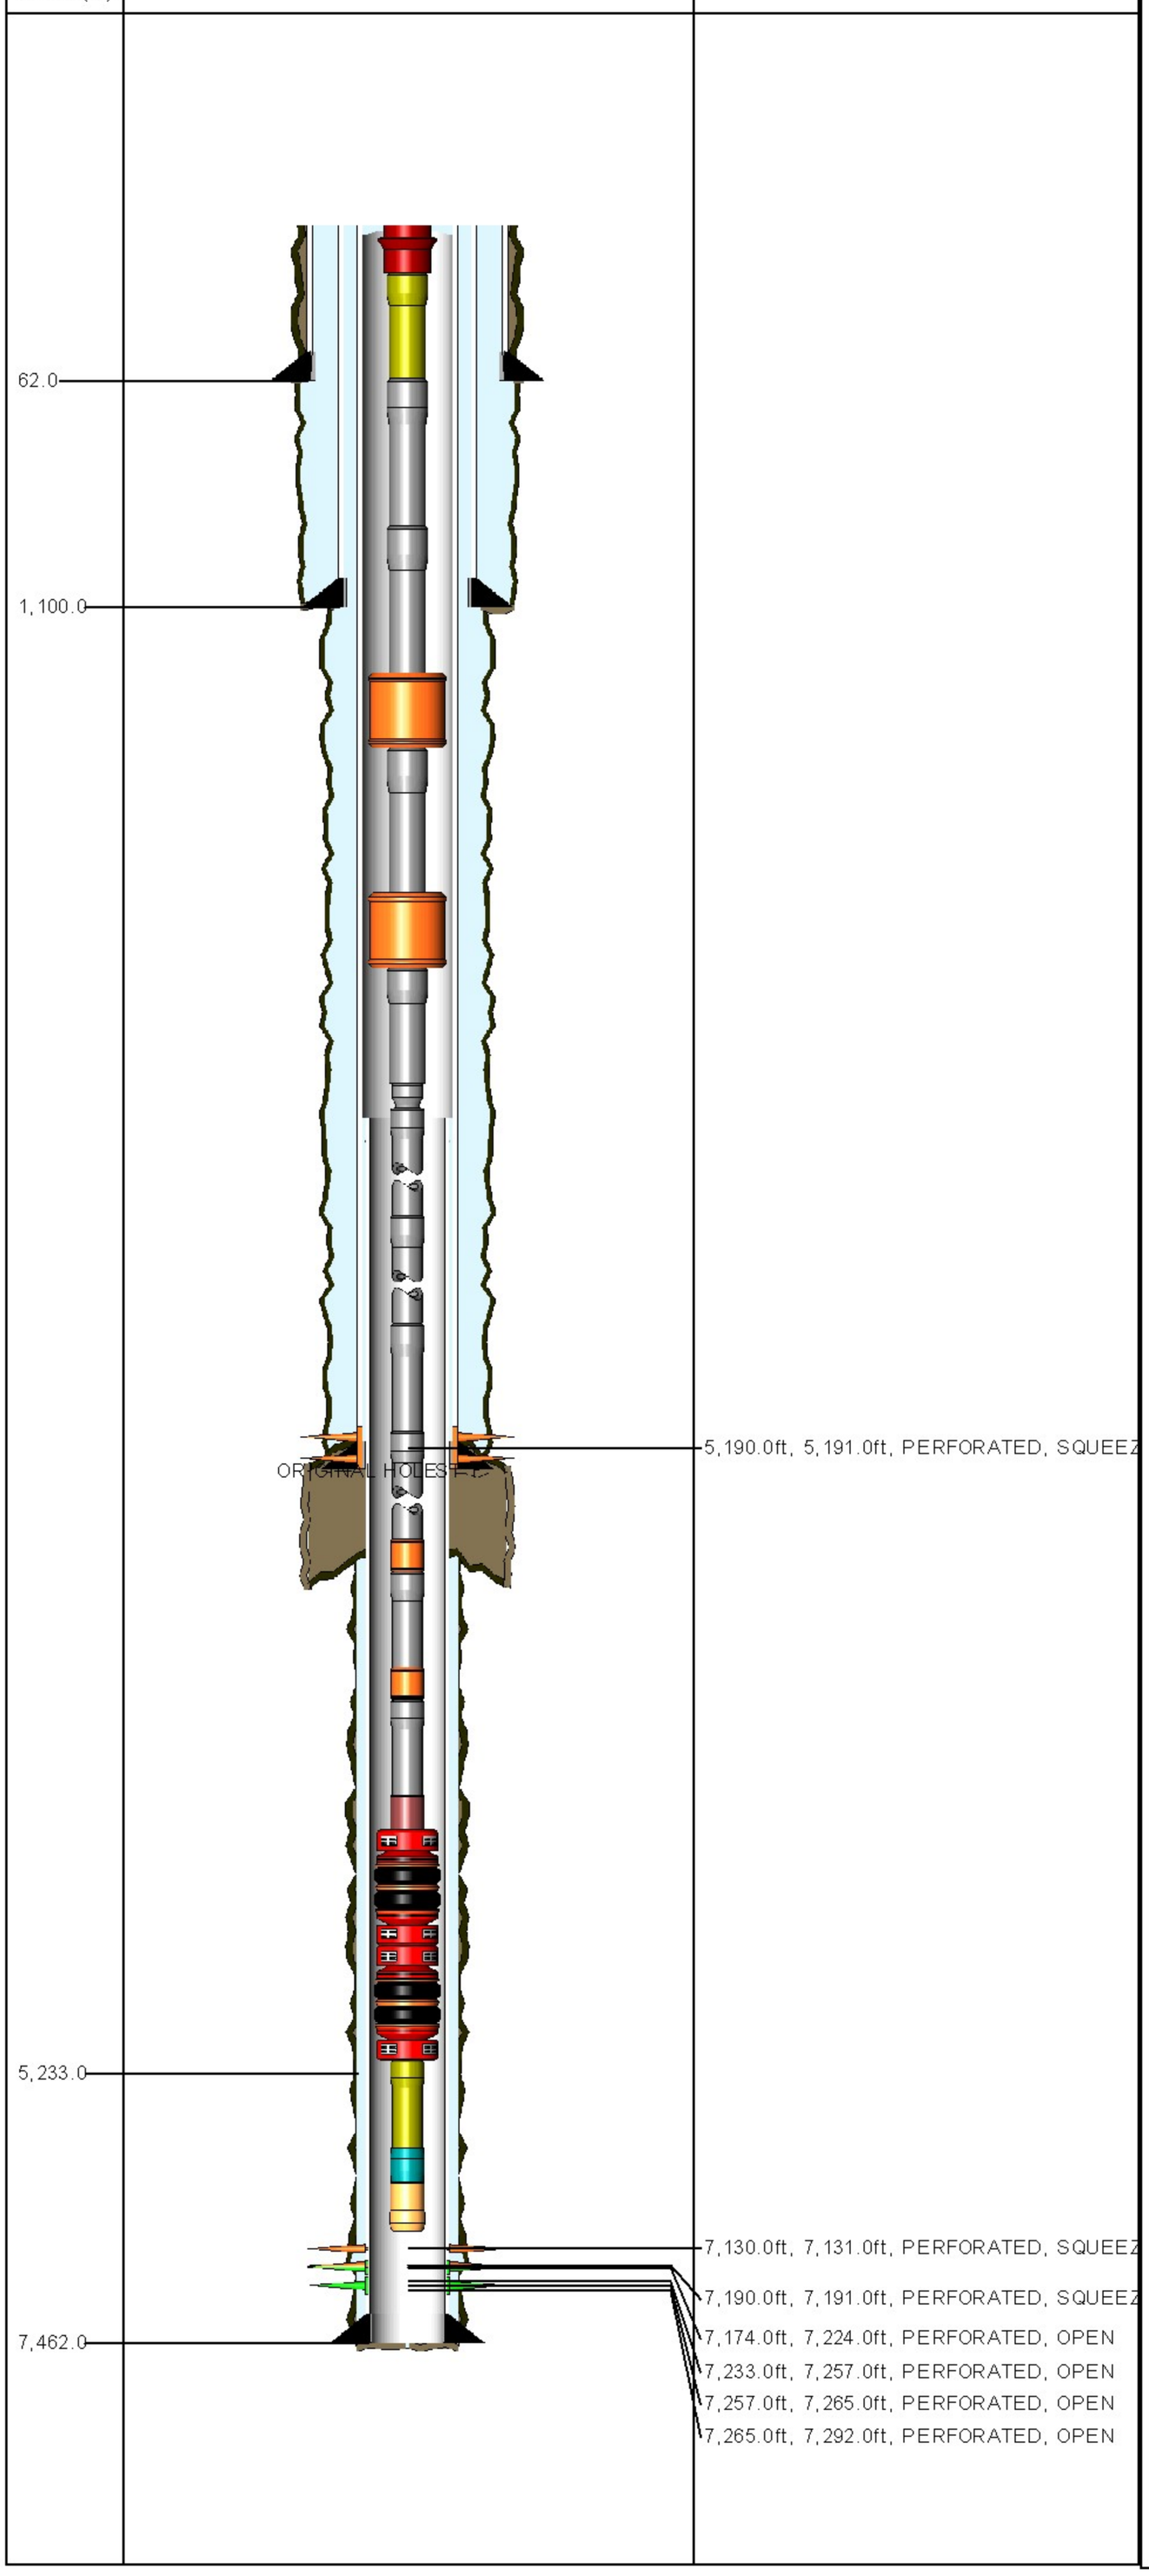

TUBING STRING Report Date: 4/30/2009 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	22.0	22.6
PUPJNT	22.6	26.8
TBGJNT	26.8	2,394.8
GLM-V	2,394.8	2,403.4
CAS	2,403.4	4,394.4
GLM-V	4,394.4	4,403.3
CAS	4,403.3	4,892.4
XO	4,892.4	4,893.5
CAS	4,893.5	5,967.5
GLM-V	5,967.5	5,974.3
CAS	5,974.3	7,019.3
GLM-V	7,019.3	7,026.1
CAS	7,026.1	7,057.3
ON-OFF	7,057.3	7,058.7
PKR	7,058.7	7,059.7
PKR	7,059.7	7,062.2
PUPJNT	7,062.2	7,072.2
PRONIP	7,072.2	7,073.2
WLREG	7,073.2	7,073.6

CONDUCTOR CASING Report Date: 1/30/2006 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	14.000			22.0	62.0

SURFACE CASING Report Date: 2/3/2006 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	36.00	22.0	1,059.6
	9.625			1,059.6	1,059.6
CASING JOINT(S)	9.625	K-55	36.00	1,059.6	1,098.9
GUIDE SHOE	9.625			1,098.9	1,100.0

PRODUCTION CASING Report Date: 2/17/2006 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	22.0	3,826.9
FLAG JOINT	7.000	N-80	26.00	3,826.9	3,839.3
CASING JOINT(S)	7.000	N-80	26.00	3,839.3	5,136.3
FLOAT COLLAR	7.000	N-80		5,136.3	5,137.9
CASING JOINT(S)	7.000	N-80	26.00	5,137.9	5,231.3
FLOAT SHOE	7.000	N-80		5,231.3	5,233.0

PRODUCTION LINER Report Date: 2/23/2006 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
TIE BACK RECEPTACLE	5.750	N-80		5,007.0	5,013.0
SETTING SLEEVE	5.750	N-80		5,013.0	5,019.4
LINER HANGER	5.934	N-80		5,019.4	5,027.3
CASING JOINT(S)	5.500	N-80	17.00	5,027.3	7,367.1
LANDING COLLAR	5.500	N-80		7,367.1	7,369.4
CASING JOINT(S)	5.500	N-80	17.00	7,369.4	7,412.2
FLOAT COLLAR	5.500	N-80		7,412.2	7,414.5
CASING JOINT(S)	5.500	N-80	17.00	7,414.5	7,459.2
FLOAT SHOE	5.500	N-80		7,459.2	7,462.0

Well: 377X-34S-RD2 S/T/R: 34/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 1027 cf
Hole Size: 9.875
Top Job: no
Rtns to Sfc: 269 cf
TOC: sfc
- - -

Interm Csg. Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -

Prod. Csg. Cmt Vol.: 1997 cf
Hole Size: 8.75
Top Job: no
Rtns to Sfc: 784 cf
TOC: sfc
- - -

Liner Cmt Vol.: 596 cf
Hole Size: 6.275
Top Job: no
Rtns to Sfc: no
TTOC: 1634
- - -
Top of Formation:
UBA: 6850'
BLW: 7323'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
JEP
