OCCIDENTAL OF ELK HILLS INC

387H-34S

Event: WELL MAINT - RIG
Event End: 7/1/2009 00:00
Sec. Reason:

Ground Level: 887.0ft
Datum: ORIGINAL KB @ 901.00ft (default)
API No.: 0402981953

Wellbore: ST 2
PBMD: 8,053.0ft
Btm TMD: 8,074.0ft
Spud Date: 2/16/1988 00:00
BH Coord X: 6,148,577.32uss ft
BH Coord Y: 2,287,401.97uss ft

Casing Shoes (ft) | Schematic (8/1/2009) | Openings Top/Btm/Type/Status

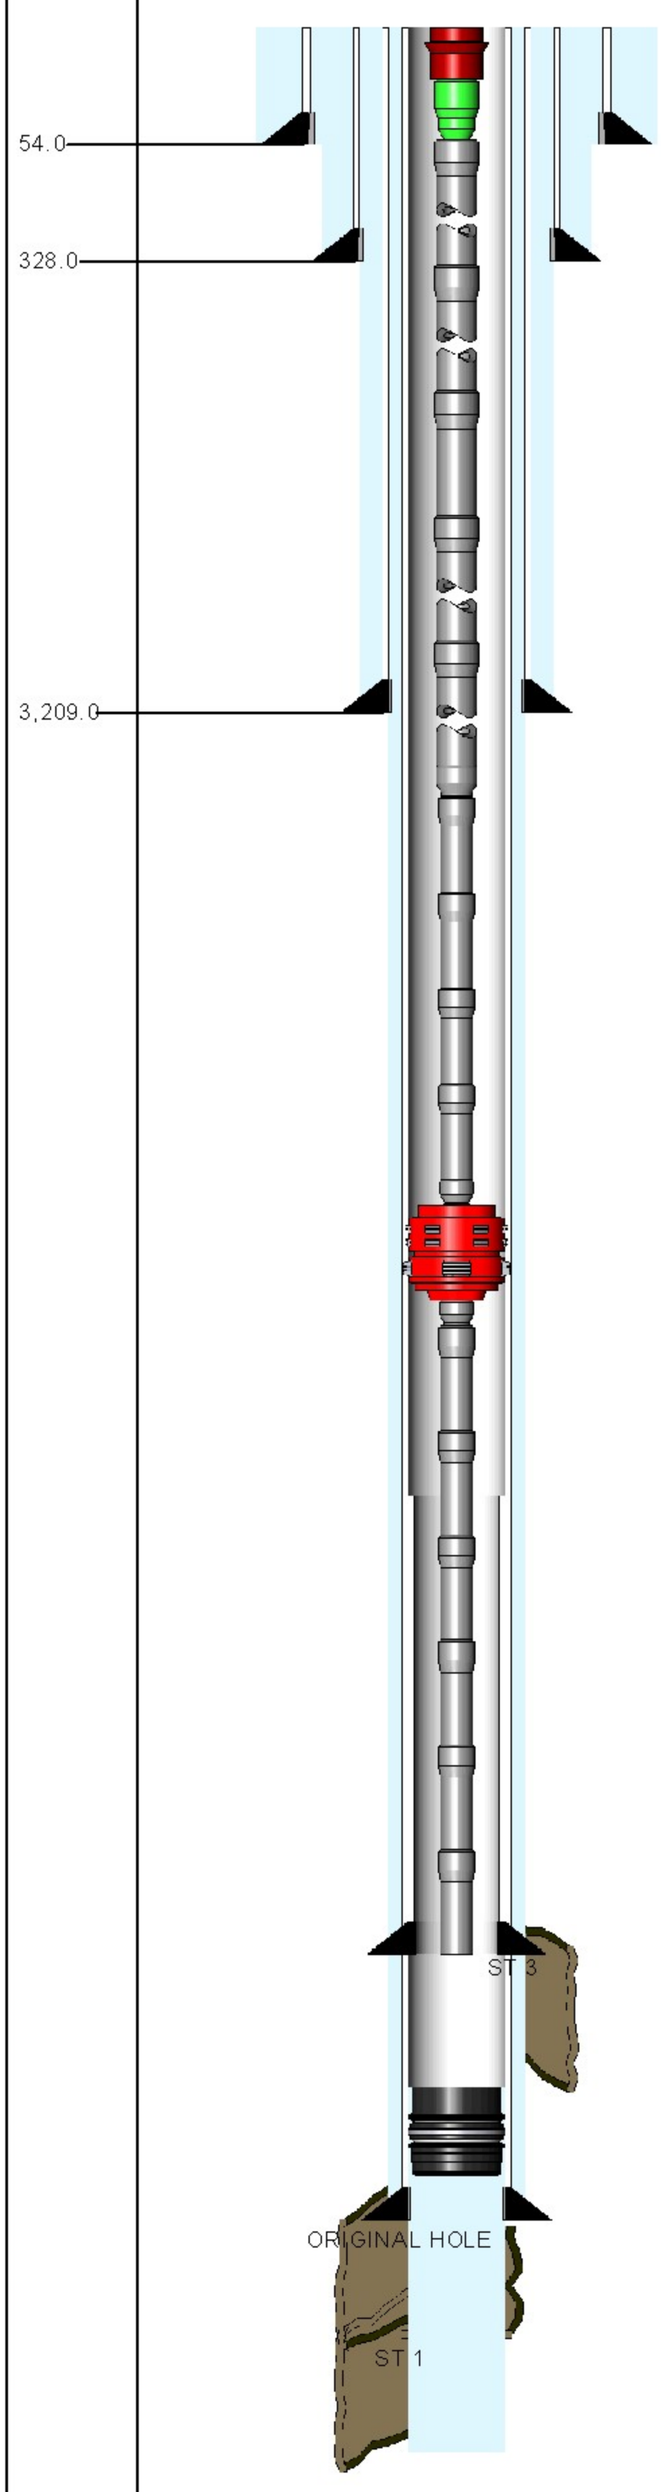

PACKER ASSEMBLY (PERMANENT) Report Date: 6/26/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CR-PRM	5,682.0	5,688.0

ROD STRING Report Date: 7/9/2009 00:00

Component	Top MD (ft)	Btm MD (ft)
POLRDL	0.0	30.0
PNYROD	30.0	50.0
COROD	50.0	1,287.0
COROD	1,287.0	6,003.0
RSTBAR	6,003.0	6,007.0
ON-OFF	6,007.0	6,008.0
RSTBAR	6,008.0	6,012.0
ROD	6,012.0	6,072.0
INSPMP	6,072.0	6,090.0

TUBING STRING Report Date: 7/8/2009 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	14.0	14.7
FATNIP	14.7	15.4
CAS	15.4	3,622.4
XO	3,622.4	3,623.5
TBGJNT	3,623.5	5,621.4
XO	5,621.4	5,622.5
AC	5,622.5	5,624.9
XO	5,624.9	5,626.0
TBGJNT	5,626.0	6,101.5
STNIP	6,101.5	6,102.6

CONDUCTOR CASING Report Date: 2/16/1988 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			14.0	54.0

SURFACE CASING Report Date: 2/24/1988 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.325	H-40	48.00	14.0	327.2
GUIDE SHOE	13.325			327.2	328.0

INTERMEDIATE CASING Report Date: 3/1/1988 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	40.00	14.0	3,208.0
GUIDE SHOE	9.625			3,208.0	3,209.0

PRODUCTION CASING Report Date: 3/18/1988 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	14.0	78.6
CASING JOINT(S)	7.000	K-55	26.00	78.6	5,140.9
CASING JOINT(S)	7.000	K-55	26.00	5,140.9	6,111.7
FLAG JOINT	7.000	K-55	26.00	6,111.7	6,128.1
CASING JOINT(S)	7.000	K-55	26.00	6,128.1	7,041.4
CASING JOINT(S)	7.000	N-80	26.00	7,041.4	7,690.6
FLOAT COLLAR	7.000	N-80	26.00	7,690.6	7,692.6
CASING JOINT(S)	7.000	N-80	26.00	7,692.6	7,738.0
FLOAT SHOE	7.000	N-80	26.00	7,738.0	7,740.0

LINER Report Date: 7/24/2002 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
LINER HANGER PACKER	6.276	N-80	26.00	5,646.0	5,652.3
CROSSOVER	5.500	N-80		5,652.3	5,653.1
CASING JOINT(S)	5.000	N-80	15.00	5,653.1	6,110.3
CROSSOVER	5.000	N-80	15.00	6,110.3	6,111.3
TUBING JOINT(S)	3.500	N-80	9.30	6,111.3	6,487.2
SLOTTED LINER	3.500	N-80	9.30	6,487.2	8,324.6
GUIDE SHOE	3.500			8,324.6	8,325.0

Well: 387H-34S-RD2 S/T/R: 34S/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 425 cf
Hole Size: 17.5"
Top Job: No
Rtns to Sfc: 45 cf
TOC: Sfc
- - -

Interm Csg. Cmt Vol.: 1450 cf
Hole Size: 12.25"
Top Job: No
Rtns to Sfc:
TTOC: Sfc
- - -

Prod. Csg. Cmt Vol.: 1500 cf
Hole Size: 8.75"
Top Job: No
Rtns to Sfc:
TTOC: Sfc
- - -

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TTOC:
- - -
Top of Formation:
UBA: 6820'
BLW: 7319'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
