October 13, 2011

Mr. Dale Rundquist
Compliance Project Manager
California Energy Commission (MS-2000)
1516 Ninth Street
Sacramento, CA 95814

Subject: CPV Sentinel Energy Project
Docket No. 07-AFC-3C
Monthly Compliance Report – Number 10
September 2011

Dear Mr. Rundquist:

Enclosed please find the Monthly Compliance Report – Number 10 for the CPV Sentinel Energy Project for the month of September 2011. If you have any questions, please feel free to contact me at (714) 648-2759.

Sincerely,

Maggie Fitzgerald
Site Compliance Manager

cc: Project File

URS Corporation
2020 East First Street, Suite 400
Santa Ana, CA92705
Tel: 714.835.6886
Fax: 714.667.7147
www.urscorp.com

CPV SENTINEL ENERGY PROJECT

MONTHLY COMPLIANCE REPORT – NUMBER 10

Report Period: September 2011

Submitted to

California Energy Commission
Energy Facilities Siting and
Environmental Protection Division
1516 9th Street
Sacramento, California 95814-5512

TABLE OF CONTENTS

SECTION **PAGE**

1.0 CURRENT PROJECT CONSTRUCTION STATUS 1
1.1 CONSTRUCTION ACTIVITIES 1
2.0 COMPLIANCE MATRIX 1
3.0 REQUIRED DOCUMENTS SUBMITTED WITH THIS REPORT 1
3.1 CBO DOCUMENTATION 1
3.2 WORKER ENVIRONMENTAL AWARENESS PROGRAM TRAINING 2
3.3 WORKER SAFETY 2
3.4 BIOLOGICAL RESOURCES 2
3.5 CULTURAL RESOURCES 2
3.6 PALEONTOLOGICAL RESOURCES 2
3.7 AIR QUALITY 3
4.0 COMPLIANCE REQUIREMENTS COMPLETED DURING THE REPORTING PERIOD 3
5.0 DELINQUENT SUBMITTALS 4
6.0 CHANGES TO CONDITIONS OF CERTIFICATION 4
7.0 FILINGS OR PERMITS ISSUED BY OTHER GOVERNMENTAL AGENCIES 4
8.0 PROJECT COMPLIANCE ACTIVITIES SCHEDULED FOR THE NEXT TWO MONTHS 4
9.0 LISTING OF THE MONTH'S ADDITIONS TO THE COMPLIANCE FILE 12
10.0 REQUESTS TO DISPOSE OF ITEMS REQUIRED TO BE MAINTAINED IN THE COMPLIANCE FILE 12
11.0 COMPLAINTS, NOTICES OF VIOLATIONS, WARNINGS AND CITATIONS 12
12.0 PENDING CEC APPROVALS 12

Figures

Figure 1 Construction Schedule

Appendices

Appendix A Key Events List & CEC Compliance Matrix
Appendix B CBO Documentation
Appendix C WEAP Acknowledgement Forms
Appendix D Worker Safety
Appendix E Biological Resources Monthly Summary Report
Appendix F Cultural Resources Monthly Summary Report
Appendix G Paleontological Resources Monthly Summary Report
Appendix H Air Quality

1.0 CURRENT PROJECT CONSTRUCTION STATUS

This section of the monthly compliance report addresses the progress of the CPV Sentinel Energy Project construction activities.

The updated construction schedule is included as Figure 1 of this report. There have been no significant changes to the construction schedule since the previous monthly report. A key events list is provided in Appendix A of this report. No changes have been made to the key events list since the previous monthly report.

1.1 Construction Activities

On-site construction activities for this reporting period included the following:

- Continued construction on Melissa Lane;
- Completed major civil activities on main site area;
- Continued laydown area preparation activities;
- Continued installation of site construction trailers;
- Continued construction of underground duct bank for construction power;
- Desert Water Agency (DWA) completed installation of recycled water line with the exception of metering and control equipment;
- Commenced work on 5-acre parking area; and,
- Commenced construction of CT 1, 2, 5 & 6 foundations.

2.0 COMPLIANCE MATRIX

An updated copy of the CEC Compliance Matrix is included with this report in Appendix A. As requested, fully satisfied conditions of certification (COCs) are not included in the matrix after they have been reported complete.

3.0 REQUIRED DOCUMENTS SUBMITTED WITH THIS REPORT

3.1 CBO Documentation

Documentation for CBO related activities for this reporting period are included as Appendix B of this report. The required documentation includes:

- Copies of all transmittal letters for submittals made to the CBO for this reporting period;
- Copies of all approvals received from the CBO during this reporting period;
- Updated CBO submittal and drawing list; and

- A copy of the CBO payment receipt for this reporting period.

3.2 Worker Environmental Awareness Program Training

Worker Environmental Awareness Program (WEAP) training was conducted for all on-site workers as they were brought onto the project. Appendix C includes all WEAP Training Acknowledgement Forms for this reporting period. During this reporting period 61 workers were trained. To date, a total of 287 workers have been WEAP trained for the project.

3.3 Worker Safety

The Construction Safety Supervisor (CSS) monthly safety inspection report is included as Appendix D of this report. As specified in WORKER SAFETY-3, the report includes:

- A record of all employees trained for that month (all records shall be kept on-site for the duration of the project);
- A summary report of safety management actions and safety-related incidents that occurred during the month;
- A report of any continuing or unresolved situations and incidents that may pose danger to life or health; and
- A report of accidents and injuries that occurred during the month.

3.4 Biological Resources

As required by the Biological Resources Mitigation Implementation and Monitoring Plan (BRMIMP), site survey reports and a summary of activities completed during this reporting period are included as Appendix E (Biological Resources Monthly Summary Report) of this report.

3.5 Cultural Resources

The designated Cultural Resources Specialist (CRS) and/or Delegate CRS continued communication with Gemma Power Engineers, CPV and URS personnel to ascertain monitoring needs based on construction activities and schedule. Cultural resources monitors (CRMs) were present on-site to monitor the ground-disturbing construction activities for this reporting period. The Cultural Resources Monthly Summary Report is included as Appendix F of this report.

3.6 Paleontological Resources

The designated Paleontological Resources Specialist (PRS) and/or Delegate PRS continued communication with Gemma Power Engineers, CPV and URS personnel to ascertain monitoring needs based on construction activities and schedule. Paleontological resources monitors (PRMs) were present on-site to monitor the ground-disturbing construction activities for this reporting period. The Paleontological Resources Monthly Summary Report is included as Appendix G of this report.

3.7 Air Quality

Documentation demonstrating compliance with the Air Quality Construction Mitigation Plan (AQCMP) and construction fugitive dust control measures for this reporting period is included as Appendix H of this report. It includes the daily AQCMP compliance forms, as required by AQ-SC3 and AQ-SC4.

Diesel-fueled engine control measures documentation for this reporting period is also included in Appendix H of this report, as required by AQ-SC5. This includes:

- Log of long-term and short-term diesel-fueled construction equipment that is on-site;
- Diesel fuel receipts; and
- Letters from on-site heavy equipment contractors new to the project expressing their commitment to compliance with the diesel-fueled engine compliance measures.

Please note that for September there was no short-term diesel-fueled equipment on-site.

The Air Quality Management District (AQMD) made a site visit on September 27th. The site visit is noted on the AQCMP form (included in Appendix H) for that day.

4.0 COMPLIANCE REQUIREMENTS COMPLETED DURING THE REPORTING PERIOD

Table 4-1 contains the compliance requirements submitted to the CEC Compliance Project Manager (CPM) during this reporting period. CEC approval is also noted. Items are listed in chronological order of date submitted to CEC. The list of CBO submittals is included in Appendix B.

Table 4-1 Compliance Submittals

COC	Description	Date Due	Date Submitted	CEC Approval Date	Status
PAL-5.1	The project owner shall ensure that the PRS and PRM(s) monitor all construction-related grading, excavation, trenching, and auguring in areas where potential fossil-bearing materials have been identified, both at the site and along any constructed linear facilities associated with the project consistent with the PRMMP. In the event that the PRS determines full-time monitoring is not necessary in locations that were identified as potentially fossil-bearing in the PRMMP, the project owner shall notify and seek the concurrence of the CPM.	As Required	9/20/2011	9/21/2011	Approved /On-going

The Notice of Decision from the CEC for the project General Arrangement Modification was posted on September 23, 2011. Also, the Notice of Determination of CEC Staff approval for the Petition to Modify the Parking Area was posted last month on August 22, 2011.

5.0 DELINQUENT SUBMITTALS

As of the end of the reporting period, there are no delinquent compliance submittals.

6.0 CHANGES TO CONDITIONS OF CERTIFICATION

No changes to any of the COCs occurred during this reporting period.

7.0 FILINGS OR PERMITS ISSUED BY OTHER GOVERNMENTAL AGENCIES

During this reporting period, the CPV Sentinel Energy Project received two temporary power permits from Riverside County. No other filings or permits were issued by other governmental agencies during this reporting period.

8.0 PROJECT COMPLIANCE ACTIVITIES SCHEDULED FOR THE NEXT TWO MONTHS

A summary of the planned submittals over the next two months is included in Table 8-1. The submittals are listed in chronological order of date due to CEC.

Table 8-1 Planned Submittals for October and November 2011

COC	Description	Verification Summary	Due Date to CEC
SOIL& WATER 1.4	SWPPP for SCE Line: The project owner shall comply with the requirements of the general National Pollution Discharge Elimination System (NPDES) permit for discharge of storm water associated with construction activity. The project owner shall develop, obtain compliance project manager (CPM) approval of, and implement a Storm Water Pollution Prevention Plan (SWPPP) for, the construction of the CPV Sentinel site, lay down area, and all linear facilities including the recycled water supply pipeline to PSNGC.	At least 60 days prior to site mobilization, the project owner shall submit to the CPM a copy of the construction SWPPP for review and approval prior to site mobilization. The project owner shall retain a copy on site. The project owner shall submit copies to the CPM of all correspondence between the project owner and the Colorado Region Regional Water Quality Control Board (RWQCB) regarding the NPDES permit for the discharge of storm water associated with construction activity within ten days of its receipt or submittal. Copies of correspondence shall include the notice of intent sent to the State Water Resources Control Board (SWRCB), and the board's confirmation letter indicating receipt and acceptance of the notice of intent.	10/15/11
TSE-1.1	The project owner shall ensure that a schedule of transmission facility design submittals, a Master Drawing List, a Master Specifications List, and a Major Equipment and Structure List are furnished to the CPM and to the CBO. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. To facilitate audits by Energy Commission staff, the project owner shall ensure that designated packages are provided to the CPM when requested. To facilitate audits by Energy Commission staff, the project owner shall provide designated packages to the CPM when requested.	The project owner shall submit the schedule, a Master Drawing List, and a Master Specifications List to the CBO and to the CPM. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. Additions and deletions shall be made to the table only with CPM and CBO approval. The project owner shall provide schedule updates in the Monthly Compliance Report.	10/15/11
TSE-1.2	The project owner shall ensure that a schedule of transmission facility design submittals, a Master Drawing List, a Master Specifications List, and a Major Equipment and Structure List are furnished to the CPM and to the CBO. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. To facilitate audits by Energy Commission staff, the project owner shall provide designated packages to the CPM when requested.	The project owner shall provide schedule updates in the Monthly Compliance Report	10/15/11
TSE-5.1	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: a) Design drawings, specifications and calculations conforming with CPUC General Order 95 or NESC, Title 8, Articles 35, 36 and 37 of the "High Voltage Electric Safety Orders", NEC, applicable interconnection standards and related industry standards, for the poles/towers, foundations, anchor bolts, conductors, grounding systems and major switchyard equipment.	10/15/11

COC	Description	Verification Summary	Due Date to CEC
TSE-5.2	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: b) For each element of the transmission facilities identified above, the submittal package to the CBO shall contain the design criteria, a discussion of the calculation method(s), a sample calculation based on "worst case conditions" and a statement signed and sealed by the registered engineer in responsible charge, or other acceptable alternative verification, that the transmission element(s) will conform with CPUC General Order 95 or NESC, Title 8, California Code of Regulations, Articles 35, 36 and 37 of the, "High Voltage Electric Safety Orders", NEC, applicable interconnection standards, and related industry standards.	10/15/11
TSE-5.3	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: c) Electrical one-line diagrams signed and sealed by the registered professional electrical engineer in responsible charge, a route map, and an engineering description of equipment and the configurations covered by requirements TSE-5 a) through f)	10/15/11
TSE-5.4	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: d) A line route drawing after selecting one of the alternate route options for the generator 230 kV interconnection tie line.	10/15/11
TSE-5.5	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: e) The SPS sequencing and timing if applicable shall be provided concurrently to the CPM.	10/15/11
TSE-5.6	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: f) The executed project owner and California ISO Large Generator Interconnection Agreement.	10/15/11
TSE-5.7	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: g) A letter stating that the mitigation measures or projects selected by the transmission owners for each criteria violation are acceptable.	10/15/11

COC	Description	Verification Summary	Due Date to CEC
TSE-5.8	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: h) The Operational study report based on 2010 system conditions (including operational mitigation measures) from the California SO and/or SCE.	10/15/11
SOIL& WATER-3.1	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	The project owner shall do all of the following: 1. No later than 30 days prior to the construction of the onsite water supply wells, the project owner shall submit two (2) copies to the CPM of the water well construction packet submitted to the County of Riverside. 2. No later than 15 days prior to the construction of the onsite water supply wells, the project owner shall submit two (2) copies of the written concurrence document from the County of Riverside indicating that the proposed well construction activities comply with all county well requirements and meet the requirements established by the county's water well permit program .	11/01/11
TSE-4	For the power plant switchyard, outlet line and termination, the project owner shall ensure that until plans for that increment have been approved by the CBO construction does not begin any increment. These plans, together with design changes and design change notices, shall remain on the site for one year after completion of construction. The project owner shall ensure that the CBO is requested to inspect the installation to ensure compliance with the requirements of applicable LORS.	At least 30 days (or a lesser number of days mutually agreed to by the project owner and the CBO) prior to the start of each increment of construction, the project owner shall ensure that the final design plans, specifications and calculations for equipment and systems of the power plant switchyard, outlet line and termination, including a copy of the signed and stamped statement from the responsible electrical engineer attesting to compliance with the applicable LORS, are submitted to the CBO for review and approval and a copy of the transmittal letter is sent to the CPM in the next Monthly Compliance Report.	11/01/11

COC	Description	Verification Summary	Due Date to CEC
TLSN-1	The project owner shall ensure that the proposed transmission lines are constructed according to the requirements of California Public Utility Commission's GO-95, GO-52, GO-131-D, Title 8, and Group 2. High Voltage Electrical Safety Orders, Sections 2700 through 2974 of the California Code of Regulations, and Southern California Edison's EMF-reduction guidelines.	The project owner shall submit to the Compliance Project Manager (CPM) a letter signed by a California registered electrical engineer affirming that the lines will be constructed according to the requirements stated in the condition.	11/14/11
TSE-2.1	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	The project owner shall submit to the CBO for review and approval, the names, qualifications and registration numbers of all engineers assigned to the project. If any one of the designated engineers is subsequently reassigned or replaced, the project owner shall submit the name, qualifications and registration number of the newly assigned engineer to the CBO for review and approval. The project owner shall notify the CPM of the CBO's approval of the new engineer. This engineer shall be authorized to halt earthwork and to require changes; if site conditions are unsafe or do not conform with predicted conditions used as a basis for design of earthwork or foundations.	11/14/11
TSE-2.2	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	The project owner shall notify the CPM of the CBO's approvals of the engineers	11/14/11

COC	Description	Verification Summary	Due Date to CEC
SOIL& WATER-3.2	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	No later than 60 days after installation of each well at the project site, the project owner shall ensure that the well driller submits a Well Completion Report to the DWR with a copy provide to the CPM. The project owner shall submit to the CPM together with the Well Completion Report a copy of well drilling logs, water quality analyses, and any inspection reports that may be: 1. Submit copies to the CPM of any proposed well construction or operation permit changes within ten (10) days of submittal to or receipt from the County of Riverside. 2. Submit copies of any water well permit-related well monitoring reports required by the County of Riverside to the CPM in the annual compliance report. 3. No later than fifteen (15) days after completion of the onsite water supply wells, the project owner shall submit documentation to the CPM and the RWQCB that well drilling ac available for each well installed.	11/30/11

COC	Description	Verification Summary	Due Date to CEC
SOIL& WATER-3.3	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	During well construction and for the operational life of the well, the project owner shall: 1. Submit copies to the CPM of any proposed well construction or operation changes. 2. Submit copies of any water well monitoring reports required by the County of Riverside to the CPM in the annual compliance report. 3. No later than fifteen (15) days after completion of the onsite water supply wells, the project owner shall submit documentation to the CPM and the RWQCB that well drilling activities were conducted in compliance with Title 23, California Code of Regulations, Chapter 15, Discharges of Hazardous Wastes to Land, (23 CCR, sections 2510 et seq.) requirements and that any onsite drilling sumps used for project drilling activities were removed in compliance with 23 CCR section 2511(c).	11/30/11

Please note that in the previous monthly report SOIL&WATER-1.3 had a due date of October 1, 2011, but the due date has been revised to January 1, 2012 based on the update construction schedule for the gas line that was provided by Southern California Gas. The first phase of gas line installation is within Melissa Lane and is part of initial SWPPP (SOIL&WATER-1.1 and 1.2), which has already been approved by the CEC. Phase 2 of gas line installation will occur in 2012 and will require a separate SWPPP as specified in SOIL&WATER-1.3.

Appendix B contains the list of anticipated CBO submittals for the project.

Table 8-2 lists the on-going construction compliance activities.

Table 8-2 On-going Construction Compliance Activities

COC	Description Summary
AQ-SC3	AQCMP documentation for dust control measures
AQ-SC4	Dust plume response
AQ-SC5	Diesel-fueled engine control
BIO-2	Biological Resources monthly summary report
BIO-6	Implementation of BRMIMP
BIO-7	Impact Avoidance Mitigation Measures
BIO-8	Mitigation Management to Avoid Harassment or Harm
BIO-5 CUL-5 PAL-4	WEAP training for all on-site workers
CUL-2	Weekly report from CRS to CPM of anticipated construction activities for the following week
CUL-3	CRMMP implementation
CUL-6	Cultural Resources monthly monitoring summary report
GEN-2.2 TSE-1.2	Project construction schedule updates
GEN-3.2	CBO Payment receipts
GEN-6.2 GEN-7.1 MECH-1.2 MECH-2.2 STRUC-4.2	Documenting of all CBO approvals (special inspections, CBO inspections, plan checks, corrective actions, submittals, and all other CBO approvals) and CBO submittal transmittal letters.
PAL-3	PRMMP implementation
PAL-5	Paleontological Resources monthly monitoring summary report
WORKER SAFETY-3.2	CSS monthly safety inspection report

9.0 LISTING OF THE MONTH'S ADDITIONS TO THE COMPLIANCE FILE

The compliance file is being maintained by URS in the Santa Ana, California office. An on-site file is also being maintained for all construction documents. For this reporting period, copies of submittals indicated in Table 4-1 were added to the compliance files.

10.0 REQUESTS TO DISPOSE OF ITEMS REQUIRED TO BE MAINTAINED IN THE COMPLIANCE FILE

For this reporting period, no requests for the disposal of items in the project owner's compliance files were made.

11.0 COMPLAINTS, NOTICES OF VIOLATIONS, WARNINGS AND CITATIONS

No complaints, notices of violation, official warnings, or citations have been received during this reporting period.

12.0 PENDING CEC APPROVALS

There are no outstanding CEC approvals for COCs submitted by the project that requested approvals by the end of September.

FIGURE 1
Construction Schedule

CPV Sentinel, LLC

Milestone

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1002	CPV / GE Owner Definition Meeting	0	0	22JUL08A	
1005	Receive GE LMS 100 Go By Design	0	0		22JUL08A
1000	CPV Provide Limited Notice to Proceed	0	0	28JUL08A	
1006	CPV Suspend the Project	0	0	02DEC08A	
1007	CPV Provide Suspension Release EPC (LNTP)	0	0		14FEB11A
1013	Release Exhaust Duct for Engineering	0	0		22FEB11A
1011	CPV Provide Suspension Release GE	0	0		11MAR11A
1017	Release Field Erected Tanks for Engineering	0	0		23MAR11A
1015	Release Wtr Treatment System for Engineering	0	0		12APR11A
1012	Release GSU for Engineering & Hold Mfg. Slot	0	0		06MAY11A
1040	CPV Provide GE LMS 100 Fnd / Struct Design GO BY	0	0		16MAY11A
1050	CPV Provide GE LMS 100 Piping Design GO BY	0	0		16MAY11A
1060	CPV Provide GE LMS 100 Elec. Design Drawings	0	0		16MAY11A
1051	CPV Provide GE LMS 100 Piping Design (IFC)	0	0		23MAY11A
1010	CPV Provide Notice To Proceed	0	0	26MAY11A	
1014	Release Gas Compressors for Engineering	0	0		27MAY11A
1016	Release Cooling Tower for Engineering	0	0		27MAY11A
1030	CPV Provide Site Access "for Mobilization"	0	0	01JUN11A	
1090	CPV Provide Site Potable Water	0	0		01JUN11A
1080	CPV Provide Site Construction Water	0	0		10JUN11A
1041	CPV Provide GE LMS 100 Fnd / Struct Design (IFC)	0	0		13JUN11A
1070	CPV Provide Site Construction Temporary Power	0	0		13JUN11A
1061	CPV Provide GE LMS 100 Electrical Design (IFC)	0	0		15JUN11A

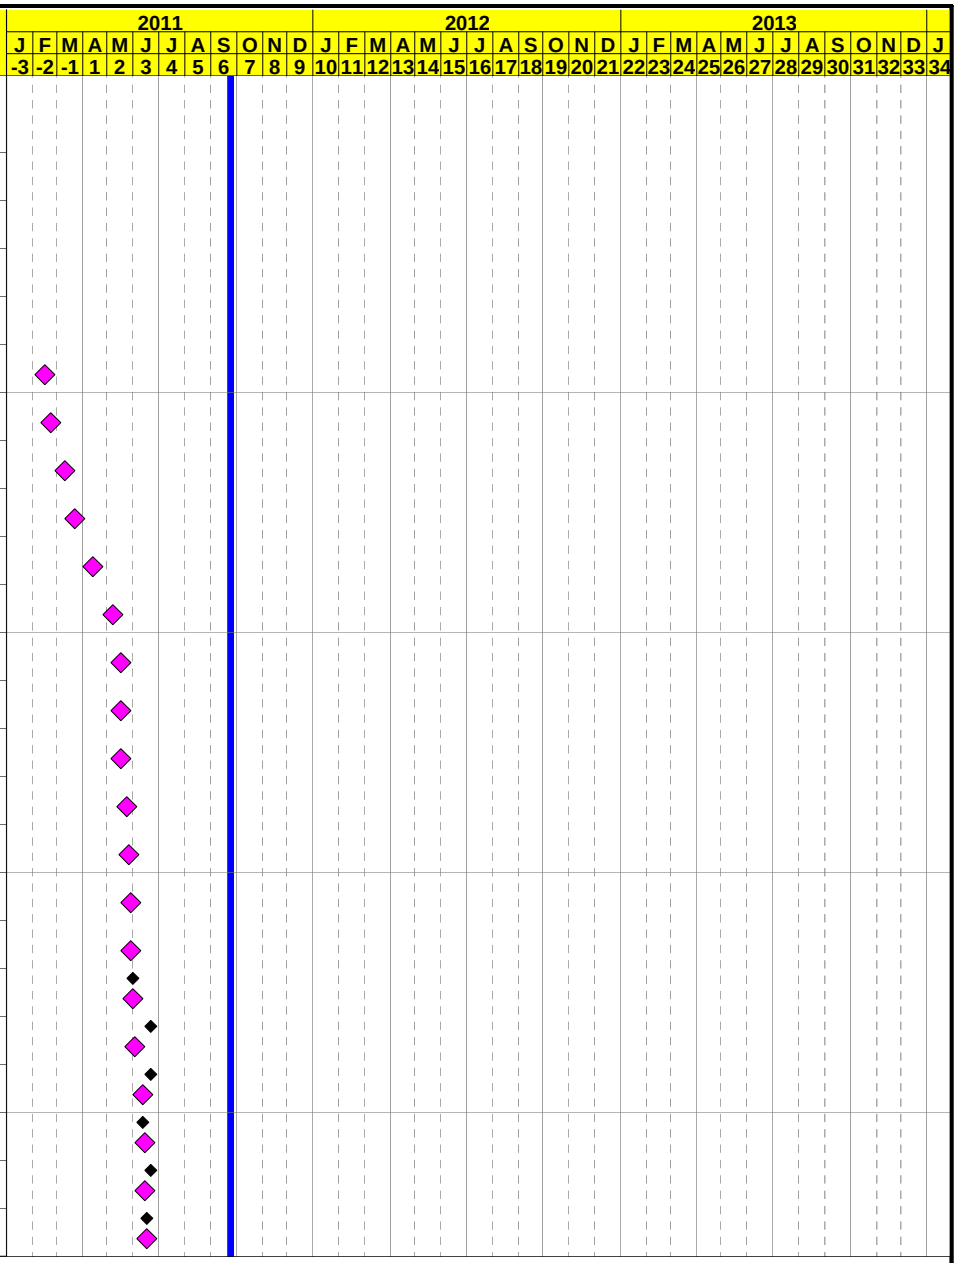

Start Date	01MAY08
Finish Date	26NOV13
Data Date	24SEP11

Gemma Power Systems

CPV Sentinel

Level One Project Schedule

Project Baseline
Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1031	CPV Provide Site Access Road Complete	0	0	22JUN11A	
1190	CPV Provide Full Construction Power	0	0		18NOV11
1191	CPV Provide Site Communication Interface	0	0		18NOV11
1100	CPV Provide Complete 4 New On Site Wells	0	0		01DEC11
1192	CPV Provide GE TA's	0	0	11JAN12	
1210	CPV Provide Back Feed Power	0	0		06OCT12
1201	CPV Provide Operators	0	0	12OCT12	
1230	CPV Provide Fuel Gas	0	0		21OCT12
1200	CPV Provide First Fills	0	0		16NOV12
1220	CPV Provide Commissioning Water & Demin Trailers	0	0		30NOV12
1240	CPV Provide the Ability to put Power to the Grid	0	0	27NOV13	
GE Equipment Delivery					
1109	GE Fabricate GTG & Accessories	259	98	12MAR11A	30DEC11
1311	RTS Balance of Equipment Unit 1, Houston	0	0		30DEC11
1312	RTS Gas Turbine Package Unit 1, Houston	0	0		30DEC11
1314	RTS PCM Unit 1, Houston	0	0		30DEC11
1318	RTS Water Pump Skid Unit 1, Mexico City	0	0		30DEC11
1321	RTS Balance of Equipment Unit 2, Houston	0	0		30DEC11
1322	RTS Gas Turbine Package Unit 2, Houston	0	0		30DEC11
1324	RTS PCM Unit 2, Houston	0	0		30DEC11
1328	RTS Water Pump Skid Unit 2, Mexico City	0	0		30DEC11
1331	RTS Balance of Equipment Unit 3, Houston	0	0		30DEC11
1332	RTS Gas Turbine Package Unit 3, Houston	0	0		30DEC11
1333	FAS Generator Unit 3, Pizen	0	0		30DEC11
1317	FAS VBV Equip. Unit 1, Shanghai	0	0		06JAN12
1327	FAS VBV Equip. Unit 2, Shanghai	0	0		06JAN12
1319	FAS Intercooler Piping Unit 1, South Korea	0	0		13JAN12
1329	FAS Intercooler Piping Unit 2, South Korea	0	0		13JAN12
1316	RTS Air Filter Unit 1	0	0		30JAN12
1326	RTS Air Filter Unit 2	0	0		30JAN12

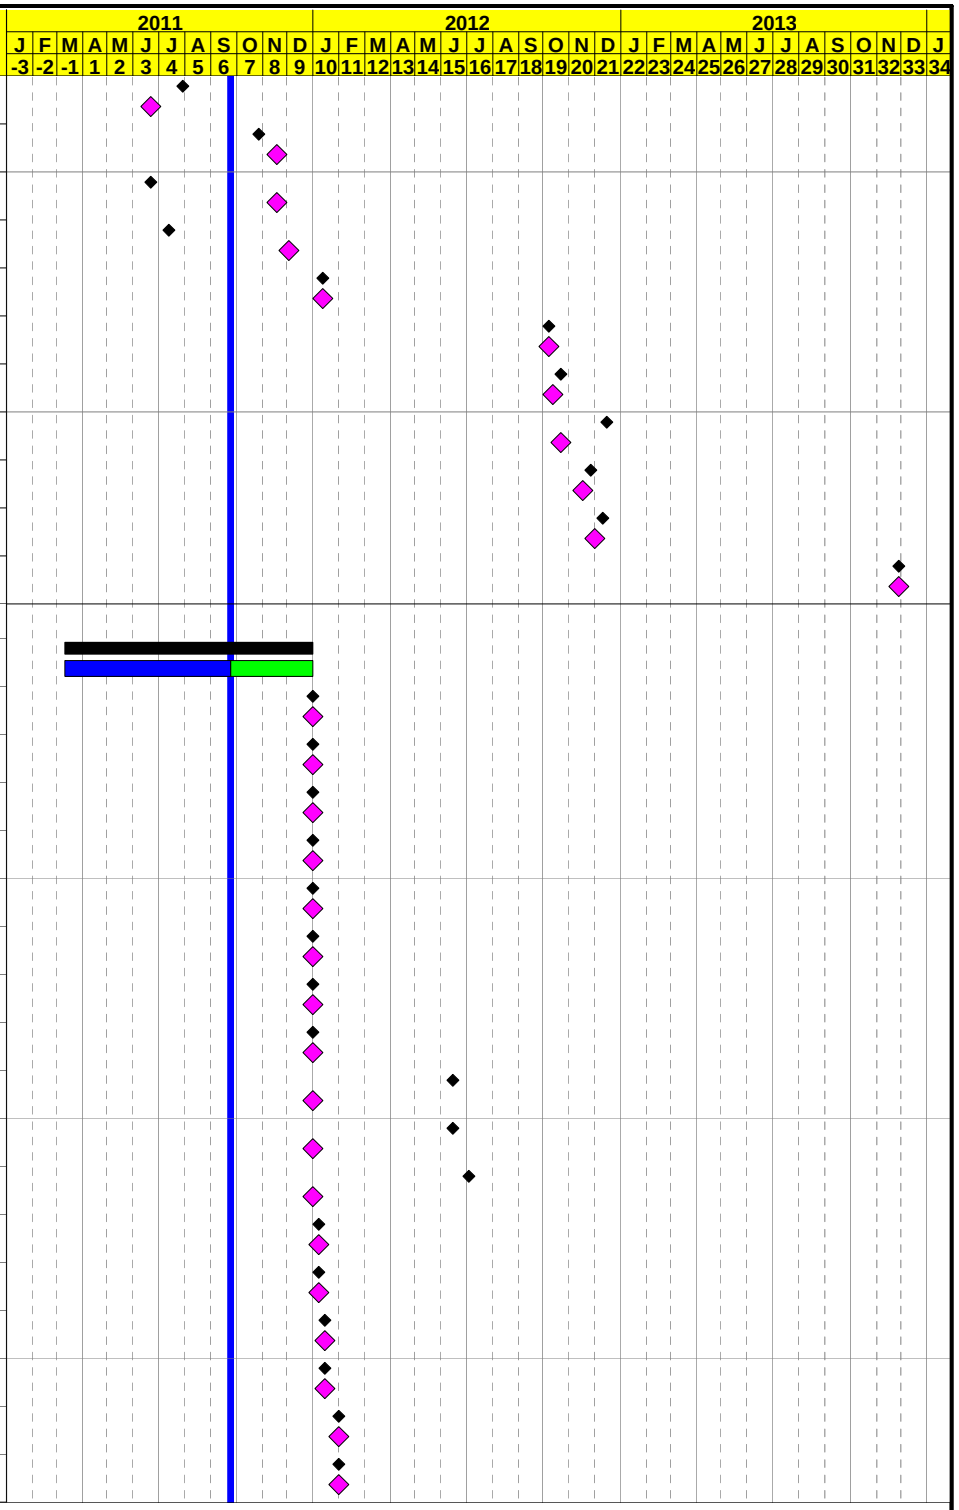

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1315	FAS Intercooler Unit 1, South Korea	0	0		13FEB12
1325	FAS Intercooler Unit 2, South Korea	0	0		13FEB12
1313	FAS Generator Unit 1, Pizen	0	0		20FEB12
1323	FAS Generator Unit 2, Pizen	0	0		20FEB12
1334	RTS PCM Unit 3, Houston	0	0		30MAR12
1335	FAS Intercooler Unit 3, South Korea	0	0		30MAR12
1336	RTS Air Filter Unit 3	0	0		30MAR12
1337	FAS VBV Equip. Unit 3, Shanghai	0	0		30MAR12
1338	RTS Water Pump Skid Unit 3, Mexico City	0	0		30MAR12
1339	FAS Intercooler Piping Unit 3, South Korea	0	0		30MAR12
1341	RTS Balance of Equipment Unit 4, Houston	0	0		02JUL12
1342	RTS Gas Turbine Package Unit 4, Houston	0	0		02JUL12
1346	RTS Air Filter Unit 4	0	0		02JUL12
1348	RTS Water Pump Skid Unit 4, Mexico City	0	0		02JUL12
1347	FAS VBV Equip. Unit 4, Shanghai	0	0		09JUL12
1345	FAS Intercooler Unit 4, South Korea	0	0		16JUL12
1349	FAS Intercooler Piping Unit 4, South Korea	0	0		16JUL12
1343	FAS Generator Unit 4, Pizen	0	0		23JUL12
1351	RTS Balance of Equipment Unit 5, Houston	0	0		30JUL12
1352	RTS Gas Turbine Package Unit 5, Houston	0	0		30JUL12
1356	RTS Air Filter Unit 5	0	0		30JUL12
1358	RTS Water Pump Skid Unit 5, Mexico City	0	0		30JUL12
1344	RTS PCM Unit 4, Houston	0	0		01AUG12
1357	FAS VBV Equip. Unit 5, Shanghai	0	0		06AUG12
1355	FAS Intercooler Unit 5, South Korea	0	0		13AUG12
1359	FAS Intercooler Piping Unit 5, South Korea	0	0		13AUG12
1361	RTS Balance of Equipment Unit 6, Houston	0	0		15AUG12
1362	RTS Gas Turbine Package Unit 6, Houston	0	0		15AUG12
1366	RTS Air Filter Unit 6	0	0		15AUG12
1368	RTS Water Pump Skid Unit 6, Mexico City	0	0		15AUG12

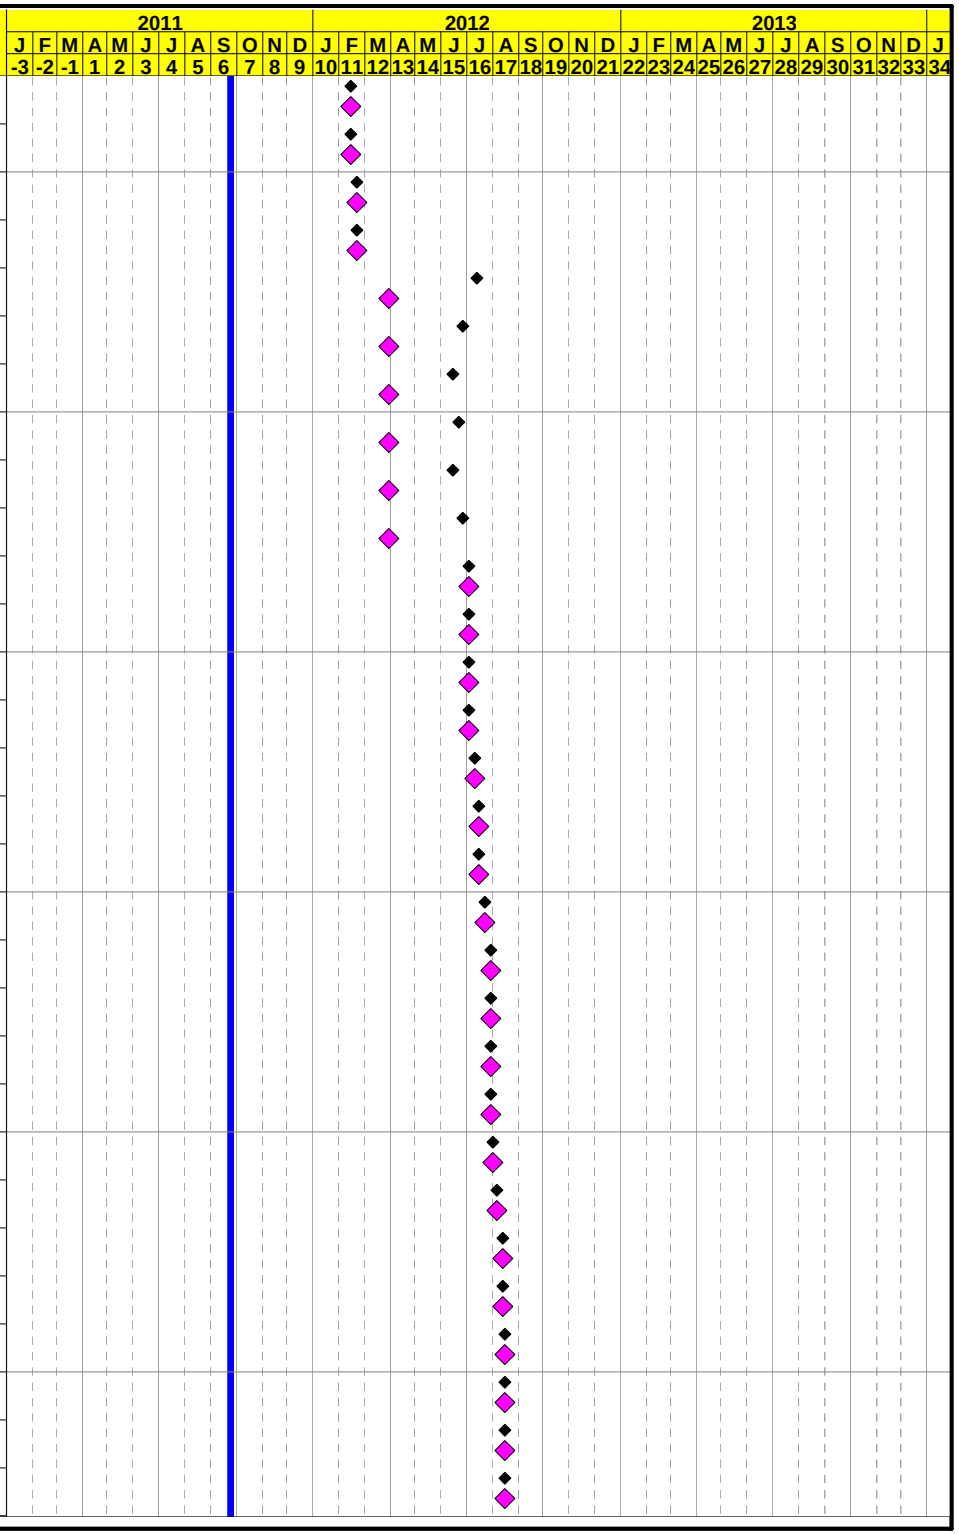

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1353	FAS Generator Unit 5, Pizen	0	0		20AUG12
1367	FAS VBV Equip. Unit 6, Shanghai	0	0		22AUG12
1354	RTS PCM Unit 5, Houston	0	0		29AUG12
1365	FAS Intercooler Unit 6, South Korea	0	0		29AUG12
1369	FAS Intercooler Piping Unit 6, South Korea	0	0		29AUG12
1371	RTS Balance of Equipment Unit 7, Houston	0	0		29AUG12
1372	RTS Gas Turbine Package Unit 7, Houston	0	0		29AUG12
1376	RTS Air Filter Unit 7	0	0		29AUG12
1378	RTS Water Pump Skid Unit 7, Mexico City	0	0		29AUG12
1363	FAS Generator Unit 6, Pizen	0	0		05SEP12
1377	FAS VBV Equip. Unit 7, Shanghai	0	0		05SEP12
1375	FAS Intercooler Unit 7, South Korea	0	0		12SEP12
1379	FAS Intercooler Piping Unit 7, South Korea	0	0		12SEP12
1381	RTS Balance of Equipment Unit 8, Houston	0	0		12SEP12
1382	RTS Gas Turbine Package Unit 8, Houston	0	0		12SEP12
1386	RTS Air Filter Unit 8	0	0		12SEP12
1388	RTS Water Pump Skid Unit 8, Mexico City	0	0		12SEP12
1364	RTS PCM Unit 6, Houston	0	0		14SEP12
1373	FAS Generator Unit 7, Pizen	0	0		19SEP12
1387	FAS VBV Equip. Unit 8, Shanghai	0	0		19SEP12
1385	FAS Intercooler Unit 8, South Korea	0	0		26SEP12
1389	FAS Intercooler Piping Unit 8, South Korea	0	0		26SEP12
1374	RTS PCM Unit 7, Houston	0	0		28SEP12
1383	FAS Generator Unit 8, Pizen	0	0		03OCT12
1384	RTS PCM Unit 8, Houston	0	0		12OCT12
MOTT MACDONALD					
Engineering Design					
EN301000	Engineering LNTP	0	0	28JUL08A	
EN301030	Water Balance Design	66	0	28JUL08A	02OCT08A
EN301010	Electrical One Line Design	44	0	28JUL08A	21NOV08A

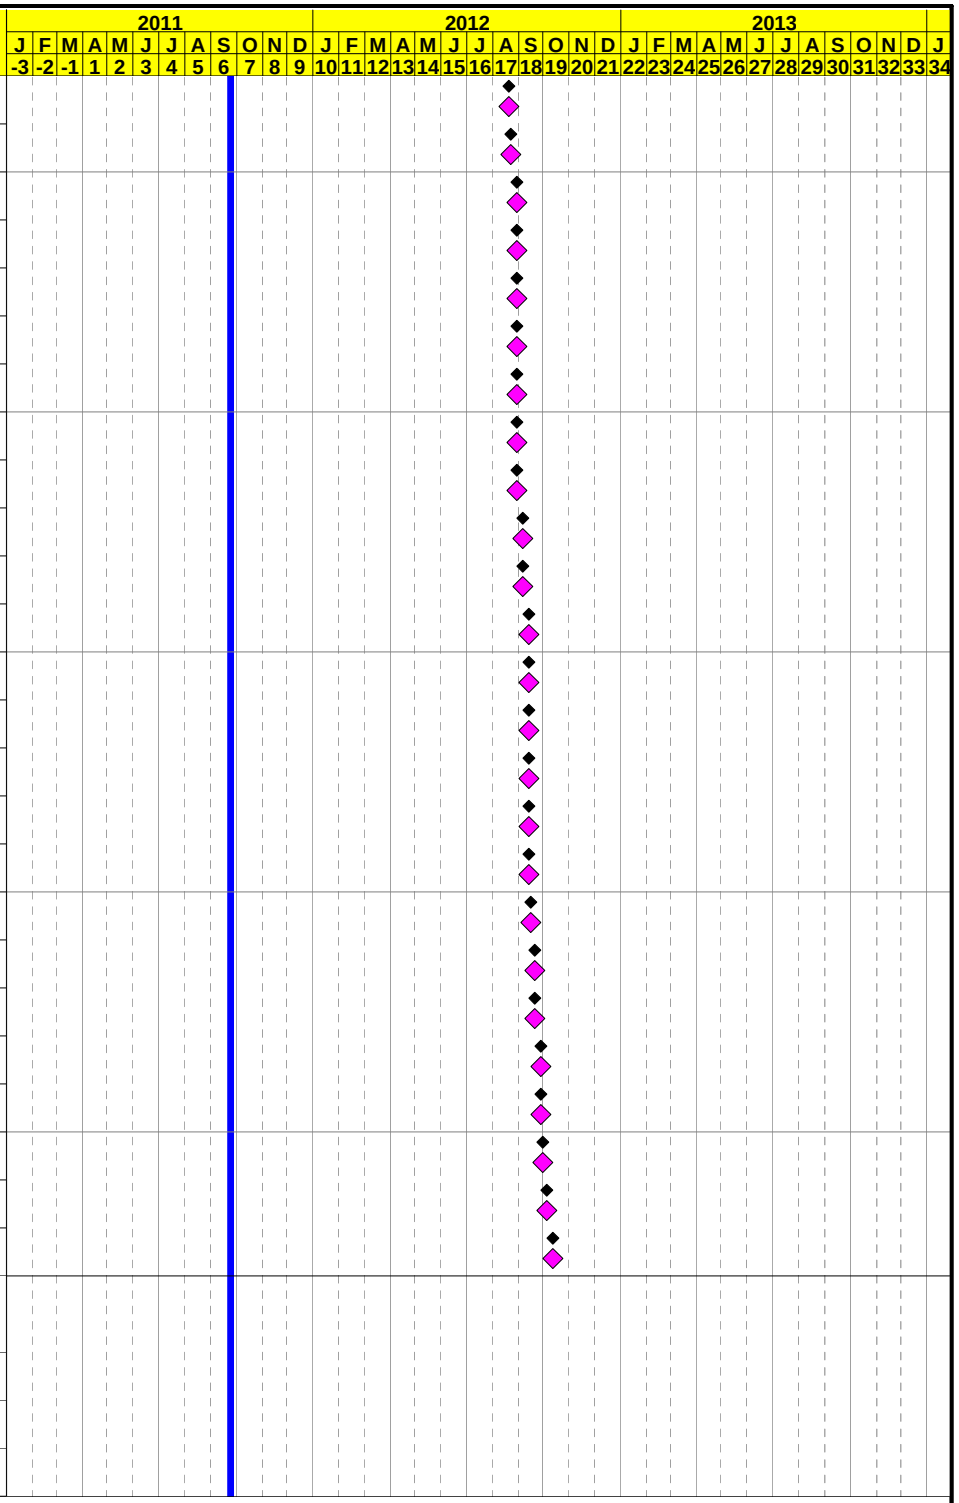

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
EN301031	P&ID Design	88	0	12AUG08A	04OCT08A
EN301001	Engineering Suspension Release (NTP)	0	0	14FEB11A	
MM Concrete Foundations Drawings					
EN301060	Foundation Design (GTG's & Ancillaries)	77*	0*	16MAY11A	02SEP11A
MM Mechanical Documents					
EN301080	Piping Under Ground Utilities Design	135*	0*	01FEB11A	12AUG11A
EN301100	Piping Above Grade Design	70*	70*	17OCT11	27JAN12
MM Mechanical Specifications					
EN301041	Equipment Specification Exhaust System	41	0	28JUL08A	26SEP08A
EN301046	Equipment Specification Cooling Towers	71*	0*	09MAR11A	17JUN11A
MM Electrical Documents					
EN301070	Electrical Under Ground Utilities Design	102*	15*	20MAY11A	14OCT11
EN301090	Electrical Above Grade Design	121*	116*	19SEP11A	13MAR12
MM Switch Yard Specifications					
EN301021	Equipment Specification / Design Switch Yard	92*	1*	16MAY11A	26SEP11
Gemma Power Systems					
GE Equipment Delivery					
1130	Start Ship - Complete Del GTG Unit 3 Package	106	106	31DEC11	14APR12
1110	Start Ship - Complete Del GTG Unit 1 Package	136	136	31DEC11	14MAY12
1120	Start Ship - Complete Del GTG Unit 2 Package	136	136	31DEC11	14MAY12
1111	Receive GTG BOP Package Eq & Piping Unit 1	0	0		20JAN12
1112	Receive GTG Unit 1	0	0		20JAN12
1121	Receive GTG BOP Package Eq & Piping Unit 2	0	0		20JAN12
1122	Receive GTG Unit 2	0	0		20JAN12
1131	Receive GTG BOP Package Eq & Piping Unit 3	0	0		10FEB12
1132	Receive GTG Unit 3	0	0		10FEB12
1133	Receive Generator Unit 3	0	0		16APR12
1113	Receive Generator Unit 1	0	0		14MAY12
1123	Receive Generator Unit 2	0	0		14MAY12
1140	Start Ship - Complete Del GTG Unit 4 Package	106	106	02JUL12	15OCT12
1141	Receive GTG BOP Package Eq & Piping Unit 4	0	0		23JUL12
1142	Receive GTG Unit 4	0	0		23JUL12

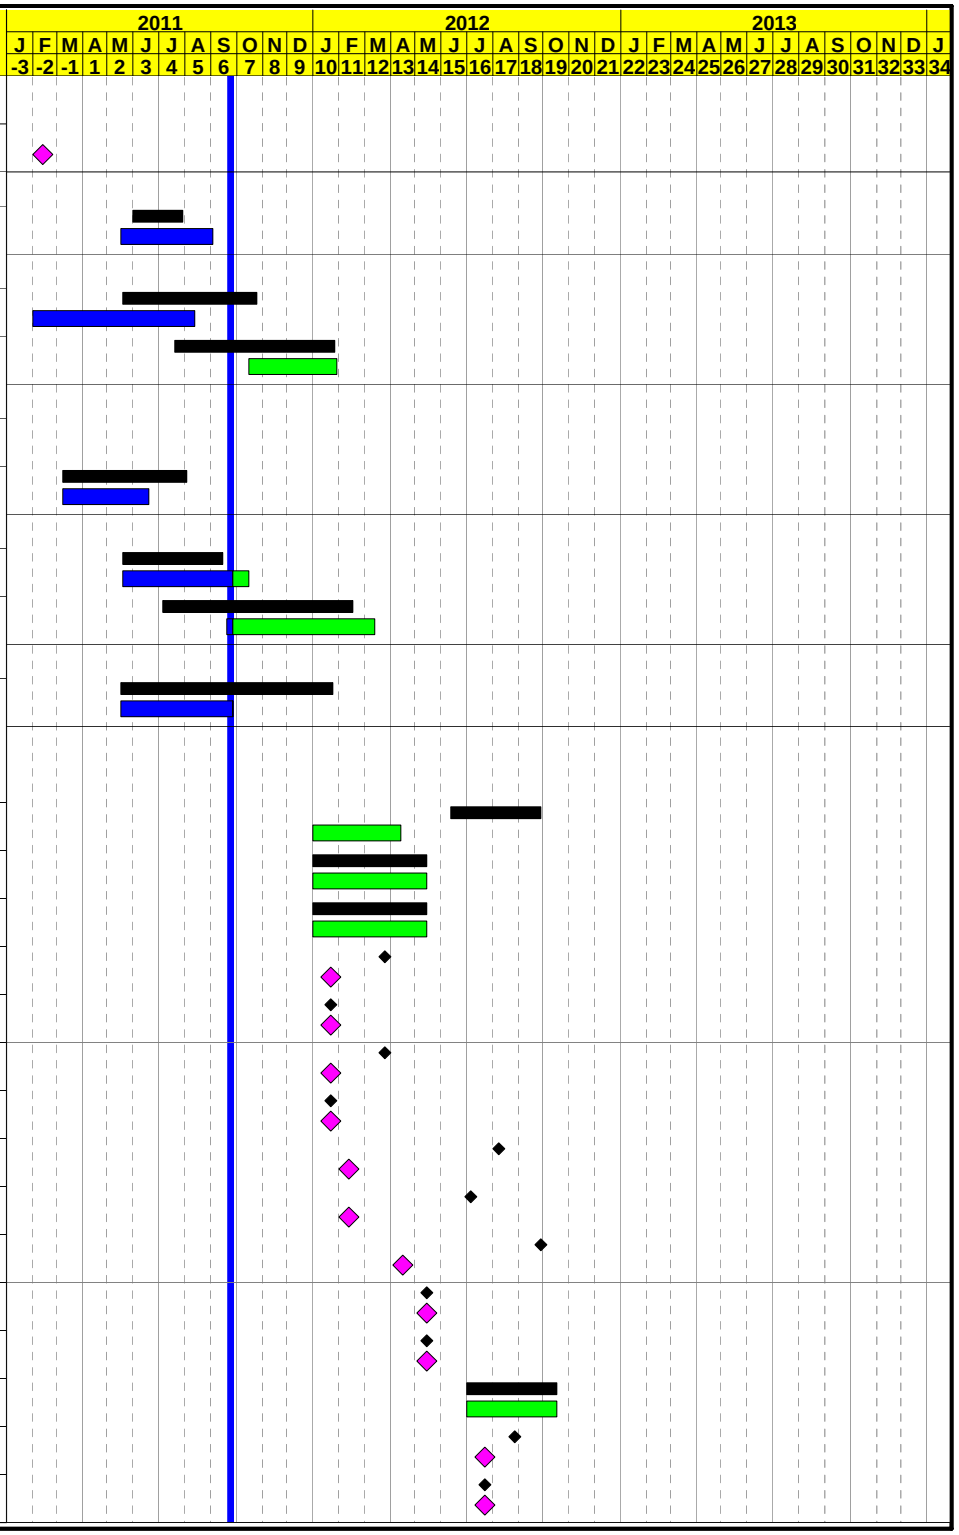

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1150	Start Ship - Complete Del GTG Unit 5 Package	106	106	30JUL12	12NOV12
1160	Start Ship - Complete Del GTG Unit 6 Package	106	106	15AUG12	28NOV12
1151	Receive GTG BOP Package Eq & Piping Unit 5	0	0		20AUG12
1152	Receive GTG Unit 5	0	0		20AUG12
1170	Start Ship - Complete Del GTG Unit 7 Package	106	106	29AUG12	12DEC12
1161	Receive GTG BOP Package Eq & Piping Unit 6	0	0		05SEP12
1162	Receive GTG Unit 6	0	0		05SEP12
1180	Start Ship - Complete Del GTG Unit 8 Package	106	106	12SEP12	26DEC12
1171	Receive GTG BOP Package Eq & Piping Unit 7	0	0		19SEP12
1172	Receive GTG Unit 7	0	0		19SEP12
1181	Receive GTG BOP Package Eq & Piping Unit 8	0	0		03OCT12
1182	Receive GTG Unit 8	0	0		03OCT12
1143	Receive Generator Unit 4	0	0		15OCT12
1153	Receive Generator Unit 5	0	0		12NOV12
1163	Receive Generator Unit 6	0	0		28NOV12
1173	Receive Generator Unit 7	0	0		12DEC12
1183	Receive Generator Unit 8	0	0		26DEC12
CEC / CBO Submittals					
CN1900	CEC 90 Day Pre-Construction Submittals	0	0	18MAR11A	
CN1910	CEC 60 Day Pre-Construction Submittals	0	0	15APR11A	
CN1920	CEC 30 Day Pre-Construction Submittals	0	0	06MAY11A	
Procurement					
PR510100	Exhaust Equipment RFP	34*	0*	15FEB11A	04APR11A
PR520100	Long Lead Transformers RFP	35*	0*	21MAR11A	06MAY11A
PR510101	Exhaust Equipment Vendor Engineering	58*	0*	05APR11A	27JUN11A
PR520101	Long Lead Transfr Vendor Engineering	73*	0*	09MAY11A	22AUG11A
PR331201	Switch Yard RFP	64*	0*	20JUN11A	19SEP11A
PR510000	Exhaust Equipment Fabrication	298*	235*	27JUN11A	29AUG12
PR520000	Long Lead Transformers Fabrication	320*	297*	23AUG11A	28NOV12
PR510050	BOP Mechanical Equipment Fabrication	271*	257*	06SEP11A	01OCT12

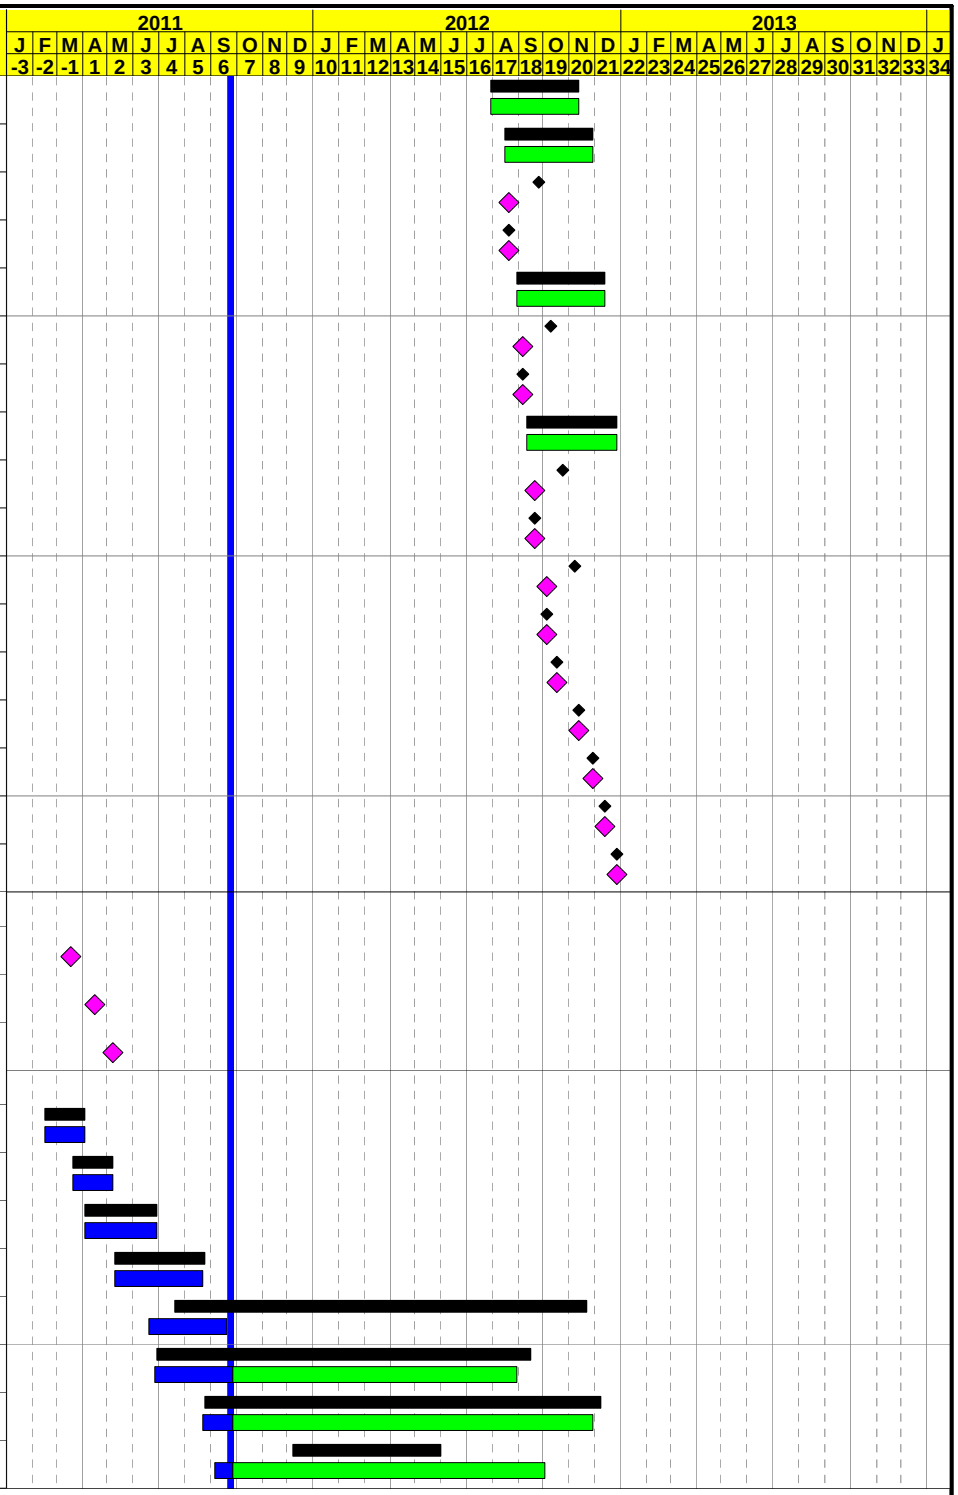

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
PR331202	Switch Yard Vendor Engineering	157*	152*	20SEP11A	03MAY12
PR331203	Switch Yard Fabrication	196	196	04OCT11	13JUL12
PR520010	BOP Electrical Equipment Fabrication	159*	159*	07DEC11	24JUL12
Unit Construction Overview					
CN313101	GTG & Ancl Unit 1 Erection Mech, Elect, & Piping	162*	162*	23JAN12	02OCT12
CN313102	GTG & Ancl Unit 2 Erection Mech, Elect, & Piping	176*	176*	26JAN12	26OCT12
CN313103	GTG & Ancl Unit 3 Erection Mech, Elect, & Piping	171*	171*	13FEB12	05NOV12
CN313104	GTG & Ancl Unit 4 Erection Mech, Elect, & Piping	102*	102*	24JUL12	31DEC12
CN313105	GTG & Ancl Unit 5 Erection Mech, Elect, & Piping	111*	111*	21AUG12	12FEB13
CN313106	GTG & Ancl Unit 6 Erection Mech, Elect, & Piping	108*	108*	06SEP12	25FEB13
CN313107	GTG & Ancl Unit 7 Erection Mech, Elect, & Piping	117*	117*	20SEP12	25MAR13
CN313108	GTG & Ancl Unit 8 Erection Mech, Elect, & Piping	108*	108*	04OCT12	25MAR13
Civil Site Work					
CN2000	Site Mobilization	5	0	01JUN11A	06JUN11A
CN340100	Soil Erosion & Control Implementation	14	0	16JUN11A	08JUL11A
CN340110	Mass Site Excavation	180	0	11JUL11A	09SEP11A
Foundation Construction					
CN34201008	Install Foundation Block Fire Pump	2	0	21JUN11A	21JUN11A
CN3419	Foundation Construction Units 1 - 8	145*	138*	15SEP11A	01MAY12
CN342090	Foundation Construction BOP	145*	145*	27SEP11	19JUN12
Buildings					
CN343500	Administration Building Erection	105	105	23MAR12	31AUG12
Mechanical					
CN313090	Mechanical Equipment Erection BOP	68*	68*	22JUN12	05OCT12
Tanks Field Erected					
CN325500	Field Erected Tanks Installation	86*	86*	29NOV11	24APR12
Piping					
CN310100	Install Under Ground Mechanical Utilities	110*	110*	27OCT11	18APR12
CN311090	Piping Installation BOP	99*	99*	29JUN12	30NOV12
Electrical					
CN330100	Under Ground Electrical Utilities	93*	93*	15DEC11	27APR12
CN331200	Electrical Equipment Switch Yard Erection	199	199	08MAR12	15JAN13

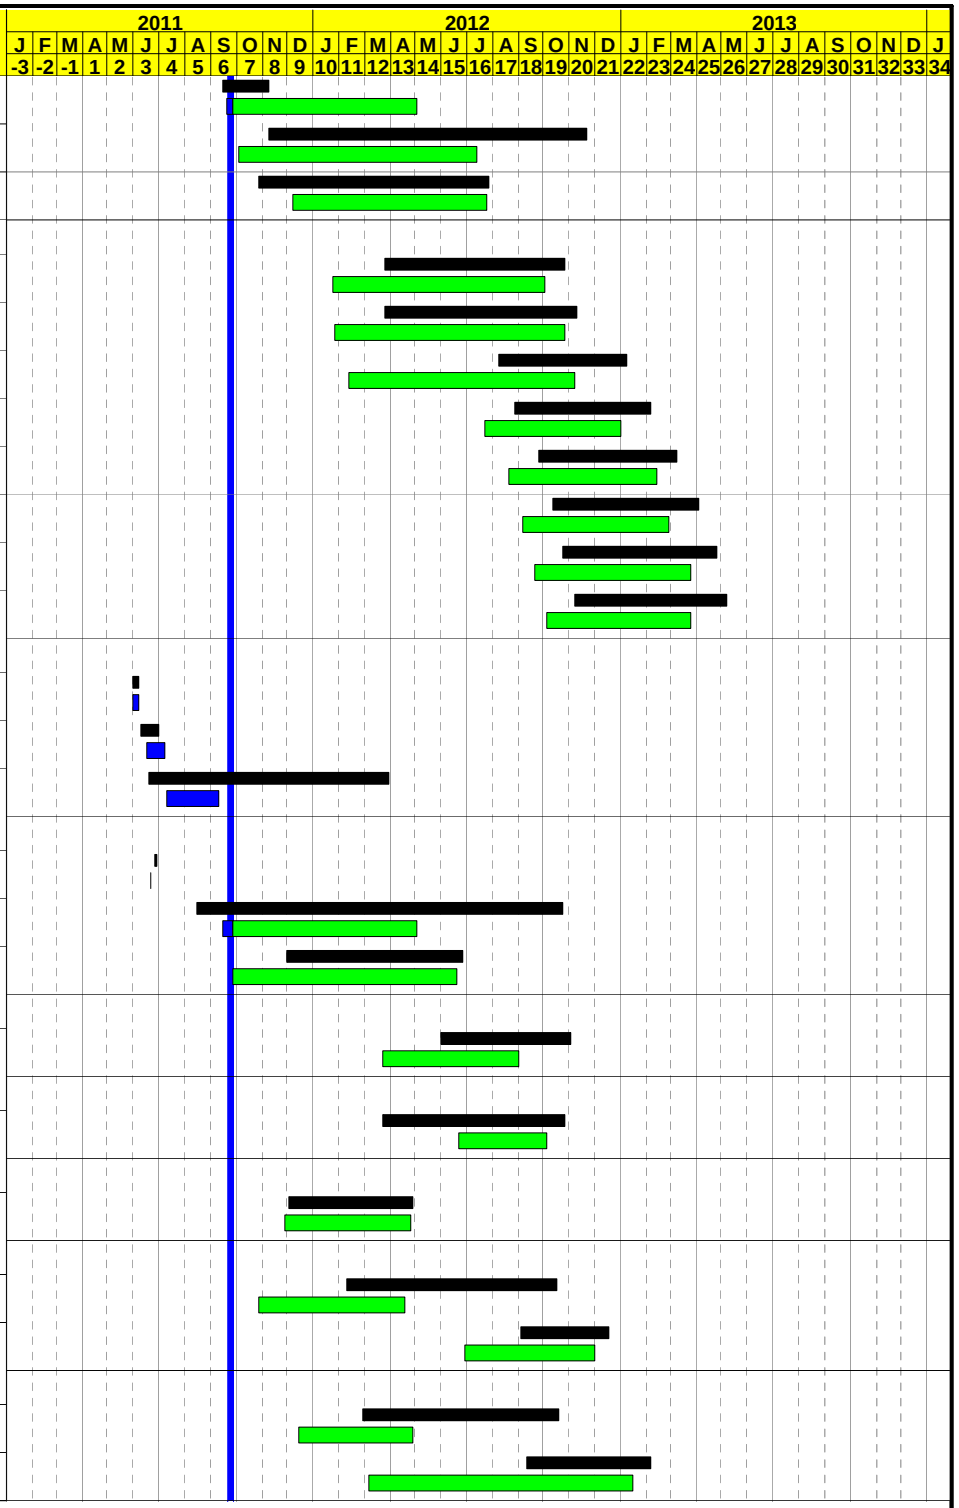

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
CN330190	Electrical Equipment BOP	82*	82*	16MAY12	20SEP12
CN331090	Electrical Conduit, Cable, Terms BOP	152*	152*	20JUN12	14FEB13
Start Up					
CN7101	Cold, Hot Commission & Performance Test Unit 1	94*	94*	11DEC12	29MAR13
CN7102	Cold, Hot Commission & Performance Test Unit 2	96*	96*	20DEC12	10APR13
CN7103	Cold, Hot Commission & Performance Test Unit 3	92*	92*	03JAN13	19APR13
CN7104	Cold, Hot Commission & Performance Test Unit 4	89*	89*	14JAN13	26APR13
CN710109	First Fire & FSNL GTG Unit 1 Package	1	1	13FEB13	13FEB13
CN3701	Seller Access Days Unit 1	45	45	13FEB13	29MAR13
CN7105	Cold, Hot Commission & Performance Test Unit 5	99*	99*	13FEB13	07JUN13
CN710111	Sync Generator, AVR, Loads GTG Unit 1 Package	1	1	14FEB13	14FEB13
CN710119	First Fire & FSNL GTG Unit 2 Package	1	1	25FEB13	25FEB13
CN3702	Seller Access Days Unit 2	45	45	25FEB13	10APR13
CN710121	Sync Generator, AVR, Loads GTG Unit 2 Package	1	1	26FEB13	26FEB13
CN7106	Cold, Hot Commission & Performance Test Unit 6	98*	98*	26FEB13	19JUN13
CN710129	First Fire & FSNL GTG Unit 3 Package	1	1	06MAR13	06MAR13
CN3703	Seller Access Days Unit 3	45	45	06MAR13	19APR13
CN710131	Sync Generator, AVR, Loads GTG Unit 3 Package	1	1	07MAR13	07MAR13
CN710139	First Fire & FSNL GTG Unit 4 Package	1	1	14MAR13	14MAR13
CN3704	Seller Access Days Unit 4	45	45	14MAR13	27APR13
CN710141	Sync Generator, AVR, Loads GTG Unit 4 Package	1	1	15MAR13	15MAR13
CN7107	Cold, Hot Commission & Performance Test Unit 7	98*	98*	02APR13	24JUL13
CN7108	Cold, Hot Commission & Performance Test Unit 8	92*	92*	11APR13	26JUL13
CN710149	First Fire & FSNL GTG Unit 5 Package	1	1	24APR13	24APR13
CN3705	Seller Access Days Unit 5	45	45	24APR13	07JUN13
CN710151	Sync Generator, AVR, Loads GTG Unit 5 Package	1	1	25APR13	25APR13
CN710159	First Fire & FSNL GTG Unit 6 Package	1	1	06MAY13	06MAY13
CN3706	Seller Access Days Unit 6	45	45	06MAY13	19JUN13
CN710161	Sync Generator, AVR, Loads GTG Unit 6 Package	1	1	07MAY13	07MAY13
CN710169	First Fire & FSNL GTG Unit 7 Package	1	1	10JUN13	10JUN13

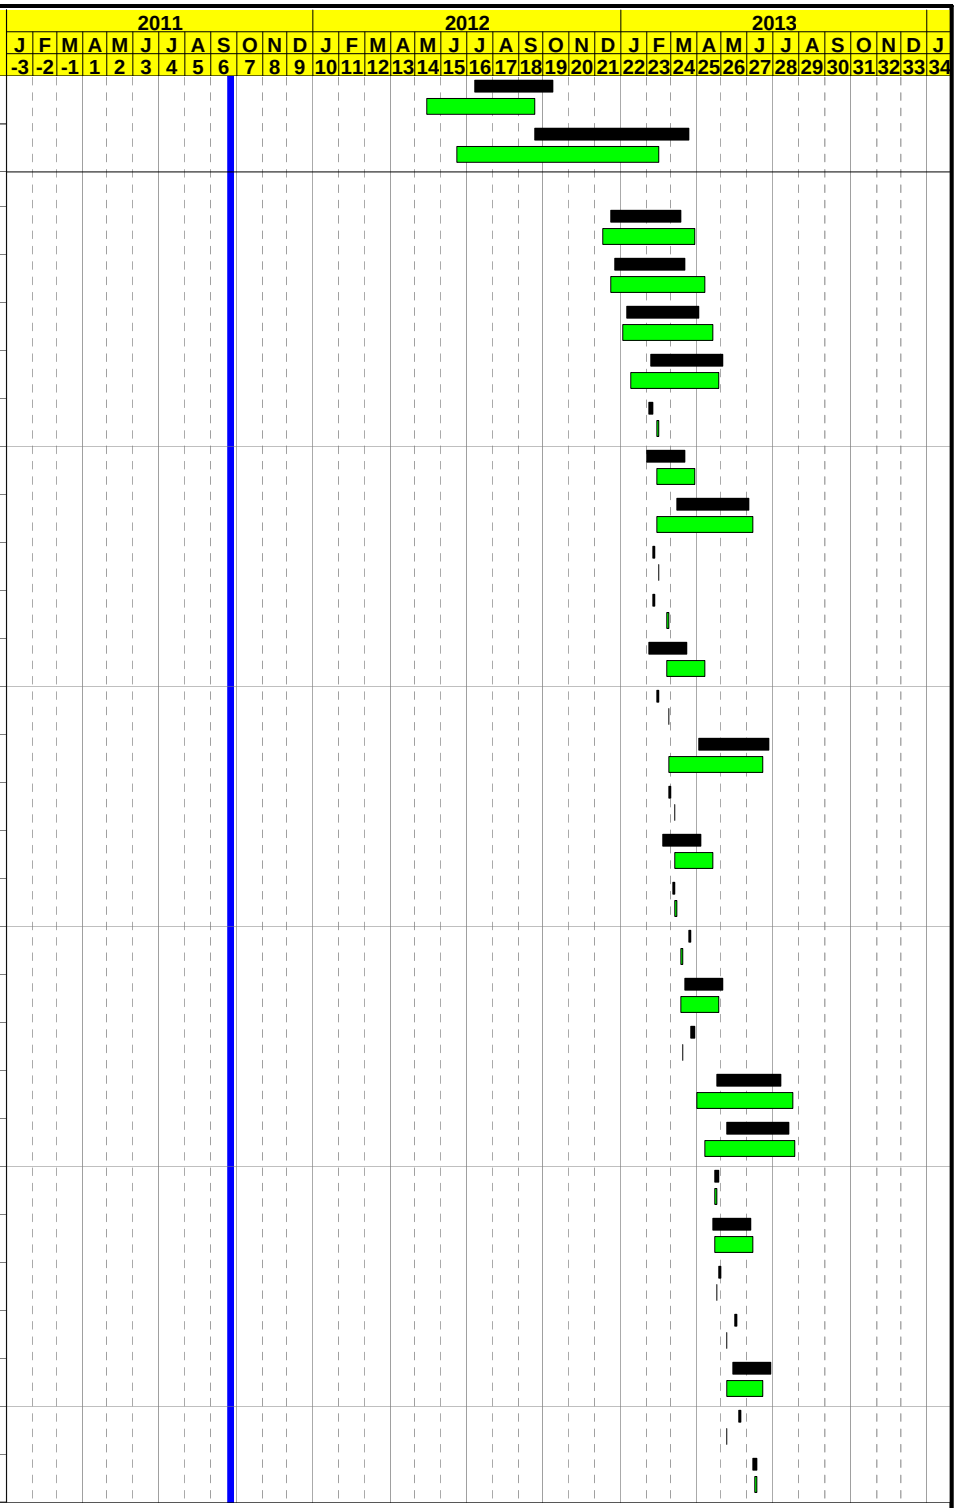

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
CN3707	Seller Access Days Unit 7	45	45	10JUN13	24JUL13
CN710171	Sync Generator, AVR, Loads GTG Unit 7 Package	1	1	11JUN13	11JUN13
CN710179	First Fire & FSNL GTG Unit 8 Package	1	1	20JUN13	20JUN13
CN3708	Seller Access Days Unit 8	30	30	20JUN13	19JUL13
CN710181	Sync Generator, AVR, Loads GTG Unit 8 Package	1	1	21JUN13	21JUN13
CN710291	All 8 Units 24-Hour Reliability Test	1	1	29JUL13	29JUL13
CN710290	Facility Auxiliary Load Test	1	1	31JUL13	31JUL13
CN2812	Final Completion	0	0		26NOV13

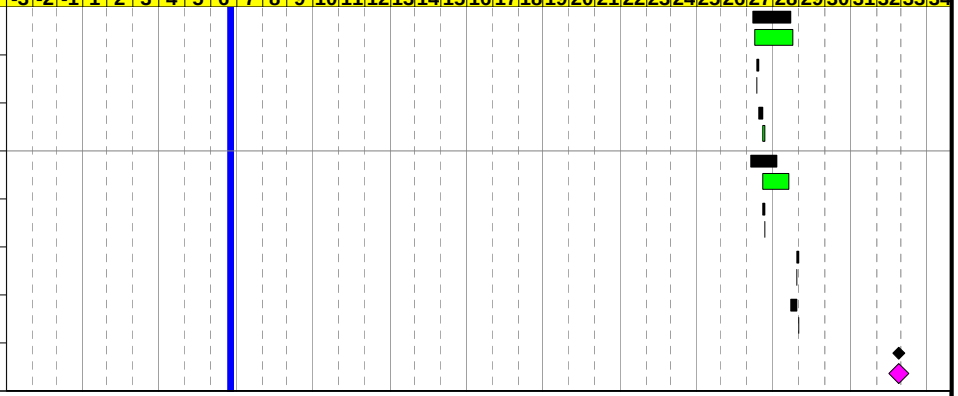

APPENDIX A
Key Events List &
CEC Compliance Matrix

KEY EVENT LIST

PROJECT: CPV Sentinel Energy Project **DATE ENTERED:** 8/3/2011

DOCKET #: 07-AFC-3C
Compliance PROJECT MANAGER: Dale Rundquist

Event Description	Date Assigned
Certification Date	1 Dec 2010
Obtain Site Control	1 Jun 2010
Online Date	1 Aug 2013
Power Plant Site Activities	
Start of Site Mobilization	1 Jun 2011
Start Ground Disturbance	1 Jun 2011
Start Grading	1 Jun 2011
Start Construction	1 Jun 2011
Begin Pouring Major Foundation Concrete	12 Sep 2011
Begin Installation of Major Equipment	13 Mar 2012
Completion of Installation of Major Equipment	6 Jun 2013
First Combustion of Gas Turbine	on or about 1 Feb 2013
Obtain Building Occupation Permit	TBD
Start Commercial Operation	1 Aug 2013
Complete All Construction	29 Nov 2013
Transmission Line Activities	
Start T/L Construction	Nov 2011
Synchronization with Grid and Interconnection	Jan 2013
Complete T/L	May 2013
Fuel Supply Line Activities	
Start Gas Pipeline Construction and Interconnection	Nov 2011
Complete Gas Pipeline Construction	Sep 2012
Water Supply Activities	
Start of Water Supply Construction	29 Aug 2011
Complete Water Supply Construction	23 Sep 2011

Compliance Matrix for CPV Sentinel Project

Assumed Construction Start Date:	06/01/11
Assumed Ground Disturbance Date	6/1/2011
Assumed Site Mobilization Date	6/1/2011

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
AQ-12	CON	The operator shall install and maintain an ammonia injection flow meter and recorder to accurately indicate and record the ammonia injection flow rate being supplied to each turbine. The device or gauge shall be accurate to within plus or minus 5 percent and shall be calibrated once every twelve months. The ammonia injection system shall be placed in full operation as soon as the minimum temperature is reached. The minimum temperature is listed as 540 degrees F at the inlet to the SCR reactor. Continuously recording is defined for this condition as at least once every hour and is based on the average of the continuous monitoring for that hour.	The project owner shall submit to the CPM no less than 30 days after installation, a written statement by a California registered Professional Engineer stating that said engineer has reviewed the as-built-designs or inspected the identified equipment and certifies that the appropriate device has been installed and is functioning properly. The project owner shall submit annual calibration results within 30 days of their successful completion.	No less than 30 days after installation - and - submit annual calibration results within 30 days of their successful completion.	04/23/12				
AQ-13	CON	The operator shall install and maintain a temperature gauge and recorder to accurately indicate and record the temperature in the exhaust at the inlet of the SCR reactor. The gauge shall be accurate to within plus or minus 5 percent and shall be calibrated once every twelve months. The catalyst temperature range shall remain between 740 degree F and 840 degree F. The catalyst temperature shall not exceed 840 degrees F. The temperature range requirement of this condition does not apply during startup operations of the turbine. Continuously recording is defined for this condition as at least once every hour and is based on the average of the continuous monitoring for that hour.	The project owner shall submit to the CPM no less than 30 days after installation, a written statement by a California registered Professional Engineer stating that said engineer has reviewed the as-built-designs or inspected the identified equipment and certifies that the appropriate device has been installed and is functioning properly. The project owner shall submit annual calibration results within 30 days of their successful completion.	No less than 30 days after installation - and - submit annual calibration results within 30 days of their successful completion.	04/13/12				
AQ-14	CON	The operator shall install and maintain a pressure gauge and recorder to accurately indicate and record the pressure differential across the SCR catalyst bed in inches of water column. The gauge shall be accurate to within plus or minus 5 percent and shall be calibrated once every twelve months. The pressure drop across the catalyst shall not exceed 12 inches of water column during the start-up period. Continuously recording is defined for this condition as at least once every month and is based on the average of the continuous monitoring for that month.	The project owner shall submit to the CPM no less than 30 days after installation, a written statement by a California registered Professional Engineer stating that said engineer has reviewed the as-built-designs or inspected the identified equipment and certifies that the appropriate device has been installed and is functioning properly. The project owner shall submit annual calibration results within 30 days of their successful completion.	No less than 30 days after installation - and - submit annual calibration results within 30 days of their successful completion.	04/13/12				
AQ-SC3	CON	Construction Fugitive Dust Control: The AQCMM shall submit documentation to the CPM in each Monthly Compliance Report that demonstrates compliance with the Air Quality Construction Mitigation Plan (AQCMP) mitigation measures for the purposes of minimizing fugitive dust emission creation from construction activities and preventing all fugitive dust plumes from leaving the project. Any deviation from the AQCMP mitigation measures shall require prior CPM notification and approval.	The AQCMM shall provide the CPM a Monthly Compliance Report (COMPLIANCE-6) to demonstrate control of fugitive dust emissions.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
AQ-SC4	CON	Dust Plume Response Requirement: The AQCMM or an AQCMM Delegate shall monitor all construction activities for visible dust plumes. Observations of visible dust plumes that have the potential to be transported (A) off the project site and within 400 feet upwind of any regularly occupied structures not owned by the project owner or (B) 200 feet beyond the centerline of the construction of linear facilities indicate that existing mitigation measures are not resulting in effective mitigation. The AQCMP shall include a section detailing how the additional mitigation measures will be accomplished within the time limits specified. The AQCMM or Delegate shall implement procedures for additional mitigation measures in the event that such visible dust plumes are observed.	The AQCMM shall provide the CPM a Monthly Compliance Report (COMPLIANCE-6).	Monthly	Monthly				On-going
AQ-SC5	CON	Diesel-Fueled Engine Control: The AQCMM shall submit to the CPM, in the Monthly Compliance Report, a construction mitigation report that demonstrates compliance with the AQCMP mitigation measures for purposes of controlling diesel construction-related emissions. Any deviation from the AQCMP mitigation measures shall require prior and CPM notification and approval.	The AQCMM shall include in the Monthly Compliance Report (COMPLIANCE-6) information that demonstrates control of diesel construction-related emissions.	Monthly	Monthly				On-going
AQ-SC6	CON	The project owner, when obtaining dedicated on-road or off-road vehicles for facility maintenance activities, shall only obtain new model year vehicles that meet California on-road vehicle emission standards or appropriate U.S.EPA/California offroad engine emission standards for the model year when obtained.	At least 60 days prior to the start commercial operation, the project owner shall submit to the CPM a copy of the plan that identifies the size and type of the on-site vehicle and equipment fleet and the vehicle and equipment purchase orders and contracts and/or purchase schedule. The plan shall be updated every other year and submitted in the Annual Compliance Report (COMPLIANCE-7).	At least 60 days prior to the start commercial operation with updates every other year.	05/15/13				
AQ-SC7	CON	The project owner shall provide the CPM copies of all District issued Authority-to-Construct (ATC) and Permit-to-Operate (PTO) documents for the facility. The project owner shall submit to the CPM for review and approval any modification proposed by the project owner to any project air permit. The project owner shall submit to the CPM any modification to any permit proposed by the District or U.S. Environmental Protection Agency (U.S. EPA), and any revised permit issued by the District or U.S. EPA, for the project.	The project owner shall submit any ATC, PTO, and proposed air permit modifications to the CPM within 15 working days of its submittal either by 1) the project owner to an agency, or 2) receipt of proposed modifications from an agency. The project owner shall submit all modified air permits to the CPM within 15 days of receipt.	As Required. Within 5 working days of submittal. All modified air permits within 15 days of receipt.	As Required	4/20/2011	5/6/2011	4/20/2011	On-going
BIO-1.2	CON	Replacement Designated Biologist - The project owner shall assign a Designated Biologist to the project. The project owner shall submit the resume of the proposed Designated Biologist, with at least 3 references and contact information, to the ECC Project Manager (CPM) for approval.	If a Designated Biologist needs to be replaced, the specified information of the proposed replacement must be submitted to the CPM at least 10 working days prior to the termination or release of the preceding Designated Biologist. In an emergency, the project owner shall immediately notify the CPM qualifications and approval of a short-term replacement while a permanent Designated Biologist is proposed to the CPM for consideration.	As Required	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-10.2	CON	The project owner shall conduct follow-up surveys to the protocol level surveys conducted in 2007 and 2008 by xeric Specialties to determine the presence of the Coachella Valley milk-vetch and the Triple-ribbed milk-vetch and implement the appropriate measures to minimize impacts if detected: 2. If either target species or another federally or State listed plant species is detected in the project area then the project owner shall be required to obtain a Biological Opinion (ESA Section 10) and/or a CESA Section 2081 Letter of Concurrence to determine appropriate mitigation for impacts	The project owner shall report to the CPM the results of the surveys and whether coverage under the CVMSHCP or a Biological Opinion (ESA Section 10) and/or a CESA Section 2081 Letter of Concurrence are required as soon as possible. At least 60 days prior to start of any project-related ground disturbance activities, the project owner shall provide the CPM final version of the BRMIMP, which includes rare/listed plant survey results to date and any necessary impact avoidance measures. Results for all protocol surveys conducted after the final version of the BRMIMP is complete shall be as a supplement to the CPM. All modifications to the approved BRMIMP shall be made only after consultation with the CPM and CDFG. The project owner shall notify the CPM five working days before implementing any modications to the BRMIMP.	Results of the surveys and whether coverage under the CVMSHCP or a Biological Opinion (ESA Section 10) and/or a CESA Section 2081 Letter of Concurrence are required as soon as possible. At least 60 days prior to start of any project-related ground disturbance activities, the project owner shall provide the CPM final version of the BRMIMP.	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-11.2	CON	The project owner shall implement the following measures to identify the presence and avoid or minimize impacts to burrowing owls and other nesting birds: 1. A qualified biologist shall conduct survey for burrowing owl activities in the project area, including the power plant site, the linear facilities (e.g. natural gas lines), and a 150 meter (approximately 500 feet) buffer (where possible and appropriate based on the habitat). The survey should follow the protocol outlined in the CDFG Staff Report on Burrowing Owl Mitigation (1995).	All modifications to the approved BRMIMP must be made only after consultation with the CPM and other appropriate agencies. The project owner shall notify the CPM five working days before implementing any modifications to the BRMIMP.	5 working days before implementing any modifications to the BRMIMP	As Required				As Required
BIO-11.3	CON	The project owner shall implement the following measures to identify the presence and avoid or minimize impacts to burrowing owls and other nesting birds: 3. If initial ground disturbance is to occur during the breeding season, complete a pre-construction survey for nesting birds on the project site and/or linear facilities no less than 30 days prior to the start of ground disturbance activities. This survey can occur in conjunction with the burrowing owl surveys.	At least 60 days prior to start of any project-related ground disturbance activities, the project owner shall provide the CPM with the final version of the BRMIMP, which includes burrowing owl/nesting bird survey results to date and any necessary impact avoidance measures. Results for all protocol surveys conducted after the final version of the BRMIMP is complete shall be submitted as a supplement to the CPM. All modifications to the approved BRMIMP must be made only after consultation with the CPM and other appropriate agencies. The project owner shall notify the CPM five working days before implementing any modifications to the BRMIMP.	At least 60 days prior to start of any project-related ground disturbance activities. 5 working days before implementing any modifications to the BRMIMP	05/02/11	3/30/2011	4/29/2011	5/10/2011	CEC Approved
BIO-2.1	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 1. Advise the project owner's Construction and Operation Managers on the implementation of the biological resources Conditions of Certification;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.2	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 2. Consult on the preparation of the Biological Resources Mitigation Implementation and Monitoring Plan (BRMIMP), to be submitted by the project owner	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.3	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 3. Be available to supervise, conduct and coordinate mitigation, monitoring, and other biological resources compliance efforts, particularly in areas requiring avoidance or containing sensitive biological resources, such as special status species or their habitat;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-2.4	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 4. Clearly mark sensitive biological resource areas, if present and inspect these areas at appropriate intervals for compliance with regulatory terms and conditions;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.5	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 5. Inspect active construction areas where animals may have become trapped prior to construction commencing each day. At the end of the day, inspect for the installation of structures that prevent entrapment or allow escape during periods of construction inactivity. Periodically inspect areas with high vehicle activity (i.e. parking lots) for animals in harm's way;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.6	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 6. Notify the project owner and the CPM of any non-compliance with any biological resources Condition of Certification;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.7	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 7. Respond directly to inquiries of the CPM regarding biological resource issues;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-2.8	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 8. Maintain written records of the tasks specified above and those included in the BRMIMP. Summaries of these records shall be submitted in the Monthly Compliance Report and the Annual Report;	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-2.9	CON	The project owner shall ensure that the Designated Biologist performs the following during any site (or related facilities) mobilization, ground disturbance, grading, construction, operation, and closure activities. The Designated Biologist may be assisted by the approved Biological Monitor(s), but remains the contact for the project owner and CPM. 9. Train the Biological Monitors as appropriate, and ensure their familiarity with the BRMIMP, Worker Environmental Awareness Program (WEAP) training and all permits.	The Designated Biologist shall submit in the Monthly Compliance Report to the CPM copies of all written reports and summaries that document biological resources activities. If actions may affect biological resources during operation, a Designated Biologist shall be available for monitoring and reporting. During project operation, the Designated Biologist shall submit record summaries in the Annual Compliance Report unless their duties are ceased as approved by the CPM.	Monthly	Monthly				On-going
BIO-4.1	CON	The project owner's Construction/ Operation Manager shall act on the advice of the Designated Biologist and Biological Monitor(s) to ensure conformance with the biological resources Conditions of Certification. If required by the Designated Biologist and Biological Monitor(s) the project owner's Construction/Operation Manager shall halt all site activities in areas specified by the Designated Biologist. The Designated Biologist shall: 1. Require a halt to all activities in any area when determined that there would be an unauthorized adverse impact to biological resources if the activities continued;	The project owner shall ensure that the Designated Biologist or Biological Monitor notifies the CPM immediately of any non-compliance or a halt of any site mobilization, ground disturbance, grading, construction, and operation activities. The project owner shall notify the CPM of the circumstances and actions being taken to resolve the problem. Whenever corrective action is taken by the project owner, a determination of success or failure will be made by the CPM within five working days after receipt of notice that corrective action is completed, or the project owner will be notified by the CPM that coordination with other agencies will require additional time before a determination can be made.	As necessary - no later than the following morning of the incident, or Monday morning in the case of a weekend. Determination of success of corrective action within 5 working days of completion of action	As Required				
BIO-4.2	CON	The Designated Biologist shall: 2. Inform the project owner and the Construction/Operation Manager when to resume activities;	The project owner shall ensure that the Designated Biologist or Biological Monitor notifies the CPM immediately of any non-compliance or a halt of any site mobilization, ground disturbance, grading, construction, and operation activities. The project owner shall notify the CPM of the circumstances and actions being taken to resolve the problem. Whenever corrective action is taken by the project owner, a determination of success or failure will be made by the CPM within five working days after receipt of notice that corrective action is completed, or the project owner will be notified by the CPM that coordination with other agencies will require additional time before a determination can be made.	As necessary - no later than the following morning of the incident, or Monday morning in the case of a weekend. Determination of success of corrective action within 5 working days of completion of action	As Required				As Required
BIO-4.3	CON	The Designated Biologist shall: 3. Notify the CPM if there is a halt of any activities, and advise the CPM of any corrective actions that have been taken, or will be instituted, as a result of the work stoppage.	The project owner shall ensure that the Designated Biologist or Biological Monitor notifies the CPM immediately of any non-compliance or a halt of any site mobilization, ground disturbance, grading, construction, and operation activities. The project owner shall notify the CPM of the circumstances and actions being taken to resolve the problem. Whenever corrective action is taken by the project owner, a determination of success or failure will be made by the CPM within five working days after receipt of notice that corrective action is completed, or the project owner will be notified by the CPM that coordination with other agencies will require additional time before a determination can be made.	As necessary - no later than the following morning of the incident, or Monday morning in the case of a weekend. Determination of success of corrective action within 5 working days of completion of action	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-5.2	CON	Each of the employees, as well as employees of contractors and subcontractors who work on the project site or any related facilities during site mobilization, ground disturbance, grading, construction, operation, and closure are informed about sensitive biological resources associated with the project.	The project owner shall provide in the Monthly Compliance Reoprt the number of persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site and related facilities mobilization, two copies of the CPM-approved materials shall be submitted. Training acknowledgement forms signed during construction shall be kept on file by the project owner for a period of at least six months after the start of commercial op During project operation, signed statements for operational personnel shall be kept on file employment. At least 60 days prior to the start of any site (or related facilities) the project owner shall provide in the Monthly Compliance Report the number of eration. for six months following the termination of an individual's mobilization, the project owner shall provide to the CPM (for review and approval) the proposed WEAP and all supporting written materials and electronic media prepared or reviewed by the Designated Biologist and a resume of the person(s) administering the program. The project owner s persons who have completed the training in the prior month and a running total of all persons who have completed the training to date. At least 10 days prior to site and related facilities mobilization, two copies of the CPM-approved materials shall be submitted. Training acknowledgement forms signed during construction shall be kept on file by the project owner for a period of at least six months after the start of commercial op During project operation, signed statements for operational personnel shall be kept on file employment.	Monthly. At least 10 days prior to site and related facilities mobilization, two copies of the CPM-approved materials shall be submitted.	Monthly				On-going
BIO-7.1	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 1. Design, install and maintain gas transmission lines, potable water lines,, access roads, and storage and parking areas to avoid identified sensitive resources;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going
BIO-7.2	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 2. Design, install, and maintain the transmission line from CPVS to SCE Devers Substation and all other electrical components if necessary in accordance with the Avian Power Line Interaction Committee (APLIC), Suggested Practices for Raptor Protection on Power Lines: The State of the Art in 2006 to reduce the likelihood of electrocutions of large birds;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-7.3	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 3. Design, install, and maintain structures and supports to prevent common raven (Corvus corax) nesting. Destroy nests that are established prior to egg laying and the modify the location to prevent future nest establishment (modified from applicant's Mitigation Measure Bio-9);	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going
BIO-7.4	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 4. Install silt fencing buried 1-foot deep and attached to a chain-link fence prior to construction to keep burrowing animals from easily tunneling into the site. Examine the fencing at least once a week and repair when necessary. Maintain the fencing until construction is complete (modified from applicant's Mitigation Measure Bio-10);	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Report - Monthly Silt Fence must be completed 2 weeks prior to construction start.	06/08/11	6/8/2011	6/8/2011	6/8/2011	On-going
BIO-7.5	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 5. Following installation of silt fence and prior to ground disturbance, conduct small mammal trapping for five nights in order to capture and relocate as many small mammals from within the project area as possible. Set traps near sign, burrows, or tracks at dusk each day and check at midnight or no later than dawn the next day to ensure no unnecessary deaths occur (modified from applicant's Mitigation Measure Bio-11);	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Report - Monthly Trapping to be completed immediately after silt fence is installed and prior to construction start.	06/08/11	6/8/2011	6/8/2011	6/8/2011	On-going
BIO-7.6	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 6. Eliminate any California Exotic Pest Plants of Concern (CalEPPC) List A species or plant species identified on Table 4-113 (Prohibited Invasive Plant Species) of the CVMSHCP from reseeding areas following temporary disturbance or from landscaping plans (integrated applicant's Mitigation Measure Bio-8);	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going
BIO-7.7	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resources, including the following: 7. Prescribe a road sealant that is non-toxic to wildlife and plants;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-7.8	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the localbiological resources, including the following: 8. Design, install, and maintain facility lighting to prevent side casting of light towards wildlife habitat.	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly	Monthly				On-going
BIO-7.9	CON	Any time the project owner modifies or finalizes the project design they shall incorporate all feasible measures that avoid or minimize impacts to the local biological resource	The project owner shall provide to the CPM for review and approval a written construction termination report identifying how measures have been completed.	Within thirty (30) days after completion of project construction	12/31/13				Not Started
BIO-8.1	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 1. Install temporary fencing and provide wildlife escape ramps for construction areas that contain steep walled holes or trenches if outside of an approved, permanent exclusionary fence. The temporary fence shall be hardware cloth or similar materials that are approved by USFWS. Before such holes or trenches are filled, they should be thoroughly inspected for trapped animals by the Designated Biologist or Biological Monitor;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.2	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 2. Make certain all food-related trash is disposed of in closed containers and removed at least once a week;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.3	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 3. Prohibit feeding of wildlife by staff and subcontractors;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.4	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 4. Prohibit non-security related firearms or weapons from being brought to the site;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
BIO-8.5	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 5. Prohibit pets from being brought to the site;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.6	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 6. Report all inadvertent deaths of sensitive species to the appropriate project representative. Injured animals shall be reported to CDFG or USFWS and the project owner shall follow instructions that are provided by CDFG or USFWS;	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.7	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 7. Minimize use of rodenticides in the project area	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going
BIO-8.8	CON	The project owner shall implement the following measures to manage their construction site, and related facilities, in a manner to avoid or minimize impacts to the local biological resources: 8. Prohibit vehicles and personnel from entering sensitive habitats.	All mitigation measures and their implementation methods shall be included in the BRMIMP. Implementation of the measures will be reported in the Monthly Compliance Reports by the Designated Biologist. Within 30 days after completion of project construction, the project owner shall provide to the CPM, for review and approval, a written construction termination report identifying how measures have been completed.	Monthly. Within 30 days after completion of project construction, a written construction termination report	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CIVIL-2	CON	The resident engineer shall, if appropriate, stop all earthwork and construction in the affected areas when the responsible soils engineer, geotechnical engineer, or the civil engineer experienced and knowledgeable in the practice of soils engineering identifies unforeseen adverse soil or geologic conditions. The project owner shall submit modified plans, specifications, and calculations to the CBO based on these new conditions. The project owner shall obtain approval from the CBO before resuming earthwork and construction in the affected area	The project owner shall notify the CPM within 24 hours when earthwork and construction are stopped as a result of unforeseen adverse geologic/soil conditions. Within 24 hours of the CBO's approval to resume earthwork and construction in the affected areas, the project owner shall provide to the CPM a copy of the CBO's approval.	Within 24 hours	As Required				As Required
CIVIL-3	CON	The project owner shall perform inspections in accordance with the 2007 CBC, Appendix Chapter 1, section 109, Inspections, and Chapter 17, section 1704, Special Inspections. All plant site grading operations for which a grading permit is required shall be subject to inspection by the CBO. If, in the course of inspection, it is discovered that the work is not being performed in accordance with the approved plans, the discrepancies shall be reported immediately to the resident engineer, the CBO, and the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The project owner shall prepare a written report, with copies to the CBO and the CPM, detailing all discrepancies, non-compliance items, and the proposed corrective action.	Within five days of the discovery of any discrepancies, the resident engineer shall transmit to the CBO and the CPM a non-conformance report (NCR) and the proposed corrective action for review and approval. Within five days of resolution of the NCR, the project owner shall submit the details of the corrective action to the CBO and the CPM. A list of NCRs for the reporting month shall also be included in the following monthly compliance report.	NCR - Within five days of the discovery of any discrepancies. Within five days of resolution of the NCR, details of the corrective action	As Required				Not Started
CIVIL-4	CON	After completion of finished grading and erosion and sedimentation control and drainage work, the project owner shall obtain the CBO's approval of the final grading plans (including final changes) for the erosion and sedimentation control work. The civil engineer shall state that the work within his/her area of responsibility was done in accordance with the final approved plans	The project owner shall submit to the CBO, for review and approval the final grading plans and the responsible civil engineer's signed statement that the installation of the facilities and all erosion control measures were completed in accordance with the final approved combined grading plans, and that the facilities are adequate for their intended purposes, along with a copy of the transmittal letter to the CPM. The project owner shall submit a copy of the CBO's approval to the CPM in the next monthly compliance report.	Within 30 days (or project owner- and CBO-approved alternative time frame) of the completion of the erosion and sediment control mitigation and drainage work	TBD				Not Started
COMPLIANCE-1	CC	The CPM, responsible Energy Commission staff, and delegate agencies or consultants shall be guaranteed and granted unrestricted access to the power plant site, related facilities, project-related staff, and the records maintained on site, for the purpose of conducting audits, surveys, inspections, or general site visits. Although the CPM will normally schedule site visits on dates and times agreeable to the project owner, the CPM reserves the right to make unannounced visits at any time.	The project owner shall grant Energy Commission staff and delegate agencies or consultants unrestricted access to the power plant site.	Ongoing	On-going				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
COMPLIANCE-10	CC	Prior to the start of construction, the project owner must send a letter to property owners living within one mile of the project notifying them of a telephone number to contact project representatives with questions, complaints or concerns. If the telephone is not staffed 24-hours per day, it shall include automatic answering with date and time stamp recording. All recorded complaints shall be responded to within 24 hours. The telephone number shall be posted at the project site and made easily visible to passersby during construction and operation. The telephone number shall be provided to the CPM who will post it on the Energy Commission's web page. Any changes to the telephone number shall be submitted immediately to the CPM, who will update the web page. In addition to the monthly and annual compliance reporting requirements described above, the project owner shall report and provide copies to the CPM of all complaint forms, including noise and lighting complaints, notices of violation, notices of fines, official warnings, and citations, within 10 days of receipt. Complaints shall be logged and numbered. Noise complaints shall be recorded on the form provided in the NOISE conditions of certification. All other complaints shall be recorded on the complaint form.	The project owner shall report to the CPM, all notices, complaints, and citations.	Within 10 days of receipt	As Required	5/2/2011			As Required
COMPLIANCE-11	CC	In order to ensure that a planned facility closure does not create adverse impacts, a closure process that provides for careful consideration of available options and applicable laws, ordinances, regulations, standards, and local/regional plans in existence at the time of closure, will be undertaken. To ensure adequate review of a planned project closure, the project owner shall submit a proposed facility closure plan to the Energy Commission for review and approval at least 12 months (or other period of time agreed to by the CPM) prior to commencement of closure activities. The project owner shall file 120 copies (or other number of copies agreed upon by the CPM) of a proposed facility closure plan with the Energy Commission.	The project owner shall submit a closure plan to the CPM	At least 12 months prior to commencement of a planned closure	TBD				
COMPLIANCE-13	CC	The on-site contingency plan required for unplanned temporary closure shall also cover unplanned permanent facility closure. All of the requirements specified for unplanned temporary closure shall also apply to unplanned permanent closure. In addition, the on-site contingency plan shall address how the project owner will ensure that all required closure steps will be successfully undertaken in the event of abandonment.	To ensure that public health and safety and the environment are protected in the event of an unplanned permanent closure, the project owner shall submit an on-site contingency plan	No less than 60 days prior to commencement of commercial operation	05/15/13				Not started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
COMPLIANCE-14	CC	The project owner must petition the Energy Commission pursuant to Title 20, California Code of Regulations, section 1769, in order to modify the project (including linear facilities) design, operation or performance requirements, and to transfer ownership or operational control of the facility. It is the responsibility of the project owner to contact the CPM to determine if a proposed project change should be considered a project modification pursuant to section 1769. Implementation of a project modification without first securing Energy Commission, or Energy Commission staff approval, may result in enforcement action that could result in civil penalties in accordance with section 25534 of the Public Resources Code. A petition is required for amendments and for insignificant project changes as specified. Both shall be filed as a "Petition to Amend." Staff will determine if the change is significant or insignificant. For verification changes, a letter from the project owner is sufficient. In all cases, the petition or letter requesting a change should be submitted to the CPM, who will file it with the Energy Commission's Dockets Unit in accordance with Title 20, California Code of Regulations, section 1209.	The project owner must petition the Energy Commission to delete or change a condition of certification, modify the project design or operational requirements and/or transfer ownership of operational control of the facility.	As needed	As Required				As Required
COMPLIANCE-2	CC	For the life of the project, the project owner shall maintain project files on-site or at an alternative site approved by the CPM, unless a lesser period of time is specified by the conditions of certification. The files shall contain copies of all "as-built" drawings, all documents submitted as verification for conditions, and all other project-related documents.	The project owner shall maintain project files onsite. Energy Commission staff and delegate agencies shall be given unrestricted access to the files.	Ongoing	On-going				On-going
COMPLIANCE-3	CC	Each condition of certification is followed by a means of verification. The verification describes the Energy Commission's procedure(s) to ensure post-certification compliance with adopted conditions. The verification procedures, unlike the conditions, may be modified as necessary by the CPM.	The project owner is responsible for the delivery and content of all verification submittals to the CPM, whether such condition was satisfied by work performed or the project owner or his agent.	Ongoing	On-going				On-going
COMPLIANCE-5	CC	A compliance matrix shall be submitted by the project owner to the CPM along with each monthly and annual compliance report. The compliance matrix is intended to provide the CPM with the current status of all conditions of certification in a spreadsheet format.	The project owner shall submit a compliance matrix with each monthly and annual compliance report.	Monthly	Monthly				On-going
COMPLIANCE-6	CON	The first Monthly Compliance Report is due one month following the Energy Commission business meeting date upon which the project was approved, unless otherwise agreed to by the CPM. The first Monthly Compliance Report shall include the AFC number and an initial list of dates for each of the events identified on the Key Events List.	During construction, the project owner shall submit Monthly Compliance Reports (MCRs). The first MCR is due the month following the Energy Commission business meeting date on which the project was approved.	Monthly	Monthly				On-going
COMPLIANCE-8	CC	Any information that the project owner deems confidential shall be submitted to the Energy Commission's Dockets Unit with an application for confidentiality pursuant to Title 20, California Code of Regulations, section 2505(a). Any information that is determined to be confidential shall be kept confidential as provided for in Title 20, California Code of Regulations, section 2501 et. seq.	Any information the project owner deems confidential shall be submitted to the Energy Commission's Dockets Unit with a request for confidentiality.	Ongoing	On-going				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
COMPLIANCE-9	CC	Pursuant to the provisions of Section 25806(b) of the Public Resources Code, the project owner is required to pay an annual compliance fee, which is adjusted annually. The amount of the fee for FY2007-2008 was $17,676. The initial payment is due on the date the Energy Commission adopts the final decision. You will be notified of the amount due. All subsequent payments are due by July 1 of each year in which the facility retains its certification. The payment instrument shall be made payable to the California Energy Commission and mailed to: Accounting Office MS-02, California Energy Commission, 1516 9th St., Sacramento, CA 95814.	Payment of Annual Energy Facility Compliance Fee	Annual	Annually				On-going
CUL-1.2	CON	The project owner shall obtain the services of a Cultural Resources Specialist (CRS), and one or more alternates, as needed.	The project owner shall submit the resume of the proposed new CRS to the CPM for review and approval. At the same time, the project owner shall also provide to the approved new CRS the AFC and all cultural documents, field notes, photographs, and other cultural materials generated by the project. If there is no alternate CRS in place to conduct the duties of the CRS, a previously approved monitor may serve in place of a CRS so that construction may continue up to a maximum of 3 days without a CRS. If cultural resources are discovered, then construction will remain halted until there is a CRS or alternate CRS to make a ecommendation regarding significance.	At least 10 days prior to a termination or release of the CRS, or within 10 days after the resignation of a CRS	As Required				As Required
CUL-1.4	CON	The project owner shall obtain the services of a Cultural Resources Specialist (CRS), and one or more alternates, as needed.	The resume(s) of any additional technical specialists shall be provided to the CPM for review and approval.	At least 10 days prior to beginning tasks	As Required				As Required
CUL-2.2	CON	Prior to ground disturbance, if the CRS has not previously worked on the project, the Project Owner shall provide the CRS with copies of the AFC, data responses, and confidential cultural resources reports for the project. The Project Owner shall also provide the CRS and the CPM with maps and drawings showing the footprint of the power plant and all linear facilities. Maps shall include the appropriate U.S. Geological Survey (USGS) quadrangles and a map at an appropriate scale (for example, 1:2000 or 1 inch = 200 feet) for plotting cultural features or materials. If the CRS requests enlargements or strip maps for linear facility routes, the Project Owner shall provide copies to the CRS and CPM. The CPM shall review submittals and, in consultation with the CRS, approve those that are appropriate for use in cultural resources planning activities. No ground disturbance shall occur prior to CPM approval of maps and drawings unless specifically approved by the CPM.	2. If there are changes to any project related-footprint, revised maps and drawings shall be provided	at least 15 days prior to start of ground disturbance, and construction for those changes.	As Required				As Required
CUL-2.3	CON	No preconstruction site activities shall occur prior to CPM approval of maps and drawings, unless specifically approved by the CPM. If construction of the project would proceed in phases, maps and drawings, not previously provided, shall be submitted prior to the start of each phase	If project construction is phased, if not previously provided, the project owner shall submit the subject maps and drawings	15 days prior to each phase	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CUL-2.4	CC	At a minimum, the CRS shall consult weekly with the project construction manager to confirm area(s) to be worked during the next week, until ground disturbance is completed. The project owner shall notify the CRS and CPM of any changes to the scheduling of the construction phases. No ground disturbance shall occur prior to CPM approval of maps and drawings, unless specifically approved by the CPM.	A current schedule of anticipated project activity shall be provided to the CRS and CPM by letter, e-mail, or fax.	On a weekly basis during ground disturbance	06/01/11	5/3/2011	5/18/2011	5/12/2011	On-going
CUL-2.5	CON	At a minimum, the CRS shall consult weekly with the project construction manager to confirm area(s) to be worked during the next week, until ground disturbance is completed. The project owner shall notify the CRS and CPM of any changes to the scheduling of the construction phases. No ground disturbance shall occur prior to CPM approval of maps and drawings, unless specifically approved by the CPM.	5. The project owner shall provide written notice of any changes to scheduling of construction phase.	Within 5 days of identifying changes	As Required				On-going
CUL-4.1	CON	The Project Owner shall submit the Cultural Resources Report (CRR) to the County of Riverside, and to the Chairpersons of all Native American groups that requested additional information on the CVP Sentinel cultural resources, for review and comment. After the Project Owner has received comments from the County of Riverside and from the Native American Chairpersons, he/she shall submit the CRR and all received comments to the CPM for review and approval. The CRR shall be written by or under the direction of the CRS, shall be provided in the ARMR format, and shall conform to Riverside County's requirements for archaeological reports. The CRR shall report on all field activities including dates, times and locations, findings, samplings, and analyses. All survey reports, Department of Parks and Recreation (DPR) 523 forms, and additional research reports not previously submitted to the California Historic Resource Information System (CHRIS) and the State Historic Preservation Officer (SHPO) shall be included as an appendix to the CRR. If the Project Owner requests a suspension of construction activities, then a draft CRR that covers all cultural resources activities associated with the project shall be prepared by the CRS and submitted to the CPM for review and approval on the same day as the suspension/extension request. The draft CRR shall be retained at the project site in a secure facility until construction resumes or the project is withdrawn. If the project is withdrawn, then a final CRR shall be submitted to the CPM for review and approval at the same time as the withdrawal request. If artifacts and documentation are to be curated, the Project Owner shall provide documentation for approval by the CPM.	Within 90 days after completion of ground disturbance (including landscaping), the Project Owner shall submit the CRR to the Cultural Resources Specialist for the County of Riverside and the Chairpersons of all Native American groups that requested additional information on CPV Sentinel cultural resources. Sixty days thereafter, whether or not the county or Native Americans provide comments, the Project Owner shall submit the CRR and the comments, if any, to the CPM for review and approval. If any reports have previously been sent to the CHRIS, then receipt letters from the CHRIS or other verification of receipt shall be included in an appendix.	Within 90 days after completion of ground disturbance	TBD				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CUL-4.2	CON	The Project Owner shall submit the Cultural Resources Report (CRR) to the County of Riverside, and to the Chairpersons of all Native American groups that requested additional information on the CVP Sentinel cultural resources, for review and comment. After the Project Owner has received comments from the County of Riverside and from the Native American Chairpersons, he/she shall submit the CRR and all received comments to the CPM for review and approval. The CRR shall be written by or under the direction of the CRS, shall be provided in the ARMR format, and shall conform to Riverside County's requirements for archaeological reports. The CRR shall report on all field activities including dates, times and locations, findings, samplings, and analyses. All survey reports, Department of Parks and Recreation (DPR) 523 forms, and additional research reports not previously submitted to the California Historic Resource Information System (CHRIS) and the State Historic Preservation Officer (SHPO) shall be included as an appendix to the CRR. If the Project Owner requests a suspension of construction activities, then a draft CRR that covers all cultural resources activities associated with the project shall be prepared by the CRS and submitted to the CPM for review and approval on the same day as the suspension/extension request. The draft CRR shall be retained at the project site in a secure facility until construction resumes or the project is withdrawn. If the project is withdrawn, then a final CRR shall be submitted to the CPM for review and approval at the same time as the withdrawal request. If artifacts and documentation are to be curated, the Project Owner shall provide documentation for approval by the CPM.	Within 90 days after completion of ground disturbance (including landscaping), the Project Owner shall provide to the CPM a copy of an agreement with, or other written commitment from, a curation facility that meets the standards stated in the California State Historical Resources Commission's Guidelines for the curation of Archaeological Collections to accept cultural materials, if any, from this project. Any agreements concerning curation will be retained and available for audit for the life of the project.	Within 90 days after completion of ground disturbance	TBD				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CUL-4.3	CON	The Project Owner shall submit the Cultural Resources Report (CRR) to the County of Riverside, and to the Chairpersons of all Native American groups that requested additional information on the CVP Sentinel cultural resources, for review and comment. After the Project Owner has received comments from the County of Riverside and from the Native American Chairpersons, he/she shall submit the CRR and all received comments to the CPM for review and approval. The CRR shall be written by or under the direction of the CRS, shall be provided in the ARMR format, and shall conform to Riverside County's requirements for archaeological reports. The CRR shall report on all field activities including dates, times and locations, findings, samplings, and analyses. All survey reports, Department of Parks and Recreation (DPR) 523 forms, and additional research reports not previously submitted to the California Historic Resource Information System (CHRIS) and the State Historic Preservation Officer (SHPO) shall be included as an appendix to the CRR. If the Project Owner requests a suspension of construction activities, then a draft CRR that covers all cultural resources activities associated with the project shall be prepared by the CRS and submitted to the CPM for review and approval on the same day as the suspension/extension request. The draft CRR shall be retained at the project site in a secure facility until construction resumes or the project is withdrawn. If the project is withdrawn, then a final CRR shall be submitted to the CPM for review and approval at the same time as the withdrawal request. If artifacts and documentation are to be curated, the Project Owner shall provide documentation for approval by the CPM.	Within 10 days after CPM approval, the Project Owner shall provide documentation to the CPM confirming that copies of the CRR have been provided to the SHPO, the CHRIS, and the curating institution if archaeological materials were collected.	Within 10 days after CPM approval	TBD				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CUL-4.4	CON	The Project Owner shall submit the Cultural Resources Report (CRR) to the County of Riverside, and to the Chairpersons of all Native American groups that requested additional information on the CVP Sentinel cultural resources, for review and comment. After the Project Owner has received comments from the County of Riverside and from the Native American Chairpersons, he/she shall submit the CRR and all received comments to the CPM for review and approval. The CRR shall be written by or under the direction of the CRS, shall be provided in the ARMR format, and shall conform to Riverside County's requirements for archaeological reports. The CRR shall report on all field activities including dates, times and locations, findings, samplings, and analyses. All survey reports, Department of Parks and Recreation (DPR) 523 forms, and additional research reports not previously submitted to the California Historic Resource Information System (CHRIS) and the State Historic Preservation Officer (SHPO) shall be included as an appendix to the CRR. If the Project Owner requests a suspension of construction activities, then a draft CRR that covers all cultural resources activities associated with the project shall be prepared by the CRS and submitted to the CPM for review and approval on the same day as the suspension/extension request. The draft CRR shall be retained at the project site in a secure facility until construction resumes or the project is withdrawn. If the project is withdrawn, then a final CRR shall be submitted to the CPM for review and approval at the same time as the withdrawal request. If artifacts and documentation are to be curated, the Project Owner shall provide documentation for approval by the CPM.	Within 30 days after requesting a suspension of construction activities, the Project Owner shall submit a draft CRR to the CPM for review and approval.	Within 30 days after requesting a suspension of construction activities	TBD				Not Started
CUL-5.2	CON	Prior to and for the duration of ground disturbance, the Project Owner shall provide Worker Environmental Awareness Program (WEAP) training to all new workers within their first week of employment. The training shall be prepared by the CRS, may be conducted by any member of the archaeological team, and may be presented in the form of a video. The CRS shall be available (by telephone or in person) to answer questions posed by employees. The training may be discontinued when ground disturbance is completed or suspended, but shall be resumed when ground disturbance, such as landscaping, resumes.	On a monthly basis, the Project Owner shall provide in the Monthly Compliance Report (MCR) the WEAP Training Acknowledgement forms of persons who have completed the training in the prior month and a running total of all persons who have completed training to date.	Monthly	Monthly				On-going
CUL-6.2	CON	The research design in the CRMMP shall govern the collection, treatment, retention/disposal, and curation of any archaeological materials encountered.	2. The CRS shall provide a statement that "no cultural resources over 50 years of age were discovered" to the CPM as an e-mail or in some other form acceptable to the CPM, except during suspension of monitoring or when monitoring has concluded.	Each day that no discoveries are made	Daily				On-going
CUL-6.3	CON	On forms provided by the CPM, CRMs shall keep a daily log of any monitoring and other cultural resources activities and any instances of noncompliance with the Conditions and/or applicable LORS.	3. The project owner shall include in each MCR a copy of the monthly summary report of cultural resources-related monitoring prepared by the CRS. Copies of daily logs shall be retained by the project owner and made available for audit by the CPM.	Monthly while monitoring is ongoing	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
CUL-6.4	CON	In the event that the CRS believes that the current level of monitoring is not appropriate in certain locations, a letter or e-mail detailing the justification for changing the level of monitoring shall be provided to the CPM for review and approval prior to any change in the level of monitoring.	4. Documentation justifying the change shall be submitted to the CPM for review and approval.	At least 24 hours prior to implementing a proposed change in monitoring level	As Required				On-going
CUL-7.2	CON	In the event cultural resources over 50 years of age or, if younger, considered exceptionally significant are found, or impacts to such resources can be anticipated, construction shall be halted or redirected in the immediate vicinity of the discovery sufficient to ensure that the resource is protected from further impacts. Monitoring and daily reporting as provided in these conditions shall continue during all ground-disturbing activities wherever project construction is not halted. The halting or redirection of construction shall remain in effect until the CRS has visited the discovery and all of the required actions have occurred	2. Completed DPR 523 forms for resources newly discovered during ground disturbance shall be submitted to the CPM for review and approval	No later than 24 hours following the notification of the CPM or 48 hours following the completion of data recordation/recovery, whichever the CRS concludes is more appropriate for the subject cultural resource.	As Required				On-going
CUL-8.1	CON	If fill soils must be acquired from a non-commercial borrow site or disposed of to a non-commercial disposal site, unless less-than-five-year-old surveys of these sites for archaeological resources are documented to and approved by the CPM, the CRS shall survey the borrow and/or disposal site(s) for cultural resources and record on DPR 523 forms any that are identified. When the survey is completed, the CRS shall convey the results and recommendations for further action to the project owner and the CPM, who will determine what, if any, further action is required. If the CPM determines that significant archaeological resources that cannot be avoided are present at the borrow site, all these conditions of certification shall apply. The CRS shall report on the methods and results of these surveys in the CRR.	1. As soon as the project owner knows that a non-commercial borrow site and/or disposal site will be used, he/she shall notify the CRS and CPM and provide documentation of previous archaeological survey, if any, dating within the past five years, for CPM approval.	Immediately as necessary	As Required				As Required
CUL-8.2	CON	If fill soils must be acquired from a non-commercial borrow site or disposed of to a non-commercial disposal site, unless less-than-five-year-old surveys of these sites for archaeological resources are documented to and approved by the CPM, the CRS shall survey the borrow and/or disposal site(s) for cultural resources and record on DPR 523 forms any that are identified. When the survey is completed, the CRS shall convey the results and recommendations for further action to the project owner and the CPM, who will determine what, if any, further action is required. If the CPM determines that significant archaeological resources that cannot be avoided are present at the borrow site, all these conditions of certification shall apply. The CRS shall report on the methods and results of these surveys in the CRR.	2. In the absence of documentation of recent archaeological survey the CRS shall survey the site(s) for archaeological resources. The CRS shall notify the project owner and the CPM of the results of the cultural resources survey, with recommendations, if any, for further action.	At least 30 days prior to any soil borrow or disposal activities on the non-commercial borrow and/or disposal sites	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
ELEC-1	CON	Prior to the start of any increment of electrical construction for all electrical equipment and systems 480 Volts or higher with the exception of underground duct work and any physical layout drawings and drawings not related to code compliance and life safety, the project owner shall submit, for CBO design review and approval, the proposed final design, specifications, and calculations. Upon approval, the listed plans, together with design changes and design change notices, shall remain on the site or at another accessible location for the operating life of the project. The project owner shall request that the CBO inspect the installation to ensure compliance with the requirements of applicable LORS	The project owner shall submit to the CBO for design review and approval the above-listed documents. The project owner shall include in this submittal a copy of the signed and stamped statement from the responsible electrical engineer attesting compliance with the applicable LORS, and shall send the CPM a copy of the transmittal letter in the next monthly compliance report.	At least 30 days (or within a project owner- and CBO-approved alternative time frame) prior to the start of each increment of electrical construction	09/29/11	6/6/2011	10/31/2011		In Progress
GEN-1.1	CON	The project owner shall design, construct, and inspect the project in accordance with the 2007 California Building Standards Code (CBSC), also known as Title 24, California Code of Regulations, which encompasses the California Building Code (CBC), California Administrative Code, California Electrical Code, California Mechanical Code, California Plumbing Code, California Energy Code, California Fire Code, California Code for Building Conservation, California Reference Standards Code, and all other applicable engineering laws, ordinances, regulations, and standards (LORS) in effect at the time initial design plans are submitted to the chief building official (CBO) for review and approval. The CBSC in effect is the edition that has been adopted by the California Building Standards Commission and published at least 180 days previously. The project owner shall ensure that all the provisions of the above applicable codes are enforced during the construction, addition, alteration, moving, demolition, repair, or maintenance of the completed facility (2007 CBC, Appendix. Chapter 1, § 101.2, Scope). All transmission facilities (lines, switchyards, switching stations, and substations) are covered in the Conditions of Certification in the Transmission System Engineering section of this Decision.	The project owner shall submit to the CPM a statement of verification, signed by the responsible design engineer, attesting that all designs, construction, installation, and inspection requirements of the applicable LORS and the Energy Commission's decision have been met in the area of facility design.	Within 30 days following receipt of the certificate of occupancy	01/01/12				Not Started
GEN-1.2	CON	The project owner shall ensure that all the provisions of the above applicable codes are enforced during the construction, addition, alteration, moving, demolition, repair, or maintenance of the completed facility (2007 CBC, Appendix. Chapter 1, § 101.2, Scope). All transmission facilities (lines, switchyards, switching stations, and substations) are covered in the Conditions of Certification in the Transmission System Engineering section of this Decision.	Once the certificate of occupancy has been issued, the project owner shall inform the CPM of any work to be performed on any portion(s) of the completed facility that requires CBO approval for compliance with the above codes. The CPM will then determine if the CBO needs to approve the work.	At least 30 days prior to any work performed	01/01/12				
GEN-2.2	CON	Before submitting the initial engineering designs for CBO review, the project owner shall furnish the CPM and the CBO with a schedule of facility design submittals, master drawing and master specifications lists. The schedule shall contain a list of proposed submittal packages of designs, calculations, and specifications for major structures and equipment. To facilitate audits by Energy Commission staff, the project owner shall provide specific packages to the CPM upon request.	The project owner shall provide schedule updates in the monthly compliance report.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
GEN-3.1	CON	The project owner shall make payments to the CBO for design review, plan checks, and construction inspections, based upon a reasonable fee schedule to be negotiated between the project owner and the CBO. These fees may be consistent with the fees listed in the 2007 CBC (2007 CBC, Appendix Chapter 1, § 108, Fees; Chapter 1, § 108.4, Permits, Fees, Applications and Inspections), adjusted for inflation and other appropriate adjustments; may be based on the value of the facilities reviewed; may be based on hourly rates; or may be otherwise agreed upon by the project owner and the CBO.	The project owner shall make the required payments to the CBO in accordance with the agreement between the project owner and the CBO.	In accordance with the agreement between the project owner and the CBO	04/15/11	4/7/2011			On-going
GEN-3.2	CON	The project owner shall make payments to the CBO for design review, plan checks, and construction inspections, based upon a reasonable fee schedule to be negotiated between the project owner and the CBO. These fees may be consistent with the fees listed in the 2007 CBC (2007 CBC, Appendix Chapter 1, § 108, Fees; Chapter 1, § 108.4, Permits, Fees, Applications and Inspections), adjusted for inflation and other appropriate adjustments; may be based on the value of the facilities reviewed; may be based on hourly rates; or may be otherwise agreed upon by the project owner and the CBO.	The project owner shall send a copy of the CBO's receipt of payment to the CPM in the next monthly compliance report indicating that applicable fees have been paid.	Monthly	Monthly				On-going
GEN-4.3	CON	The project owner shall assign a California registered architect, structural engineer, or civil engineer as the resident engineer in charge of the project.	If the resident engineer or the delegated engineer(s) is subsequently reassigned or replaced, the project owner shall submit the resume and registration number of the newly assigned engineer to the CBO for review and approval.	Within 5 days of designation	As Required				As Required
GEN-4.4	CON	The project owner shall assign a California registered architect, structural engineer, or civil engineer as the resident engineer in charge of the project.	The project owner shall notify the CPM of the CBO's approval of the new engineer	Within five days of approval	As Required				
GEN-5.4	CON	Prior to the start of construction, the project owner shall assign at least one of each of the following California registered engineers to the project: a design engineer who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; a mechanical engineer; and an electrical engineer.	If the designated responsible engineer is subsequently reassigned or replaced, the project owner has five days in which to submit the resume and registration number of the newly assigned engineer to the CBO for review and approval. The project owner shall notify the CPM of the CBO's approval of the new engineer	Within five days of the approval	As Required				As Required
GEN-6.2	CON	Prior to the start of an activity requiring special inspection, the project owner shall assign to the project qualified and certified special inspector(s) who shall be responsible for the special inspections required by the 2007 CBC, Chapter 17, Section 1704, Special Inspections; Chapter 17A, Section 1704A, Special Inspections; and Appendix Chapter 1, Section 109, Inspections. All transmission facilities (lines, switchyards, switching stations, and substations) are addressed in Conditions of Certification in the Transmission System Engineering section of this Decision.	The project owner shall also submit to the CPM a copy of the CBO's approval of the qualifications of all special inspectors in the next monthly compliance report.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
GEN-6.3	CON	Prior to the start of an activity requiring special inspection, the project owner shall assign to the project qualified and certified special inspector(s) who shall be responsible for the special inspections required by the 2007 CBC, Chapter 17, Section 1704, Special Inspections; Chapter 17A, Section 1704A, Special Inspections; and Appendix Chapter 1, Section 109, Inspections. All transmission facilities (lines, switchyards, switching stations, and substations) are addressed in Conditions of Certification in the Transmission System Engineering section of this Decision.	If the special inspector is subsequently reassigned or replaced, the project owner shall submit the name and qualifications of the newly assigned special inspector to the CBO for approval.	Within 5 days of designation	As Required				As Required
GEN-6.4	CON	Prior to the start of an activity requiring special inspection, the project owner shall assign to the project qualified and certified special inspector(s) who shall be responsible for the special inspections required by the 2007 CBC, Chapter 17, Section 1704, Special Inspections; Chapter 17A, Section 1704A, Special Inspections; and Appendix Chapter 1, Section 109, Inspections. All transmission facilities (lines, switchyards, switching stations, and substations) are addressed in Conditions of Certification in the Transmission System Engineering section of this Decision.	The project owner shall notify the CPM of the CBO's approval of the newly assigned inspector	Within five days of the approval	As Required				As Required
GEN-7.1	CON	If any discrepancy in design and/or construction is discovered in any engineering work that has undergone CBO design review and approval, the project owner shall document the discrepancy and recommend required corrective actions. The discrepancy documentation shall be submitted to the CBO for review and approval. The discrepancy documentation shall reference this condition of certification and, if appropriate, applicable sections of the CBC and/or other LORS.	The project owner shall transmit a copy of the CBO's approval of any corrective action taken to resolve a discrepancy to the CPM in the next monthly compliance report.	Monthly	As Required				As Required
GEN-7.2	CON	If any discrepancy in design and/or construction is discovered in any engineering work that has undergone CBO design review and approval, the project owner shall document the discrepancy and recommend required corrective actions. The discrepancy documentation shall be submitted to the CBO for review and approval. The discrepancy documentation shall reference this condition of certification and, if appropriate, applicable sections of the CBC and/or other LORS.	If any corrective action is disapproved the project owner shall advise the CPM of the reason for disapproval and the revised corrective action to obtain CBO's approval.	Within five days of disapproval	As Required				As Required
GEN-8.1	CON	The project owner shall obtain the CBO's final approval of all completed work that has undergone CBO design review and approval. The project owner shall request the CBO to inspect the completed structure and review the submitted documents. The project owner shall notify the CPM after obtaining the CBO's final approval. The project owner shall retain one set of approved engineering plans, specifications, and calculations (including all approved changes) at the project site or at an alternative site approved by the CPM during the operating life of the project.	The project owner shall submit to the CBO, with a copy to the CPM, in the next monthly compliance report, (a) a written notice that the completed work is ready for final inspection, and (b) a signed statement that the work conforms to the final approved plans. After storing the final approved engineering plans, specifications, and calculations described above, the project owner shall submit to the CPM a letter stating both that the above documents have been stored and the storage location of those documents	Within 15 days of the completion of any work	TBD				Not Started
GEN-8.2	CON	Electronic copies of the approved plans, specifications, calculations, and marked-up as-builts shall be provided to the CBO for retention by the CPM.	The project owner shall provide to the CBO three sets of electronic copies of the above documents at its own expense.	Within 90 days of the completion of construction	11/01/13				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
MECH-1.1	CON	The project owner shall submit, for CBO design review and approval, the proposed final design, specifications and calculations for each plant major piping and plumbing system listed in FACILITY DESIGN Table 1, Condition of Certification GEN-2. The submittal shall also include the applicable QA/QC procedures. Upon completion of construction of any such major piping or plumbing system, the project owner shall request the CBO's inspection approval of that construction	The project owner shall submit to the CBO for design review and approval the final plans, specifications, and calculations, including a copy of the signed and stamped statement from the responsible mechanical engineer certifying compliance with applicable LORS, and shall send the CPM a copy of the transmittal letter in the next monthly compliance report.	At least 30 days (or within a project owner- and CBO-approved alternative time frame) prior to the start of any increment of major piping or plumbing construction listed in FACILITY DESIGN Table 1, Condition of Certification GEN-2	On-going				In Progress
MECH-1.2	CON	The project owner shall submit, for CBO design review and approval, the proposed final design, specifications and calculations for each plant major piping and plumbing system listed in FACILITY DESIGN Table 1, Condition of Certification GEN-2. The submittal shall also include the applicable QA/QC procedures. Upon completion of construction of any such major piping or plumbing system, the project owner shall request the CBO's inspection approval of that construction	The project owner shall transmit to the CPM, in the monthly compliance report following completion of any inspection, a copy of the transmittal letter conveying the CBO's inspection approvals.	Monthly as required	As Required				Not Started
MECH-2.1	CON	For all pressure vessels installed in the plant, the project owner shall submit to the CBO and California Occupational Safety and Health Administration (Cal-OSHA), prior to operation, the code certification papers and other documents required by applicable LORS. Upon completion of the installation of any pressure vessel, the project owner shall request the appropriate CBO and/or Cal-OSHA inspection of that installation.	The project owner shall submit to the CBO for design review and approval, the above-listed documents, including a copy of the signed and stamped engineer's certification, with a copy of the transmittal letter to the CPM.	At least 30 days (or within a project owner- and CBO-approved alternative time frame) prior to the start of on-site fabrication or installation of any pressure vessel	TBD				Not Started
MECH-2.2	CON	For all pressure vessels installed in the plant, the project owner shall submit to the CBO and California Occupational Safety and Health Administration (Cal-OSHA), prior to operation, the code certification papers and other documents required by applicable LORS. Upon completion of the installation of any pressure vessel, the project owner shall request the appropriate CBO and/or Cal-OSHA inspection of that installation.	The project owner shall transmit to the CPM, in the monthly compliance report following completion of any inspection, a copy of the transmittal letter conveying the CBO's and/or Cal/OSHA inspection approvals.	Monthly as required	TBD				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
MECH-3	CON	The project owner shall submit to the CBO for design review and approval the design plans, specifications, calculations, and quality control procedures for any heating, ventilating, air conditioning (HVAC), or refrigeration system. Packaged HVAC systems, where used, shall be identified with the appropriate manufacturer's data sheets. The project owner shall design and install all HVAC and refrigeration systems within buildings and related structures in accordance with the CBC and other applicable codes. Upon completion of any increment of construction, the project owner shall request the CBO's inspection and approval of that construction. The final plans, specifications and calculations shall include approved criteria, assumptions, and methods used to develop the design. In addition, the responsible mechanical engineer shall sign and stamp all plans, drawings and calculations and submit a signed statement to the CBO that the proposed final design plans, specifications and calculations conform with the applicable LORS.	The project owner shall submit to the CBO the required HVAC and refrigeration calculations, plans, and specifications, including a copy of the signed and stamped statement from the responsible mechanical engineer certifying compliance with the CBC and other applicable codes, with a copy of the transmittal letter to the CPM.	At least 30 days (or within a project owner- and CBO-approved alternative time frame) prior to the start of construction of any HVAC or refrigeration system	2/29/2011				Not Started
NOISE-2.1	CON	Throughout the construction and operation of the CPV Sentinel project, the project owner shall document, investigate, evaluate, and attempt to resolve all project-related noise complaints. • Use the Noise Complaint Resolution Form (below), or a functionally equivalent procedure acceptable to the CPM, to document and respond to each noise complaint;	The project owner shall file a copy of the Noise Complaint Resolution Form with the CPM, documenting the resolution of the complaint. If mitigation is required to resolve a complaint, and the complaint is not resolved within a three-day period, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	As Required				As Required
NOISE-2.2	CON	• Attempt to contact the person(s) making the noise complaint within 24 hours;	The project owner shall file a copy of the Noise Complaint Resolution Form with the CPM, documenting the resolution of the complaint. If mitigation is required to resolve a complaint, and the complaint is not resolved within a three-day period, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	As Required				As Required
NOISE-2.3	CON	• Conduct an investigation to determine the source of noise related to the complaint;	The project owner shall file a copy of the Noise Complaint Resolution Form with the CPM, documenting the resolution of the complaint. If mitigation is required to resolve a complaint, and the complaint is not resolved within a three-day period, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	As Required				As Required
NOISE-2.4	CON	• Take all feasible measures to reduce the noise at its source if the noise is project related;	The project owner shall file a copy of the Noise Complaint Resolution Form with the CPM, documenting the resolution of the complaint. If mitigation is required to resolve a complaint, and the complaint is not resolved within a three-day period, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
NOISE-2.5	CON	• Submit a report documenting the complaint and the actions taken. The report shall include: a complaint summary, including final results of noise reduction efforts, and if obtainable, a signed statement by the complainant stating that the noise problem is resolved to the complainant's satisfaction	The project owner shall file a copy of the Noise Complaint Resolution Form with the CPM, documenting the resolution of the complaint. If mitigation is required to resolve a complaint, and the complaint is not resolved within a three-day period, the project owner shall submit an updated Noise Complaint Resolution Form when the mitigation is implemented.	Within five days of receiving a noise complaint	As Required				As Required
PAL-1.3	CON	The project owner shall ensure that the PRS obtains qualified paleontological resource monitors to monitor as he or she deems necessary on the project.	If additional monitors are obtained during the project, the PRS shall provide additional letters and resumes to the CPM.	No later than one week prior to the monitor's beginning on-site duties	As Required				As Required
PAL-2.2	CON	If the footprint of the project or its linear facilities change, the project owner shall provide maps and drawings reflecting those changes to the PRS and CPM.	Revised maps and drawings shall be provided to the PRS and CPM	At least 15 days prior to the start of ground disturbance	As Required				As Required
PAL-2.3	CON	If construction of the project proceeds in phases, maps and drawings may be submitted prior to the start of each phase. A letter identifying the proposed schedule of each project phase shall be provided to the PRS and CPM. The project owner shall ensure that the PRS obtains qualified paleontological resource monitors to monitor as he or she deems necessary on the project. At a minimum, the Project Owner shall ensure that the PRS or PRM consults weekly with the project superintendent or construction field manager to confirm area(s) to be worked the following week, and until ground disturbance is completed.	The project owner shall notify the PRS and CPM of any construction phase scheduling changes. If there are changes to the scheduling of the construction phases, the project owner shall submit a letter to the CPM.	Within 5 days of identifying the changes and before work commences on affected phases. Consultations weekly until complete	As Required				
PAL-4.3	CON	Prior to ground disturbance and for the duration of construction activities involving ground disturbance, the project owner and the PRS shall prepare and conduct weekly CPM-approved training for the following workers: project managers, construction supervisors, foremen and general workers involved with or who operate ground-disturbing equipment or tools. Workers shall not excavate in sensitive units prior to receiving CPM-approved worker training. Worker training shall consist of an initial in-person PRS training during the project kick-off, for those mentioned above. Following initial training, a CPM approved video or in-person training may be used for new employees. The training program may be combined with other training programs prepared for cultural and biological resources, hazardous materials, or other areas of interest or concern. No ground disturbance shall occur prior to CPM approval of the Worker Environmental Awareness Program (WEAP), unless specifically approved by the CPM.	If the owner requests an alternate paleontological trainer, the resume and qualifications of the trainer shall be submitted to the CPM for review and approval. Alternate trainers shall not conduct training prior to CPM authorization.	Prior to installation of an alternate trainer	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
PAL-4.4	CON	Prior to ground disturbance and for the duration of construction activities involving ground disturbance, the project owner and the PRS shall prepare and conduct weekly CPM-approved training for the following workers: project managers, construction supervisors, foremen and general workers involved with or who operate ground-disturbing equipment or tools. Workers shall not excavate in sensitive units prior to receiving CPM-approved worker training. Worker training shall consist of an initial in-person PRS training during the project kick-off, for those mentioned above. Following initial training, a CPM approved video or in-person training may be used for new employees. The training program may be combined with other training programs prepared for cultural and biological resources, hazardous materials, or other areas of interest or concern. No ground disturbance shall occur prior to CPM approval of the Worker Environmental Awareness Program (WEAP), unless specifically approved by the CPM.	In the monthly compliance report (MCR, the project owner shall provide copies of the WEAP certification of completion forms with the names of those trained and the trainer or type of training (in-person or video) offered that month. The MCR shall also include a running total of all persons who have completed the training to date.	Monthly	Monthly				On-going
PAL-5.1	CON	The project owner shall ensure that the PRS and PRM(s) monitor all construction-related grading, excavation, trenching, and augering in areas where potential fossil-bearing materials have been identified, both at the site and along any constructed linear facilities associated with the project consistent with the PRMMP . In the event that the PRS determines full-time monitoring is not necessary in locations that were identified as potentially fossil-bearing in the PRMMP, the project owner shall notify and seek the concurrence of the CPM.	The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified if changes in the monitoring plan identified in the PRMMP. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	10 days in advance of any proposed changes in monitoring	As Required	9/20/2011	9/21/2011	9/21/2011	On-going
PAL-5.2	CON	The project owner shall ensure that the PRS and PRM(s) have the authority to halt or redirect construction if paleontological resources are encountered. The project owner shall ensure that there is no interference with monitoring activities unless directed by the PRS. The project owner shall ensure that the PRS prepares a summary of monitoring and other paleontological activities placed in the monthly compliance reports. The summary will include the name(s) of PRS or PRM(s) active during the month, general descriptions of training and monitored construction activities, and general locations of excavations, grading, and other activities. A section of the report shall include the geologic units or subunits encountered, descriptions of samplings within each unit, and a list of identified fossils. A final section of the report will address any issues or concerns about the project relating to paleontologic monitoring, including any incidents of non-compliance or any changes to the monitoring plan that have been approved by the CPM. If no monitoring took place during the month, the report shall include an explanation in the summary as to why monitoring was not conducted.	The project owner shall ensure that the PRS submits the summary of monitoring and paleontological activities in the MCR. When feasible, the CPM shall be notified if changes in the monitoring plan identified in the PRMMP. If there is any unforeseen change in monitoring, the notice shall be given as soon as possible prior to implementation of the change.	Monthly	Monthly				On-going

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
PAL-6	CON	The project owner, through the designated PRS, shall ensure that all components of the PRMMP are adequately performed including collection of fossil materials, preparation of fossil materials for analysis, analysis of fossils, identification and inventory of fossils, the preparation of fossils for curation, and the delivery for curation of all significant paleontological resource materials encountered and collected during project construction.	The project owner shall maintain in his/her compliance file copies of signed contracts or agreements with the designated PRS and other qualified research specialists. The project owner shall maintain these files for a period of three years after project completion and approval of the CPM-approved paleontological resource report. The project owner shall be responsible for paying any curation fees charged by the museum for fossils collected and curated as a result of paleontological mitigation. A copy of the letter of transmittal submitting the fossils to the curating institution shall be provided to the CPM.	Per PAL-7	As Required				As Required
PAL-7	CON	The project owner shall ensure preparation of a Paleontological Resources Report (PRR) by the designated PRS. The PRR shall be prepared following completion of the ground-disturbing activities. The PRR shall include an analysis of the collected fossil materials and related information, and submit it to the CPM for review and approval.	The project owner shall submit the PRR under confidential cover to the CPM.	Within 90 days after completion of ground-disturbing activities, including landscaping	TBD				Not Started
PUBLIC HEALTH-1	CON	The project owner shall develop and implement a Cooling Water Management Plan that is consistent with either Staff's *Cooling Water Management Program Guidelines* or the Cooling Technology Institute's *Best Practices for Control of Legionella* guidelines.	At least 30 days prior to the commencement of cooling tower operations, the Cooling Water Management Plan shall be provided to the Compliance Project Manager for review and approval.	At least 30 days prior to commencement of cooling tower operations	TBD				Not Started
SOIL&WATER 1.3	CON	**SWPPP for SoCal Gas Line:** The project owner shall comply with the requirements of the general National Pollution Discharge Elimination System (NPDES) permit for discharge of storm water associated with construction activity. The project owner shall develop, obtain compliance project manager (CPM) approval of, and implement a Storm Water Pollution Prevention Plan (SWPPP) for, the construction of the CPV Sentinel site, lay down area, and all linear facilities including the recycled water supply pipeline to PSNGC.	At least 60 days prior to site mobilization, the project owner shall submit to the CPM a copy of the construction SWPPP for review and approval prior to site mobilization. The project owner shall retain a copy on site. The project owner shall submit copies to the CPM of all correspondence between the project owner and the Colorado Region Regional Water Quality Control Board (RWQCB) regarding the NPDES permit for the discharge of storm water associated with construction activity within ten days of its receipt or submittal. Copies of correspondence shall include the notice of intent sent to the State Water Resources Control Board (SWRCB), and the board's confirmation letter indicating receipt and acceptance of the notice of intent.	At least 60 days prior to site mobilization	01/01/12				Not Started
SOIL&WATER 1.4	CON	**SWPPP for SCE Line:** The project owner shall comply with the requirements of the general National Pollution Discharge Elimination System (NPDES) permit for discharge of storm water associated with construction activity. The project owner shall develop, obtain compliance project manager (CPM) approval of, and implement a Storm Water Pollution Prevention Plan (SWPPP) for, the construction of the CPV Sentinel site, lay down area, and all linear facilities including the recycled water supply pipeline to PSNGC.	At least 60 days prior to site mobilization, the project owner shall submit to the CPM a copy of the construction SWPPP for review and approval prior to site mobilization. The project owner shall retain a copy on site. The project owner shall submit copies to the CPM of all correspondence between the project owner and the Colorado Region Regional Water Quality Control Board (RWQCB) regarding the NPDES permit for the discharge of storm water associated with construction activity within ten days of its receipt or submittal. Copies of correspondence shall include the notice of intent sent to the State Water Resources Control Board (SWRCB), and the board's confirmation letter indicating receipt and acceptance of the notice of intent.	At least 60 days prior to site mobilization	10/15/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
SOIL&WATER 10.1	CON	The project owner shall ensure that its recharge of groundwater complies with the following: 1. Recharge shall occur at the Desert Water Agency's (DWA's) Mission Creek Spreading Grounds	Verification: If recharge of other water is approved by the CPM pursuant to SOIL&WATER-11, the project owner shall, within 60 days of that approval, submit to the CPM copies of final agreements between the purchaser and the seller of the other water, between it and DWA, and between DWA and MWD (if water is to be delivered through an exchange with MWD) that ensure that the other water will be delivered to the Mission Creek spreading grounds.	Within 60 days of that approval of recharge of other water by the CPM	As Required				Not Started
SOIL&WATER-2.2	CON	The project owner shall complete all necessary plans, reports, documents, and monitoring necessary to satisfy the Conditions of Approval related to grading and flooding outlined in Draft Public Use Permit Number 897 issued by the County of Riverside, dated August 11, 2008, and Riverside County's Ordinance 754.2. Prior to initiation of construction activities, the project owner shall submit to the County of Riverside all necessary documentation, plans, and fees normally required for County's determination of compliance with Conditions of Approval, with copies to the CPM. The project shall not commence construction until the county of Riverside provides its written evaluation as to whether the proposed grading and flood control construction and operation activities complies with all county requirements and the CPM provides approval for construction. The project owner shall ensure compliance with all county standards and requirements for grading, erosion control, and flooding for the life of the project and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside requirements.	No later than 60 days prior to the start of facility construction the project owner will provide to the County of Riverside and CPM a copy of all necessary information to satisfy the Conditions of Approval for grading and flooding and for a building permit from the County of Riverside. The submittal must be reviewed by the County of Riverside and approved by the CPM.	No later than 60 days prior to the start of facility construction	01/13/11				In Progress

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
SOIL&WATER-3.1	CON	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	Verification: The project owner shall do all of the following: 1. No later than 30 days prior to the construction of the onsite water supply wells, the project owner shall submit two (2) copies to the CPM of the water well construction packet submitted to the County of Riverside. 2. No later than 15 days prior to the construction of the onsite water supply wells, the project owner shall submit two (2) copies of the written concurrence document from the County of Riverside indicating that the proposed well construction activities comply with all county well requirements and meet the requirements established by the county's water well permit program .	No later than 30 days prior to the construction of the onsite water supply wells	11/01/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
SOIL&WATER-3.2	CON	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	No later than 60 days after installation of each well at the project site, the project owner shall ensure that the well driller submits a Well Completion Report to the DWR with a copy provide to the CPM. The project owner shall submit to the CPM together with the Well Completion Report a copy of well drilling logs, water quality analyses, and any inspection reports that may be: 1. Submit copies to the CPM of any proposed well construction or operation permit changes within ten (10) days of submittal to or receipt from the County of Riverside. 2. Submit copies of any water well permit-related well monitoring reports required by the County of Riverside to the CPM in the annual compliance report. 3. No later than fifteen (15) days after completion of the onsite water supply wells, the project owner shall submit documentation to the CPM and the RWQCB that well drilling ac available for each well installed.	No later than 60 days after installation of each well at the project site, submit a Well Completion Report	11/30/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
SOIL&WATER-3.3	CON	The project owner shall construct and operate up to five onsite groundwater wells that produce water from the Mission Creek Groundwater Sub-basin (MCGS). The project owner shall ensure that the wells are completed in accordance with all applicable state and local water well construction permits and requirements. Prior to initiation of well construction activities, the project owner shall submit a well construction packet to the County of Riverside, in accordance with the County of Riverside Ordnance 682, containing all documentation, plans, and fees normally required for the county's well permit, with copies to the CPM. The project shall not construct a well or extract and use any groundwater therefrom until the County of Riverside issues its written evaluation as to whether the proposed well construction and operation activities comply with all applicable county well requirements, and the CPM provides approval to construct the well. The project owner shall provide documentation to the CPM that the well has been properly completed. In accordance with California's Water Code section 13754, the driller of the well shall submit to the Department of Water Resources (DWR) a Well Completion Report for each well installed. The project owner shall ensure the Well Completion reports are submitted. The project owner shall ensure compliance with all county water well standards and requirements for the life of the wells and shall provide the CPM with two (2) copies of all monitoring or other reports required for compliance with the County of Riverside water well standards and operation requirements, as well as any changes made to the operation of the well.	During well construction and for the operational life of the well, the project owner shall: 1. Submit copies to the CPM of any proposed well construction or operation changes. 2. Submit copies of any water well monitoring reports required by the County of Riverside to the CPM in the annual compliance report. 3. No later than fifteen (15) days after completion of the onsite water supply wells, the project owner shall submit documentation to the CPM and the RWQCB that well drilling activities were conducted in compliance with Title 23, California Code of Regulations, Chapter 15, Discharges of Hazardous Wastes to Land, (23 CCR, sections 2510 et seq.) requirements and that any onsite drilling sumps used for project drilling activities were removed in compliance with 23 CCR section 2511(c).	During well construction and for the operational life of the well, submit proposed well construction or operation, Annually, Submit copies of any water well monitoring reports , No later than fifteen (15) days after completion of the onsite water supply wells, submit documentation that well drilling activities were conducted	11/30/11				Not Started
STRUC-2.1	CON	The project owner shall submit to the CBO the required number of sets of the following documents related to work that has undergone CBO design review and approval: 1. Concrete cylinder strength test reports	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the CBO, with a copy of the transmittal letter to the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the CBO and the CPM. The project owner shall transmit a copy of the CBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, the reason for disapproval, and the revised corrective action necessary to obtain the CBO's approval.	Within five days of the discovery of any discrepancies - Within five days of disapproval - Within five days of resolution of the NCR - Within 15 days of approval - Within five days of disapproval	As Required				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
STRUC-2.2	CON	The project owner shall submit to the CBO the required number of sets of the following documents related to work that has undergone CBO design review and approval: 2. Concrete pour sign-off sheets	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the CBO, with a copy of the transmittal letter to the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the CBO and the CPM. The project owner shall transmit a copy of the CBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, the reason for disapproval, and the revised corrective action necessary to obtain the CBO's approval.	Within five days of the discovery of any discrepancies - Within five days of disapproval - Within five days of resolution of the NCR - Within 15 days of approval - Within five days of disapproval	As Required				Not Started
STRUC-2.3	CON	The project owner shall submit to the CBO the required number of sets of the following documents related to work that has undergone CBO design review and approval: 3. Bolt torque inspection reports (including location of test, date, bolt size, and recorded torques)	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the CBO, with a copy of the transmittal letter to the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the CBO and the CPM. The project owner shall transmit a copy of the CBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, the reason for disapproval, and the revised corrective action necessary to obtain the CBO's approval.	Within five days of the discovery of any discrepancies - Within five days of disapproval - Within five days of resolution of the NCR - Within 15 days of approval - Within five days of disapproval	As Required				As Required
STRUC-2.4	CON	The project owner shall submit to the CBO the required number of sets of the following documents related to work that has undergone CBO design review and approval: 4. Field weld inspection reports (including type of weld, location of weld, inspection of non-destructive testing procedure and results, welder qualifications, certifications, qualified procedure description or number	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the CBO, with a copy of the transmittal letter to the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the CBO and the CPM. The project owner shall transmit a copy of the CBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, the reason for disapproval, and the revised corrective action necessary to obtain the CBO's approval.	Within five days of the discovery of any discrepancies - Within five days of disapproval - Within five days of resolution of the NCR - Within 15 days of approval - Within five days of disapproval	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
STRUC-2.5	CON	The project owner shall submit to the CBO the required number of sets of the following documents related to work that has undergone CBO design review and approval: 5. Reports covering other structural activities requiring special inspections shall be in accordance with the 2007 CBC, Chapter 17, section 1704, Special Inspections, and section 1709.1, Structural Observations.	If a discrepancy is discovered in any of the above data, the project owner shall, within five days, prepare and submit an NCR describing the nature of the discrepancies and the proposed corrective action to the CBO, with a copy of the transmittal letter to the CPM (2007 CBC, Chapter 17, § 1704.1.2, Report Requirements). The NCR shall reference the condition(s) of certification and the applicable CBC chapter and section. Within five days of resolution of the NCR, the project owner shall submit a copy of the corrective action to the CBO and the CPM. The project owner shall transmit a copy of the CBO's approval or disapproval of the corrective action to the CPM within 15 days. If disapproved, the project owner shall advise the CPM, within five days, the reason for disapproval, and the revised corrective action necessary to obtain the CBO's approval.	Within five days of the discovery of any discrepancies - Within five days of disapproval - Within five days of resolution of the NCR - Within 15 days of approval - Within five days of disapproval	As Required				As Required
STRUC-3	CON	The project owner shall submit to the CBO design changes to the final plans required by the 2007 CBC, including the revised drawings, specifications, calculations, and a complete description of, and supporting rationale for, the proposed changes, and shall give to the CBO prior notice of the intended filing.	On a schedule suitable to the CBO, the project owner shall notify the CBO of the intended filing of design changes and shall submit the required number of sets of revised drawings and required number of copies of any other documents to the CBO, with a copy of the transmittal letter to the CPM. The project owner shall notify the CPM, via the monthly compliance report, when the CBO has approved the revised plans.	As required	As Required				As Required
STRUC-4.1	CON	Tanks and vessels containing quantities of toxic or hazardous materials exceeding amounts specified in the 2007 CBC, Chapter 3, Table 307.1(2), shall, at a minimum, be designed to comply with the requirements of that chapter.	The project owner shall submit to the CBO for design review and approval final design plans, specifications, and calculations, including a copy of the signed and stamped engineer's certification.	At least 30 days (or within a project owner- and CBO-approved alternate time frame) prior to the start of installation of tanks or vessels containing specified toxic or hazardous materials	TBD				Not Started
STRUC-4.2	CON	Tanks and vessels containing quantities of toxic or hazardous materials exceeding amounts specified in the 2007 CBC, Chapter 3, Table 307.1(2), shall, at a minimum, be designed to comply with the requirements of that chapter.	The project owner shall send copies of the CBO approvals of plan checks to the CPM in the following monthly compliance report. The project owner shall also transmit a copy of the CBO's inspection approvals to the CPM in the monthly compliance report following completion of any inspection.	Monthly as required	As Required				As Required
TLSN-1	CON	The project owner shall ensure that the proposed transmission lines are constructed according to the requirements of California Public Utility Commission's GO-95, GO-52, GO-131-D, Title 8, and Group 2. High Voltage Electrical Safety Orders, Sections 2700 through 2974 of the California Code of Regulations, and Southern California Edison's EMF-reduction guidelines.	The project owner shall submit to the Compliance Project Manager (CPM) a letter signed by a California registered electrical engineer affirming that the lines will be constructed according to the requirements stated in the condition.	At least 30 days before starting construction of the transmission line or related structures and facilities	11/14/11				In Progress

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TRANS-2.1	CON	The project owner shall comply with the applicable parking standards of the county of Riverside. The project owner shall prepare and submit to the CPM for approval a parking plan for the operation phase of the project in consultation with the county of Riverside. The operational parking plan shall show the location of the proposed parking area(s), a plot plan (diagram) with dimensions with an accurate portrayal of the number of parking spaces in accordance to the sizes stipulated in the applicable parking standards by the county of Riverside Transportation and Land Management Agency. The plan shall also show ingress/egress access (including emergency services vehicle access), parking lot circulation, car/van pool loading and unloading area(s) and any other item(s) that are requested by the county of Riverside Transportation and Land Use Management Agency subject to approval by the CPM. The operational parking plan shall include a policy to be enforced by the project owner stating all project-related parking occur onsite or in designated offsite parking areas as shown on the plan.	The project owner shall submit the proposed operation parking plan to the county of Riverside Department of Transportation for review and comment. The project owner shall provide to the CPM a copy of the transmittal letter submitted to the county of Riverside Department of Transportation requesting their review of the parking plan. The project owner shall provide any comment letters to the CPM for review. The applicant shall provide the county of Riverside Transportation and Land Management Agency 30 calendar days to review the parking plan and provide written comments to the project owner. The project owner shall provide a copy of the county of Riverside Transportation and Land Management Agency written comments and a copy of the parking plan(s) to the CPM for review and approval.	At least 90 days prior to operation, allow 30 days to review	04/05/13				Not Started
TRANS-2.2	CON	The project owner shall comply with the applicable parking standards of the county of Riverside. The project owner shall prepare and submit to the CPM for approval a parking plan for the operation phase of the project in consultation with the county of Riverside. The operational parking plan shall show the location of the proposed parking area(s), a plot plan (diagram) with dimensions with an accurate portrayal of the number of parking spaces in accordance to the sizes stipulated in the applicable parking standards by the county of Riverside Transportation and Land Management Agency. The plan shall also show ingress/egress access (including emergency services vehicle access), parking lot circulation, car/van pool loading and unloading area(s) and any other item(s) that are requested by the county of Riverside Transportation and Land Use Management Agency subject to approval by the CPM. The operational parking plan shall include a policy to be enforced by the project owner stating all project-related parking occur onsite or in designated offsite parking areas as shown on the plan.	At least 60 calendar days prior to the start of commercial operation, the project owner shall provide a copy of the operation phase parking plan to the CPM for review and approval.	At least 60 days prior to start of commercial operation	05/15/13				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TRANS-4.2	CON	The project owner shall repair affected public rights-of-way (e.g., highway, road, bicycle path, pedestrian path) to original or near original condition that has been damaged due to construction activities conducted for the project and its associated facilities.	Within 60 calendar days after completion of construction, the project owner shall meet with the CPM, the county of Riverside Transportation and Land Management Agency, the city of Palm Springs Department of Public Works and Engineering, and Caltrans to identify sections of public right-of-way to be repaired, to establish a schedule to complete the repairs and to receive approval for the action(s). Following completion of any public right-of-way repairs, the project owner shall provide to the CPM a letter signed by the county of Riverside Transportation and Land Management Agency, the city of Palm Springs Department of Public Works and Engineering, and Caltrans stating their satisfaction with the repairs.	Within 60 calendar days after completion of construction	11/29/13				Not Started
TRANS-5	CON	Prior to the start of commercial operation, the project owner shall dedicate, and complete improvement of Melissa Lane from Dillon Road to the 16th Avenue according to the county of Riverside standard for a collector rural road – Riverside County Standard No. 136. The project owner shall improve this portion of Melissa Lane with 28-feet of asphalt concrete pavement within a 60-foot full-width dedicated right-of-way including standard corner cutback in accordance to county standards. The project owner shall also dedicate and complete improvement of roadway from 16th Avenue north to the project site to the County of Riverside standard for a commercial driveway – Riverside County Standard No. 207A, or improved to a standard agreed to by the Director of the County of Riverside Transportation and Land Management.	Not later than a 180 days prior to the estimated start of commercial operation, the project owner shall submit to the Director of the county of Riverside Transportation and Land Management Agency, Planning Department for review, the required improvement plan(s) for Melissa Lane, and the roadway north of 16th Avenue to the project site, and the completed forms for the dedication of the roadway segments. The project owner shall provide to the CPM a copy of the transmittal letter submitted to the county of Riverside Department of Transportation and Land Management Agency, Planning Department requesting their review of the improvement plans and dedication of roadway submitted for Melissa Lane and the roadway north of 16th Avenue to the project site. The project owner shall allow the Director of the county of Riverside Transportation and Land Management Agency, Planning Department 30 days to provide comment on the improvement plans and roadway dedication. The project owner shall provide a copy of the Director of the county of Riverside Transportation and Land Management Agency, Planning Department comments to the CPM prior to the start of construction of the improvements to Melissa Lane and the roadway north of 16th Avenue to the project site, and roadway dedication. If the CPM determines that the improvement plans and/or the roadway dedication requires revision, the project owner shall provide to the CPM and the Director of the county of Riverside Transportation and Land Management Agency, Planning Department a plan and/or roadway dedication	Not later than a 180 days prior to the estimated start of commercial operation	01/01/13				Not Started
TSE-1.1	CON	The project owner shall ensure that a schedule of transmission facility design submittals, a Master Drawing List, a Master Specifications List, and a Major Equipment and Structure List are furnished to the CPM and to the CBO. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. To facilitate audits by Energy Commission staff, the project owner shall ensure that designated packages are provided to the CPM when requested. To facilitate audits by Energy Commission staff, the project owner shall provide designated packages to the CPM when requested.	The project owner shall submit the schedule, a Master Drawing List, and a Master Specifications List to the CBO and to the CPM. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. Additions and deletions shall be made to the table only with CPM and CBO approval. The project owner shall provide schedule updates in the Monthly Compliance Report.	At least 60 days (or a lesser number of days mutually agreed to by the project owner and the CBO) prior to the start of construction	10/15/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TSE-1.2	CON	The project owner shall ensure that a schedule of transmission facility design submittals, a Master Drawing List, a Master Specifications List, and a Major Equipment and Structure List are furnished to the CPM and to the CBO. The schedule shall contain a description and list of proposed submittal packages for design, calculations, and specifications for major structures and equipment. To facilitate audits by Energy Commission staff, the project owner shall provide designated packages to the CPM when requested.	The project owner shall provide schedule updates in the Monthly Compliance Repor	Monthly	10/15/11				On-going
TSE-2.1	CON	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	The project owner shall submit to the CBO for review and approval, the names, qualifications and registration numbers of all engineers assigned to the project. If any one of the designated engineers is subsequently reassigned or replaced, the project owner shall submit the name, qualifications and registration number of the newly assigned engineer to the CBO for review and approval. The project owner shall notify the CPM of the CBO's approval of the new engineer. This engineer shall be authorized to halt earthwork and to require changes; if site conditions are unsafe or do not conform with predicted conditions used as a basis for design of earthwork or foundations.	At least 30 days (or a lesser number of days mutually agreed to by the project owner and the CBO) prior to the start of rough grading	11/14/11				Not Started
TSE-2.2	CON	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	The project owner shall notify the CPM of the CBO's approvals of the engineers	Within five days of the approval	11/14/11				Not Started
TSE-2.3	CON	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	If the designated responsible engineer is subsequently reassigned or replaced, the project owner must submit the name, qualifications, and registration number of the newly assigned engineer to the CBO for review and approval. The project owner shall notify the CPM of the CBO's approval of the new engineer within five days of the approval.	Within five days from notification	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TSE-2.4	CON	Prior to the start of construction the project owner shall ensure that an electrical engineer and at least one of each of the following are assigned to the project: A) a civil engineer; B) a geotechnical engineer, or a civil engineer experienced and knowledgeable in the practice of soils engineering; C) a design engineer, who is either a structural engineer or a civil engineer fully competent and proficient in the design of power plant structures and equipment supports; or D) a mechanical engineer. (Bus.& Prof. Code §§ 6704 et seq., require state registration to practice as a civil engineer or structural engineer in California.)	The project owner shall notify the CPM of the CBO's approval of the new engineer	Within five days of the approval	As Required				As Required
TSE-3	CON	If any discrepancy in design and/or construction is discovered in any engineering work that has undergone CBO design review and approval, the project owner shall ensure that the discrepancy is documented and corrective action is recommended. (1998 CBC, Chap. 1, § 108.4, Approval Required; Chap. 17, § 1701.3, Duties and Responsibilities of the Special Inspector; appen. Chap. 33, § 3317.7, Notification of Noncompliance). The project owner shall ensure that the discrepancy documentation becomes a controlled document and is submitted to the CBO for review and approval and references this condition of certification.	The project owner shall ensure that a copy of the CBO's approval or disapproval of any corrective action taken to resolve a discrepancy is submitted to the CPM within 15 days of receipt. If disapproved, the project owner shall ensure that the CPM is advised, within five days, the reason for disapproval, and the revised corrective action required to obtain the CBO's approval.	Within 15 days of receipt	As Required				As Required
TSE-4	CON	For the power plant switchyard, outlet line and termination, the project owner shall ensure that until plans for that increment have been approved by the CBO construction does not begin any increment. These plans, together with design changes and design change notices, shall remain on the site for one year after completion of construction. The project owner shall ensure that the CBO is requested to inspect the installation to ensure compliance with the requirements of applicable LORS.	At least 30 days (or a lesser number of days mutually agreed to by the project owner and the CBO) prior to the start of each increment of construction, the project owner shall ensure that the final design plans, specifications and calculations for equipment and systems of the power plant switchyard, outlet line and termination, including a copy of the signed and stamped statement from the responsible electrical engineer attesting to compliance with the applicable LORS, are submitted to the CBO for review and approval and a copy of the transmittal letter is sent to the CPM in the next Monthly Compliance Report.	At least 30 days (or a lesser number of days mutually agreed to by the project owner and the CBO) prior to the start of each increment of construction	11/01/11				Not Started
TSE-5.1	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: a) Design drawings, specifications and calculations conforming with CPUC General Order 95 or NESC, Title 8, Articles 35, 36 and 37 of the "High Voltage Electric Safety Orders", NEC, applicable interconnection standards and related industry standards, for the poles/towers, foundations, anchor bolts, conductors, grounding systems and major switchyard equipment.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TSE-5.2	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: b) For each element of the transmission facilities identified above, the submittal package to the CBO shall contain the design criteria, a discussion of the calculation method(s), a sample calculation based on "worst case conditions" and a statement signed and sealed by the registered engineer in responsible charge, or other acceptable alternative verification, that the transmission element(s) will conform with CPUC General Order 95 or NESC, Title 8, California Code of Regulations, Articles 35, 36 and 37 of the, "High Voltage Electric Safety Orders", NEC, applicable interconnection standards, and related industry standards.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-5.3	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: c) Electrical one-line diagrams signed and sealed by the registered professional electrical engineer in responsible charge, a route map, and an engineering description of equipment and the configurations covered by requirements TSE-5 a) through f)	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-5.4	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall submit to the CBO for approval: d) A line route drawing after selecting one of the alternate route options for the generator 230 kV interconnection tie line.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-5.5	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: e) The SPS sequencing and timing if applicable shall be provided concurrently to the CPM.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-5.6	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: f) The executed project owner and California ISO Large Generator Interconnection Agreement.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
TSE-5.7	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: g) A letter stating that the mitigation measures or projects selected by the transmission owners for each criteria violation are acceptable.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-5.8	CON	The project owner shall ensure that the design, construction and operation of the proposed transmission facilities will conform to all applicable LORS, including the requirements listed below. The project owner shall ensure that the required number of copies of the design drawings and calculations are submitted to the CBO as determined by the CBO.	The project owner shall ensure that the following are submitted to the CBO for approval: h) The Operational study report based on 2010 system conditions (including operational mitigation measures) from the California SO and/or SCE.	At least 60 days prior to the start of construction of transmission facilities (or a lesser number of days mutually agree to by the project owner and CBO	10/15/11				Not Started
TSE-6	CON	The project owner shall ensure that the CPM and CBO are informed of any impending changes that may not conform to requirements TSE-5 a) through f), and have not received CPM and CBO approval, and request approval to implement such changes. A detailed description of the proposed change and complete engineering, environmental, and economic rationale for the change shall accompany the request. Construction involving changed equipment or substation configurations shall not begin without prior written approval of the changes by the CBO and the CPM.	At least 60 days prior to the construction of transmission facilities, the project owner shall ensure that the CBO and the CPM are informed of any impending changes that may not conform to requirements of TSE-5 and request approval to implement such changes.	At least 60 days prior to the construction of transmission facilities	As Required				As Required
VIS-1.2	CON	The project owner shall treat the surfaces of all project structures and buildings visible to the public so that their colors minimize visual intrusion and contrast by blending with the desert landscape in both color and value; b) their colors and finishes do not create excessive glare; and c) their colors and finishes are consistent with local policies and ordinances.	If the CPM determines that the plan requires revision, the project owner shall provide to the CPM a plan with the specified revision(s) for review and approval by the CPM before any treatment is applied. Any modifications to the treatment plan must be submitted to the CPM for review and approval and simultaneously to Riverside County for review and comment.	Immediately as necessary	As Required				Not Started
VIS-1.3	CON	The project owner shall treat the surfaces of all project structures and buildings visible to the public so that their colors minimize visual intrusion and contrast by blending with the desert landscape in both color and value; b) their colors and finishes do not create excessive glare; and c) their colors and finishes are consistent with local policies and ordinances.	The project owner shall notify the CPM that surface treatment of all listed structures and buildings has been completed and they are ready for inspection and shall submit one set of electronic color photographs from the same key observation points (KOPs) analyzed in this report.	Prior to the start of commercial operation	TBD				Not Started

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
VIS-2.1	CON	To the extent feasible and consistent with safety and security considerations, the project owner shall design and install all permanent exterior lighting so that: a) lamps and reflectors are not visible from beyond the project site, including any off-site construction laydown areas and security buffer areas; b) lighting does not cause excessive reflected glare; c) direct lighting does not illuminate the nighttime sky; d) illumination of the project and its immediate vicinity is minimized; e) lighting on the exhaust stacks shall be the minimum needed to satisfy safety and security concerns; and f) the plan complies with local policies and ordinances of Riverside County.	The project owner shall contact the CPM to discuss the documentation required in the lighting mitigation plan.	At least 90 days prior to ordering any permanent exterior lighting	01/01/12				Not Started
VIS-2.2	CON	The project owner shall not order any exterior lighting until receiving CPM approval of the lighting mitigation plan.	The project owner shall submit to the CPM for review and approval and simultaneously to Riverside County for review and comment a lighting mitigation plan.	At least 60 days prior to ordering any permanent exterior lighting	01/01/12				Not Started
VIS-2.3	CON	The project owner shall not order any exterior lighting until receiving CPM approval of the lighting mitigation plan.	If the CPM determines that the plan requires revision, the project owner shall provide to the CPM a revised plan for review and approval by the CPM.	At least 7 days prior to ordering	01/01/12				Not Started
VIS-2.4	CON	Prior to commercial operation the project owner shall notify the CPM that the lighting has been completed and is ready for inspection.	If after inspection the CPM notifies the project owner that modifications to the lighting are needed the project owner shall implement the modifications and notify the CPM that the modifications have been completed and are ready for inspection.	Within 30 days of receiving that notification	As Required				As Required
VIS-3.1	CON	The project owner shall develop a landscape plan that: a) reduces the visibility of the project from the south and west; b) utilizes drought tolerant landscaping and incorporates adequate drought-conscious irrigation systems; and c) complies with local policies and ordinances of Riverside County, including Policy WCVAP 12.4 which requires screening and/or landscaping of outdoor storage areas, such as contractor storage yards and similar uses. Plantings on the south side of the project are to screen views of the project by residents that live to the south and west of the project	The project owner shall submit to the CPM for review and approval and simultaneously to Riverside County for review and comment, a landscaping plan providing proper implementation that will satisfy these requirements.	At least 90 days prior to installation. Installation must occur the first optimal planting season following site mobilization.	TBD				Not Started
VIS-3.2	CON	The project owner shall develop a landscape plan that: a) reduces the visibility of the project from the south and west; b) utilizes drought tolerant landscaping and incorporates adequate drought-conscious irrigation systems; and c) complies with local policies and ordinances of Riverside County, including Policy WCVAP 12.4 which requires screening and/or landscaping of outdoor storage areas, such as contractor storage yards and similar uses. Plantings on the south side of the project are to screen views of the project by residents that live to the south and west of the project	If the CPM determines that the plan requires revision, the project owner shall provide to the CPM and simultaneously to Riverside County a revised plan for review and approval by the CPM.	Within 30 days of receipt of comments	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
VIS-3.3	CON	The project owner shall develop a landscape plan that: a) reduces the visibility of the project from the south and west; b) utilizes drought tolerant landscaping and incorporates adequate drought-conscious irrigation systems; and c) complies with local policies and ordinances of Riverside County, including Policy WCVAP 12.4 which requires screening and/or landscaping of outdoor storage areas, such as contractor storage yards and similar uses. Plantings on the south side of the project are to screen views of the project by residents that live to the south and west of the project	The planting must occur during the first optimal planting season following site mobilization. The project owner shall simultaneously notify the CPM and Riverside County that the landscaping is ready for inspection.	Within seven days after completing installation of the landscaping	TBD				Not Started
WASTE-2.1	CON	If potentially hazardous material or contaminated soil is identified during project construction or operation at the proposed site or linear facilities as evidenced by discoloration, odor, detection by handheld instruments, or other signs, the Registered PE or Geologist shall inspect the site, determine the need for sampling to confirm the nature and extent of the hazardous material or contamination soil, and file a written report to the project owner, appropriate regulatory agency, and CPM stating the recommended course of action.	The project owner shall submit any final reports filed by the Registered Professional Engineer or Geologist to the CPM	Within 5 days of their receipt	As Required				As Required
WASTE-2.2	CON	The Registered PE or Geologist shall have the authority to temporarily suspend construction activity at that location for the protection of workers or the public. If, in the opinion of the Registered PE or Geologist, significant remediation may be required, the project owner shall contact representatives of the Riverside County Department of Environmental Health for guidance and possible oversight.	The project owner shall notify the CPM within 24 hours of any orders issued to halt construction.	Within 24 hours	As Required				As Required
WASTE-3	CON	If an abandoned well is located during construction or operation, the project owner shall comply with Division of Oil, Gas, and Geothermal Resources (DOGGR) procedures for abandonment of an orphaned oil or gas wells and CCR Title 14, Division 2. The project owner shall also submit to the DOGGR, in writing: (1) a detailed description of the status of the oil/gas well; (2) an explanation of the results of the visual site survey and geophysical survey; and (3) a request, in accordance with DOGGR requirements to certify the well has been properly abandoned.	A copy of the project owner's written submittal to the DOGGR and a copy of the DOGGR response indicating the well has been properly abandoned, shall be forwarded to the CPM	Within 10 days of submittal and receipt of response	As Required				As Required
WASTE-6	CON	The project owner shall ensure that spills or releases of hazardous substances, hazardous materials, or hazardous wastes associated with the construction or operation of the project are reported, delineated, cleaned-up, and remediated as necessary, under the supervision of a California Professional Geologist or Engineer and in accordance with the requirements of the Riverside County Department of Environmental Health. This responsibility excludes construction, operation, and maintenance of the transmission lines, which will be installed, operated, and maintained by Southern California Edison.	The project owner shall document all unauthorized spills or releases of hazardous substances, materials, or wastes that occur on the project property or related pipeline and transmission corridors. Copies of the unauthorized spill documentation shall be provided to the CPM	Within 30 days of the date the release was discovered	As Required				As Required

CEC Cond. #	Sort Code	Description	Verification/Action/Submittal Required by Project Owner	Timeframe	Date Due to CEC CPM	Date Submitted to CEC, CBO or Agency	Requested CEC (or CBO or Agency) Approval Date	CEC/ Agency Approval Date	Status
WASTE-7	CON	Upon becoming aware of any impending waste management-related enforcement action by any local, state, or federal authority, the project owner shall notify the CPM of any such action taken or proposed to be taken against the project itself, or against any waste hauler or disposal facility or treatment operator with which the project owner contracts.	The project owner shall notify the CPM, in writing. The CPM shall notify the project owner of any changes that would be required in the way project-related wastes are managed.	Within 10 days of becoming aware of an impending enforcement action	As Required				As Required
WORKER SAFETY-3.2	CON	The project owner shall provide a site Construction Safety Supervisor (CSS) who is knowledgeable of power plant construction activities and relevant laws, ordinances, regulations, and standards; is capable of identifying workplace hazards relating to construction activities; and has authority to take appropriate action to assure compliance and mitigate hazards.	The CSS shall submit in the Monthly Compliance Report a monthly safety inspection report	Monthly	Monthly				On-going

APPENDIX B
CBO Documentation

Submittals to CBO

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0302-MM-M- Cooling Tower.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/01/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specification	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☒ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15230 Cooling Tower Rev 1.pdf	289497-M-SP-15230 Cooling Tower Rev 1		1	289497-M-SP-15230 Cooling Tower Rev 1	**Revised Conformed**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0304-MM-M-Ammonia.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/01/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specification	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: John Antkowiak

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☒ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15306-Ammonia-R0.pdf	289497-M-SP-15306-Ammonia-R0		0	289497-M-SP-15306-Ammonia-R0	For Bid

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0305-MM-E-Underground Conduit & Raceway .doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**8/31/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Electrical Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bill Carey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-E-401 OVERALL UG RACEWAY PLANS REV 0.pdf	289497-E-401 REV 0	-	0	Overall Underground Raceway Plans	For Construction
289497-E-403 SH 1 GSU#1 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 1 REV 0	1	0	GSU#1 Underground Raceway Plan Sheet 1 of 10	For Construction
289497-E-403 SH 2 GSU#2 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 2 REV 0	2	0	GSU#2 Underground Raceway Plan Sheet 2 of 10	For Construction
289497-E-403 SH 3 GSU#3 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 3 REV 0	3	0	GSU#3 Underground Raceway Plan Sheet 3 of 10	For Construction
289497-E-403 SH 4 GSU#4 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 4 REV 0	4	0	CTG#4 Underground Raceway Plan Sheet 4 of 10	For Construction
289497-E-403 SH 5 GSU#5 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 5 REV 0	5	0	Unit#5 & Station Service XFMR Underground Raceway Plan Sheet 5 of 10	For Construction
289497-E-403 SH 6 GSU#6 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 6 REV 0	6	0	GSU#6 Underground Raceway Plan Sheet 6 of 10	For Construction
289497-E-403 SH 7 GSU#7 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 7 REV 0	7	0	GSU#7 Underground Raceway Plan Sheet 7 of 10	For Construction
289497-E-403 SH 8 GSU#8 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-403 SH 8 REV 0	8	0	GSU#8 Underground Raceway Plan Sheet 8 of 10	For Construction
289497-E-403 403 SH 9 GSU #1-8 UNDERGROUND RACEWAYSCETIONS REV 0.pdf	289497-E-403 SH 9 REV 0	9	0	GSU#1-8 Underground Raceway Sections Sheet 9 of 10	For Construction
289497-E-403 403 SH 10 STATION SERVICE XFMR SECTIONS REV 0.pdf	289497-E-403 SH 10 REV 0	10	0	GSU#8 Station Service XFMR Sections Sheet 10 of 10	For Construction
289497-E-404 404 SH 1 UNIT #1 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 1 REV 0	1	0	Unit#1 Underground Raceway Plan Sheet 1o f 12	For Construction
289497-E-404 404 SH 2 UNIT #2 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 2 REV 0	2	0	Unit#2 Underground Raceway Plan Sheet 2 of 12	For Construction
289497-E-404 404 SH 3 UNIT #3 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 3 REV 0	3	0	Unit#3 Underground Raceway Plan Sheet 3 of 12	For Construction
289497-E-404 404 SH 4 UNIT #4 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 4 REV 0	4	0	Unit#4 Underground Raceway Plan Sheet 4 of 12	For Construction
289497-E-404 404 SH 5 UNIT #5 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 5 REV 0	5	0	Unit#5 Underground Raceway Plan Sheet 5 of 12	For Construction

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

289497-E-404 404 SH 6 UNIT #6 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 6 REV 0	6	0	Unit#6 Underground Raceway Plan Sheet 6 of 12	**For Construction**
289497-E-404 404 SH 7 UNIT #7 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 7 REV 0	7	0	Unit#7 Underground Raceway Plan Sheet 7 of 12	**For Construction**
289497-E-404 404 SH 8 UNIT #8 UNDERGROUND RACEWAY PLAN REV 0.pdf	289497-E-404 SH 8 REV 0	8	0	Unit#8 Underground Raceway Plan Sheet 8 of 12	**For Construction**
289497-E-404 SH 9 UG CONDUIT SECTIONS & DETAILS REV 0.pdf	289497-E-404 SH 9 REV 0	9	0	Underground Conduit Sections and Details Sheet 9 of 12	**For Construction**
289497-E-404 404 SH 10 UNDERGROUND CONDUIT SECTIONS AND DETAILS REV 0.pdf	289497-E-404 SH 10 REV 0	10	0	Underground Conduit Sections and Details Sheet 10 of 12	**For Construction**
289497-E-404 404 SH 11 UNDERGROUND CONDUIT SECTIONS AND DETAILS REV 0.pdf	289497-E-404 SH 11 REV 0	11	0	Underground Conduit Sections and Details Sheet 11 of 12	**For Construction**
289497-E-404 404 SH 12 UNDERGROUND CONDUIT SECTIONS AND DETAILS REV 0.pdf	289497-E-404SH 12 REV 0	12	0	Underground Conduit Sections and Details Sheet 12 of 12	**For Construction**
289497-E-405 SH 1 RAW WATER STORAGE TANK AREA UG RACEWAY PLAN REV 0.pdf	289497-E-405 SH 1 REV 0	1	0	Raw Water Storage Tank Area Underground Raceway Plan Sheet 1 of 7	**For Construction**
289497-E-405 SH 2 DEMIN WATER STORAGE TANK UG RACEWAY PLAN REV 0.pdf	289497-E-405 SH 2 REV 0	2	0	Demin Water Storage Tank Underground Raceway Plan Sheet 2 of 7	**For Construction**
289497-E-405 SH 3 WASTE WATER TREATMENT AREA UG RACEWAY PLAN REV 0.pdf	289497-E-405 SH 3 REV 0	3	0	Waste Water Treatment Area Underground Raceway Plan Sheet 3 of 7	**For Construction**
289497-E-405 SH 4 WAREHOUSE & OPER. BLDG. UG RACEWAY PLAN REV 0.pdf	289497-E-405 SH 4 REV 0	4	0	Warehouse & oper. Building Underground Raceway Plan Sheet 4 of 7	**For Construction**
289497-E-405 SH 5 GAS COMPRESSOR AREA UG RACEWAY PLAN REV 0.pdf	289497-E-405 SH 5 REV 0	5	0	Gas Compressor Area Underground Raceway Plan Sheet 5 of 7	**For Construction**
289497-E-405 SH 6 BOP AREA UG RACEWAY SECTIONS REV 0.pdf	289497-E-405 SH 6 REV 0	6	0	Ammonia Storage Area Underground Raceway Plan Sheet 6 of 7	**For Construction**
289497-E-405 SH 7 BOP AREA UG RACEWAY SECTIONS REV 0.pdf	289497-E-405 SH 7 REV 0	7	0	BOP Area Underground Raceway Sections Sheet 7 of 7	**For Construction**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0306-MM-M-Cooling Tower.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/02/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specification	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: John Antkowiak

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☒ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15230 Cooling Tower Rev 2.pdf	289497-M-SP-15230 Cooling Tower Rev 2		2	289497-M-SP-15230 Cooling Tower Rev 2	Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0308-MM-M-Isometrics.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/02/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Isometrics	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☒ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
0PW-106Y-005-RA.pdf	0PW-106Y-005-RA.pdf		A	0PW-106Y-005-RA.pdf	For Review
0AA-156Z-025_S1-RA.pdf	0AA-156Z-025_S1-RA.pdf		A	0AA-156Z-025_S1-RA.pdf	For Review
0AA-156Z-025_S2-RA.pdf	0AA-156Z-025_S2-RA.pdf		A	0AA-156Z-025_S2-RA.pdf	For Review
0AA-156Z-025_S3-RA.pdf	0AA-156Z-025_S3-RA.pdf		A	0AA-156Z-025_S3-RA.pdf	For Review
0DW-106-016-RA.pdf	0DW-106-016-RA.pdf		A	0DW-106-016-RA.pdf	For Review
0DW-106-017-RA.pdf	0DW-106-017-RA.pdf		A	0DW-106-017-RA.pdf	For Review
0DW-106-050-RA.pdf	0DW-106-050-RA.pdf		A	0DW-106-050-RA.pdf	For Review
0FG-601X-017-RA.pdf	0FG-601X-017-RA.pdf		A	0FG-601X-017-RA.pdf	For Review
0FG-601X-020-RA.pdf	0FG-601X-020-RA.pdf		A	0FG-601X-020-RA.pdf	For Review
0FG-601X-026-RA.pdf	0FG-601X-026-RA.pdf		A	0FG-601X-026-RA.pdf	For Review
0FP-110-001_S1-RA.pdf	0FP-110-001_S1-RA.pdf		A	0FP-110-001_S1-RA.pdf	For Review
0FP-110-001_S2-RA.pdf	0FP-110-001_S2-RA.pdf		A	0FP-110-001_S2-RA.pdf	For Review
0FP-110-001_S3-RA.pdf	0FP-110-001_S3-RA.pdf		A	0FP-110-001_S3-RA.pdf	For Review
0FP-110-002-RA.pdf	0FP-110-002-RA.pdf		A	0FP-110-002-RA.pdf	For Review
0FP-110-003-RA.pdf	0FP-110-003-RA.pdf		A	0FP-110-003-RA.pdf	For Review
0FP-110-004-RA.pdf	0FP-110-004-RA.pdf		A	0FP-110-004-RA.pdf	For Review
0FP-110-007-RA.pdf	0FP-110-007-RA.pdf		A	0FP-110-007-RA.pdf	For Review
0FP-110-008-RA.pdf	0FP-110-008-RA.pdf		A	0FP-110-008-RA.pdf	For Review
0FP-110-009-RA.pdf	0FP-110-009-RA.pdf		A	0FP-110-009-RA.pdf	For Review
0FP-110-010-RA.pdf	0FP-110-010-RA.pdf		A	0FP-110-010-RA.pdf	For Review
0FP-110-011-RA.pdf	0FP-110-011-RA.pdf		A	0FP-110-011-RA.pdf	For Review
0FP-110-012-RA.pdf	0FP-110-012-RA.pdf		A	0FP-110-012-RA.pdf	For Review
0FP-110-013-RA.pdf	0FP-110-013-RA.pdf		A	0FP-110-013-RA.pdf	For Review
0FP-110-014-RA.pdf	0FP-110-014-RA.pdf		A	0FP-110-014-RA.pdf	For Review
0FP-110-015-RA.pdf	0FP-110-015-RA.pdf		A	0FP-110-015-RA.pdf	For Review
0FP-110-016-RA.pdf	0FP-110-016-RA.pdf		A	0FP-110-016-RA.pdf	For Review
0FP-110-017-RA.pdf	0FP-110-017-RA.pdf		A	0FP-110-017-RA.pdf	For Review
0IA-126-001_S1-RA.pdf	0IA-126-001_S1-RA.pdf		A	0IA-126-001_S1-RA.pdf	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

0IA-126-001_S2-RA.pdf	0IA-126-001_S2-RA.pdf		A	0IA-126-001_S2-RA.pdf	For Review
0IA-126-003-RA.pdf	0IA-126-003-RA.pdf		A	0IA-126-003-RA.pdf	For Review
0IA-126-004-RA.pdf	0IA-126-004-RA.pdf		A	0IA-126-004-RA.pdf	For Review
0IA-126-005-RA.pdf	0IA-126-005-RA.pdf		A	0IA-126-005-RA.pdf	For Review
0IA-126-006-RA.pdf	0IA-126-006-RA.pdf		A	0IA-126-006-RA.pdf	For Review
0IA-126-008-RA.pdf	0IA-126-008-RA.pdf		A	0IA-126-008-RA.pdf	For Review
0OW-106-005_S1-RA.pdf	0OW-106-005_S1-RA.pdf		A	0OW-106-005_S1-RA.pdf	For Review
0OW-106-005_S2-RA.pdf	0OW-106-005_S2-RA.pdf		A	0OW-106-005_S2-RA.pdf	For Review
0OW-106-006-RA.pdf	0OW-106-006-RA.pdf		A	0OW-106-006-RA.pdf	For Review
0OW-106-009-RA.pdf	0OW-106-009-RA.pdf		A	0OW-106-009-RA.pdf	For Review
0PW-106Y-001_S1-RA.pdf	0PW-106Y-001_S1-RA.pdf		A	0PW-106Y-001_S1-RA.pdf	For Review
0PW-106Y-001_S2-RA.pdf	0PW-106Y-001_S2-RA.pdf		A	0PW-106Y-001_S2-RA.pdf	For Review
0PW-106Y-003-RA.pdf	0PW-106Y-003-RA.pdf		A	0PW-106Y-003-RA.pdf	For Review
0PW-106Y-006-RA.pdf	0PW-106Y-006-RA.pdf		A	0PW-106Y-006-RA.pdf	For Review
0PW-106Y-009-RA.pdf	0PW-106Y-009-RA.pdf		A	0PW-106Y-009-RA.pdf	For Review
0PW-106Y-017-RA.pdf	0PW-106Y-017-RA.pdf		A	0PW-106Y-017-RA.pdf	For Review
0RW-106-008-RA.pdf	0RW-106-008-RA.pdf		A	0RW-106-008-RA.pdf	For Review
0RW-106-019-RA.pdf	0RW-106-019-RA.pdf		A	0RW-106-019-RA.pdf	For Review
0RW-106-020_S1-RA.pdf	0RW-106-020_S1-RA.pdf		A	0RW-106-020_S1-RA.pdf	For Review
0RW-106-020_S2-RA.pdf	0RW-106-020_S2-RA.pdf		A	0RW-106-020_S2-RA.pdf	For Review
0RW-106-110-RA.pdf	0RW-106-110-RA.pdf		A	0RW-106-110-RA.pdf	For Review
0WW-106-010-RA.pdf	0WW-106-010-RA.pdf		A	0WW-106-010-RA.pdf	For Review
0WW-106-014-RA.pdf	0WW-106-014-RA.pdf		A	0WW-106-014-RA.pdf	For Review
0WW-106-020_S1-RA.pdf	0WW-106-020_S1-RA.pdf		A	0WW-106-020_S1-RA.pdf	For Review
0WW-106-020_S2-RA.pdf	0WW-106-020_S2-RA.pdf		A	0WW-106-020_S2-RA.pdf	For Review
0WW-106-023-RA.pdf	0WW-106-023-RA.pdf		A	0WW-106-023-RA.pdf	For Review
0WW-106-055-RA.pdf	0WW-106-055-RA.pdf		A	0WW-106-055-RA.pdf	For Review
1AA-156Z-001-RA.pdf	1AA-156Z-001-RA.pdf		A	1AA-156Z-001-RA.pdf	For Review
1CW-106-002-RA.pdf	1CW-106-002-		A	1CW-106-002-RA.pdf	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	RA.pdf				
1CW-106-005-RA.pdf	1CW-106-005-RA.pdf		A	1CW-106-005-RA.pdf	For Review
1CW-106-006-RA.pdf	1CW-106-006-RA.pdf		A	1CW-106-006-RA.pdf	For Review
1DW-106-001-RA.pdf	1DW-106-001-RA.pdf		A	1DW-106-001-RA.pdf	For Review
1DW-106-009-RA.pdf	1DW-106-009-RA.pdf		A	1DW-106-009-RA.pdf	For Review
1FG-601X-001-RA.pdf	1FG-601X-001-RA.pdf		A	1FG-601X-001-RA.pdf	For Review
1IA-126-001-RA.pdf	1IA-126-001-RA.pdf		A	1IA-126-001-RA.pdf	For Review
1IA-126-002-RA.pdf	1IA-126-002-RA.pdf		A	1IA-126-002-RA.pdf	For Review
1IA-126-010-RA.pdf	1IA-126-010-RA.pdf		A	1IA-126-010-RA.pdf	For Review
1OW-106-020-RA.pdf	1OW-106-020-RA.pdf		A	1OW-106-020-RA.pdf	For Review
1PW-106Y-001-RA.pdf	1PW-106Y-001-RA.pdf		A	1PW-106Y-001-RA.pdf	For Review
1RW-106-001-RA.pdf	1RW-106-001-RA.pdf		A	1RW-106-001-RA.pdf	For Review
1RW-106-038-RA.pdf	1RW-106-038-RA.pdf		A	1RW-106-038-RA.pdf	For Review
1WW-106-003-RA.pdf	1WW-106-003-RA.pdf		A	1WW-106-003-RA.pdf	For Review
1WW-106-011-RA.pdf	1WW-106-011-RA.pdf		A	1WW-106-011-RA.pdf	For Review
1WW-106-014-RA.pdf	1WW-106-014-RA.pdf		A	1WW-106-014-RA.pdf	For Review
2AA-156Z-001-RA.pdf	2AA-156Z-001-RA.pdf		A	2AA-156Z-001-RA.pdf	For Review
2CW-106-002-RA.pdf	2CW-106-002-RA.pdf		A	2CW-106-002-RA.pdf	For Review
2CW-106-005-RA.pdf	2CW-106-005-RA.pdf		A	2CW-106-005-RA.pdf	For Review
2CW-106-006-RA.pdf	2CW-106-006-RA.pdf		A	2CW-106-006-RA.pdf	For Review
2DW-106-001-RA.pdf	2DW-106-001-RA.pdf		A	2DW-106-001-RA.pdf	For Review
2DW-106-009-RA.pdf	2DW-106-009-RA.pdf		A	2DW-106-009-RA.pdf	For Review
2FG-601X-001-RA.pdf	2FG-601X-001-RA.pdf		A	2FG-601X-001-RA.pdf	For Review
2IA-126-001-RA.pdf	2IA-126-001-RA.pdf		A	2IA-126-001-RA.pdf	For Review
2IA-126-002-RA.pdf	2IA-126-002-RA.pdf		A	2IA-126-002-RA.pdf	For Review
2IA-126-010-RA.pdf	2IA-126-010-RA.pdf		A	2IA-126-010-RA.pdf	For Review
2OW-106-020-RA.pdf	2OW-106-020-RA.pdf		A	2OW-106-020-RA.pdf	For Review
2PW-106Y-001-RA.pdf	2PW-106Y-001-RA.pdf		A	2PW-106Y-001-RA.pdf	For Review
2RW-106-001-RA.pdf	2RW-106-001-RA.pdf		A	2RW-106-001-RA.pdf	For Review
2RW-106-038-RA.pdf	2RW-106-038-		A	2RW-106-038-RA.pdf	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	RA.pdf				
2WW-106-003-RA.pdf	2WW-106-003-RA.pdf		A	2WW-106-003-RA.pdf	For Review
2WW-106-011-RA.pdf	2WW-106-011-RA.pdf		A	2WW-106-011-RA.pdf	For Review
2WW-106-014-RA.pdf	2WW-106-014-RA.pdf		A	2WW-106-014-RA.pdf	For Review
3AA-156Z-001-RA.pdf	3AA-156Z-001-RA.pdf		A	3AA-156Z-001-RA.pdf	For Review
3CW-106-002-RA.pdf	3CW-106-002-RA.pdf		A	3CW-106-002-RA.pdf	For Review
3CW-106-005-RA.pdf	3CW-106-005-RA.pdf		A	3CW-106-005-RA.pdf	For Review
3CW-106-006-RA.pdf	3CW-106-006-RA.pdf		A	3CW-106-006-RA.pdf	For Review
3DW-106-001-RA.pdf	3DW-106-001-RA.pdf		A	3DW-106-001-RA.pdf	For Review
3DW-106-009-RA.pdf	3DW-106-009-RA.pdf		A	3DW-106-009-RA.pdf	For Review
3FG-601X-001-RA.pdf	3FG-601X-001-RA.pdf		A	3FG-601X-001-RA.pdf	For Review
3IA-126-001-RA.pdf	3IA-126-001-RA.pdf		A	3IA-126-001-RA.pdf	For Review
3IA-126-002-RA.pdf	3IA-126-002-RA.pdf		A	3IA-126-002-RA.pdf	For Review
3IA-126-010-RA.pdf	3IA-126-010-RA.pdf		A	3IA-126-010-RA.pdf	For Review
3OW-106-020-RA.pdf	3OW-106-020-RA.pdf		A	3OW-106-020-RA.pdf	For Review
3PW-106Y-001-RA.pdf	3PW-106Y-001-RA.pdf		A	3PW-106Y-001-RA.pdf	For Review
3RW-106-001-RA.pdf	3RW-106-001-RA.pdf		A	3RW-106-001-RA.pdf	For Review
3RW-106-038-RA.pdf	3RW-106-038-RA.pdf		A	3RW-106-038-RA.pdf	For Review
3WW-106-003-RA.pdf	3WW-106-003-RA.pdf		A	3WW-106-003-RA.pdf	For Review
3WW-106-011-RA.pdf	3WW-106-011-RA.pdf		A	3WW-106-011-RA.pdf	For Review
3WW-106-014-RA.pdf	3WW-106-014-RA.pdf		A	3WW-106-014-RA.pdf	For Review
4AA-156Z-001-RA.pdf	4AA-156Z-001-RA.pdf		A	4AA-156Z-001-RA.pdf	For Review
4CW-106-002-RA.pdf	4CW-106-002-RA.pdf		A	4CW-106-002-RA.pdf	For Review
4CW-106-005-RA.pdf	4CW-106-005-RA.pdf		A	4CW-106-005-RA.pdf	For Review
4CW-106-006-RA.pdf	4CW-106-006-RA.pdf		A	4CW-106-006-RA.pdf	For Review
4DW-106-001-RA.pdf	4DW-106-001-RA.pdf		A	4DW-106-001-RA.pdf	For Review
4DW-106-009-RA.pdf	4DW-106-009-RA.pdf		A	4DW-106-009-RA.pdf	For Review
4FG-601X-001-RA.pdf	4FG-601X-001-RA.pdf		A	4FG-601X-001-RA.pdf	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

4IA-126-001-RA.pdf	4IA-126-001-RA.pdf		A	4IA-126-001-RA.pdf	**For Review**
4IA-126-002-RA.pdf	4IA-126-002-RA.pdf		A	4IA-126-002-RA.pdf	**For Review**
4IA-126-010-RA.pdf	4IA-126-010-RA.pdf		A	4IA-126-010-RA.pdf	**For Review**
4OW-106-020-RA.pdf	4OW-106-020-RA.pdf		A	4OW-106-020-RA.pdf	**For Review**
4PW-106Y-001-RA.pdf	4PW-106Y-001-RA.pdf		A	4PW-106Y-001-RA.pdf	**For Review**
4RW-106-001-RA.pdf	4RW-106-001-RA.pdf		A	4RW-106-001-RA.pdf	**For Review**
4RW-106-038-RA.pdf	4RW-106-038-RA.pdf		A	4RW-106-038-RA.pdf	**For Review**
4WW-106-003-RA.pdf	4WW-106-003-RA.pdf		A	4WW-106-003-RA.pdf	**For Review**
4WW-106-011-RA.pdf	4WW-106-011-RA.pdf		A	4WW-106-011-RA.pdf	**For Review**
4WW-106-014-RA.pdf	4WW-106-014-RA.pdf		A	4WW-106-014-RA.pdf	**For Review**
5AA-156Z-001-RA.pdf	5AA-156Z-001-RA.pdf		A	5AA-156Z-001-RA.pdf	**For Review**
5CW-106-002-RA.pdf	5CW-106-002-RA.pdf		A	5CW-106-002-RA.pdf	**For Review**
5CW-106-005-RA.pdf	5CW-106-005-RA.pdf		A	5CW-106-005-RA.pdf	**For Review**
5IA-126-010-RA.pdf	5IA-126-010-RA.pdf		A	5IA-126-010-RA.pdf	**For Review**
5OW-106-020-RA.pdf	5OW-106-020-RA.pdf		A	5OW-106-020-RA.pdf	**For Review**
5PW-106Y-001-RA.pdf	5PW-106Y-001-RA.pdf		A	5PW-106Y-001-RA.pdf	**For Review**
5CW-106-006-RA.pdf	5CW-106-006-RA.pdf		A	5CW-106-006-RA.pdf	**For Review**
5DW-106-001-RA.pdf	5DW-106-001-RA.pdf		A	5DW-106-001-RA.pdf	**For Review**
5DW-106-009-RA.pdf	5DW-106-009-RA.pdf		A	5DW-106-009-RA.pdf	**For Review**
5FG-601X-001-RA.pdf	5FG-601X-001-RA.pdf		A	5FG-601X-001-RA.pdf	**For Review**
5IA-126-001-RA.pdf	5IA-126-001-RA.pdf		A	5IA-126-001-RA.pdf	**For Review**
5IA-126-002-RA.pdf	5IA-126-002-RA.pdf		A	5IA-126-002-RA.pdf	**For Review**
5RW-106-038-RA.pdf	5RW-106-038-RA.pdf		A	5RW-106-038-RA.pdf	**For Review**
5RW-106-001-RA.pdf	5RW-106-001-RA.pdf		A	5RW-106-001-RA.pdf	**For Review**
5WW-106-003-RA.pdf	5WW-106-003-RA.pdf		A	5WW-106-003-RA.pdf	**For Review**
6AA-156Z-001-RA.pdf	6AA-156Z-001-RA.pdf		A	6AA-156Z-001-RA.pdf	**For Review**
5WW-106-011-RA.pdf	5WW-106-011-RA.pdf		A	5WW-106-011-RA.pdf	**For Review**
5WW-106-014-RA.pdf	5WW-106-014-RA.pdf		A	5WW-106-014-RA.pdf	**For Review**
6CW-106-002-RA.pdf	6CW-106-002-RA.pdf		A	6CW-106-002-RA.pdf	**For Review**

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

6CW-106-005-RA.pdf	6CW-106-005-RA.pdf		A	6CW-106-005-RA.pdf	For Review
6CW-106-006-RA.pdf	6CW-106-006-RA.pdf		A	6CW-106-006-RA.pdf	For Review
6DW-106-001-RA.pdf	6DW-106-001-RA.pdf		A	6DW-106-001-RA.pdf	For Review
6DW-106-009-RA.pdf	6DW-106-009-RA.pdf		A	6DW-106-009-RA.pdf	For Review
6FG-601X-001-RA.pdf	6FG-601X-001-RA.pdf		A	6FG-601X-001-RA.pdf	For Review
6IA-126-001-RA.pdf	6IA-126-001-RA.pdf		A	6IA-126-001-RA.pdf	For Review
6IA-126-002-RA.pdf	6IA-126-002-RA.pdf		A	6IA-126-002-RA.pdf	For Review
6IA-126-010-RA.pdf	6IA-126-010-RA.pdf		A	6IA-126-010-RA.pdf	For Review
6OW-106-020-RA.pdf	6OW-106-020-RA.pdf		A	6OW-106-020-RA.pdf	For Review
6PW-106Y-001-RA.pdf	6PW-106Y-001-RA.pdf		A	6PW-106Y-001-RA.pdf	For Review
6RW-106-001-RA.pdf	6RW-106-001-RA.pdf		A	6RW-106-001-RA.pdf	For Review
6RW-106-038-RA.pdf	6RW-106-038-RA.pdf		A	6RW-106-038-RA.pdf	For Review
6WW-106-003-RA.pdf	6WW-106-003-RA.pdf		A	6WW-106-003-RA.pdf	For Review
6WW-106-011-RA.pdf	6WW-106-011-RA.pdf		A	6WW-106-011-RA.pdf	For Review
6WW-106-014-RA.pdf	6WW-106-014-RA.pdf		A	6WW-106-014-RA.pdf	For Review
7AA-156Z-001-RA.pdf	7AA-156Z-001-RA.pdf		A	7AA-156Z-001-RA.pdf	For Review
7CW-106-002-RA.pdf	7CW-106-002-RA.pdf		A	7CW-106-002-RA.pdf	For Review
7CW-106-005-RA.pdf	7CW-106-005-RA.pdf		A	7CW-106-005-RA.pdf	For Review
7CW-106-006-RA.pdf	7CW-106-006-RA.pdf		A	7CW-106-006-RA.pdf	For Review
7DW-106-001-RA.pdf	7DW-106-001-RA.pdf		A	7DW-106-001-RA.pdf	For Review
7DW-106-009-RA.pdf	7DW-106-009-RA.pdf		A	7DW-106-009-RA.pdf	For Review
7FG-601X-001-RA.pdf	7FG-601X-001-RA.pdf		A	7FG-601X-001-RA.pdf	For Review
7IA-126-001-RA.pdf	7IA-126-001-RA.pdf		A	7IA-126-001-RA.pdf	For Review
7IA-126-002-RA.pdf	7IA-126-002-RA.pdf		A	7IA-126-002-RA.pdf	For Review
7OW-106-020-RA.pdf	7OW-106-020-RA.pdf		A	7OW-106-020-RA.pdf	For Review
7IA-126-010-RA.pdf	7IA-126-010-RA.pdf		A	7IA-126-010-RA.pdf	For Review
7PW-106Y-001-RA.pdf	7PW-106Y-001-RA.pdf		A	7PW-106Y-001-RA.pdf	For Review
7RW-106-001-RA.pdf	7RW-106-001-RA.pdf		A	7RW-106-001-RA.pdf	For Review
7RW-106-038-RA.pdf	7RW-106-038-RA.pdf		A	7RW-106-038-RA.pdf	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

7WW-106-003-RA.pdf	7WW-106-003-RA.pdf		A	7WW-106-003-RA.pdf	For Review
7WW-106-011-RA.pdf	7WW-106-011-RA.pdf		A	7WW-106-011-RA.pdf	For Review
7WW-106-014-RA.pdf	7WW-106-014-RA.pdf		A	7WW-106-014-RA.pdf	For Review
8AA-156Z-001-RA.pdf	8AA-156Z-001-RA.pdf		A	8AA-156Z-001-RA.pdf	For Review
8CW-106-002-RA.pdf	8CW-106-002-RA.pdf		A	8CW-106-002-RA.pdf	For Review
8CW-106-005-RA.pdf	8CW-106-005-RA.pdf		A	8CW-106-005-RA.pdf	For Review
8CW-106-006-RA.pdf	8CW-106-006-RA.pdf		A	8CW-106-006-RA.pdf	For Review
8DW-106-001-RA.pdf	8DW-106-001-RA.pdf		A	8DW-106-001-RA.pdf	For Review
8DW-106-009-RA.pdf	8DW-106-009-RA.pdf		A	8DW-106-009-RA.pdf	For Review
8FG-601X-001-RA.pdf	8FG-601X-001-RA.pdf		A	8FG-601X-001-RA.pdf	For Review
8IA-126-001-RA.pdf	8IA-126-001-RA.pdf		A	8IA-126-001-RA.pdf	For Review
8IA-126-002-RA.pdf	8IA-126-002-RA.pdf		A	8IA-126-002-RA.pdf	For Review
8IA-126-010-RA.pdf	8IA-126-010-RA.pdf		A	8IA-126-010-RA.pdf	For Review
8OW-106-020-RA.pdf	8OW-106-020-RA.pdf		A	8OW-106-020-RA.pdf	For Review
8PW-106Y-001-RA.pdf	8PW-106Y-001-RA.pdf		A	8PW-106Y-001-RA.pdf	For Review
8RW-106-001.pdf	8RW-106-001.pdf		A	8RW-106-001.pdf	For Review
8RW-106-001-RA.pdf	8RW-106-001-RA.pdf		A	8RW-106-001-RA.pdf	For Review
8WW-106-003-RA.pdf	8WW-106-003-RA.pdf		A	8WW-106-003-RA.pdf	For Review
8WW-106-011-RA.pdf	8WW-106-011-RA.pdf		A	8WW-106-011-RA.pdf	For Review
8WW-106-014-RA.pdf	8WW-106-014-RA.pdf		A	8WW-106-014-RA.pdf	For Review
8RW-106-038-RA.pdf	8RW-106-038-RA.pdf		A	8RW-106-038-RA.pdf	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0310-MM-M-Piping.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/02/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specifications and Piping Class Sheets	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-SP-15550 Piping Spec Rev C.pdf	289497-SP-15550 Piping Spec Rev C.pdf		C	289497-SP-15550 Piping Spec Rev C.pdf	For Review
289497-List-15560_Rev._8-12-11.pdf	289497-List-15560_Rev._8-12-11.pdf		-	289497-List-15560_Rev._8-12-11.pdf	For Review
289497-SP-15552-Piping Installation- Rev B.pdf	289497-SP-15552-Piping Installation- Rev B.pdf		B	289497-SP-15552-Piping Installation- Rev B.pdf	For Review
Addendum_to_PMC_156Z_Sentinel_Rev_C.pdf	Addendum_to_PMC_156Z_Sentinel_Rev_C.pdf		C	Addendum_to_PMC_156Z_Sentinel_Rev_C.pdf	For Review
289497-M-094-Piping Class Sheet-RC.pdf	289497-M-094-Piping Class Sheet-RC.pdf		C	289497-M-094-Piping Class Sheet-RC.pdf	For Review
289497-M-106-Piping Class Sheet-RC.pdf	289497-M-106-Piping Class Sheet-RC.pdf		C	289497-M-106-Piping Class Sheet-RC.pdf	For Review
289497-M-106Y-Piping Class Sheet-RC.pdf	289497-M-106Y-Piping Class Sheet-RC.pdf		C	289497-M-106Y-Piping Class Sheet-RC.pdf	For Review
289497-M-110-Piping Class Sheet-RC.pdf	289497-M-110-Piping Class Sheet-RC.pdf		C	289497-M-110-Piping Class Sheet-RC.pdf	For Review
289497-M-126-Piping Class Sheet-RD.pdf	289497-M-126-Piping Class Sheet-RD.pdf		D	289497-M-126-Piping Class Sheet-RD.pdf	For Review
289497-M-151-Piping Class Sheet-RD.pdf	289497-M-151-Piping Class Sheet-RD.pdf		D	289497-M-151-Piping Class Sheet-RD.pdf	For Review
289497-M-156Z-Piping Class Sheet-RD.pdf	289497-M-156Z-Piping Class Sheet-RD.pdf		D	289497-M-156Z-Piping Class Sheet-RD.pdf	For Review
289497-M-601X-Piping Class Sheet-RD.pdf	289497-M-601X-Piping Class Sheet-RD.pdf		D	289497-M-601X-Piping Class Sheet-RD.pdf	For Review
289497-M-606-Piping Class Sheet-RD.pdf	289497-M-606-Piping Class Sheet-RD.pdf		D	289497-M-606-Piping Class Sheet-RD.pdf	For Review
289497-M-156-Piping Class Sheet-RD.pdf	289497-M-156-Piping Class Sheet-RD.pdf		D	289497-M-156-Piping Class Sheet-RD.pdf	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0311-MM-M-Ammonia.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/02/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Drawing	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-G-101-GA Plan & Legend-RD.pdf	289497-G-101-GA Plan & Legend-RD		D	289497-G-101-GA Plan & Legend-RD	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0317-MM-CSA-Station Service Transformer Foundation Plan BOTH.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/08/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: CSA Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Mike Laffey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☒ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-C-602 Sataion Service Transformer Foundation Plan BOTH-R1.pdf	289497-C-602 Sataion Service Transformer Foundation Plan BOTH-R1		1	289497-C-602 Sataion Service Transformer Foundation Plan BOTH-R1	Construction Revision

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0319-MM-E-Grounding.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/09/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Electrical Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bill Carey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☒ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-E-200 ELECTRICAL GROUNDING PLAN REV 0.pdf	289497-E-200 ELECTRICAL GROUNDING PLAN REV 0		0	289497-E-200 ELECTRICAL GROUNDING PLAN REV 0	For Construction
289497-E-204 SH 1 CTG #1 GROUNDING PLAN REV 0. PLAN.pdf	289497-E-204 SH 1 CTG #1 GROUNDING PLAN REV 0. PLAN		0	289497-E-204 SH 1 CTG #1 GROUNDING PLAN REV 0. PLAN	For Construction
289497-E-204 SH 10 SECTIONS AND DETAILS REV 0.pdf	289497-E-204 SH 10 SECTIONS AND DETAILS REV 0		0	289497-E-204 SH 10 SECTIONS AND DETAILS REV 0	For Construction
289497-E-204 SH 2 CTG#2 GROUNDING PLAN REV 0. PLAN.pdf	289497-E-204 SH 2 CTG#2 GROUNDING PLAN REV 0. PLAN		0	289497-E-204 SH 2 CTG#2 GROUNDING PLAN REV 0. PLAN	For Construction
289497-E-204 SH 3 CTG#3 GROUNDING PLAN REV 0.pdf	289497-E-204 SH 3 CTG#3 GROUNDING PLAN REV 0		0	289497-E-204 SH 3 CTG#3 GROUNDING PLAN REV 0	For Construction
289497-E-204 SH 4 CTG#4 GROUNDING PLAN REV 0.pdf	289497-E-204 SH 4 CTG#4 GROUNDING PLAN REV 0		0	289497-E-204 SH 4 CTG#4 GROUNDING PLAN REV 0	For Construction
289497-E-204 SH 5 CTG#5 GROUNDING PLAN REV 0.pdf	289497-E-204 SH 5 CTG#5 GROUNDING PLAN REV 0		0	289497-E-204 SH 5 CTG#5 GROUNDING PLAN REV 0	For Construction
289497-E-204 SH 6 CTG#6 GROUNDING PLAN REV 0.pdf	289497-E-204 SH 6 CTG#6 GROUNDING PLAN REV 0		0	289497-E-204 SH 6 CTG#6 GROUNDING PLAN REV 0.pdf	For Construction
289497-E-204 SH 7 CTG#7 GROUDING PLAN REV 0.pdf	289497-E-204 SH 7 CTG#7 GROUDING PLAN REV 0		0	289497-E-204 SH 7 CTG#7 GROUDING PLAN REV 0	For Construction
289497-E-204 SH 8 CTG#8 GROUNDING PLAN REV 0.pdf	289497-E-204 SH 8 CTG#8 GROUNDING PLAN REV 0		0	289497-E-204 SH 8 CTG#8 GROUNDING PLAN REV 0	For Construction
289497-E-204 SH 9 SECTIONS AND DETAILS REV 0.pdf	289497-E-204 SH 9 SECTIONS AND DETAILS REV 0		0	289497-E-204 SH 9 SECTIONS AND DETAILS REV 0	For Construction
289497-E-205 SH 1 RAW WATER STORAGE TANK AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 1 RAW WATER STORAGE TANK AREA GROUNDING PLAN REV 0		0	289497-E-205 SH 1 RAW WATER STORAGE TANK AREA GROUNDING PLAN REV 0	For Construction
289497-E-205 SH 2 DEMINERALIZED WATER STORAGE TANK AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 2 DEMINERALIZED WATER STORAGE TANK AREA		0	289497-E-205 SH 2 DEMINERALIZED WATER STORAGE TANK AREA GROUNDING PLAN REV 0	For Construction

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	GROUNDING PLAN REV 0				
289497-E-205 SH 3 WASTE WATER TREATMET AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 3 WASTE WATER TREATMET AREA GROUNDING PLAN REV 0		0	289497-E-205 SH 3 WASTE WATER TREATMET AREA GROUNDING PLAN REV 0	**For Construction**
289497-E-205 SH 4 WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 4 WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN REV 0		0	289497-E-205 SH 4 WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN REV 0	**For Construction**
289497-E-205 SH 5 GAS COMPRESSOR AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 5 GAS COMPRESSOR AREA GROUNDING PLAN REV 0		0	289497-E-205 SH 5 GAS COMPRESSOR AREA GROUNDING PLAN REV 0	**For Construction**
289497-E-205 SH 6 AMMONIA STORAGE AREA GROUNDING PLAN REV 0.pdf	289497-E-205 SH 6 AMMONIA STORAGE AREA GROUNDING PLAN REV 0		0	289497-E-205 SH 6 AMMONIA STORAGE AREA GROUNDING PLAN REV 0	**For Construction**
289497-E-SP-16060 Underground Electrical Construction Methods Rev 0.pdf	289497-E-SP-16060 Underground Electrical Construction Methods Rev 0		0	289497-E-SP-16060 Underground Electrical Construction Methods Rev 0	**For Construction**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0322-MM-Specification Number Change.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**09/12/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mott MacDonald Specification Name Change	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Val Madden

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☒ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
Specification No. 15560 "Piping Fabrication" is now numbered 15550					
Specification No. 15561 "Piping Installation" is now numbered 15552					
All the documents with the old numbers will be placed in the Superseded folder on the FTP Site.					

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0323-MM-E-Non-Segregated Phase Bus Duct. Generator Leads Open Aluminum Bus.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/13/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Electrical Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bill Carey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☒ Other: For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-E-SP-16347 Non-Segregated Phase Bus Duct Rev 0.pdf	289497-E-SP-16347 Non-Segregated Phase Bus Duct Rev 0		0	Non-Segregated Phase Bus Duct Specification	For Purchase
289497-E-SP-16645 Generator Leads Open Aluminum Bus Rev 0.pdf	289497-E-SP-16645 Generator Leads Open Aluminum Bus Rev 0		0	Generator Leads Open Aluminum Bus Specification	For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0324-MM-E-Non-Segregated Phase Bus Duct.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/14/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Electrical Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bill Carey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☒ Other: For Purchase

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-E-SP-16347 Non-Segregated Phase Bus Duct Rev 1.pdf	289497-E-SP-16347 Non-Segregated Phase Bus Duct Rev 1		1	Non-Segregated Phase Bus Duct Specification	For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0334-MM-CSA-CTG Foundation.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/19/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: CSA Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Mike Laffey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☒ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-C-201 CTG Sections-R1.pdf	289497-C-201 CTG Sections-R1		1	289497-C-201 CTG Sections-R1	For Construction
289497-C-202 CTG Anchorage Plan-R0.pdf	289497-C-202 CTG Anchorage Plan-R0		0	289497-C-202 CTG Anchorage Plan-R0	For Construction
289497-C-500 Raw Water Tank Foundation-R1.pdf	289497-C-500 Raw Water Tank Foundation-R1		1	289497-C-500 Raw Water Tank Foundation-R1	For Construction
289497-C-501 Demin Water Tank Foundation-R2.pdf	289497-C-501 Demin Water Tank Foundation-R2		2	289497-C-501 Demin Water Tank Foundation-R2	For Construction
289497-C-502 Waste Water Tank Foundation-R1.pdf	289497-C-502 Waste Water Tank Foundation-R1		1	289497-C-502 Waste Water Tank Foundation-R1	For Construction
289497-C-200 CTG Foundation Plan-R1.pdf	289497-C-200 CTG Foundation Plan-R1		1	289497-C-200 CTG Foundation Plan-R1	For Construction

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0343-MM-M-Butterfly Valve.Piping Installation and Steel Large Bore Valves

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/22/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specifications	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Val Madden

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15563-Butterfly and Wafer Check Valves-RC.pdf	289497-M-SP-15563-Butterfly and Wafer Check Valves-RC		C	289497-M-SP-15563-Butterfly and Wafer Check Valves-RC	**For Bid**
289497-M-SP-15552-Piping Installation RC.pdf	289497-M-SP-15552-Piping Installation RC		C	289497-M-SP-15552-Piping Installation RC	**For Bid**
289497-M-SP-15556-Cast and Forged Steel Large Bore Valves-RC.pdf	289497-M-SP-15556-Cast and Forged Steel Large Bore Valves-RC		C	289497-M-SP-15556-Cast and Forged Steel Large Bore Valves-RC	**For Bid**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0344-MM-I&C-Valves.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/22/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: I&C Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bob Figuerado

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☒ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-I-SP-I-18780 Back-Pressure Regulating Valve-RB.pdf	289497-I-SP-I-18780 Back-Pressure Regulating Valve-RB		B	289497-I-SP-I-18780 Back-Pressure Regulating Valve-RB	For Bid
289497-I-SP-18707 On-Off Firesafe Ball Valve-RB.pdf	289497-I-SP-18707 On-Off Firesafe Ball Valve-RB		B	289497-I-SP-18707 On-Off Firesafe Ball Valve-RB	For Bid
289497-I-SP-18712 On-Off Butterfly Valve-RA.pdf	289497-I-SP-18712 On-Off Butterfly Valve-RA		A	289497-I-SP-18712 On-Off Butterfly Valve-RA	For Bid
289497-I-SP-18790 Solenoid Valves-RB.pdf	289497-I-SP-18790 Solenoid Valves-RB		B	289497-I-SP-18790 Solenoid Valves-RB	For Bid

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0346-MM-M-Underground Piping.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/22/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Piping Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-P-212-Piping Underground Part Plan AdminWarehouse-R2.pdf	289497-P-212-Piping Underground Part Plan AdminWarehouse-R2		2	289497-P-212-Piping Underground Part Plan AdminWarehouse-R2	**For Review**
289497-P-213-Piping Underground Part Plan Area Zero-R2.pdf	289497-P-213-Piping Underground Part Plan Area Zero-R2		2	289497-P-213-Piping Underground Part Plan Area Zero-R2	**For Review**
289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R2.pdf	289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R2		2	289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R2	**For Review**
289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R2.pdf	289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R2		2	289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R2	**For Review**
289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R1.pdf	289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R1		1	289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R1	**For Review**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0347-MM-I&C-Valves.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/22/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: I&C Documents	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bob Figuerado

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☐ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☒ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-I-SP-I-18780 Back-Pressure Regulating Valve-RC.pdf	289497-I-SP-I-18780 Back-Pressure Regulating Valve-RC		C	289497-I-SP-I-18780 Back-Pressure Regulating Valve-RC	For Bid

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0348-MM-I&C-P&ID's.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/23/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: I&C P&ID's	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bob Figuerado

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-D-001 RD-LEGEND & SYMBOLS SHEET 1.PDF	289497-D-001 RD-LEGEND & SYMBOLS SHEET 1		D	289497-D-001 RD-LEGEND & SYMBOLS SHEET 1	For Review
289497-D-002 RD-LEGEND & SYMBOLS SHEET 2.PDF	289497-D-002 RD-LEGEND & SYMBOLS SHEET 2		D	289497-D-002 RD-LEGEND & SYMBOLS SHEET 2	For Review
289497-D-007 RD-FUEL GAS SYSTEM SHT 1.PDF	289497-D-007 RD-FUEL GAS SYSTEM SHT 1		D	289497-D-007 RD-FUEL GAS SYSTEM SHT 1	For Review
289497-D-008 RD-FUEL GAS SYSTEM SHT 2.PDF	289497-D-008 RD-FUEL GAS SYSTEM SHT 2		D	289497-D-008 RD-FUEL GAS SYSTEM SHT 2	For Review
289497-D-009 RD-FUEL GAS SYSTEM SHT 3.PDF	289497-D-009 RD-FUEL GAS SYSTEM SHT 3		D	289497-D-009 RD-FUEL GAS SYSTEM SHT 3	For Review
289497-D-010 RD-FUEL GAS SYSTEM SHT 4.PDF	289497-D-010 RD-FUEL GAS SYSTEM SHT 4		D	289497-D-010 RD-FUEL GAS SYSTEM SHT 4	For Review
289497-D-011 RD-FUEL GAS SYSTEM SHT 5.PDF	289497-D-011 RD-FUEL GAS SYSTEM SHT 5		D	289497-D-011 RD-FUEL GAS SYSTEM SHT 5	For Review
289497-D-012 RD-FUEL GAS SYSTEM SHT 6.PDF	289497-D-012 RD-FUEL GAS SYSTEM SHT 6		D	289497-D-012 RD-FUEL GAS SYSTEM SHT 6	For Review
289497-D-013 RD-FUEL GAS SYSTEM SHT 7.PDF	289497-D-013 RD-FUEL GAS SYSTEM SHT 7		D	289497-D-013 RD-FUEL GAS SYSTEM SHT 7	For Review
289497-D-014 RE-FUEL GAS FILTERS SHT 8.PDF	289497-D-014 RE-FUEL GAS FILTERS SHT 8		E	289497-D-014 RE-FUEL GAS FILTERS SHT 8	For Review
289497-D-015-RD LMS100 SHT 1.PDF	289497-D-015-RD LMS100 SHT 1		D	289497-D-015-RD LMS100 SHT 1	For Review
289497-D-016-RD LMS100 SHT 2.PDF	289497-D-016-RD LMS100 SHT 2		D	289497-D-016-RD LMS100 SHT 2	For Review
289497-D-017-RD LMS100 SHT 3.PDF	289497-D-017-RD LMS100 SHT 3		D	289497-D-017-RD LMS100 SHT 3	For Review
289497-D-018-RC LMS100 SHT 4.PDF	289497-D-018-RC LMS100 SHT 4		C	289497-D-018-RC LMS100 SHT 4	For Review
289497-D-020 RD-COMPRESSED AIR	289497-D-020 RD-		D	289497-D-020 RD-	

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SYSTEM.PDF	COMPRESSED AIR SYSTEM			COMPRESSED AIR SYSTEM	**For Review**
289497-D-021 RD-AMMONIA SYSTEM.PDF	289497-D-021 RD-AMMONIA SYSTEM		D	289497-D-021 RD-AMMONIA SYSTEM	**For Review**
289497-D-022 RE-WELL&RAW WATER SYSTEM.PDF	289497-D-022 RE-WELL&RAW WATER SYSTEM		E	289497-D-022 RE-WELL&RAW WATER SYSTEM	**For Review**
289497-D-023 RE-DEMINERALIZED WATER SYSTEM.PDF	289497-D-023 RE-DEMINERALIZED WATER SYSTEM		E	289497-D-023 RE-DEMINERALIZED WATER SYSTEM	**For Review**
289497-D-024 RF-WASTE WATER COLLECTION SHT 1.PDF	289497-D-024 RF-WASTE WATER COLLECTION SHT 1		F	289497-D-024 RF-WASTE WATER COLLECTION SHT 1	**For Review**
289497-D-025 RD-FIRE PROTECTION.PDF	289497-D-025 RD-FIRE PROTECTION		D	289497-D-025 RD-FIRE PROTECTION	**For Review**
289497-D-026 RD-POTABLE WATER.PDF	289497-D-026 RD-POTABLE WATER		D	289497-D-026 RD-POTABLE WATER	**For Review**
289497-D-027 RC-WASTE WATER COLLECTION SHT 2.PDF	289497-D-027 RC-WASTE WATER COLLECTION SHT 2		C	289497-D-027 RC-WASTE WATER COLLECTION SHT 2	**For Review**
289497-D-029 RD-ZLD SYSTEM.PDF	289497-D-029 RD-ZLD SYSTEM		D	289497-D-029 RD-ZLD SYSTEM	**For Review**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0351-MM-M-Piping Installation.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/23/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Specification	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-SP-M-15552-Piping Installation-Rev D.pdf	289497-SP-M-15552-Piping Installation-Rev D		D	289497-SP-M-15552-Piping Installation- Rev D	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0356-MM-M-Underground Piping.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/23/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Piping Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-P-201-Piping Underground Part Plan Area CTG Unit#1_Rev_1.pdf	289497-P-201-Piping Underground Part Plan Area CTG Unit#1_Rev_1		1	289497-P-201-Piping Underground Part Plan Area CTG Unit#1_Rev_1	For Review
289497-P-202-Piping Underground Part Plan Area CTG Unit#2_Rev_1.pdf	289497-P-202-Piping Underground Part Plan Area CTG Unit#2_Rev_1		1	289497-P-202-Piping Underground Part Plan Area CTG Unit#2_Rev_1	For Review
289497-P-203-Piping Underground Part PlanArea CTG Unit#3_Rev_1.pdf	289497-P-203-Piping Underground Part PlanArea CTG Unit#3_Rev_1		1	289497-P-203-Piping Underground Part PlanArea CTG Unit#3_Rev_1	For Review
289497-P-204-Piping Underground Part Plan Area CTG Unit#4_Rev_1.pdf	289497-P-204-Piping Underground Part Plan Area CTG Unit#4_Rev_1		1	289497-P-204-Piping Underground Part Plan Area CTG Unit#4_Rev_1	For Review
289497-P-205-Piping Underground Part Plan Area CTG Unit#5_Rev_1.pdf	289497-P-205-Piping Underground Part Plan Area CTG Unit#5_Rev_1		1	289497-P-205-Piping Underground Part Plan Area CTG Unit#5_Rev_1	For Review
289497-P-206-Piping Underground Part Plan Area CTG Unit#6_Rev_1.pdf	289497-P-206-Piping Underground Part Plan Area CTG Unit#6_Rev_1		1	289497-P-206-Piping Underground Part Plan Area CTG Unit#6_Rev_1	For Review
289497-P-207-Piping Underground Part Plan Area CTG Unit#7_Rev_1.pdf	289497-P-207-Piping Underground Part Plan Area CTG Unit#7_Rev_1		1	289497-P-207-Piping Underground Part Plan Area CTG Unit#7_Rev_1	For Review
289497-P-208-Piping Underground Part Plan Area CTG Unit#8_Rev_1.pdf	289497-P-208-Piping Underground Part Plan Area CTG Unit#8_Rev_1		1	289497-P-208-Piping Underground Part Plan Area CTG Unit#8_Rev_1	For Review
289497-P-209-Piping Underground Part Plan Area Ammonia Tank_Rev_1.pdf	289497-P-209-Piping Underground Part Plan Area Ammonia Tank_Rev_1		1	289497-P-209-Piping Underground Part Plan Area Ammonia Tank_Rev_1	For Review
289497-P-210-Piping Underground Part Plan Area Fuel Gas Compressors-Rev2.pdf	289497-P-210-Piping Underground Part Plan Area Fuel Gas Compressors-Rev2		2	289497-P-210-Piping Underground Part Plan Area Fuel Gas Compressors-Rev2	For Review
289497-P-212-Piping Underground Part Plan Area Admin Warehouse-Rev3.pdf	289497-P-212-Piping Underground Part Plan Area Admin		3	289497-P-212-Piping Underground Part Plan Area Admin Warehouse-Rev3	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	Warehouse-Rev3				
289497-P-213-Piping Underground Part Plan Area Zero-R3.pdf	289497-P-213-Piping Underground Part Plan Area Zero-R3		3	289497-P-213-Piping Underground Part Plan Area Zero-R3	**For Review**
289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R3.pdf	289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R3		3	289497-P-215-Piping Underground Part Plan Area Demineralized Water Tanks-R3	**For Review**
289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R3.pdf	289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R3		3	289497-P-216-Piping Underground Part Plan Area Demineralized Trailers Raw Water Storage-R3	**For Review**
289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R2.pdf	289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R2		2	289497-P-218-Piping Underground Part Plan Area Gas Metering Septic-R2	**For Review**
289497-P-219-Piping Underground Part Plan Area Potable Water Pump-Rev0.pdf	289497-P-219-Piping Underground Part Plan Area Potable Water Pump-Rev0		0	289497-P-219-Piping Underground Part Plan Area Potable Water Pump-Rev0	**For Review**
289497-P-220-Piping Underground Part Plan Area Potable Water Pump-Rev0.pdf	289497-P-220-Piping Underground Part Plan Area Potable Water Pump-Rev0		0	289497-P-220-Piping Underground Part Plan Area Potable Water Pump-Rev0	**For Review**
289497-P-221-Piping Underground Part Plan Area Potable Water Pump-Rev0.pdf	289497-P-221-Piping Underground Part Plan Area Potable Water Pump-Rev0		0	289497-P-221-Piping Underground Part Plan Area Potable Water Pump-Rev0	**For Review**
289497-P-222-Piping Underground Fire Protection Part Plan Area CTG Units 1 2 & 3-Rev0.pdf	289497-P-222-Piping Underground Fire Protection Part Plan Area CTG Units 1 2 & 3-Rev0		0	289497-P-222-Piping Underground Fire Protection Part Plan Area CTG Units 1 2 & 3-Rev0	**For Review**
289497-P-223-Piping Underground Fire Protection Part Plan Area CTG Units 4 5 & 6-Rev0.pdf	289497-P-223-Piping Underground Fire Protection Part Plan Area CTG Units 4 5 & 6-Rev0		0	289497-P-223-Piping Underground Fire Protection Part Plan Area CTG Units 4 5 & 6-Rev0	**For Review**
289497-P-224-Piping Underground Fire Protection Part Plan Area CTG Units 7 & 8-Rev0.pdf	289497-P-224-Piping Underground Fire Protection Part Plan Area CTG Units 7 & 8-Rev0		0	289497-P-224-Piping Underground Fire Protection Part Plan Area CTG Units 7 & 8-Rev0	**For Review**
289497-P-226-Piping Underground Part Plan Area Gas Metering Septic-R0.pdf	289497-P-226-Piping Underground Part Plan Area Gas Metering Septic-R0		0	289497-P-226-Piping Underground Part Plan Area Gas Metering Septic-R0	**For Review**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0359-MM-M-Centrifugal Pump Systems.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/23/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Piping Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: John Antkowiak

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15307 Centrifugal Pump Systems Rev 0.pdf	289497-M-SP-15307 Centrifugal Pump Systems Rev 0	-	0	Centrifugal Pump Systems Specification	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0360-MM-M-Centrifugal Pump Systems.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/23/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Piping Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☐ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Val Madden

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Bid Revised

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-M-SP-15100-Onsite Wastewater Treatment System Rev C.pdf	289497-M-SP-15100-Onsite Wastewater Treatment System Rev C		C	289497-M-SP-15100-Onsite Wastewater Treatment System Rev C	**Bid Issue**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

SENTINEL-0366-MM-M-GA.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/281/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Mechanical Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Revised Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-G-152-RC Eqp Loc PP Area CTG Unit 1.pdf	289497-G-152-RC Eqp Loc PP Area CTG Unit 1		C	289497-G-152-RC Eqp Loc PP Area CTG Unit 1	For Review
289497-G-153-RB Eqp Loc PP Area CTG Unit 2.pdf	289497-G-153-RB Eqp Loc PP Area CTG Unit 2		B	289497-G-153-RB Eqp Loc PP Area CTG Unit 2	For Review
289497-G-154-RB Eqp Loc PP Area CTG Unit 3.pdf	289497-G-154-RB Eqp Loc PP Area CTG Unit 3		B	289497-G-154-RB Eqp Loc PP Area CTG Unit 3	For Review
289497-G-155-RB Eqp Loc PP Area CTG Unit 4.pdf	289497-G-155-RB Eqp Loc PP Area CTG Unit 4		B	289497-G-155-RB Eqp Loc PP Area CTG Unit 4	For Review
289497-G-156-RB Eqp Loc PP Area CTG Unit 5.pdf	289497-G-156-RB Eqp Loc PP Area CTG Unit 5		B	289497-G-156-RB Eqp Loc PP Area CTG Unit 5	For Review
289497-G-157-RB Eqp Loc PP Area CTG Unit 6.pdf	289497-G-157-RB Eqp Loc PP Area CTG Unit 6		B	289497-G-157-RB Eqp Loc PP Area CTG Unit 6	For Review
289497-G-158-RB Eqp Loc PP Area CTG Unit 7.pdf	289497-G-158-RB Eqp Loc PP Area CTG Unit 7		B	289497-G-158-RB Eqp Loc PP Area CTG Unit 7	For Review
289497-G-159-RB Eqp Loc PP Area CTG Unit 8.pdf	289497-G-159-RB Eqp Loc PP Area CTG Unit 8		B	289497-G-159-RB Eqp Loc PP Area CTG Unit 8	For Review

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0367-MM-E-Underground Drawings.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/28/2011**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: Electrical Drawings	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Bill Carey

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: For Purchase

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-E-100 Electrical Symbols and Legend REV 1.pdf	289497-E-100 Electrical Symbols and Legend REV 1		1	289497-E-100 Electrical Symbols and Legend REV 1	For Review
289497-E-200 ELECTRICAL GROUNDING PLAN REV 1.pdf	289497-E-200 ELECTRICAL GROUNDING PLAN REV 1		1	289497-E-200 ELECTRICAL GROUNDING PLAN REV 1	For Review
289497-E-201 Overall Grounding Plan REV 0.pdf	289497-E-201 Overall Grounding Plan REV 0		0	289497-E-201 Overall Grounding Plan REV 0	For Review
289497-E-202 CTG #1 Grounding Plan REV 0.pdf	289497-E-202 CTG #1 Grounding Plan REV 0		0	289497-E-202 CTG #1 Grounding Plan REV 0	For Review
289497-E-203-GSU #1 Grounding Plan SHEET 1 REV 0.pdf	289497-E-203-GSU #1 Grounding Plan SHEET 1 REV 0		0	289497-E-203-GSU #1 Grounding Plan SHEET 1 REV 0	For Review
289497-E-203-GSU #2 Grounding Plan SHEET 2 REV 0.pdf	289497-E-203-GSU #2 Grounding Plan SHEET 2 REV 0		0	289497-E-203-GSU #2 Grounding Plan SHEET 2 REV 0	For Review
289497-E-203-GSU #3 Grounding Plan SHEET 3 REV 0.pdf	289497-E-203-GSU #3 Grounding Plan SHEET 3 REV 0		0	289497-E-203-GSU #3 Grounding Plan SHEET 3 REV 0	For Review
289497-E-203-GSU #4 Grounding Plan SHEET 4 REV 0.pdf	289497-E-203-GSU #4 Grounding Plan SHEET 4 REV 0		0	289497-E-203-GSU #4 Grounding Plan SHEET 4 REV 0	For Review
289497-E-203-GSU #5 Grounding Plan SHEET 5 REV 0.pdf	289497-E-203-GSU #5 Grounding Plan SHEET 5 REV 0		0	289497-E-203-GSU #5 Grounding Plan SHEET 5 REV 0	For Review
289497-E-203-GSU #6 Grounding Plan SHEET 6 REV 0.pdf	289497-E-203-GSU #6 Grounding Plan SHEET 6 REV 0		0	289497-E-203-GSU #6 Grounding Plan SHEET 6 REV 0	For Review
289497-E-203-GSU #7 Grounding Plan SHEET 7 REV 0.pdf	289497-E-203-GSU #7 Grounding Plan SHEET 7 REV 0		0	289497-E-203-GSU #7 Grounding Plan SHEET 7 REV 0	For Review
289497-E-203 SHEET 8 GSU #8 Grounding Plan REV 0.pdf	289497-E-203 SHEET 8 GSU #8 Grounding Plan REV 0		0	289497-E-203 SHEET 8 GSU #8 Grounding Plan REV 0	For Review
289497-E-203 SHEET 9 GSU #9 Grounding Plan REV 0.pdf	289497-E-203 SHEET 9 GSU #9 Grounding Plan REV 0		0	289497-E-203 SHEET 9 GSU #9 Grounding Plan REV 0	For Review
289497-E-203-GSU #10 Grounding Plan SHEET 10 REV 0.pdf	289497-E-203-GSU #10 Grounding Plan SHEET 10 REV 0		0	289497-E-203-GSU #10 Grounding Plan SHEET 10 REV 0	For Review
289497-E-204-CTG #1 GROUNDING PLAN SHEET 1 REV 1.pdf	289497-E-204-CTG #1 GROUNDING PLAN		1	289497-E-204-CTG #1 GROUNDING PLAN SHEET 1	For Review

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	SHEET 1 REV 1			REV 1	
289497-E-204-CTG#2 GROUNDING PLAN SHEET 2 REV 1.pdf	289497-E-204-CTG#2 GROUNDING PLAN SHEET 2 REV 1		1	289497-E-204-CTG#2 GROUNDING PLAN SHEET 2 REV 1	**For Review**
289497-E-204-CTG#3 GROUNDING PLAN SHEET 3 REV 1.pdf	289497-E-204-CTG#3 GROUNDING PLAN SHEET 3 REV 1		1	289497-E-204-CTG#3 GROUNDING PLAN SHEET 3 REV 1	**For Review**
289497-E-204-SH 4 CTG#4 GROUNDING PLAN SHEET 4 REV 1.pdf	289497-E-204-SH 4 CTG#4 GROUNDING PLAN SHEET 4 REV 1		1	289497-E-204-SH 4 CTG#4 GROUNDING PLAN SHEET 4 REV 1	**For Review**
289497-E-204-CTG#5 GROUNDING PLAN SHEET 5 REV 1.pdf	289497-E-204-CTG#5 GROUNDING PLAN SHEET 5 REV 1		1	289497-E-204-CTG#5 GROUNDING PLAN SHEET 5 REV 1	**For Review**
289497-E-204-CTG#6 GROUNDING PLAN SHEET 6 REV 1.pdf	289497-E-204-CTG#6 GROUNDING PLAN SHEET 6 REV 1		1	289497-E-204-CTG#6 GROUNDING PLAN SHEET 6 REV 1	**For Review**
289497-E-204 SHEET 7 CTG#7 GROUDING PLAN REV 1.pdf	289497-E-204 SHEET 7 CTG#7 GROUDING PLAN REV 1		1	289497-E-204 SHEET 7 CTG#7 GROUDING PLAN REV 1	**For Review**
289497-E-204-CTG#8 GROUNDING PLAN SHEET 8 REV 1.pdf	289497-E-204-CTG#8 GROUNDING PLAN SHEET 8 REV 1		1	289497-E-204-CTG#8 GROUNDING PLAN SHEET 8 REV 1	**For Review**
289497-E-204-SECTIONS AND DETAILS SHEET 9 REV 1.pdf	289497-E-204-SECTIONS AND DETAILS SHEET 9 REV		1	289497-E-204-SECTIONS AND DETAILS SHEET 9 REV 1	**For Review**
289497-E-204-SECTIONS AND DETAILS SHEET 10 REV 1.pdf	289497-E-204-SECTIONS AND DETAILS SHEET 10 REV 1		1	289497-E-204-SECTIONS AND DETAILS SHEET 10 REV 1	**For Review**
289497-E-205-RAW WATER STORAGE TANK AREA GROUNDING PLAN SHEET 1 REV 1.pdf	289497-E-205-RAW WATER STORAGE TANK AREA GROUNDING PLAN SHEET 1 REV 1		1	289497-E-205-RAW WATER STORAGE TANK AREA GROUNDING PLAN SHEET 1 REV 1	**For Review**
289497-E-205-DEMINERALIZED WATER STORAGE TANK AREA GROUNDING PLAN SHEET 2 REV 1.pdf	289497-E-205-DEMINERALIZED WATER STORAGE TANK AREA GROUNDING PLAN SHEET 2 REV 1		1	289497-E-205-DEMINERALIZED WATER STORAGE TANK AREA GROUNDING PLAN SHEET 2 REV 1	**For Review**
289497-E-205-WASTE WATER TREATMET AREA GROUNDING PLAN SHEET 3 REV 1.pdf	289497-E-205-WASTE WATER TREATMET AREA GROUNDING PLAN SHEET 3 REV 1		1	289497-E-205-WASTE WATER TREATMET AREA GROUNDING PLAN SHEET 3 REV 1	**For Review**
289497-E-205-WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN SHEET 4 REV 1.pdf	289497-E-205-WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN SHEET 4 REV 1		1	289497-E-205-WAREHOUSE & OPERATIONS BLDG. AREA GROUNDING PLAN SHEET 4 REV 1	**For Review**
289497-E-205-GAS COMPRESSOR AREA GROUNDING PLAN SHEET 5 REV 0.pdf	289497-E-205-GAS COMPRESSOR AREA GROUNDING PLAN		0	289497-E-205-GAS COMPRESSOR AREA GROUNDING PLAN SHEET 5	**For Review**

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	SHEET 5 REV 0			REV 0	
289497-E-205-AMMONIA STORAGE AREA GROUNDING PLAN SHEET 6 REV 1.pdf	289497-E-205-AMMONIA STORAGE AREA GROUNDING PLAN SHEET 6 REV 1		1	289497-E-205-AMMONIA STORAGE AREA GROUNDING PLAN SHEET 6 REV 1	**For Review**
289497-E-403-GSU#1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1.pdf	289497-E-403-GSU#1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1		1	289497-E-403-GSU#1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1	**For Review**
289497-E-403-GSU#2 UNDERGROUND RACEWAY PLAN SHEET 2 REV 1.pdf	289497-E-403-GSU#2 UNDERGROUND RACEWAY PLAN SHEET 2 REV 1		1	289497-E-403-GSU#2 UNDERGROUND RACEWAY PLAN SHEET 2 REV 1	**For Review**
289497-E-403-GSU#3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1.pdf	289497-E-403-GSU#3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1		1	289497-E-403-GSU#3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1	**For Review**
289497-E-403-GSU#4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1.pdf	289497-E-403-GSU#4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1		1	289497-E-403-GSU#4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1	**For Review**
289497-E-403-GSU#5 & STATION SERVICE XFMR UG RACEWAY PLAN SHEET 5 REV 1.pdf	289497-E-403-GSU#5 & STATION SERVICE XFMR UG RACEWAY PLAN SHEET 5 REV 1		1	289497-E-403-GSU#5 & STATION SERVICE XFMR UG RACEWAY PLAN SHEET 5 REV 1	**For Review**
289497-E-403-GSU#6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1.pdf	289497-E-403-GSU#6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1		1	289497-E-403-GSU#6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1	**For Review**
289497-E-403-GSU#7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1.pdf	289497-E-403-GSU#7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1		1	289497-E-403-GSU#7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1	**For Review**
289497-E-403-GSU#8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1.pdf	289497-E-403-GSU#8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1		1	289497-E-403-GSU#8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1	**For Review**
289497-E-403-GSU#9 UNDERGROUND RACEWAY PLAN SHEET 9 REV 1.pdf	289497-E-403-GSU#9 UNDERGROUND RACEWAY PLAN SHEET 9 REV 1		1	289497-E-403-GSU#9 UNDERGROUND RACEWAY PLAN SHEET 9 REV 1	**For Review**
289497-E-403-GSU#10 UNDERGROUND RACEWAY PLAN SHEET 10 REV 1.pdf	289497-E-403-GSU#10 UNDERGROUND RACEWAY PLAN SHEET 10 REV 1		1	289497-E-403-GSU#10 UNDERGROUND RACEWAY PLAN SHEET 10 REV 1	**For Review**
289497-E-404- UNIT #1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1.pdf	289497-E-404- UNIT #1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1		1	289497-E-404- UNIT #1 UNDERGROUND RACEWAY PLAN SHEET 1 REV 1	**For Review**
289497-E-404-UNIT #2 UNDERGROUND RACEWAY PLAN SHEET 2 REV 1.pdf	289497-E-404-UNIT #2 UNDERGROUND RACEWAY PLAN		1	289497-E-404-UNIT #2 UNDERGROUND RACEWAY PLAN SHEET 2 REV 1	**For Review**

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	SHEET 2 REV 1				
289497-E-404-UNIT #3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1.pdf	289497-E-404-UNIT #3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1		1	289497-E-404-UNIT #3 UNDERGROUND RACEWAY PLAN SHEET 3 REV 1	**For Review**
289497-E-404-UNIT #4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1.pdf	289497-E-404-UNIT #4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1		1	289497-E-404-UNIT #4 UNDERGROUND RACEWAY PLAN SHEET 4 REV 1	**For Review**
289497-E-404- UNIT #5 UNDERGROUND RACEWAY PLAN SHEET 5 REV 1.pdf	289497-E-404- UNIT #5 UNDERGROUND RACEWAY PLAN SHEET 5 REV 1		1	289497-E-404- UNIT #5 UNDERGROUND RACEWAY PLAN SHEET 5 REV 1	**For Review**
289497-E-404-UNIT #6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1.pdf	289497-E-404-UNIT #6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1		1	289497-E-404-UNIT #6 UNDERGROUND RACEWAY PLAN SHEET 6 REV 1	**For Review**
289497-E-404-UNIT #7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1.pdf	289497-E-404-UNIT #7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1		1	289497-E-404-UNIT #7 UNDERGROUND RACEWAY PLAN SHEET 7 REV 1	**For Review**
289497-E-404-UNIT #8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1.pdf	289497-E-404-UNIT #8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1		1	289497-E-404-UNIT #8 UNDERGROUND RACEWAY PLAN SHEET 8 REV 1	**For Review**
289497-E-404-UG CONDUIT SECTIONS & DETAILS SHEET 9 REV 1.pdf	289497-E-404-UG CONDUIT SECTIONS & DETAILS SHEET 9 REV 1		1	289497-E-404-UG CONDUIT SECTIONS & DETAILS SHEET 9 REV 1	**For Review**
289497-E-404-UNIT #10 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 10 REV 1.pdf	289497-E-404-UNIT #10 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 10 REV 1		1	289497-E-404-UNIT #10 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 10 REV 1	**For Review**
289497-E-404-UNIT #11 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 11 REV 1.pdf	289497-E-404-UNIT #11 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 11 REV 1		1	289497-E-404-UNIT #11 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 11 REV 1	**For Review**
289497-E-404-UNIT #12 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 12 REV 1.pdf	289497-E-404-UNIT #12 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 12 REV 1		1	289497-E-404-UNIT #12 UNDERGROUND CONDUIT SECTIONS AND DETAILS SHEET 12 REV 1	**For Review**
289497-E-405 RAW WATER STORAGE TANK AREA UG RACEWAY PLAN REV 1 SH 1 (1).pdf	289497-E-405 RAW WATER STORAGE TANK AREA UG RACEWAY PLAN REV 1 SH 1 (1)		1	289497-E-405 RAW WATER STORAGE TANK AREA UG RACEWAY PLAN REV 1 SH 1 (1)	**For Review**
289497-E-405-DEMIN WATER STORAGE TANK UG RACEWAY PLAN SHEET 2 REV 1.pdf	289497-E-405-DEMIN WATER STORAGE TANK UG RACEWAY		1	289497-E-405-DEMIN WATER STORAGE TANK UG RACEWAY PLAN SHEET 2	**For Review**

Mott MacDonald
400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

	PLAN SHEET 2 REV 1			REV 1	
289497-E-405-WASTE WATER TREATMENT AREA UG RACEWAY PLAN SHEET 3 REV 1.pdf	289497-E-405-WASTE WATER TREATMENT AREA UG RACEWAY PLAN SHEET 3 REV 1		1	289497-E-405-WASTE WATER TREATMENT AREA UG RACEWAY PLAN SHEET 3 REV 1	**For Review**
289497-E-405-WAREHOUSE & OPER. BLDG. UG RACEWAY PLAN SHEET 4 REV 1.pdf	289497-E-405-WAREHOUSE & OPER. BLDG. UG RACEWAY PLAN SHEET 4 REV 1		1	289497-E-405-WAREHOUSE & OPER. BLDG. UG RACEWAY PLAN SHEET 4 REV 1	**For Review**
289497-E-405 GAS COMPRESSOR AREA UG RACEWAY PLAN REV 1 SH 5.pdf	289497-E-405 GAS COMPRESSOR AREA UG RACEWAY PLAN REV 1 SH 5		1	289497-E-405 GAS COMPRESSOR AREA UG RACEWAY PLAN REV 1 SH	**For Review**
289497-E-405 AMMONIA STORAGE AREA UG RACEWAY PLAN REV 1 SH 6.pdf	289497-E-405 AMMONIA STORAGE AREA UG RACEWAY PLAN REV 1 SH 6		1	289497-E-405 AMMONIA STORAGE AREA UG RACEWAY PLAN REV 1 SH 6	**For Review**
289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 7 (1).pdf	289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 7 (1)		1	289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 7 (1)	**For Review**
289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 8.pdf	289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 8		1	289497-E-405 BOP AREA UG RACEWAY SECTIONS REV 1 SH 8	**For Review**
289497-DC-404_Sentinel Plant Grounding Study_Rev A.pdf	289497-DC-404_Sentinel Plant Grounding Study_Rev A		A	289497-DC-404_Sentinel Plant Grounding Study_Rev A.	**For Review**
289497-DC-402_Sentinel Switchyard Grounding Study_Rev A.pdf	289497-DC-402_Sentinel Switchyard Grounding Study_Rev A		A	289497-DC-402_Sentinel Switchyard Grounding Study_Rev A	**For Review**

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Sentinel-0375-MM-M-Underground Piping.doc

ATTENTION:	DATE:	ACTION DATE:
See Distribution List	**9/30/11**	**N/A**
SHIP TO: **Gemma Power Systems** **2461 Main Street** **Glastonbury, CT 06033**	PROJECT: CPV Sentinel Project DESCRIPTION: I&C P&ID's	

SHIPPING METHOD: ☐ **NEXT BUSINESS MORNING** ♦ ☐ **NEXT BUSINESS DAY** ♦ ☐ **2ND DAY** ♦ ☐ **GROUND** ♦ ☐ **USPS EXPRESS** ♦ ☐ **USPS** ♦ ☒ **FTP TRANSFER** ♦ ☒ **EMAIL** ♦ ☐ **OTHER:**

Issuing Engineer: Jim Walsh

Project Engineering Manager: Val Madden

Quantity of Sets Sent to Primary Destination: **Issued electronically**

SEE ATTACHED LIST OF TRANSMITTED DRAWINGS AND DOCUMENTS

Please mark VOID or destroy all previous versions of the documents issued as Mott MacDonald Deliverables unless the documents are a partial substitution into a larger package as defined in Special Notes or Actions. Mott MacDonald's deliverables which have an APPROVED status are considered released for all of the above stated purposes.

FOR MM ENGINEER USE ONLY – TYPE AND PURPOSE OF TRANSMITTAL	
VENDOR DRAWING REVIEW:	**MOTT MACDONALD DELIVERABLES SUBMITTAL:**
☐ Mott MacDonald comments on vendor documents issued for Client Review	☐ Issued for Information Only
☐ Copy of vendor documents sent by Mott MacDonald directly to the vendor.	☒ Issued for Review and Comments
☐ Return of created documents submitted for Mott MacDonald review	☐ Issued for Approval
☐ Other:	☐ Issued for Constructability Review
	☐ Issued for Bidding Purpose
	☐ Issued for Ordering Material
	☐ Issued for Construction
	☐ Issued for Permitting
	☐ Issued for Fabrication
	☐ Issued for Record Purposes
	☐ Other: Conformed

Mott MacDonald

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

Issued Document Transmittal List

STATUS LEGEND			
RN	Reviewed As Noted-Extra Data Required	PR	Preliminary
RA	Reviewed and Accepted	SP	Superseded
CF	Certified – Final	VV	Void
IO	Information Only – No Approval Required		
NA	Not Approved – Not Released for Fabrication		

Electronic File Name	Document Number	Sht	Rev	Title	Status
289497-P-210_R3_PIPING UG GAS COMP.pdf	289497-P-210_R3_PIPING UG GAS COMP	-	3	289497-P-210_R3_PIPING UG GAS COMP	For Review
289497-P-212 _R4_PIPING UG ADMIN-WAREHOUSE.pdf	289497-P-212 _R4_PIPING UG ADMIN-WAREHOUSE	-	4	289497-P-212 _R4_PIPING UG ADMIN-WAREHOUSE	For Review
289497-P-213_R4_PIPING UG ZLD.pdf	289497-P-213_R4_PIPING UG ZLD	-	4	289497-P-213_R4_PIPING UG ZLD	For Review
289497-P-216_R4_PIPING UG DEMIN TRAILERS-RW TANK.pdf	289497-P-216_R4_PIPING UG DEMIN TRAILERS-RW TANK	-	4	289497-P-216_R4_PIPING UG DEMIN TRAILERS-RW TANK	For Review
289497-P-225_R0_PIP1NG UG RW WELL.pdf	289497-P-225_R0_PIP1NG UG RW WELL	-	0	289497-P-225_R0_PIP1NG UG RW WELL	For Review
289497-P-201_R2_PIPING UG CTG1.pdf	289497-P-201_R2_PIPING UG CTG1	-	2	289497-P-201_R2_PIPING UG CTG1	For Review
289497-P-202_R2_PIPING UG CTG2.pdf	289497-P-202_R2_PIPING UG CTG2	-	2	289497-P-202_R2_PIPING UG CTG2	For Review
289497-P-203_R2_PIPING UG CTG3.pdf	289497-P-203_R2_PIPING UG CTG3	-	2	289497-P-203_R2_PIPING UG CTG3	For Review
289497-P-204_R2_PIPING UG CTG4.pdf	289497-P-204_R2_PIPING UG CTG4	-	2	289497-P-204_R2_PIPING UG CTG4	For Review
289497-P-205_R2_PIPING UG CTG5.pdf	289497-P-205_R2_PIPING UG CTG5	-	2	289497-P-205_R2_PIPING UG CTG5	For Review
289497-P-206_R2_PIPING UG CTG6.pdf	289497-P-206_R2_PIPING UG CTG6	-	2	289497-P-206_R2_PIPING UG CTG6	For Review
289497-P-207_R2_PIPING UG CTG7.pdf	289497-P-207_R2_PIPING UG CTG7	-	2	289497-P-207_R2_PIPING UG CTG7	For Review
289497-P-208_R2_PIPING UG	289497-P-	-	2	289497-P-208_R2_PIPING	For Review

400 Blue Hill Drive, Suite 100 ♦ Westwood, MA 02090
(Tel) 781-915-0015 ♦ (Fax) 781-915-0001

CTG8.pdf	208_R2_PIPING UG CTG8			UG CTG8	

CBO Approvals

Johnson, Amanda

From: shamica.zenn@us.bureauveritas.com
Sent: Monday, September 19, 2011 7:47 AM
To: karent@gemmapower.com; charlescollins@gemmapower.com; paulwest@gemmapower.com; thomasmastronarde@gemmapower.com; glennlacey@gemmapower.com; curtbrainard@gemmapower.com; trishkohler@gemmapower.com; norbertmichnowski@gemmapower.com; ericwhitehouse@gemmapower.com; carlflodquist@gemmapower.com; jean.dillon@mottmacinc.com; john.davenport@mottmacinc.com; larry.sullivan@mottmacinc.com; val.madden@mottmacinc.com; charlie.davis@mottmacinc.com; eric.pretorius@mottmacinc.com; michael.laffey@mottmacinc.com; robert.figuerado@mottmacinc.com; jim.walsh@mottmacinc.com; Nizom.ghantous@mottmacinc.com; mmcdaniels@cpv.com; jmurphy@cpv.com; mturner@cpv.com; jmcclelland@cpv.com; john.kiefer@ge.com; john.nutter@ge.com; joelkasper@aquagenicsinc.com; Fitzgerald, Maggie; Rushmore, Kathy; johnseidler@spectrumenergy.com; Johnson, Amanda; sharikiefer@spectrumenergy.com; William.carey@mottmacinc.com; Scott.kibby@hatchmott.com; Christopher.kirby@mottmacinc.com; Ethanmccrea@gemmapower.com; robertnosal@hatchmott.com; David.porter@mottmacinc.com; melissaslusz@gemmapower.com; brettgish@gemmapower.com; emily.smith@mottmacinc.com
Cc: jamie.saldana@us.bureauveritas.com; christy.pinney@us.bureauveritas.com; michele.clark@us.bureauveritas.com; keith.long@us.bureauveritas.com; raynard.hughes@us.bureauveritas.com
Subject: CPV Sentinel – FAB-1-2.0-Submittal of BMT-NW-PC1 - Approved

Hello,

The CPV Sentinel submittal FAB-1-2.0-Submittal of BMT-NW-PC1, has been reviewed and approved. You will find the documents on BVnet under the respective title. Feel free to contact me with any questions or concerns.

Thank you,

Shamica Zenn
Project Coordinator
Bureau Veritas North America, Inc.
180 Promenade Circle, Suite 150
Sacramento, CA 95834
Phone: 916.617.2028
Fax: 916.617.2068
shamica.zenn@us.bureauveritas.com
www.us.bureauveritas.com
ISO 9001:2008 Certified

NOTICE:
This message contains information which is confidential and the copyright of our company or a third party. If you are not the intended recipient of this message, please delete it and destroy all copies. If you are the intended recipient of this message, you should not disclose or distribute this message to third parties without the consent of our company. Our company does not represent, warrant and/or guarantee that the integrity of this message has been maintained, nor that the communication is free of virus, interception, or interference. The liability of our company is limited by our General Conditions of Services.

Please consider the environment before printing this e-mail

Johnson, Amanda

From: shamica.zenn@us.bureauveritas.com
Sent: Tuesday, September 27, 2011 2:07 PM
To: karent@gemmapower.com; charlescollins@gemmapower.com; paulwest@gemmapower.com; thomasmastronarde@gemmapower.com; glennlacey@gemmapower.com; curtbrainard@gemmapower.com; trishkohler@gemmapower.com; norbertmichnowski@gemmapower.com; ericwhitehouse@gemmapower.com; carlflodquist@gemmapower.com; jean.dillon@mottmacinc.com; john.davenport@mottmacinc.com; larry.sullivan@mottmacinc.com; val.madden@mottmacinc.com; charlie.davis@mottmacinc.com; eric.pretorius@mottmacinc.com; michael.laffey@mottmacinc.com; robert.figuerado@mottmacinc.com; jim.walsh@mottmacinc.com; Nizom.ghantous@mottmacinc.com; mmcdaniels@cpv.com; jmurphy@cpv.com; mturner@cpv.com; jmcclelland@cpv.com; john.kiefer@ge.com; john.nutter@ge.com; joelkasper@aquagenicsinc.com; Fitzgerald, Maggie; Rushmore, Kathy; johnseidler@spectrumenergy.com; Johnson, Amanda; sharikiefer@spectrumenergy.com; William.carey@mottmacinc.com; Scott.kibby@hatchmott.com; Christopher.kirby@mottmacinc.com; Ethanmccrea@gemmapower.com; robertnosal@hatchmott.com; David.porter@mottmacinc.com; melissaslusz@gemmapower.com; brettgish@gemmapower.com; emily.smith@mottmacinc.com
Cc: jamie.saldana@us.bureauveritas.com; christy.pinney@us.bureauveritas.com; barbara.tomajic@us.bureauveritas.com; gloria.cochran@us.bureauveritas.com; keith.long@us.bureauveritas.com; raynard.hughes@us.bureauveritas.com
Subject: CPV Sentinel – STRUC-1-10.0 CTG Foundation-PC2 – Conditionally Approved

Hello,

The CPV Sentinel submittal STRUC-1-10.0 CTG Foundation-PC2, has been reviewed and conditionally approved. You will find the documents on BVnet under the respective title. Feel free to contact me with any questions or concerns.

Thank you,

Shamica Zenn
Project Coordinator
Bureau Veritas North America, Inc.
180 Promenade Circle, Suite 150
Sacramento, CA 95834
Phone: 916.617.2028
Fax: 916.617.2068
shamica.zenn@us.bureauveritas.com
www.us.bureauveritas.com
ISO 9001:2008 Certified

NOTICE:
This message contains information which is confidential and the copyright of our company or a third party. If you are not the intended recipient of this message, please delete it and destroy all copies. If you are the intended recipient of this message, you should not disclose or distribute this message to third parties without the consent of our company. Our company does not represent, warrant and/or guarantee that the integrity of this message has been maintained, nor that the communication is free of virus, interception, or interference. The liability of our company is limited by our General Conditions of Services.

Please consider the environment before printing this e-mail

Johnson, Amanda

From: shamica.zenn@us.bureauveritas.com
Sent: Thursday, September 29, 2011 10:31 AM
To: karent@gemmapower.com; charlescollins@gemmapower.com; paulwest@gemmapower.com; thomasmastronarde@gemmapower.com; glennlacey@gemmapower.com; curtbrainard@gemmapower.com; trishkohler@gemmapower.com; norbertmichnowski@gemmapower.com; ericwhitehouse@gemmapower.com; carlflodquist@gemmapower.com; jean.dillon@mottmacinc.com; john.davenport@mottmacinc.com; larry.sullivan@mottmacinc.com; val.madden@mottmacinc.com; charlie.davis@mottmacinc.com; eric.pretorius@mottmacinc.com; michael.laffey@mottmacinc.com; robert.figuerado@mottmacinc.com; jim.walsh@mottmacinc.com; Nizom.ghantous@mottmacinc.com; mmcdaniels@cpv.com; jmurphy@cpv.com; mturner@cpv.com; jmcclelland@cpv.com; john.kiefer@ge.com; john.nutter@ge.com; joelkasper@aquagenicsinc.com; Fitzgerald, Maggie; Rushmore, Kathy; johnseidler@spectrumenergy.com; Johnson, Amanda; sharikiefer@spectrumenergy.com; William.carey@mottmacinc.com; Scott.kibby@hatchmott.com; Christopher.kirby@mottmacinc.com; Ethanmccrea@gemmapower.com; robertnosal@hatchmott.com; David.porter@mottmacinc.com; melissaslusz@gemmapower.com; brettgish@gemmapower.com; emily.smith@mottmacinc.com
Cc: jamie.saldana@us.bureauveritas.com; christy.pinney@us.bureauveritas.com; barbara.tomajic@us.bureauveritas.com; gloria.cochran@us.bureauveritas.com; keith.long@us.bureauveritas.com; raynard.hughes@us.bureauveritas.com; dan.enright@us.bureauveritas.com
Subject: CPV Sentinel – GEN-5-4.1-Delegate Civil Engineers-PC1 - Approved

Hello,

The CPV Sentinel submittal GEN-5-4.1-Delegate Civil Engineers-PC1, has been reviewed and approved. You will find the documents on BVnet under the respective title. Feel free to contact me with any questions or concerns.

Thank you,

Shamica Zenn
Project Coordinator
Bureau Veritas North America, Inc.
180 Promenade Circle, Suite 150
Sacramento, CA 95834
Phone: 916.617.2028
Fax: 916.617.2068
shamica.zenn@us.bureauveritas.com
www.us.bureauveritas.com
ISO 9001:2008 Certified

NOTICE:
This message contains information which is confidential and the copyright of our company or a third party. If you are not the intended recipient of this message, please delete it and destroy all copies. If you are the intended recipient of this message, you should not disclose or distribute this message to third parties without the consent of our company. Our company does not represent, warrant and/or guarantee that the integrity of this message has been maintained, nor that the communication is free of virus, interception, or interference. The liability of our company is limited by our General Conditions of Services.

Please consider the environment before printing this e-mail

CBO Submittal and Drawing List

Submittal and Drawing List

Rev. 7

October 6, 2011

CPV Sentinel Energy Project

Gemma Power Systems, LLC
2461 Main Street
Glastonbury, CT 06033

Mott MacDonald, 400 Blue Hill Drive, Suite 100, North Lobby, Westwood, MA 02090, United States
T +1 (781) 915-0015 F +1 (781) 915-0001 W www.mottmac.com

CIVIL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
CIVIL-1.4	CIVIL-1.4	Report	URS	Approval	Geotech Report	3/21/2011
GEO-1	GEO-1.0	Report	URS	Approval	Geotech Report	4/26/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Existing Site Plan, Sheet 1	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Existing Site Plan, Sheet 2	5/12/2011
CIVIL-1	CIVIL-1-2.1	Drawing	Mott MacDonald	Approval	Soil and Erosion Control Plan, Sheet 1	5/12/2011
CIVIL-1	CIVIL-1-2.1	Drawing	Mott MacDonald	Approval	Soil and Erosion Control Plan, Sheet 2	5/12/2011
CIVIL-1	CIVIL-1-2.1	Drawing	Mott MacDonald	Approval	Soil and Erosion, Phase I - Preliminary Construction	5/12/2011
CIVIL-1	CIVIL-1-2.1	Drawing	Mott MacDonald	Approval	Soil and Erosion, Phase Plan	5/12/2011
CIVIL-1	CIVIL-1-2.1	Drawing	Mott MacDonald	Approval	Soil and Erosion, Road Plan	5/12/2011
CIVIL-1	CIVIL-1-XX	Drawing	Mott MacDonald	Approval	Soil and Erosion Control, Typical Details	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Mass Earthwork Plan	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Grading Plan	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Fire Pump Foundaton Grading	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Grading and Drainage Plan, Sheet 1	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Grading and Drainage Plan, Sheet 2	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Grading and Drainage Plan, Sheet 3	5/12/2011
CIVIL-1	CIVIL-1-1.2	Drawing	Mott MacDonald	Approval	Grading Plan - Construction Parking and Laydown	5/12/2011
CIVIL-1	CIVIL-1-XX	Drawing	Mott MacDonald	Approval	Site Roads	10/1/2011
CIVIL-1	CIVIL-1-XX	Drawing	Mott MacDonald	Approval	Pavement Details	10/15/2011
CIVIL-1	CIVIL-1-XX	Drawing	Mott MacDonald	Approval	Fence Details	10/15/2011
TRANS-2	TRANS-2.1	Drawings	Mott MacDonald	Approval	Site Trailer and Parking Plan and Details	4/8/2011
TRANS-2	TRANS-2.1	Drawings	Mott MacDonald	Approval	Off Site Construction Parking and Laydown Plan	4/8/2011
CIVIL-1	CIVIL-1	Drawings	Big Horn Consulting	Approval	Melissa Lane Drawings	4/12/2011
CIVIL-1	CIVIL-1-2.1	Report	Mott MacDonald	Approval	SWPPP Plan	5/13/2011
CIVIL-1	CIVIL-1	Specification	Mott MacDonald	Approval	Clearing and Grubbing	6/15/2011
CIVIL-1	CIVIL-1	Specification	Mott MacDonald	Approval	Erosion / Sediment Control	6/15/2011
CIVIL-1	CIVIL-1	Specification	Mott MacDonald	Approval	Excavation & Back Fill	5/2/2011
CIVIL-1	CIVIL-1	Specification	Mott MacDonald	Approval	Chain Link Fencing	9/15/2011
CIVIL-1	CIVIL-1-XX	Specification	Mott MacDonald	Approval	Asphalt Paving	9/15/2011
CIVIL-1	CIVIL-1-XX	Specification	Mott MacDonald	Approval	Septic System Performance Specification	11/1/2011
CIVIL-1	CIVIL-1-XX	Specification	Mott MacDonald	Approval	Field Painting	1/1/2012
CIVIL-1	CIVIL-1-3.0	Report	Mott MacDonald	Approval	Hydrology Report	5/5/2011
GEN-1	GEN-1-1.0	Drawings	Mott MacDonald	Approval	Power Duct Profile-Road	5/13/2011

STRUCTURAL DESIGN SUBMITTALS

CEC Cond	Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
STRUC-1	STRUC-1-1.0 PC1	Calculation	Mott MacDonald	Approval	Lateral Force Procedure	4/1/2011
STRUC-1	STRUC-1-1.0 PC2	Calculation	Mott MacDonald	Approval	Lateral Force Procedure	4/29/2011
STRUC-1	STRUC-1-2.0	Technical Specifications	Mott MacDonald	Approval	Cast-in-Place Concrete	4/29/2011
STRUC-1	STRUC-1-2.0	Drawing	Mott MacDonald	Approval	Concrete General Notes	4/29/2011
STRUC-1	STRUC-1-2.0 PC1	Drawing, Calculations	Mott MacDonald	Approval	Fire Pump Enclosure Foundation	4/1/2011
STRUC-1	STRUC-1-2.0 PC2	Drawing, Calculations	Mott MacDonald	Approval	Fire Pump Enclosure Foundation	4/29/2011
STRUC-1	STRUC-1	Drawing	Mott MacDonald	Reference	Foundation Location Plan	6/15/2011
STRUC-1	STRUC-1-10	Drawing, Calculations	Mott MacDonald	Approval	Combustion Turbine Generator/Air Inlet Fndns	7/29/2011
STRUC-1	STRUC-1-15	Drawing, Calculations	Vendor	Approval	GE CTG & Air Inlet Structures	7/29/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	CTG Auxiliaries and PCM Foundations	8/26/2011
STRUC-1	STRUC-1-9	Drawing, Calculations	Mott MacDonald	Approval	SCR/Exhaust Stack Foundation	7/29/2011
STRUC-1	STRUC-1-3	Drawing, Calculations	Vendor	Approval	SCR/Exhaust Stack Structure	7/29/2011
STRUC-1	STRUC-1-14	Drawing, Calculations	Mott MacDonald	Approval	Cooling Tower Foundation	8/16/2011
STRUC-1	STRUC-1-11	Drawing, Calculations	Mott MacDonald	Approval	Raw Water/Fire Water Tank Foundation	8/5/2011
STRUC-1	STRUC-1-4	Vendor Drawings, Calculations	Vendor	Approval	Raw Water/Fire Water Tank Structure	8/3/2011
STRUC-1	STRUC-1-12	Drawing, Calculations	Mott MacDonald	Approval	Demin Water Tank Foundations	8/5/2011
STRUC-1	STRUC-1-6,7	Vendor Drawings, Calculations	Vendor	Approval	Demin Water Tank Structure	8/3/2011
STRUC-1	STRUC-1-13	Drawing, Calculations	Mott MacDonald	Approval	Wastewater Tank Foundation	8/5/2011
STRUC-1	STRUC-1-5	Vendor Drawings, Calculations	Vendor	Approval	Wastewater Tank Structure	8/3/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Vendor	Approval	Water Treatment Trailers [bracing/anchorage]	8/3/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Gas Compressor Foundations	10/28/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Vendor	Approval	Gas Compressor	11/1/2011
STRUC-1	STRUC-1-8.0	Drawing, Calculations	Mott MacDonald	Approval	GSU Transformer Foundations	7/28/2011
STRUC-1	STRUC-1-16	Drawing, Calculations	Mott MacDonald	Approval	Station Service Transformer Foundations	9/9/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Miscellaneous Pump Foundations,	12/1/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	ZLD System Foundation	10/21/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Miscellaneous Sump Foundations	1/1/2012
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Admin/Warehouse Building Foundations	12/15/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Unit Control/Electric Room Foundations	10/21/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	CEMS Enclosure Foundations	12/1/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Switchyard Building Foundations	12/1/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Ammonia Unloading and Storage Tank Foundations	12/15/2011
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Miscellaneous Equipment and Sump Foundations	1/1/2012
STRUC-1	STRUC-1-XX	Drawing, Calculations	Mott MacDonald	Approval	Septic Tank Foundation	3/1/2012
STRUC-1	STRUC-1-XX	Drawing, Calculations	Vendor	Approval	Septic Tank Structure	3/1/2012
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Structural Steel	1/1/2012
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Steel General Notes	1/1/2012
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Stair Plan Sections and Details	1/1/2012
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Ladder Details	1/1/2012
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Misc Framing details	1/1/2012
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Pre-Engineered Control/Warehouse Building	11/1/2011
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Pre-Engineered Prefabricated 230 kV Substation Control Building	11/15/2011
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Architectural General Notes	12/1/2011
STRUC-1	STRUC-1-XX	Drawing	Mott MacDonald	Approval	Admin/Warehouse Plans, Sections and Details	11/1/2011
STRUC-1	STRUC-1-XX	Vendor Drawings, Calculations	Vendor	Approval	Admin/Warehouse Plans, Sections and Details	11/1/2011
STRUC-1	STRUC-1-XX	Drawing	Vendor	Approval	Switchgear Building, Plans, Sections and Details	12/15/2011
STRUC-1	STRUC-1-XX	Vendor Drawings, Calculations	Vendor	Approval	Switchgear Building, Plans, Sections and Details	12/1/2011
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Structural Data for Mechanical and Electrical Equipment	9/9/2011
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Septic System Performance Specification	11/1/2011
STRUC-1	STRUC-1-XX	Technical Specifications	Mott MacDonald	Approval	Field Painting	1/1/2012

MECHANICAL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Approval	General Arrangement Plan & Legend	07/10/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	General Arrangement - Overall CTG Unit Typical	07/10/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Equipment Location Plan	07/15/11
MECH-1	MECH-1-XX	Drawings	Mott MacDonald	Reference	Equipment Location Part Plan- Area CTG 01 -08	07/15/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Equipment Location Plan Ammonia Tank Area	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Fuel Gas Compressors 1	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Fuel Gas Compressors 2	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Admin/Warehouse	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Zero Discharge System	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Waste Water Storage Tank	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Demineralized Water Tanks	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Demineralizer Trailers	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Raw Water Storage	10/21/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Eq. Loc. Part Plan - Area Fuel Gas Metering Station	12/01/11
MECH-1	MECH-1-1.0	Drawings	Mott MacDonald	Approval	Underground Piping Plans -	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Approval	Composite Piping Plans	02/01/12
MECH-1	MECH-1	Technical Specification	Mott MacDonald	Approval	CTG Exhaust System SCR	08/26/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Zero Discharge System	08/26/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Fire Pump (Packaged Unit) & Building	08/19/11
MECH-1	MECH-1	Technical Specification	Mott MacDonald	Approval	Field Erected Tanks – , Raw Water, Demin Water,etc	08/12/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Fuel Gas Compressors	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	CTG Unit Cooling Tower	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Well Water Pumps	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Ammonia Storage Tank	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Gas Turbine Water Wash Drains Tank	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Piping Spec (includes all pipe classes)	08/12/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Piping Line List	08/12/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Buried Polyethylene Plastic Piping (Fire Protection)	09/09/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Secondary Containment Piping (PermaPipe)	08/12/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Fuel Gas Filter/Separator	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Air Comp. Skid, Receiver, & Dryer	09/09/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Cooling tower chem feed systems	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Reference	Equipment list	11/15/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Cast and Forged Steel Valves	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Small Bore Valves	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Large Butterfly and Wafer Check Valves	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Cast Iron & Ductile Valves (for underground)	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Insulation	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Wastewater Sump Pumps	10/21/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Demin Water Pumps	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Ammonia unloading and forwarding pumps	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Misc Centrifugal Pumps	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Service Water Pumps	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Oil / Water Separator	10/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Fuel Gas drains tank	10/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Miscellaneous Piping Specialties	11/01/11
MECH-1	MECH-1-XX	Technical Specification	Mott MacDonald	Approval	Pipe Hangers	02/01/12
MECH-1	MECH-1-XX	Drawings, Calculation, Specification	Mott MacDonald/Vendor	Approval	Fuel Gas System -Pressure Drop/Line Sizing Calculations; P&ID; Orthographics, Isometrics, Pipe Support Drawings, Pipe Support Calculations, Supporting Vendor Documents	11/01/11
MECH-1	MECH-1-XX	Drawings, Calculation, Specification	Vendor	Approval	Sanitary Drains- Pressure Drop/Line Sizing Calculations; P&ID; Orthographics, Isometrics, Pipe Support Drawings, Pipe Support Calculations, Supporting Vendor Documents.	01/01/12
MECH-1	MECH-1-XX	Drawings, Calculation, Specification	Mott MacDonald/Vendor	Approval	Wastewater -Pressure Drop/Line Sizing Calculations; P&ID; Orthographics, Isometrics, Pipe Support Drawings, Pipe Support Calculations, Supporting Vendor Documents.	01/01/12
MECH-1	MECH-1-XX	Drawings, Calculation, Specification	Mott MacDonald/Vendor	Approval	Fire Protection System -Pressure Drop/Line Sizing Calculations; P&ID; Orthographics, Zone Drawings, Isometrics, Pipe Support Drawings, Underground Composites, Supporting Vendor Docuements.	01/01/12
MECH-1	MECH-1-XX	Drawings, Calculation, Specification	Mott MacDonald/Vendor	Approval	Other Systems to be reviewed per CBO direction.	TBD

MECHANICAL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
MECH-1	MECH-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	CT Equipment	01/01/12
MECH-1	MECH-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Fuel Gas Compressors	03/01/12
MECH-1	MECH-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Compressed Air Receiver	03/01/12
MECH-1	MECH-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Field Erected Tanks	01/01/12
MECH-1	MECH-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Pre-Engineered Buildings	11/01/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	P&ID LMS100 Sheets 1, 2, 3	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	P&ID Compressed Air system	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	P&ID Ammonia System	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	P&ID Well & Raw Water System	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	P&ID Service and Potable Water Systems	08/12/11
MECH-1	MECH-1-XX	Drawing	Mott MacDonald	Reference	Water Balance Diagram	10/21/11
MECH-2	MECH-2-XX	Certifications, Reports	Vendor	Approval	Aqueous Ammonia Tank	01/15/12
MECH-2	MECH-2-XX	Certifications, Reports	Vendor	Approval	Shop Fabricated tanks	11/15/11
MECH-2	MECH-2-XX	Certifications, Reports	Vendor	Approval	Compressed Air Receiver	11/15/11
MECH-3	MECH-3-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Pre-Engineered Buildings - HVAC	12/15/11

ELECTRICAL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Reference	Electrical Symbols And Legend	6/15/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Overall Plant Power One Line Diagram	9/16/2011
ELEC-1	ELEC-1-XX	Drawings	Vendor - GE	Approval	One Line Generator Protection And Metering	11/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 4160 V Swgr	10/21/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 4160 V MCC	10/21/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V Load Center Unit 1 (sheet 1)	1/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V Load Center Unit 2-8	10/21/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V BOP swgr	1/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V MCC Unit 1 (sheet 1)	3/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V MCC Unit 2-8	3/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V Distribution Board schedules	3/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V MCC Bop	1/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	One Line Diagram 480 V MCC water treatment	1/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Dc One Line Diagram	11/15/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Vital Ac One Line Diagram	12/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Refernce	Power Panel schedules	4/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Grounding Details	1/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Grounding Plans Sh 1-13	1/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Area Classification Plan Sh 1-4	2/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Reference	General Site Plan - Sh1-4	2/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Reference	Power Block Part Plan Sh1-8	2/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Generator Leads Open Aluminum Bus	11/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	CEMs Electrical Plan	11/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Non-Seg Bus Duct	10/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	General Site Lighting Plan & Details	4/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	General Site Lighting Plan Sh 1-5	4/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Lighting - Ctg Areas Task Lighting - Sh 1- 8	5/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Lighting Misc Areas - Sh 1-12	5/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Underground Raceway Plans Sh 1-12	9/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Power Block Underground Raceway Plan Sh1 -8	10/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Underground Raceway Details Sh 1-16	10/1/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Above Ground Power Block Raceway Plans	3/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Above Ground Raceway Plan Area 2	3/15/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Above Ground BOP Raceway Plan Areas	4/1/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Schematic / Wiring Diagrams 480V Mcc Starter Typ1, 2, 3 4	2/17/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Schematic / Wiring Diagrams 480V Swgr Breaker Typical	2/17/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Schematic / Wiring Diagrams 4160 Starter Typical	2/17/2012
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Schematic / Wiring Diagrams 4160 Breaker Typical	11/18/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Wiring Diagrams CTG1/ Interfaces Typical	11/18/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Wiring Diagrams CTG 1-8/ Interfaces Table	12/15/2011
ELEC-1	ELEC-1-XX	Drawings	Mott MacDonald	Approval	Connection Diagrams Sh 1-32	12/15/2011
ELEC-1	ELEC-1-XX	List	Mott MacDonald	Reference	Cable / Conduit Schedule	5/1/2012
ELEC-1	ELEC-1-XX	List	Mott MacDonald	Reference	Electrical Equipment List	12/15/2011
ELEC-1	ELEC-1-XX	List	Mott MacDonald	Reference	Motor & Load Schedule	12/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Main Generator Stepup Transformer Spec	9/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Station Service transformers 220kv-4.16 kv	9/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	4160 V Swgr Spec	10/21/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	4160 V Mcc Spec	10/21/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Auxiliary Transformers BOP & U AUX 4 KV-480 V	10/1/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	480 V Substation/SWGR BOP & U AUX	12/1/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	480V Mcc Spec	12/1/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Generator Leads Open Aluminum Bus	12/1/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	4 KV Non-Seg Bus	10/21/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Dc Battery & Charger Spec	12/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	120 Vac Ups Spec	12/1/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	4 Kv Motor Spec	6/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Low Voltage Motors (600 V And Below)	6/15/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Cathodic Protection (Performance Spec.)	10/21/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Small Distribution Transformers	2/1/2012
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Elec. Req. For Packaged Mec. Systems	10/21/2011
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Lightning Protection Systems (Performance Spec)	5/1/2012
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Manholes & Ductbank	2/1/2012
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Grounding & Bonding	2/1/2012
ELEC-1	ELEC-1-XX	Technical Specification	Mott MacDonald	Approval	Electrical Construction Methods	2/1/2012
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Generator Step-up Transformer	11/1/2011

ELECTRICAL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Station Service transformers 220kv-4.16 kv	12/15/2011
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	4160 V Switchgear	12/15/2011
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	480 V Motor Control Center	12/15/2011
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	Generator Leads Open Aluminum Bus	11/15/2011
ELEC-1	ELEC-1-XX	Vendor Drawings, Vendor Code Certs, Specifications, Vendor Calculations	Vendor	Approval	4 KV Non-Seg Bus	11/15/2011
ELEC-1	ELEC-1-XX	Drawings, Calculation, Specification	Vendor	Approval	GE Electrical Equipment	10/28/2011
ELEC-1	ELEC-1-XX	Drawings, Calculation, Specification	Mott MacDonald/Vendor	Approval	Other Systems to be reviewed per CBO direction.	TBD
220KV SWITCHYARD						
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	DC One Line Diagram	10/15/2011
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Revenue Metering Diagram	12/1/2011
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Ac Station Service One Line Diagram	12/15/2011
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Layout	1/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Sections	1/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Control Building Plans & Details	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Transmission Line Interface	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Relaying and Metering Control Panels	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Revenue Metering Panel	3/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Above Ground Raceway Plan	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	SWYD Underground Raceway Plan- Plant	4/11/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	SWYD Underground Raceway Plan- UTL	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	SWYD Underground Raceway Details-Plant	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	SWYD Underground Raceway Details-UTL	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Relay & Metering Legend	9/1/2011
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Line Differential Relay Elementary Diagram	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Lock-Out & Breaker Failure Relay Elementary Diagram	1/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Utility Line Three-Line Metering & Relaying Diagram	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Unit Three-Line Metering & Relaying Diagram Typical	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Station Service Three-Line Metering & Relaying Diagram	1/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Unit #2-8 Three-Line Metering & Relaying Diagram	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Generator Breaker Close Elementary Diagram	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Generator Breaker Trip #1 Elementary Diagram	2/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Generator Breaker Trip #2 Elementary Diagram	3/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Breaker 9001 Close Elementary Diagram	4/1/2012

ELECTRICAL DESIGN SUBMITTALS

CEC Cond	CBO Submittal Number	Document Type	Source	Submittal Purpose	Description	Submittal Date
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Breaker 9001 Trip Elementary Diagram	4/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Generator 1 Breaker Wiring Diagram Typical	6/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	220 kV Station Service Breaker Wiring Diagram Typical For 1 & 2	6/1/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Relay & Control Panel Wiring Diagram	7/15/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Metering Panel Wiring Diagram	8/15/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Communication Panel Wiring Diagram	8/15/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Utility Aux Metering Cabinet Wiring Diagram	8/15/2012
TSE-4	TSE-4-XX	Drawings	Mott MacDonald/Vendor	Approval	Switchyard Communication Cable Wiring Diagrams	10/1/2012
TSE-4	TSE-4-XX	List	Mott MacDonald/Vendor	Approval	SCADA I/O List	10/15/2012
TSE-4	TSE-4-XX	List	Mott MacDonald/Vendor	Approval	Cable & Raceway Schedule -	11/1/2012
Switchyard Specifications						
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	High Voltage SF6 220 kV Circuit Breaker	10/21/2011
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	220 kV Substation Specification	12/1/2011
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	SCADA Design Specification And Programing	2/1/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	Relay And Control Panels	2/1/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	Revenue Metering Equipment- Switchyard	2/1/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	DC System (Battery Sizing & Spec)	2/1/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	20 kV Disconnect Switches	3/15/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	CCVT Specification	2/1/2012
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	PT, CT Specification	10/28/2011
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	Revenue metering CT/PT combo unit	10/28/2011
TSE-4	TSE-4-XX	Technical Specification	Mott MacDonald	Approval	Surge Arrestors	10/28/2011
Electrical Calculations & Studies						
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Short Circuit Study (Plant)	10/28/2011
TSE-4	TSE-4-XX	Studies, Calculations	Vendor	Approval	Short Circuit Study (Switchyard)	11/15/2011
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Grounding Calculations (Plant)	10/28/2011
TSE-4	TSE-4-XX	Studies, Calculations	Vendor	Approval	Grounding Calculations (Switchyard)	11/15/2011
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Plant Relay Settings & Protection Coordination	8/1/2012
TSE-4	TSE-4-XX	Studies, Calculations	Mott MacDonald/Vendor	Approval	Switchyard Relay Settings & Protection Coordination	8/15/2012
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald/Vendor	Approval	Generator Protection Relay Settings (By GE) & Protection Coordination	8/1/2012
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Cable Ampacity & Derating Calculations	12/1/2011
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Arc Flash Study	9/1/2012
TSE-4	TSE-4-XX	Studies, Calculations	Vendor	Approval	Lightning Study	2/1/2012
ELEC-1	ELEC-1-XX	Studies, Calculations	Mott MacDonald	Approval	Lighting Calculations (Plant)	2/1/2012
TSE-4	TSE-4-XX	Studies, Calculations	Vendor	Approval	Lighting Calculations (Switchyard)	3/1/2012

Civil/Structural/Architectural Drawings

Drawing Number	Description	Number of Drawings
Y-001	Title Sheet	1
Y-100	Existing Site Plan, Sheet 1	1
Y-101	Existing Site Plan, Sheet 2	1
Y-110	Site Plan	1
Y-120	Soil and Erosion Control Plan, Sheet 1	1
Y-121	Soil and Erosion Control Plan, Sheet 2	1
Y-122	Soil and Erosion, Phase I - Plan - Preliminary Construction	1
Y-123	Soil and Erosion, Phase 2 - Plan	1
Y-124	Soil and Erosion, Road Plan	1
Y-125	Soil and Erosion Control, Typical Details - Sheet 1	1
Y-126	Soil and Erosion Control, Typical Details - Sheet 2	1
Y-127	Soil and Erosion Control, Typical Details - Sheet 3	1
Y-130	Mass Earthwork Plan	1
Y-131	Mass Earthwork Sections	1
Y-140	Grading Plan - Key Plan	1
Y-141	Fire Pump Foundaton Grading	1
Y-142	Grading Plan - South	1
Y-143	Grading Plan - Center	1
Y-144	Grading Plan - North	1
Y-145	Grading Plan - Parcel 3 (South East)	1
Y-150	Grading Plan - Construction Parking and Laydown	1
Y-160	Site Roads	1
Y-165	Pavement Details	1
Y-170	Fence Details	1
Y-200	Site Trailer and Parking Plan	1
Y-201	Off Site Construction Parking and Laydown Plan	1
Y-202	Site trailer Deck, Landing, and Ramp Details	1
Y-203	Power Duct Profile	1
Y-204	Plan-Construction Services Roadway	1
C-001	Concrete General Notes	1
C-010	Fire Pumphouse Foundation Plan & Details	1
C-100	Foundation Location Plan	2
C-200	Combustion Turbine Generator Fnd. Plan Sections and Details	5
C-203	Intercooler and Cooling Water Pump Foundation	1
C-205	Fuel Gas filter Foundation	1
C-300	SCR Foundation Sections and Details	3
C-301	Ammonia Flow Control Unit Skid Foundation	1
C-400	Cooling Tower Fdns, Sections and Details	3
C-410	Cooling Tower Chem Feed Skid Foundation	

Civil/Structural/Architectural Drawings

Drawing Number	Description	Number of Drawings
C-500	Tank Foundations drawings	4
C-504	Demineralized Water Forwarding Pump Skid Foundation	1
C-505	Wastewater Forwarding Pump Skid Foundation	1
C-550	Gas Compressor Foundations	2
C-555	Gas Filter Separator	
C-600	GSU Transformer Foundations	2
C-602	Station Service Transformer Foundations	2
C-604	Auxiliary Transformer Foundations	1
C-605	Open Tube Bus Support Foundations	1
C-700	Miscellaneous Foundations, ZLD System and Pumps	3
C-710	Miscellaneous Sump Foundations	2
C-800	Admin/Warehouse Building Foundations	2
C-810	Unit Control/Electric Room Foundations	2
C-820	CEMS Enclosure Foundations	1
C-830	Switchyard Building Foundations	2
C-840	Miscellaneous Foundations for Stairs and Access	3
C-900	Ammonia Unloading and Storage Tank Foundations	4
S-001	Steel General Notes	1
S-100	Stair Plan Sections and Details	3
S-200	Ladder Details	2
S-300	Misc Framing details	3
A-100	Operations/Warehouse Building Plan	1
A-101	Operations/Warehouse Building Elevations	1
A-102	Operations/Warehouse Building Details	1
A-103	Operations/Warehouse Building Ceiling	1

Mechanical Drawings

Drawing Number	Description	Number of Drawings
G-101	General Arrangement Plan & Legend	1
G-125	General Arrangement – Overall CTG Unit Typical	1
G-152	Eq. Loc. Part Plan - Area CTG 01	1
G-153	Eq. Loc. Part Plan - Area CTG 02	1
G-154	Eq. Loc. Part Plan - Area CTG 03	1
G-155	Eq. Loc. Part Plan - Area CTG 04	1
G-156	Eq. Loc. Part Plan - Area CTG 05	1
G-157	Eq. Loc. Part Plan - Area CTG 06	1
G-158	Eq. Loc. Part Plan - Area CTG 07	1
G-159	Eq. Loc. Part Plan - Area CTG 08	1
G-160	Eq. Loc. Part Plan - Area Ammonia Tank	1
G-161	Eq. Loc. Part Plan - Area Fuel Gas Compressors 1	1
G-162	Eq. Loc. Part Plan - Area Fuel Gas Compressors 2	1
G-163	Eq. Loc. Part Plan - Area Admin/Warehouse	1
G-164	Eq. Loc. Part Plan - Area Zero Discharge System	1
G-165	Eq. Loc. Part Plan - Area Waste Water Storage Tank	1
G-166	Eq. Loc. Part Plan - Area Demineralized Water Tanks	1
G-167	Eq. Loc. Part Plan - Area Demineralizer Trailers	1
G-168	Eq. Loc. Part Plan - Area Raw Water Storage	1
G-169	Eq. Loc. Part Plan - Area Fuel Gas Metering Station	1
P-201	Underground Piping Plan - Area CTG 01	1
P-202	Underground Piping Plan - Area CTG 02	1
P-203	Underground Piping Plan - Area CTG 03	1
P-204	Underground Piping Plan - Area CTG 04	1
P-205	Underground Piping Plan - Area CTG 05	1
P-206	Underground Piping Plan - Area CTG 06	1
P-207	Underground Piping Plan - Area CTG 07	1
P-208	Underground Piping Plan - Area CTG 08	1
P-209	Underground Piping Plan - Area Ammonia Tank	1
P-210	Underground Piping Plan - Area Fuel Gas Compressors 1	1
P-211	Underground Piping Plan - Area Fuel Gas Compressors 2	1
P-212	Underground Piping Plan - Area Admin/Warehous	1
P-213	Underground Piping Plan - Area Zero Discharge System	1
P-214	Underground Piping Plan - Area Waste Water Storage Tank	1
P-215	Underground Piping Plan - Area Demineralized Water Tanks	1
P-216	Underground Piping Plan - Area Demineralizer Trailers	1
P-217	Underground Piping Plan - Area Raw Water Storage	1
P-218	Underground Piping Plan - Area Fuel Gas Metering Station	1
P-219	Underground Piping Plan - Area Potable Water Pump	
P-221	Underground Piping Plan - Area Potable Water Pump	
P-222	Underground Piping Plan - Fire Protection Area CTG Units 1,2 and 3	
P-223	Underground Piping Plan - Fire Protection Area CTG Units 4,5 and 6	
P-224	Underground Piping Plan - Fire Protection Area CTG Units 7 and 8	

Mechanical Drawings

Drawing Number	Description	Number of Drawings
P-225	Underground Piping Plan - Area Raw Water Pump PW-2	
	First Review of 3D Model	1
P-101	Composite Piping Plan - Area CTG 01	1
P-102	Composite Piping Plan - Area CTG 02	1
P-103	Composite Piping Plan - Area CTG 03	1
P-104	Composite Piping Plan - Area CTG 04	1
P-105	Composite Piping Plan - Area CTG 05	1
P-106	Composite Piping Plan - Area CTG 06	1
P-107	Composite Piping Plan - Area CTG 07	1
P-108	Composite Piping Plan - Area CTG 08	1
P-109	Composite Piping Plan - Area Ammonia Tank	1
P-110	Composite Piping Plan - Area Fuel Gas Compressors 1	1
P-111	Composite Piping Plan - Area Fuel Gas Compressors 2	1
P-112	Composite Piping Plan - Area Admin/Warehous	1
P-113	Composite Piping Plan - Area Zero Discharge System	1
P-114	Composite Piping Plan - Area Waste Water Storage Tank	1
P-115	Composite Piping Plan - Area Demineralized Water Tanks	1
P-116	Composite Piping Plan - Area Demineralizer Trailers	1
P-117	Composite Piping Plan - Area Raw Water Storage	1
P-118	Composite Piping Plan - Area Fuel Gas Metering Station	1
P-401	Isometeric Piping Plan - Area CTG 01	1
P-402	Isometeric Piping Plan - Area CTG 02	1
P-403	Isometeric Piping Plan - Area CTG 03	1
P-404	Isometeric Piping Plan - Area CTG 04	1
P-405	Isometeric Piping Plan - Area CTG 05	1
P-406	Isometeric Piping Plan - Area CTG 06	1
P-407	Isometeric Piping Plan - Area CTG 07	1
P-408	Isometeric Piping Plan - Area CTG 08	1
P-409	Isometeric Piping Plan - Area Ammonia Tank	1
P-410	Isometeric Piping Plan - Area Fuel Gas Compressors 1	1
P-411	Isometeric Piping Plan - Area Fuel Gas Compressors 2	1
P-412	Isometeric Piping Plan - Area Admin/Warehous	1
P-413	Isometeric Piping Plan - Area Zero Discharge System	1
P-414	Isometeric Piping Plan - Area Waste Water Storage Tank	1
P-415	Isometeric Piping Plan - Area Demineralized Water Tanks	1
P-416	Isometeric Piping Plan - Area Demineralizer Trailers	1
P-417	Isometeric Piping Plan - Area Raw Water Storage	1
P-418	Isometeric Piping Plan - Area Fuel Gas Metering Station	1

Electrical Drawings

Drawing Number	Description	Number of Drawings
E-100	Electrical Symbols And Legend	1
E-101	Overall Plant Power One Line Diagram	1
E-104	One Line Diagram 4160 V Swgr	1
E-106	One Line Diagram 480 V Load Center Unit 1 (sheet 1)	1
E-106	One Line Diagram 480 V Load Center Unit 2-8	7
E-107	One Line Diagram 480 V BOP swgr	1
E-108	One Line Diagram 480 V MCC Unit 1 (sheet 1)	1
E-108	One Line Diagram 480 V MCC Unit 2-8	7
E-108	One Line Diagram 480 V Distribution Board scheduels	10
E-109	One Line Diagram 480 V MCC Bop	1
E-111	DC One Line Diagram	1
E-112	Vital AC One Line Diagram	1
E-113	Power Panel Schedules	10
E-200	Grounding Details	1
E-201	Overall Grounding Plan	1
E-204	CTG Area Grounding Plans Sheets 1 through 8	8
E-205	Grounding Plans BOP Areas Sheets 1 through 6	6
E-300	Area Classification Plan Sh 1-4	4
E-301	General Site Plan - Sh1-4	4
E-302	Power Block Part Plan Sh1-8	8
E-303	Cems Electrical Plan	1
E-310	Generator Leads Open Aluminum Bus	1
E-311	Non-Seg Bus Duct	1
E-360	General Site Lighting Plan & Details	1
E-361	General Site Lighting Plan Sh 1-5	5
E-362	Lighting - Ctg Areas Task Lighting - Sh 1- 8	8
E-363	Lighting Misc Areas - Sh 1-12	12
E-401	Underground Raceway Plans Sh 1-12	12
E-402	Power Block Underground Raceway Plan Sh1 -8	8
E-410	Underground Raceway Details Sh 1-16	16
E-501	Above GroundPower Block Raceway Plans	8
E-502	Above Ground Raceway Plan Area 2	8
E-503	Above Ground BOP Raceway Plan Areas	5
E-701	Schematic / Wiring Diagrams 480V Mcc Starter Typ1, 2, 3 4	4
E-710	Schematic / Wiring Diagrams 480V Swgr Breaker Typical	1
E-711	Schematic / Wiring Diagrams 4160 Starter Typical	1
E-712	Schematic / Wiring Diagrams 4160 Breaker Typical	1
E-720	Wiring Diagrams CTG1/ Interfaces Tpical	6
E-721	Wiring Diagrams CTG 1-8/ Interfaces Table	7
E-730	Connection Diagrams Sh 1-32	32
E-901	Cable / Conduit Schedule	1
E-920	Electrical Equipment List	1
E-950	Motor & Load Schedule	1
	230KV SWITCHYARD	
E-170	Switchyard Rel& Mtr One Line Diagram	1

Electrical Drawings

Drawing Number	Description	Number of Drawings
E-171	Dc One Line Diagram	1
E-172	Switchyard Revenue Metering Diagram	1
E-173	Ac Station Service One Line Diagram	1
E-370	Switchyard Layout	1
E-371	Switchyard Sections	4
E-373	Switchyard Control Building Plans & Details	5
E-374	Transmission Line Interface	1

I&C Drawings

Drawing Number	Description	Number of Drawings
D-001	P&ID Lead Sheet 1a	1
D-002	P&ID Lead Sheet 1b	1
D-006	P&ID Fuel Gas System Sheet 1 (Metering)	1
D-007	P&ID Fuel Gas System Sheet 2 (FGC 1)	1
D-008	P&ID Fuel Gas System Sheet 3 (FGC 2)	1
D-009	P&ID Fuel Gas System Sheet 4 (FGC 3)	1
D-010	P&ID Fuel Gas System Sheet 5 (FGC 4)	1
D-011	P&ID Fuel Gas System Sheet 6 (FGC 5)	1
D-012	P&ID Fuel Gas System Sheet 7 (FGC 6)	1
D-013	P&ID Fuel Gas System Sheet 8 (FG Filters)	1
D-015	P&ID LMS100 Sheet 1	1
D-016	P&ID LMS100 Sheet 2	1
D-017	P&ID LMS100 Sheet 3	1
D-020	P&ID Compressed Air system	1
D-021	P&ID Ammonia System	1
D-022	P&ID Well & Raw Water System	1
D-023	P&ID Demin Water System	1
D-024	P&ID Waste Water Collection	1
D-025	P&ID Fire Protection	1
D-026	P&ID Potable Water	1
D-029	P&ID Zero Discharge System	1
D-050	Water Balance Diagram	1
D-18XXX	Instrument Installation Details (As Required)	25
-SP-18001	Instrument Index	1
-SP-18050	I/O List	1
-D-18200	Control System Architecture (Network Diagram)	1
-D-18201	Switchyard SCADA Network Diagram	1

CBO Payment Receipt

Johnson, Amanda

From: Mark McDaniels <mmcdaniels@cpv.com>
Sent: Wednesday, September 28, 2011 3:05 PM
To: Johnson, Amanda
Subject: FW: CPV Sentinel - Payment Receipt for August Invoice

---

From: sabrina.dickinson@us.bureauveritas.com [mailto:sabrina.dickinson@us.bureauveritas.com]
Sent: Wednesday, September 28, 2011 2:42 PM
To: Mark McDaniels; Michael Lewis
Cc: dan.enright@us.bureauveritas.com
Subject: CPV Sentinel - Payment Receipt for August Invoice

Good Afternoon,

This is to confirm that Bureau Veritas has received payment for the following invoice:

Invoice 1125158
Dated 08/24/11
In the amount of $61,435.47

Thank you!

Sabrina Dickinson
Office Manager – Power & Utilities
Bureau Veritas North America, Inc.
180 Promenade Circle Suite 150
Sacramento, CA 95834
P: 916.617.2028
F: 916.617.2068
D: 916.514.4513
C: 916-627-9832
sabrina.dickinson@us.bureauveritas.com
www.us.bureauveritas.com/energyusa
ISO 9001:2008 Certified

NOTICE:
This message contains information which is confidential and the copyright of our company or a third party. If you are not the intended recipient of this message, please delete it and destroy all copies. If you are the intended recipient of this message, you should not disclose or distribute this message to third parties without the consent of our company. Our company does not represent, warrant and/or guarantee that the integrity of this message has been maintained, nor that the communication is free of virus, interception, or interference. The liability of our company is limited by our General Conditions of Services.
Please consider the environment before printing this e-mail

"NOTICE: This message contains information which is confidential and the copyright of our company or a third party. If you are not the intended recipient of this message please delete it and destroy all copies. If you are the intended recipient of this message you should not disclose or distribute this message to third parties without the consent of our company. Our company does not represent, warrant and/or guarantee that the integrity of this message has been maintained nor that the communication is free of virus, interception or interference. The liability of our company is limited by our General Conditions of Services."

APPENDIX C
WEAP Acknowledgement Forms

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/1/2011	DAVE MARKS	I.F.S.A.	Dave Marks	[illegible]
9/1/11	Abdul Asfour	I.F.S.A	Abdul Asfour	
9/1/11	Marco Calderon	I.F.S.A	Marco A Calderon	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9-6-11	Manuel Espilla	SUKUT	[illegible]	[illegible]
9-6-11	HUGO CRUZ	SUKUT	Hugo Cruz	[illegible]

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/8	[illegible]	Sukut	[illegible]	[illegible]

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/9/11	Kevin Wedman	BV-CBO	[signature]	Mike Lee

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/12/11	Javier Vega			
09/12/11	Roger Sosa			
9/12/11	Carlos A. Mendoza			
9/12/11	STEVEN REISER	SUKUT CONST.		

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9-12-2011	Eddie Luna	SUKUT	[illegible]	[illegible]
9-12-11	David Gomez	SUKUT	David Gomez	
9-12-11	Victor Guillen	SUKUT	[illegible]	
9-12-11	Angel Magdaleno	SUKUT	[illegible]	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9-11-201	John S. Trotter	Carpenter Foreman	John S. Trotter	[illegible]

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/15/2011	MATT DISHER	Southwest Networks	[illegible]	[illegible]
9/15/11	JARED BOWERS	Southwest Networks	[illegible]	
9-15-11	Tim Gaylor	Southwest Networks	[illegible]	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9-16-11	Greg Blake	Griffith Co	[illegible]	[illegible]
9-16-11	Gilbert Salgado	Griffith Co	[illegible]	
9-16-11	Salvador Castro	Griffith Co.	[illegible]	
9/16/11	KYLE BEATY	GRIFFITH Co.	[illegible]	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/19/2011	Jessica Valdez	Agua Caliente	[illegible]	[illegible]

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
09/21	Michael VanCosten	Griffith		[illegible]
	Eddie Flores	Griffith		
	Victor Valencia	Griffith		
	George Alvarez	GRIFFITH Co.		
	Jesus Espinoza	SUKUT		
	Rogelio Gonzalez	SUKUT		

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/22/11	DANA HIRSCH	GRIFF		
9-22-11	Fred Stowestreet	GRIFFITH		
9-22-11	JOE L. TORRES	GRIFF.		
9-22-11	Victor Pinedo	GRIFF		
9-22-11	ENRIQUE ORTIZ	GRIFF		
9-22-11	Gualeriando Hgalo	GRIFFITH		
9-22-11	David Sanchez	GRIFFT		
9-22-11	JOSE CONTRERAS	Griffith		
9-22-11	Miguel Lopez	Griffith		
9-22-11	Dagoberto VERA	GRIFFITH		
9-22-11	Francisco Reyes	Griffith		
9/22/11	JOSE OMAÑA	GRIFFITH		
9/22/11	Vramontes Jose	Griffith		
9/22/11	ELIAS HARO	Griffith		

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
4/23	STEVE GRUEGOS	SUKUT	[illegible]	M. LEE

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9-26	Cole McKinstry	Halloday/Minimal	[illegible]	[illegible]
9-26	Guillermo Lozo	HTM INC	[illegible]	
9-26	Lawrence Fournier	Griffith	[illegible]	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/28	Doug Jordan	PCS		
	Seth Osorio			
	Frank Chavez	PCS		
	Carlos Tatoya	PCS		
	Chris Walker	PCS		
	Ernesto Reyna	PCS		
9-28	MATT THOMPSON	SoCal Testing		
	Kyle Carlson	PCS		

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/29	RON MCCAE	GRIFFITH	[illegible]	[illegible]
9/29	MARK SLUNTER	GRIFFITH	[illegible]	
9/29	COSME DIAZ JR	GEMMA	Cosme Diaz Jr	

WORKER ENVIRONMENTAL AWARENESS PROGRAM

TRAINING ACKNOWLEDGEMENT

CPV Sentinel Energy Project

PLEASE NOTE: By signing below, I acknowledge that I have received training at education session prior to beginning work on this project. During that session, I was provided information about the biology resources, cultural resources and paleontological resources in the project area.

I, the undersigned individual, have read and understand the measures and agree to comply with all provisions of the program. I am aware that I may incur civil and/or criminal penalties if I do not conform to the required measures.

Date	Trainee (Print Name)	Trainee Affiliation	Trainee Signature	Trainer
9/29	Stacey R. McLain	CPV	Stacey R. McLain	[illegible]
9/29	Jack Hickey	CPV	Jack Hickey	[illegible]

APPENDIX D
Worker Safety

PROJECT SAFETY EVALUATION - Jobsite Inspection

Project Name:	CPV-Sentinel	Project #:	1101253	Site Manager:	Charles Collins
Client:	CPV	Date:	09/15/11	Project Superintendent:	Paul West
# Workers:	38	Evaluator:	M. Bennett	Safety Manager:	M. Lee

Current Safety Statistics

Incident Rate:	0	Lost Time Rate:	0	Lost Work Day Incident Rate:	0

Total Points Received	198
Total Points Possible	207
Points Received divided by Points Possible = % Compliance	96%

Subtract points if item not required to be implemented.

Rating	Percent	Action
Excellent	>95%	No action needed, strive for 100%. Safety plan is fully implemented.
Good	90-95%	Develop and publish action plans for improvement
Fair	80-90%	Arrange for on-site assistance
Marginal	<80%	

Safety Manager Signature

Site Manager Signature

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
1. Safety Program Administration			
a. Incident Rate at 0 (3 points), improving (1 point), increasing (0 points)	3	3	
b. Lost Time Rate at 0 (3 points), improving (1 point), increasing (0 points)	3	3	
c. LWDI at 0 (3 points), improving (1 point), increasing (0 points)	3	3	
d. Workers' Comp $/mh .03 or less (3 points) .03-.10 (1 point)	3	3	
e. Are OSHA and other required notices posted	2	2	
f. Are required safety meetings held	4	4	
g. Are medical service, first aid equipment, and emergency plans in place	2	2	
h. Is the relationship with a doctor, clinic, and hospital established and effective	2	2	
i. Are safety records kept up-to-date and available	3	3	
j. Are emergency numbers and access/egress posted	2	2	
Total Points	27	27	
2. Housekeeping and Sanitation			
a. General neatness of work areas	2	2	
b. Regular disposal of waste and trash	2	2	
c. Passageways and walkways clear and unobstructed	2	2	
d. There is adequate lighting	2	2	
e. Projecting nails are removed	2	2	
f. Oil and grease is removed	2	2	
g. Waste containers are provided and used	2	2	
h. Sanitary facilities are adequate and clean	2	2	
I. An adequate supply of water or water jugs is available	3	3	
j. Disposable drinking cups and waste containers are available	2	2	
Total Points	21	21	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
3. Fire Prevention			
a. Fire instructions are given to personnel	2	2	
b. Fire extinguishers are identified and checked monthly	3	3	
c. Phone number of the fire department is posted	2	2	
d. Hydrants are clear and access to public thoroughfare is open	0	n/a	
e. "No Smoking" signs are posted and enforced where needed	2	2	
f. Fire extinguishers are properly mounted or placed	2	2	
Total Points	11	11	
4. Hand Tools			
a. Proper tools are being used for each job	2	2	
b. Tools are stored neatly and carried safety	2	2	
c. Tools are inspected and maintained	2	2	
d. Damaged tools are repaired or replaced promptly. Employee tools are inspected and repaired.	2	2	
Total Points	8	8	
5. Electrical			n/a
a. Adequate wiring, well insulated			
b. Proper fuse and breaker protection is provided			
c. Monthly ground assurance programs are in effect			
d. Electrical dangers are posted			
e. Proper fire extinguishers are provided			
f. Breaker boxes and switches are properly labeled			
g. Lockout/Tagout procedures are fully implemented			
Total Points	0	0	
6. Power Tools			
a. Good housekeeping is maintained where tools are used	2	2	
b. Tools and cords are in good condition	2	2	
c. Proper grounding	2	2	
d. Proper instruction is in use	2	2	
e. All mechanical safeguards are in use	2	2	
f. Tools are stored neatly when not in use	2	2	
g. Correct tool is being used for the job at hand	2	2	
h. Wiring is properly installed	2	2	
i. Pressure locks are removed	2	2	
Total Points	18	18	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
7. Powder-Actuated Tools			n/a
a. All laws and ordinances are complied with			
b. All operators are qualified, carded and trained			
c. Tools and charges secured and separated			
d. Competent instruction and supervision is given			
e. Tools are checked and in good working order			
f. Tools are not used on anything other than recommended materials			
g. Safety goggles or face shields are worn			
h. Flying hazards checked by backing up, removal of personnel, or use of captive stud tool			
Total Points	0	0	
8. Ladders			
a. Ladders are inspected and in good condition	2	2	
b. Ladders are properly secured to prevent slipping, sliding, or falling	2	2	
c. Do ladder side rails extend 36" above top of landing?	2	2	
d. Rungs or cleats over 12" on center	2	2	
e. Step-ladders are fully open when in use	2	2	
f. Metal ladders are not used around electrical hazards	2	2	
g. Proper maintenance and storage of ladders	2	2	
Total Points	14	14	
9. Steel Erection			n/a
a. Safety nets or planked floors are used			
b. Temporary periphery cable is at each floor level			
c. Taglines are used for tools			
d. Floor opening is covered and barricaded			
e. Ladders, stairs, or other access is provided			
f. Hoisting apparatus is checked			
Total Points	0	0	
10. Motor Vehicles			
a. Vehicles regularly inspected	2	2	
b. Drivers are qualified	2	2	
c. Local and state vehicle laws and regulations are observed	2	2	
d. Brakes, lights, and warning devices are operational	2	2	
e. Weight limits and load sizes controlled. Ice, grease?	2	2	
g. All glass in good condition	2	2	
h. Back up alarms provided when needed	2	2	
i. Fire extinguishers installed	2	2	
j. Seat belts used	2	2	
Total Points	18	18	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
11. Scaffolding			n/a
a. Erection is properly supervised by a competent person			
b. All structural members meet the safety factor			
c. All connections are secure			
d. Working areas are free of debris, snow, ice, and grease			
e. Planking cleats in place			
f. Workers are protected from falling objects			
g. The scaffold is plumb and square, with cross bracing			
h. Guard rails, intermediate rails and toe boards are in place			
i. Scaffold equipment is in good working order			
j. Ropes and cables are in good condition			
Total Points	0	0	
12. Hoists, Cranes, and Derricks			n/a
a. A competent person is designated			
b. Cables and sheaves inspected monthly			
b. Slings and chains, hook and eyes checked			
c. Equipment is firmly supported			
d. Outriggers used as required			
e. Power lines inactivated, removed, or at a safe distance			
f. Proper loading for capacity at lifting radius			
g. All equipment is properly lubricated and maintained			
h. There are signalmen where needed			
i. Signals are understood and observed			
j. Inspection and maintenance logs maintained			
k. Load charts are posted in the cab			
l. Fire extinguisher is installed			
Total Points	0	0	
13. Heavy Equipment			
a. Regular inspection and maintenance logs completed	2	2	
b. Lubrication and repair of moving parts done	2	2	
c. Lights, brakes, and warning signals are operative	2	2	
d. Wheels chocked when necessary	2	2	
e. Haul road well maintained and laid out properly	2	2	
f. Back-up alarms installed and audible	2	2	
g. High-visibility safety vests required	2	2	
h. Equipment is protected from theft when not in use	2	2	
i. Shut-off devices are on hose lines in case of hose failure	2	2	
j. Noise arresters are in use	2	2	
k. Fire extinguisher is installed	2	2	
Total Points	22	22	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
14. Barricades			
a. Floor openings planked over or barricaded	0	n/a	
b. Red and Yellow barricade tape used	2	2	
c. Roadways and sidewalks are effectively protected	2	1	Improving
d. Adequate lighting is provided	2	2	
e. All barricades labeled	2	1	Corrected
f. Traffic controlled	2	1	Improving
Total Points	10	7	
15. Personal Protective Equipment			
a. Eye protection	2	2	
b. Face shields	2	2	
c. Respirators and masks	0	n/a	
d. Helmets and hoods	0	n/a	Not observed
e. Head protection	2	2	
f. Gloves, aprons, and sleeves; rubber or plastic, designed to afford protection from alkalis and acids; electricians' rubber gloves with protectors	2	1	Improving
g. Respirators for harmful dust, asbestos, sand blasting, welding (lead paint and galvanized zinc or cadmium). Adequate ventilation when painting or applying epoxy resins. When there is question about injurious exposure, notify superior immediately who in turn shall arrange for atmospheric samples to be taken.	0	n/a	Not observed
h. Proper fall protection (safety harness, retractables, etc)	2	n/a	Not observed
Total Points	10	7	
16. Handling and Storage of Materials			n/a
a. Materials are properly stored or stacked			
b. Passageways are clear			
c. Stacks on firm footings and not too high			
d. Laydown areas neat and organized			
e. Workers are lifting loads correctly			
f. Materials protected from weather conditions			
g. Protection against falling into hoppers and bins provided			
h. Dust protection is observed			
i. Extinguishers and other fire protection available			
j. Traffic in storage area controlled			
Total Points	0	0	
17. Masonry			n/a
a. Proper scaffolding used			
b. Masonry saws properly equipped and dust protection provided			
c. Safe hoisting equipment used			
Total Points	0	0	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
18. Welding and Cutting			n/a
a. Screens and shields used			
b. Goggles, gloves, and proper clothing worn			
c. Equipment is in good operating condition			
d. Electrical equipment is grounded			
e. Power cables are protected and in good repair			
f. Fire extinguishers of proper type nearby			
g. Inspection for fire hazards done			
h. Flammable materials are protected			
i. Gas cylinders are chained upright and caps are in use			
j. Gas lines are protected and in good condition			
k. Carts are available for moving cylinders			
Total Points	0	0	
19. Flammable Gases and Liquids			
a. All containers clearly identified	2	1	Corrected
b. Signs posted: "No Smoking", "Flammable Materials"	2	1	Ongoing
c. Fire Extinguishers within 25 feet	2	2	
d. Proper storage practices are observed	2	2	
e. Fire hazards checked	2	2	
f. Proper types and number of extinguishers are kept nearby	2	2	
g. Carts are available for moving cylinders	0	n/a	not observed
h. Storage area bermed for spills (should hold 2 1/2 times largest tank)	2	2	
Total Points	14	12	
20. Excavation and Shoring			
a. Adjacent structures properly shored	2	2	
b. Proper shoring and sheathing used for soil and depth	2	2	
c. Roads and sidewalks supported and protected	2	2	
d. Excavation barricaded and lighting is provided	2	2	
e. Equipment is a safe distance from edge of excavation	2	2	
f. Ladders provided where needed	2	1	Corrected
g. Equipment ramps are adequate	2	2	
h. Competent person designated	2	2	
i. Job supervision is adequate	2	2	
Total Points	18	17	

PROJECT SAFETY EVALUATION - Jobsite Inspection

AREA OF EVALUATION	Points Possible	Points Earned	ACTION REQUIRED
21. Garages and Repair Shops			n/a
a. Fire hazards checked			
b. Proper dispensing of fuels and lubricants			
c. Good housekeeping observed			
d. Adequate lighting			
e. Fuels and lubricants in proper condition			
f. Area is well ventilated to prevent carbon monoxide and other fumes			
g. Proper grounding and bonding used			
Total Points	0	0	
22. Concrete Construction			
a. Forms properly installed and braced	2	2	
b. Adequate shoring, plumbed and cross braced	2	2	
c. Shoring remains in place until strength is attained	2	2	
d. Heating devices checked	0	n/a	
e. Mixing and transport equipment is supported and traffic planned and routed	2	2	
f. Adequate runways provided	2	2	
g. Protection from cement dust and concrete contact observed	2	2	
h. Shirts covering skin used	2	2	
i. Nails and stripped form material removed from area	2	2	
Total Points	16	16	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: I.F.S.A.

Date Given: 9/1/2011

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
DAVE MARKS	Dave Marks
Abdul Asfour	Abdul Asfour
Marco A. Calderon	Marco A Calderon

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA

Date Given: 9-6-11

Name of Person Conducting Meeting: [illegible]

Attendees

Name	Signature
Manuel Capilla	[illegible]
Hugo Cruz	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA

Date Given: 9/8/11

Name of Person Conducting Meeting: [illegible]

Attendees

Name	Signature
[illegible]	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA

Date Given: 9-12-11

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
Javier Vega	
Roger Sosa	
Carlos Mendoza	
STEVEN REISER	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA / SUKUT.

Date Given: 9/13/11

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
Eddie LUNA	Eddie Luna
David Gomez	David Gomez
Victor Guillen	[illegible]
Angel Magdaleno	Angel [illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: Griffith Co.

Date Given: 9-14-2011

Name of Person Conducting Meeting: Mike Lee

Attendees

Name	Signature
John S. Trotter	John S. Trotter
Ronnie W. Grace	Ronnie Grace
KASH KHAN	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: Southwest Networks

Date Given: 9/15/2011

Name of Person Conducting Meeting: Mike B.

Attendees

Name	Signature
MATT BISHER	
JARED POWERS	
Timothy Gaylor	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: EMMA (GRIFFITH)

Date Given: 9/16/11

Name of Person Conducting Meeting:

Attendees

Name	Signature
Greg Blake	
GILBERT H SALGADO	
Salvador Castro	
KYLE BEATY	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA (Agua Caliente Band of Cahuilla Indians)

Date Given: 9/19/11

Name of Person Conducting Meeting: M. [illegible]

Attendees

Name	Signature
Jessica Valdez	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA / GRIFFITH & SUKUT

Date Given: 9/21/11

Name of Person Conducting Meeting: [illegible]

Attendees

Name	Signature
Michael VanCosten	[illegible]
Eddie Flores	[illegible]
George Alvarez	[illegible]
Victor Valencia	[illegible]
Jesus Espinoza Jr	Jesus F. Espinoza Jr

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA GRIFFITH

Date Given: 9/22/11

Name of Person Conducting Meeting: M. [illegible]

Attendees

Name	Signature
DANA HIRSCH	[illegible]
Fred Stonestreet	[illegible]
JOE L. TORRES	[illegible]
Victor Pinedo	[illegible]
ENRIQUE ORTIZ	[illegible]
GUMERCINDO AGUILAR	[illegible]
JOSE E. CONTRERAS	[illegible]
David Sanchez	[illegible]
Miguel Lopez	[illegible]
Dagoberto VELIZ	[illegible]
Francisco Rojas	[illegible]
Jose Contreras	[illegible]
VIRAMONTES JOSE	[illegible]
Eddie Haro	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA (SUKUT)

Date Given: 9/23/11

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
STEVE GALLEGOS	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA (Ashtabula + Min Mack)

Date Given: 9/26/11

Name of Person Conducting Meeting: M. [illegible]

Attendees

Name	Signature
Cole McKinney	[illegible]
Guillermo Lazo	[illegible]
Lawrence Fournier	[illegible]

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA

Date Given: 9/28/11

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
Doug Jordan	
Seth R. Osorio	
Frank Chavez	
Carlos Tatoya	
Ernesto Lopez	
Mark Thomason	
Kyle Carlson	

Gemma Power Systems California, Inc.

PROJECT ORIENTATION ATTENDANCE FORM

Contractor: GEMMA

Date Given: 9/29/11

Name of Person Conducting Meeting: M. LEE

Attendees

Name	Signature
RON MICHO	[illegible]
COSME DIAZ JR	C. D. [illegible]
MARK D. SWATZ	[illegible]

APPENDIX E
Biological Resources Monthly Summary Report

URS

Memorandum

Date: October 4, 2011

To: Amanda Johnson, CPV Sentinel Assistant Compliance Manager, URS Corporation

From: David Kisner, CPV Sentinel Designated Biologist, URS Corporation

Subject: **September 2011 Monthly Biology Compliance Summary Report for the CPV Sentinel Project**

This monthly compliance summary report is being submitted to comply with conditions set forth by California Energy Commission (CEC). Project description information is contained within the following references and summarized below:

1. CPV Sentinel, LLC. 2007. CPV Sentinel Energy Project Application for Certification (07-AFC-35); and

2. California Energy Commission. 2010. Final Commission Decision – CPV Sentinel Energy Project Application for Certification (07-AFC-3) Riverside County.

Table 5 within the CPV Sentinel (Sentinel) Biological Resources Mitigation Implementation and Monitoring Plan (BRMIMP) provides a summary of compliance and mitigation measures identified by the CEC in the Conditions of Certification. Biological impacts have been minimized to the extent practical and linear facilities have been sited adjacent to existing roadways, to the greatest extent practical. The Project is located in, and surrounded by existing wind farms.

September 2011 Construction Activities Monitored

Sentinel construction activities during this reporting period within the 37-acre project site and along Melissa Lane included:

- Melissa Lane surfacing
- Grading of Plant Site and foundation work
- Laydown area final leveling and graveling
- Continued construction of underground duct bank for construction power
- Desert Water Agency (DWA) completed installation of recycled water line with the exception of metering and control equipment
- Commenced work on 5-acre parking area

Specific Mitigation Measures Implemented in August 2011 Include:

- **BIO-5**: Worker Environmental Awareness (WEAP) training.

The WEAP training video is administered on the first day that staff joins the Sentinel project. A complete list of all Sentinel project employees trained is available upon request.

- **BIO-8**: Mitigation Management to Avoid Harassment or Harm.

  The on-site biological monitors are ensuring that the following measures are being followed:
  1. Install temporary fencing and provide wildlife escape ramps for construction areas that contain steep-walled holes or trenches if outside of an approved, permanent exclusionary fence. The temporary fence shall be hardware cloth or similar materials that are approved by USFWS. Before such holes or trenches are filled, they shall be thoroughly inspected for trapped animals by the Designated Biologist or Biological Monitor;
  2. Make certain all food-related trash is disposed of in closed containers and removed at least once a week;
  3. Prohibit feeding of wildlife by staff and subcontractors;
  4. Prohibit non-security related firearms or weapons from being brought to the site;
  5. Prohibit pets from being brought to the site;
  6. Report all inadvertent deaths of sensitive species to the appropriate project representative. Injured animals shall be reported to CDFG or USFWS and the project owner shall follow instructions that are provided by CDFG or USFWS;
  7. Minimize use of rodenticides in the project area; and
  8. Prohibit vehicles and personnel from entering sensitive habitats.

Results of Condition of Certification Activities:

- **BIO-8**: Mitigation Management to Avoid Harassment or Harm.

  No animals found dead on the project site.

Compliance Issues Reported by the Designated Biologist and / or Biological Monitor:

- No compliance issues were present at the time of the monitoring. All construction activities were in compliance.

Summary of Site Conditions:

Conditions during the monitoring period included disturbance due to site preparation and grading. No listed wildlife species were observed during these activities.

cc: Maggie Fitzgerald, URS Corp

CPV Sentinel Power Project
Weekly Summary Sheet

Dates covered: Thursday September 1 to Sunday September 4, 2011
Gemma Biological Monitor(s) Bob Linder
Days Worked: September 1 and 2, 2011

Activities During the Week:
Construction Monitoring

Species Detected: None

Any wildlife injured or killed? No__X___ Yes____

Compliance Observations and Issues

Noise
Trash
Work Limits
Other Notes:

CPV Sentinel Power Project
Weekly Summary Sheet

Dates covered: Monday September 5 to Sunday September 11, 2011
Gemma Biological Monitor(s) Bob Linder
Days Worked: Tuesday September 6 to Friday September 9, 2011
URS Biological Monitor(s): Carol Thompson
Days Worked: Friday September 9, 2011

Activities During the Week:

Project Area Small Mammal Trapping
Construction monitoring
Grubbing of 5 acre addition

Species Detected During Small Mammal Trapping:

Any wildlife injuried or killed? No_____ Yes__X__

9-9: self re-located and consisted of 4 desert woodrats, 2 antelope ground squirrels, 1 CA pocket mouse, and 1 western fence lizard. One woodrat was killed during grubbing area.

Compliance Observations and Issues

Noise
Trash
Work Limits
Other Notes:

CPV Sentinel Power Project
Weekly Summary Sheet

Dates covered: Monday September 12 to Sunday September 18, 2011
Gemma Biological Monitor(s): Bob Linder
Days Worked: Monday Septemer 12 to Friday September 16

Activities During the Week:
Project Area Grubbing
Construction Monitoring

Species Detected During Grubbing:

Any wildlife injuried or killed? No_____ Yes__X__

Compliance Observations and Issues

Noise
Trash
Work Limits
Other Notes:

CPV Sentinel Power Project
Weekly Summary Sheet

Dates covered: Monday September 19 to Sunday September 25, 2011
Gemma Biological Monitor(s): Bob Linder
Days Worked: Monday September 19 to Friday September 23

Activities During the Week:

Species Detected:
7/21 two woodrats removed from Project Site

Any wildlife injuried or killed? No__X___ Yes____

Compliance Observations and Issues

Noise
Trash
Work Limits
Other Notes:

CPV Sentinel Power Project
Weekly Summary Sheet

Dates covered: Monday September 26 to Friday September 30, 2011
Gemma Biological Monitor(s): Bob Linder
Days Worked: Monday September 26 to Friday September 30

Activities During the Week:
Grading of previously impacted areas

Species Detected:

Any wildlife injuried or killed? No__X___ Yes____

Compliance Observations and Issues

Noise
Trash
Work Limits
Other Notes:

APPENDIX F
Cultural Resources Monthly Summary Report

October 6, 2011

Dale Rundquist
Compliance Project Manager
California Energy Commission
1516 Ninth Street, MS-2000
Sacramento, CA 95814-5512

RE: CPV Sentinel Energy Project (07-AFC-3) Monthly Monitoring Summary Report, Cultural Resources

Dear Mr. Rundquist:

In accordance with CUL-6 of the California Energy Commission's (CEC's) Conditions for Certification (COCs), this letter report summarizes the cultural resources monitoring activities which took place at the CPV Sentinel Energy Project (CPVS) construction site in September 2011.

Project Description

The CPVS is a nominally rated 850-megawatt (MW) electrical generating facility. The power plant site encompasses 37 acres of land situated within unincorporated Riverside County, California. The 37-acre proposed power plant site is currently vacant, with the exception of an unoccupied dwelling unit at the southeastern corner of the site. The surrounding area is primarily characterized by industrial use with extensive development of wind energy and transmission infrastructure.

The project consists of eight natural gas-fired General Electric (GE) LMS100 combustion turbine generators (CTGs) operating in simple cycle mode. The project will supply quick-start peaking capacity, energy, and ancillary services into the California Independent System Operator's (CAISO) Los Angeles Basin Local Capacity Requirement (LCR) Area, which has been identified as an area in need of additional peaking capacity to meet resource adequacy requirements and ensure grid reliability.

Cultural Resources Monitoring

In accordance with Condition of Certification CUL-6, to ensure that there are no impacts to undiscovered resources, the Cultural Resources Specialist (CRS) or Cultural Resources Monitors (CRMs) will monitor full-time all ground disturbing activities on the project site, at the laydown areas, along the linear facility routes, and at roads or other ancillary areas, for as long as the activities are ongoing.

Full- time archaeological monitoring requires at least one monitor per excavation area where earthmoving equipment is actively removing native soils. If an excavation area is too large for one monitor to effectively observe the soil removal, one or more additional monitors are retained to observe the area.

In the event that the CRS determines that the current level of monitoring is not appropriate in certain locations, the CEC's Compliance Project Manager (CPM) shall be notified by letter or e-mail detailing the justification for the change in the level of monitoring. This request will be reviewed and must be approved by the CPM prior to any change in monitoring level.

Cultural resources monitoring activities are the responsibility of the CRS. Any interference with monitoring activities, removal of a monitor from duties assigned by the CRS, or direction to a monitor to

relocate monitoring activities by anyone other than the CRS shall be considered non-compliance with the COCs.

Monitoring/Cultural Resources Activities

Cultural resources monitoring activities at the CPVS site for the month of September included monitoring utility trenching and grading. Monitoring took place on September 1, 2, 6, 7, 8, 9, 12 and 19, 2011. At least one CRM and a Native American Monitor were on site for all ground disturbing activities.

Monitoring activities and observations are summarized in Table 1 below, and Daily Monitoring Logs are attached to this letter report.

Table 1. Summary of Cultural Resources Monitoring Activities September 2011.

Date	Monitors	Activities/Observations	Discoveries
09.01.2011	Robert Lichtenstein	Monitored trenching for buried utility line in bedded medium coarse gravelly sands up to 8 feet below ground surface (bgs).	None
09.02.2011	Robert Lichtenstein	Monitored trenching for buried utility line in bedded medium coarse gravelly sands up to 8 feet bgs.	None
09.06.2011	Audrey Podratz	Monitored trenching 8 feet bgs at Dillon Rd at Melissa Lane. Soils were coarse gravels with some disturbed areas noted.	None
09.07.2011	Audrey Podratz	Monitored trenching 8 feet bgs at Dillon Rd at Melissa Lane. Soils were coarse gravelly sands.	None
09.08.2011	Audrey Podratz	Monitored excavation for installation of box culvert at Dillon Rd & Melissa Lane in inconsistent sandy silt to a depth of 4feet bgs.	None
09.09.2011	Audrey Podratz	Monitored grading at project site of the employee parking lot 6-12 inches bgs. Soils appear native.	None
09.12.2011	Audrey Podratz	Monitored grading at project site of the employee parking lot 6-12 inches bgs, and 3-4 feet along the north and east edge walls. Soils were inconsistent sandy silt with rocks.	None
09.19.2011	Jonathan Riehn	Monitored excavation of T-line trench to a depth of 26 inches bgs. Loose silt, dune sand and granite rocks and pebbles noted.	None

Conditions/LORS Compliance
No instances of non-compliance with the Conditions of Certification or applicable LORS were recorded.

Summary and Conclusions

Cultural resources monitoring took place on September 1, 2, 6, 7, 8, 9, 12 and 19, 2011. At least one CRM and one Native American Monitor were onsite to monitor all ground disturbing activities. No discoveries occurred in the month of September. Ground disturbing activities at CPVS are not anticipated for the near future. Work related to the preparation of archaeological materials from site AE-2204-1 for curation are anticipated to occur in the month of October 2011.

Maureen Kick

Sincerely,

Maureen Kick
Cultural Resources Specialist, CPV Sentinel Generating Station

Attachments: Monitoring Logs

cc: Kathy Rushmore, URS
Maggie Fitzgerald, URS
Mark McDaniels, CPV

Attachment A

Daily Cultural Resources Monitoring Logs
September 2011
CPV Sentinel Energy Project

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 01 Sept 2011 Monitor Name: R.F. Lichtenstein

Weather Conditions: Hot
Hours on Site Not Worked and Reason:
Work Location (Project Component): Dillon Road Laterals Sta 38+85 - 39+10
Work Type (Machine): Mechanical Trenching For Buried Utilities
Depth of Excavation: 8'
Observed Native Soils (Stratigraphy): Bedded Med Coarse Gravelly Sands
Disturbed/Redeposited Soils: ~38+70 - 39+10 0 to 4' Modern Fill
Features:
No Cultural Features Noted

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):

No Artifacts Noted

Assessment of Significance of Any Finds? (As recommended by the CRS):

NA

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):

No Action Taken

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 02 Sept 2011 Monitor Name: R.T. Lichtenstein

Weather Conditions: Hot (100°F) Scattered Clouds Dry Sweet Breeze (3-4 MPH)
Hours on Site Not Worked and Reason:
Work Location (Project Component): Dillon Road / Mesquite Lane
Work Type (Machine): Mechanical Removal Fill Berm along Lane
Depth of Excavation: 8"
Observed Native Soils (Stratigraphy): Brown, Moderately Compact Gravelly Sands
Disturbed/Redeposited Soils: 0-2' Modern Fill South Side of Right-of-Way Interface
Features: Sidecast Mound (Mesquite Lane) Engelmann Fill (VDL Zone)
No Cultural Features Noted

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
No Artifacts Noted

Assessment of Significance of Any Finds? (As recommended by the CRS):
NA

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):
No Action Taken

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG,
CPV SENTINEL ENERGY PROJECT

Date: 9/6/11 Monitor Name: Andrey Podratz

Weather Conditions: Hot - Scattered Clouds
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component): Dillon Rd @ Melissa Lane
Work Type (Machine): Excavator + Loader
Depth of Excavation: 8'
Observed Native Soils (Stratigraphy): inconsistant Coarse gravel +
Disturbed/Redeposited Soils: some backfill areas
Features:
N/A

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
N/A

Assessment of Significance of Any Finds? (As recommended by the CRS):
N/A

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):
No action taken

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 9/7/11 Monitor Name: Audrey Podratz

Weather Conditions: Clear + Hot
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component): Melissa Lane / Dillon Rd
Work Type (Machine): Excavator + Loader
Depth of Excavation: 8' @ corner 5' along Melissa Lane
Observed Native Soils (Stratigraphy): Coarse gravelly sands
Disturbed/Redeposited Soils: no
Features:
None

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
NONE

Assessment of Significance of Any Finds? (As recommended by the CRS):
NONE

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):
No actions taken

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 9/8/11 Monitor Name: Audrey Dodratz

Weather Conditions: Hot
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component): Box culvert @ Dillon Rd + Melissa Lane
Work Type (Machine): excavator, loader
Depth of Excavation: 4'
Observed Native Soils (Stratigraphy): Inconsistant sandy silt
Disturbed/Redeposited Soils: Backfill portions of trench for reversion
Features:
N/A

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
N/A

Assessment of Significance of Any Finds? (As recommended by the CRS):
N/A

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):
N/A

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 9/9/11 Monitor Name: Audrey Podratz

Weather Conditions: Hot 105+
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component): Employee Parking lot prep.
Work Type (Machine): scraper, cat, water truck
Depth of Excavation: 6-12"
Observed Native Soils (Stratigraphy): native inconsistant
Disturbed/Redeposited Soils: N/A
Features:
None

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
None

Assessment of Significance of Any Finds? (As recommended by the CRS):
None

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):

No action taken.

This page can be duplicated and copies completed daily by each CRM.

APPENDIX C
CULTURAL RESOURCES MONITORING LOG, CPV SENTINEL ENERGY PROJECT

Date: 12 Sept 2011 Monitor Name: Audrey Podratz

Weather Conditions: Very warm 95-97°
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component): Employee Parking lot
Work Type (Machine): grading - Cat, scraper, loader, water truck
Depth of Excavation: 6-12 in + 3-4' along N + E edge walls
Observed Native Soils (Stratigraphy): inconsistant sandy/silt w/rocks
Disturbed/Redeposited Soils: none
Features:
None

Artifacts (Isolated? Diagnostic? Greater than 50 years? Exceptional? Include description, provenience, stratigraphic context.):
None

Assessment of Significance of Any Finds? (As recommended by the CRS):
None

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling):
No action taken

Cultural Resources Daily Monitoring Log

CPV Sentinel Project, Date: ___9/19/11_____, Monitor Name: Jonathan Riehn
Weather Conditions: ____Hot, Dry, Windy and High of 93
Hours on Site Not Worked and Reason: N/A
Work Location (Project Component):_Main Project Area Near Fence, T-Line Trench
Work Type (Machine): ____Backhoe, Super Extender_____
Depth of Excavation: ____36 inches; 280ft trench cont. by 84 ft trench and a 64ft trench
Observed Native Soils (Stratigraphy): **Loose silt, Dune Sand, Granite Rocks and Pebbles**

Disturbed/Redeposited Soils: **Dune sand, granite pebbles, gravel pavement**

Features: __**N/A**_____

Artifacts (Isolated? Diagnostic? Greater than 45 years? Exceptional? Include description, provenience, stratigraphic context.):

Nothing significant.

Assessment of Significance of Any Finds?

No Significance

Actions Taken (Halt/Resume Construction; Identification; Notifications; Recommendations; Photography; Collecting; Sampling), Other Observations:

__**None**_____

APPENDIX G
Paleontological Resources Monthly Summary Report

CPV Sentinel Energy Project
Paleontological Resource Monitoring and Mitigation Program

Monthly Progress Report

Project Name: CPV Sentinel Energy Project

Clients: URS Corporation/CPV Sentinel, LLC **Month:** September 2011

Project Paleontologist/Designated Paleontological Specialist: Dr. Lanny H. Fisk, PhD, PG

Monthly Progress Report for September 2011:

During the month of September 2011, PaleoResource Consultants (PRC) continued to work with CPV Sentinel, LLC through their environmental consultants, URS Corporation, to mitigate potential adverse impacts to paleontological resources (fossils) which might result from the construction of the Sentinel Energy Project (Project), located near the City of Desert Hot Springs in Riverside County, California. Activities requiring monitoring during the month of September consisted of trenching for electrical lines along Melissa Road on 01, 02, and 06 through 08 September. These excavation activities disturbed coarse-grained and, occasionally, finer-grained Pleistocene and Holocene age alluvial fan deposits. No significant paleontological resources were encountered during monitoring of these activities.

Six sediment samples collected during June and July were processed for plant microfossils. Three of these samples produced a small but significant number of well-preserved palynomorphs (pollen, spores, etc.). These samples could provide information on the age of the sediments underlying the Project site as well as the climate of the local area during the time that the sediments were deposited. A brief report on these plant microfossils will be included in the final report.

In a letter dated 19 September 2011, Project Paleontological Resource Specialist Dr. Lanny H. Fisk, PhD recommended to CEC that monitoring of Project excavation activities be reduced from full-time because no significant paleontological resources had been encountered and over 50% of Project excavations had been completed (Condition of Certification PAL-5. CEC Compliance Project Manager Dale Rundquist approved Dr. Fisk's recommendation on 21 September.

Other project related activities completed this month included revisions of a draft stratigraphic section, preparation of a monthly progress report, completion of daily monitoring reports, communication with URS and staff, project record keeping, and other management activities

For October, monitoring of Project activities will continue on an as needed basis.

APPENDIX H
Air Quality

AQCM TEMPLATE

Date: September 01, 2011 **Hours of Operation: __6:00_____am** **_2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.3 mph 4.8 mph gusts 82.6 degrees; P.M. low winds 5.4 mph with 9.6 mph gusts from the west, 104.8 degrees, No ppt.

Current Construction Activities (e.g., Grading, Pile-Driving, linear installation, etc.); Sub-contractor laying asphalt paving Melissa Lane with peripheral utility work with water truck support. Sub-contractor using 500-gallon water buffaloes for dust control along Dillon Road trenching.

Approximate Acreage of ground disturbed today: 2 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - 2_____ Other - Dozer and 1 excavators _____

Loader, Roller - _____ Other – Cat 430 Backhoe, Cat D10, 651 Scraper, 824 RTD, Cat D9T _____

Water Trucks - __3 and water pulls_____ Number of Water Loads - __75_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		No paved roads adjacent to project site
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	N/A		No paved roads within the project site (TBD).
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date**__**09 01 2011**_____

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _____

Signature:_____

AQCM TEMPLATE

Date: September 02, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.0 mph 1.2 mph gusts 79.2 degrees; P.M. low winds 1.4 mph with 3.4 mph gusts from the west, 96.8 degrees, No ppt.

Current Construction Activities (e.g., Grading, Pile-Driving, linear installation, etc.); Lay Down area deliver rock base leveled to grade. Plant Site maintainer and scraper leveling grade. Sub-contractor using 500-gallon water buffaloes for dust control along Dillon Road trenching.

Approximate Acreage of ground disturbed today: 6 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _2_____ Fork Lift - _____

Grader - 2_____ Other - Dozer and 1 excavators _____

Loader, Roller - _____ Other – Cat 430 Backhoe, Cat D10, 651 Scraper, 824 RTD, Cat D9T _____

Water Trucks - __3 and 1water pull_____ Number of Water Loads - __75_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Carter B Carter **Date** 09 02 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature: _____

AQCM TEMPLATE

Date: September 06, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.0 mph 1.2 mph gusts 86.0 degrees; P.M. low winds 0.4 mph with 0 mph gusts from the west, 106 degrees, No ppt.

Current Construction Activities (e.g., Grading, Pile-Driving, linear installation, etc.); Lay Down area deliver rock base leveled to grade. Plant Site maintainer and scraper leveling grade. Sub-contractor using 500-gallon water buffaloes for dust control along Dillon Road trenching.

Approximate Acreage of ground disturbed today: 6 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _2_____ Fork Lift - _____

Grader - 2_____ Other - Dozer and 1 excavators _____

Loader, Roller - _____ Other – Cat 430 Backhoe, Cat D10, 651 Scraper, 824 RTD, Cat D9T _____

Water Trucks - __2 _____ Number of Water Loads -__75_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date** ~~09/03/2011~~ 9/6/11

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _____

Signature:_____

AQCM TEMPLATE

Date: September 07, 2011 **Hours of Operation: __6:00____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.0 mph 1.2 mph gusts 86.0 degrees; P.M. low winds 0.4 mph with 0 mph gusts from the west, 106 degrees, No ppt.

Current Construction Activities (e.g., Grading, Pile-Driving, linear installation, etc.); Lay Down area deliver rock base leveled to grade. Plant Site maintainer and scraper leveling grade. Sub-contractor using 500-gallon water buffaloes for dust control along Dillon Road trenching.

Approximate Acreage of ground disturbed today: 6 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _2_____ Fork Lift - _____

Grader - 2_____ Other - Dozer and 1 excavators _____

Loader, Roller - _____ Other – Cat 430 Backhoe, , 651 Scraper, 824 RTD, Cat D9T _____

Water Trucks - __2 _____ Number of Water Loads -__75_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date** ~~09-02-2011~~ 9/7/11

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _____

Signature:_____

AQCM TEMPLATE

Date: September 08, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 6.5 mph 8.1 mph gusts 91.5 degrees; P.M. low winds 6.4 mph with 11.4 mph gusts from the north west, 106.9 degrees, No ppt.

Current Construction Activities; Lay Down area deliver rock base leveled to grade on west side. Plant Site minor excavations for water line and storm drain with dozers leveling grade. Removal of surface from CTG foundations. Sub-contractor using 500-gallon water buffaloes for dust control I Area A along Dillon Road excavation and backfill.

Approximate Acreage of ground disturbed today: 1 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - 2_____ Other - 2 Dozers and 1 excavator _____

Loader, Roller - _____ Other – Cat 430 Backhoe, Cat 345, Cat 160, Cat 950 _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __75_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date**__**09 08 2011**_____

Circle Title **(AQCMM)** **(AQCMM Delegate)**

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _____

Signature:_____

AQCM TEMPLATE

Date: September 09, 2011 **Hours of Operation: __6:00____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.7 mph 2.3 mph gusts 79.4 degrees; P.M. low winds 1.2 mph with 2.1 mph gusts from the north west, 104.4 degrees, No ppt.

Current Construction Activities; Lay Down area deliver rock base leveled to grade on west side. Plant Site minor excavations for water line and storm drain with dozers leveling grade. Grading in new Parking area. Sub-contractor using 500-gallon water buffaloes for dust control I Area A along Dillon Road excavation and backfill.

Approximate Acreage of ground disturbed today: 1 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _1_____ Fork Lift - _____

Grader - 2_____ Other - 2 Dozers and 1 excavator _____

Loader, Roller - _____ Other – Cat 430 Backhoe, Cat 345, Cat 160, Cat 950 _____

Water Trucks - __3 and 0 water pull_____ Number of Water Loads - __85_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature _____ **Date**__**09 09 2011**_____

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _09 09 11_____

Name: _Bob Linder; Temporary shut down for lack of water truck support for scraper grading New Parking area. Contractor brought in a new water truck to support operations in compliance.

AQCM TEMPLATE

Date: September 12, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 0.8 mph 1.4 mph gusts 73.9 degrees; P.M. low winds 2.4 mph with 3.8 mph gusts from the north west, 105.1 degrees, No ppt.

Current Construction Activities; Plant Site minor excavations for water line, manholes, and storm drain. Scraper and maintainer grading in new Parking area. Sub-contractor using 500-gallon water buffaloes for dust control working at new office complex. Sub-contractor fencing along Melissa Lane. Utility crew removing rocks from Fill Area 1 & 2.

Approximate Acreage of ground disturbed today: 1 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _1__(half Day)_____ Fork Lift - _____

Grader - Cat 16G_____ Other - 2 Dozers and 1 excavator _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B, Cat 345C, Cat D5K _____

Water Trucks - __3 and 0 water pull_____ Number of Water Loads - __85_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date**__**09 12 2011**_____

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

AQCM TEMPLATE

Date: September 13, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 2.5 mph 3.3 mph gusts 76.7 degrees; P.M. low winds 0.8 mph with 1.8 mph gusts from the north west, 75.9 degrees, Precipitation intermittent < 0.1-inches.

Current Construction Activities: Parking Area Rubber Tire Dozer leveling and grading truck loads of laid road base.

Approximate Acreage of ground disturbed today: 3 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - ___(half Day)_____ Fork Lift - _____

Grader - Other - 1 Dozers _____

Loader - _____ Other _____

Water Trucks - __0 and 0 water pull_____ Number of Water Loads - __0_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project. **Signature** _____ **Date** **09 13 2011** **Circle Title (AQCMM) (AQCMM Delegate)**			

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

AQCM TEMPLATE

Date: September 14, 2011 **Hours of Operation: __6:00____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 0.0 mph 0.8 mph gusts 72.1 degrees; P.M. low winds 1.1 mph with 1.3 mph gusts from the north west, 85.6 degrees, No ppt.

Current Construction Activities; Plant Site minor excavations for water line, manholes, and storm drain. Maintainer grading in new Parking area. Final grading of Lay Down areas. Utility crew removing rocks from Fill Area 1 & 2 and magnetic roller picking up nails and metallic debris.

Approximate Acreage of ground disturbed today: 2 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - 2 Dozers and 1 excavator _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B (idle), Cat 345C, Cat 414E _____

Water Trucks - __3 and 0 water pull_____ Number of Water Loads - __85_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** 09 14 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

AQCM TEMPLATE

Date: September 15, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 2.2 mph 3.4 mph gusts 73.9 degrees; P.M. low winds 5.5 mph with 10.5 mph gusts from the south, 93.3 degrees, No ppt.

Current Construction Activities; Plant Site minor excavations for water line, manholes, and storm drain. Maintainer completes final grading in new Employee Parking area. Final grading of Lay Down areas. Utility crew removing rocks from Fill Area 1 & 2 and use magnetic roller to pick up nails and metallic debris.

Approximate Acreage of ground disturbed today: 2 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - 2 Dozers and 1 excavator _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B (idle), Cat 345C, Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __60_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** 09 15 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

AQCM TEMPLATE

Date: September 16, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) **During the Day: A.M. calm winds 0.0 mph 1.0 mph gusts 79.5 degrees; P.M. low winds 6.8 mph with 10.4 mph gusts from the south, 94.1 degrees, No ppt.**

Current Construction Activities; Plant Site minor excavations for catch basins, manholes, and storm drain. Utility crew removing rocks from Fill Area 1 & 2 and using a magnetic roller to pick up nails and metallic debris. Maintainer grading #2 gravel around office trailer complex and warehouse yard area.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - 2 Dozers and 1 excavator _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B (idle), Cat 345C, Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __60_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** **09 16 2011**

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

AQCM TEMPLATE

Date: September 19, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.4 mph 2.4 mph gusts 85.4 degrees; P.M. low winds 1.9 mph with 2.5 mph gusts from the south, 99.4 degrees, No ppt.

Current Construction Activities; Plant Site excavations for catch basins, manholes for storm drain. Utility crew removing rocks from foundation areas. Maintainer and Dozer remedial grading around office trailer complex. Trench excavation along Employee Parking fence line.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B (idle), Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __32_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checkiug Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature_____ **Date**__**09 19 2011**_____

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

Signature:_____

AQCM TEMPLATE

Date: September 20, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.9 mph 2.9 mph gusts 77.5 degrees; P.M. low winds 6.0 mph with 8.3 mph gusts from the south, 104 degrees, No ppt.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Maintainer and Dozer remedial grading around office trailer complex. Trench excavation along Employee Parking fence line and from trailer office complex downhill to junction box on southmost Plant Site.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __30_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	

All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** 09 20 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name: _

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

0.8AQCM TEMPLATE

Date: September 21, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 0.8 mph 1.4 mph gusts79.7 degrees; P.M. low winds 2.2 mph with 4,4 mph gusts from the south, 104.5 degrees, No ppt.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Maintainer and Dozer remedial grading around office trailer complex. Trench excavation along Employee Parking fence line and from trailer office complex downhill to junction box on southmost Plant Site.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __34_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** **09 21 2011**

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: 09 21 11

Name: Bob Linder; SUKUT 4000-gallon water truck disabled for half day. Maintenance scheduled for tomorrow AM. Truck shall be replaced if not repaired. Otherwise only one 2000-gallon capacity truck is in service today. There were no adverse results from this reduction in water truck support.

Signature:_____

0.8AQCM TEMPLATE

Date: September 22, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.4 mph 2.9 mph gusts79.2 degrees; P.M. low winds 3.4 mph with 5.8 mph gusts from the south, 107 degrees, No ppt.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Trench backfill along Employee Parking fence line. Foundation contractor excavations for concrete pour operations.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __1 and 1 for half day _____ Number of Water Loads - __36_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Bob A. Linder **Date** **09 22 2011**

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: 09 22 11

Name: Bob Linder; SUKUT 4000-gallon water truck disabled AM then maintained for appropriate water support operations.

Signature:

0.8AQCM TEMPLATE

Date: September 23, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 2.4 mph 4.8 mph gusts 85.9 degrees; P.M. low winds 4.2 mph with mph 9.0 gusts from the south, 104.7 degrees, Thunderstorms from 11:00 AM forecast 20%.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Trench backfill along Employee Parking fence line. Foundation contractor pumping concrete AM.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __38_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).

Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** 09 23 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name:

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

0.8AQCM TEMPLATE

Date: September 26, 2011 **Hours of Operation:** __6:00_____am _2:30_____pm

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 6.0 mph 9.9 mph gusts 70.8 degrees; P.M. low winds 1.3 mph with mph 2.7 gusts from the south, 100.2 degrees.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Employee Parking area and Lay Down area; geotextile fabric and #2 gravel laid with maintainer grading.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating;

Scraper - _____ **Fork Lift -** _____

Grader - Cat 16G_____ **Other -** _____

Loader Cat 950G _____ **Other – Cat 430 Backhoe, Cat 345B , Cat 414E** _____

Water Trucks - __2 and 0 water pull_____ **Number of Water Loads -** __38_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project. **Signature** _____ **Date** **09 26 2011** **Circle Title (AQCMM) (AQCMM Delegate)**			

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name:

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

0.8AQCM TEMPLATE

Date: September 27, 2011 **Hours of Operation:** __6:00____am _2;30_____pm

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.2 mph 2.9 mph gusts 78.3 degrees; P.M. low winds 1.3 mph with 2.3 mph gusts from the south, 98.9 degrees.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Employee Parking area and Lay Down area: geotextile fabric and #2 gravel lay with maintainer grading.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ **Fork Lift -** _____

Grader - Cat 16G_____ **Other -** _____

Loader Cat 950G _____ **Other – Cat 430 Backhoe, Cat 345B , Cat 414E** _____

Water Trucks - __2 and 0 water pull_____ **Number of Water Loads -** __40_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature _____ **Date** 09 27 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center
Date: 09 28 11
Name: Bob Linder,

Martha Thomas AQMD Air Quality Inspector from the South Coast Air Quality District Martha Thomas paid a visit to the CPV Sentinel Energy Project to inspect two generators and was provided copies of the Statewide Portable Equipment Registration issued by the California Environmental Protection agency. The registration Number 154532 and 142079 are printed on the Permit documents and copies were provided. The general project layout was observed and she did not communicate any issues with activities at the project site. She volunteered to email Bob Linder any questions regarding inspection or record keeping.

0.8AQCM TEMPLATE

Date: September 28, 2011 **Hours of Operation: __6:00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.3 mph 4.3 mph gusts 76.8 degrees; P.M. low winds 5.7 mph with 7.0 mph gusts from the east, 96.1 degrees.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation areas. Employee Parking area and Lay Down area: geotextile fabric and #2 gravel lay with maintainer grading.

Approximate Acreage of ground disturbed today: <4 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __40_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project. **Signature:** Robert A. Linder **Date** 09 28 2011 **Circle Title (AQCMM) (AQCMM Delegate)**			

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name:

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

0.8AQCM TEMPLATE

Date: September 29, 2011 **Hours of Operation: __6;00_____am _2:30_____pm**

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 0.9 mph 3.8 mph gusts 75.2 degrees; P.M. low winds 1.9 mph with 5.6 mph gusts from the east, 105.6 degrees.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation area and Lay Down area. Geotextile fabric and #2 gravel lain with maintainer grading in Lay Down.

Approximate Acreage of ground disturbed today: <3 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ Fork Lift - _____

Grader - Cat 16G_____ Other - _____

Loader Cat 950G _____ Other – Cat 430 Backhoe, Cat 345B , Cat 414E _____

Water Trucks - __2 and 0 water pull_____ Number of Water Loads - __40_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project. **Signature** _____ **Date** 09 29 2011 **Circle Title (AQCMM) (AQCMM Delegate)**			

Field Notes

Project Name: Sentinel Energy Center

Date: _____

Name:

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

Signature:_____

0.8AQCM TEMPLATE

Date: September 30, 2011 **Hours of Operation:** __6:00_____am _2:30_____pm

Form Completed by (AQCMM or Delegate): Robert A. Linder

Site Conditions (e.g., calm windy) During the Day: A.M. calm winds 1.6 mph 2.8 mph gusts 81.4 degrees; P.M. low winds 0.8 mph with mph 2.0 gusts from the east, 92.8 degrees.

Current Construction Activities; Plant Site excavations for catch basins and manholes for storm drain system. Utility crew removing rocks from foundation area and Lay Down area. Geotextile fabric and #2 gravel lain with maintainer grading in Lay Down.

Approximate Acreage of ground disturbed today: <3 acres

Quantity, Model #, Serial # of Equipment Operating:

Scraper - _____ **Fork Lift -** _____

Grader - Cat 16G_____ **Other -** _____

Loader Cat 950G _____ **Other – Cat 430 Backhoe, Cat 345B , Cat 414E** _____

Water Trucks - __1 and 0 water pull_____ **Number of Water Loads -** __30_____

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved roads and disturbed areas in the project and linear construction sites shall be watered as frequently as necessary to comply with the dust mitigation objectives.	Yes	Monitored	
No vehicle shall exceed 10 miles per hour within the construction site, with the exception that vehicles may travel up to 25 miles per hour on stabilized unpaved roads.	Yes	Monitored	
The construction site entrances shall be posted with visible speed-limit signs.	Yes	Monitored	
All construction vehicle tires shall be inspected and washed as necessary to be cleaned free of dirt prior to entering paved roadways.	N/A		No paved roads adjacent to project site (TBD).
Gravel ramps at least 20 feet in length must be provided at the tire washing/cleaning station.	N/A		No paved roads adjacent to project site

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All unpaved exits from the construction site shall be graveled or treated to prevent track-out to public roadways.	Yes	Monitored	
All construction vehicles shall enter the construction site through the treated entrance roadways, unless an alternative route has been submitted to and approved by the CPM.	Yes	Monitored	
Construction areas adjacent to any paved roadway shall be provided with sandbags or other measures as specified in the Storm Water Pollution Prevention Plan (SWPPP) to prevent run-off to roadways.	N/A		New paved road does not reach Dillon Road.
All paved roads within the construction site shall be swept daily (or less during periods of precipitation) on days when construction activity occurs to prevent the accumulation of dirt and debris.	Yes	Monitored	New paved road within the project site swept.
At least the first 500 feet of any public roadway exiting from the construction site shall be swept at least twice daily (or less during periods of precipitation) on days when construction activity occurs or on any other day when dirt or runoff from the construction site is visible on the public roadways. Track out extending more than 25 feet (cumulative) from any site access point will be removed.	Yes	Monitored	
All soil storage piles that remain inactive for longer than 10 days shall be covered, or shall be treated with appropriate dust suppressant compounds.	Yes	N/A	Nothing on site inactive for >10 days
All vehicles that are used to transport solid bulk material on public roadways and that have potential to cause visible emissions shall be provided with a cover, or the materials shall be sufficiently wetted and loaded onto the trucks in a manner to provide at least 2 feet of freeboard.	N/A		No bulk transported on roadways
Wind erosion control techniques (such as windbreaks, water, chemical dust suppressants, and/or vegetation) shall be used on all construction areas that may be disturbed. Any windbreaks installed to comply with this measure/condition shall remain in place until the soil is stabilized or permanently covered with vegetation.	Yes	Inspected	Water application for worker eye protection

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
Signage that identifies 24-hour manned phone numbers for dust complaints shall be installed and maintained on each side of the Project area and within 50 feet of the Project site boundary. The telephone number listed for the developer contact must be a local or a toll-free number and manned 24 hours a day, 7 days per week.	Yes	Monitored	
A copy of AQCMP must be on site and available to workers and SCAQMD employees. All work on the site is subject to the requirements of the approved Dust Control Plan. Failure to abide by the Plan by anyone on site may be subject to enforcement action.	Yes	Monitored	
All construction activities for visible dust plumes are monitored. Observations of visible dust plumes that are 100 feet in length, 20 percent opacity, or have the potential to be transported: (1) off the Project site or (2) 200 feet beyond the center line of the construction of linear facilities; or (3) within 400 feet upwind of any regularly occupied structures not owned by the Project owner indicate that existing mitigation measures are not resulting in effective mitigation. In the event that such visible dust plumes are observed, implement a more intensive application of existing mitigation methods within 15 minutes of making such a determination.	Yes	Monitored	No dust plumes observed.
If the above fails, direct an implementation of additional methods of dust suppression to result in adequate mitigation within 30 minutes of the original determination.	NA		
Direct a temporary shutdown of activity causing the emissions if the additional dust suppression methods above fail to result in effective reduction of dust within 1 hour of the original determination. Activity will not restart until appropriate additional mitigation/other site conditions have changed such that visual dust plumes will not result upon restarting the shutdown fugitive dust source. The owner/operator may appeal to the CPM directive to shut down activity, provided that shutdown shall go into effect within 1 hour of the original determination, unless the CPM overrules appeal before that time.	N/A		

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant
All diesel-fueled engines used in the construction of the facility shall have clearly visible tags issued by the on-site AQCMM showing that the engine meets the conditions set forth herein.	Yes	Monitored	All vehicles have tags
All construction diesel engines with a rating of 50 hp or more shall meet, at a minimum, the Tier 3 California Emission Standards for Off-Road Compression-Ignition Engines, as specified in California Code of Regulations, Title 13, section 2423(b)(1) unless a good-faith effort to the satisfaction of the —certified by the on-site AQCMM—demonstrates that such engine is not available for a particular item of equipment. In the event that a Tier 3 engine is not available for any off-road equipment larger than 50 hp, that equipment shall be equipped with a Tier 2 engine, or an engine that is equipped with retrofit controls to reduce exhaust emissions of nitrogen oxides (NO_X) and diesel particulate matter (DPM) to no more than Tier 2 levels, unless certified by engine manufacturers or the on-site AQCMM that the use of such devices is not practical for specific engine types.	Yes	Monitored	All applicable vehicles have been checked
The use of a retrofit control device may be terminated immediately, provided that the CPM and AO are informed within 10 working days of the termination, and that a replacement for the equipment item in question meeting the controls required above occurs within 10 days of termination of use, if the equipment would be needed to continue working at this site for more than 15 days after use of the retrofit control device is terminated.	N/A		
All heavy earthmoving equipment and heavy-duty construction-related trucks with engines meeting the above requirements shall be properly maintained, and the engines tuned to the engine manufacturer's specifications.	Yes	Contact with owner	
All diesel heavy construction equipment shall not remain running at idle for more than 5 minutes, to the extent practical. Vehicles that need to idle as part of their normal operation (such as concrete trucks) are exempted from this requirement.	Yes	Monitored	

Required Mitigation	Activities in Compliance?	Method of Checking Compliance	Explanation and Actions Taken if Non-Compliant

I confirm that the information presented above accurately represents mitigation measures for control of air pollutant emissions for this day of the construction project.

Signature Robert A. Linder **Date** 09 30 2011

Circle Title (AQCMM) (AQCMM Delegate)

Field Notes

Project Name: Sentinel Energy Center
Date: 09 30 11
Name: Bob Linder; New sub-contractor Cattrac has brought in a water truck to support scraper mass grading and leveling in the Plant Site. Truck loads total includes 1-SUKUT and 1-Cattrac. SUKUT had one truck become disabled at the start of the work shift.

Signature:

CPV Sentinel Energy Project Site
Long Term Equipment
September 2011

Water Trucks

Sub ID	Brand	Type	CARB/License Tag	F/R	Model	Engine Type	URS ID	Arrive on-site	Leave Site
B+B Equipment	Mack	Water Truck	550477 (CA plate)	R		On-Road	0162	7-Jun-11	7-Sep-11
B+B Equipment	Freightliner	Water Truck	8M46367 (CA plate)	R		On-Road	0161	9-Jun-11	12-Jul-11
Bertha Water Trucks	Freightliner	Water Truck	478674 (CA plate)	R		On-Road	0018	9-Jun-11	
Johnson Equipment	Freightliner	Water Truck	8F05800 (CA plate)	R		On-Road	0115	5-Jul-11	5-Aug-11
Western Rentals	Freightliner	Water Truck	567428 (CA plate)	R		On-Road	0173	20-Jul-11	15-Sep-11
Rental	Peterbuil	Water Truck	576180 (CA plate)	R		On-Road	0165	29-Aug-11	

Rental Equipment

Sub ID	Brand	Type	CARB/License Tag	F/R	Model	Engine Type	URS ID	Arrive on-site	Leave Site
RJ &J	Case	Excavator	BK6P56	F/R	E60	Tier 3	0190	29-Jul-11	16-Aug-11
RJ&J	Case	Front End Loader	DA7M75	F/R	580	Tier 3	0189	29-Jul-11	
RJ&J	Case	Front End Loader	FA4U95	F/R	821C	Tier 3	0240	5-Aug-11	25-Aug-11
RJ&J	Case	Front End Loader	FP3G85	F/R	580 Super	Tier 3	0198	16-Aug-11	
RJ&J	ZAXIS	Excavator	SE8D78	F/R	E136	Tier 3	0182	29-Aug-11	
RJ&J	Ingersoll-Rand	Sheeps Foot	XB9P36	R	088-05-6008	Tier 3	0206	23-Aug-11	26-Aug-11

PW1 Generator

Sub ID	Brand	Type	CARB/DMV Tag	F/R	Model	Engine Type	URS ID	Arrive on-site	Leave Site
Rental	Isuzu	Generator	142079 (PERP)	NA	6WG1X	Tier 3	0081	13-Jul-11	
Rental	Isuzu	Generator	154532	NA	DF-44001	Tier 3	0010	1-Sep-11	

Sukut Equipment

Sub ID	Brand	Type	CARB/DMV Tag	F/R	Model	Engine Type	URS ID	Arrive on-site	Leave Site
430-01	CAT	Backhoe	DH7W39	F	430	Tier 2	0019	1-Jun-11	19-Sep-11
90-33	CAT	Dozer	HV5D73	F	D9T	Tier 3	0002	8-Jun-11	15-Aug-11
Rental	CAT	Excavator	AW4499	F	329D6	Tier 2	0033	7-Jun-11	8-Aug-11
24-18	CAT	Rubber Tire Dozer	AG6C65	F	A24	Tier 3	0003	7-Jun-11	7-Sep-11
51-45	CAT	Water Pull	YC4X44	F	651E	Tier 3	0001	10-Jun-11	7-Sep-11
T1055-101	CAT	Forklift	KY3W36	F	TL1055	Tier 2	0034	7-Jun-11	5-Aug-11
Rental	CAT	Motor Grader	BU3S35	F	140H	Tier 3	0083	16-Jun-11	7-Sep-11
10-40	CAT	Dozer	BJ6R55	F	D10N	Tier 3	0147	17-Jun-11	5-Aug-11
51-52	CAT	Scraper	DD8V84	F	651B	Tier 3	0146	16-Jun-11	7-Sep-11
51-75	CAT	Scraper	WY4U67	F	651B	Tier 3	0113	17-Jun-11	23-Aug-11
51-69	CAT	Scraper	NK6U99	F	651B	Tier 3	0129	16-Jun-11	29-Aug-11
51-79	CAT	Scraper	FC9W49	F	651B	Tier 3	0130	20-Jun-11	9-Sep-11
51-62	CAT	Scraper	UB6X73	F	651B	Tier 3	0131	17-Jun-11	9-Sep-11
DZD4K-002	CAT	Dozer	TN4J44	F	D4K	Tier 3	0082	5-Jul-11	7-Sep-11
10-24	CAT	Dozer	KC3R76	F	D10N	Tier 3	0114	20-Jun-11	9-Sep-11
Rental	CAT	Dozer Rock Bucket	K68E76	F	950G	Tier 2	0174	19-Jul-11	
51-83	CAT	Water Pull	CF4M43	F	651B	Tier 3	0175	22-Jul-11	9-Sep-11
Rental Miller-Blades	CAT	Roller	UL6L85	F	CV-120	On Road	0192	19-Jul-11	2-Sep-11
Rental Miller-Blades	CAT	Scraper	FW6W46	F	613	Tier 3	0176	27-Jul-11	2-Sep-11
51-50	CAT	Scraper	VN7R68	F	651 B	Tier 3	0207	18-Jul-11	12-Sep-11
10-11	CAT	Dozer	TG3K55	F	10-29	Tier 3	0223	22-Jul-11	7-Sep-11
Rental/Gemma	Genie	Forklift	PK4G83	F	GTH-1056	Tier2	0239	29-Jul-11	
Rental	John Deere	Dozer	YT6B64	F	844	Tier 3	0205	1-Aug-11	3-Aug-11
Rental	Komatsu Rental	Dozer Rock Bucket	TBD-SUKUT ?	F	WA450-3F	Tier 3	0191	5-Aug-11	9-Aug-11
Miller-Blades	CAT	Maintainer	VX6L67	F	16G	Tier 3	0230	8-Aug-11	7-Sep-11
Miller-Blades	CAT	Vermeer/bore rig	TJ8N46	R	24x40 A	NA	0246	8-Aug-11	8-Aug-11
Sukut Equipment	John Deere	Dozer	AM5M46	F	450T	Tier 3	0214	17-Aug-11	7-Sep-11
Miller-Blades	CAT	Maintainer	HM5E53	F	MT140H	Tier 3	0241	23-Aug-11	2-Sep-11
Rental EX 321-901	CAT	Excavator	EB5N75	F	321 D	Tier 3	0238	23-Aug-11	7-Sep-11
Rental	CAT	Excavator	HM3M43	F	345C	Tier3	0221	24-Aug-11	15-Sep-11
Rental	CAT	Excavator	EG9W95	F	345B	Tier3	0245	6-Sep-11	
Rental	CAT	Back/Loader	GH8F39	F	420E	Tier3	0237	19-Sep-11	
Rental	CAT	Dozer	SW8U63	F	D5K xl	Tier3	0244	19-Sep-11	
Rental	CAT	Loader/Dozer	KF6F93	F	414E	Tier3	0228	19-Sep-11	
Rental	CAT	Maintainer	SC5M77	F	16G	Tier3	0229	7-Sep-11	

Griffith Company

Rental	Ingersoll-Rand	Fork Lift	VA5E67	F	VR-843C	Tier3	0212	19-Sep-11	21-Sep-11
Rental	Case	Backhoe/Loader	PF9V55	F	590-05	Tier3	0181	20-Sep-11	21-Sep-11
Rental	JLG(97296)	Fork Lift	MY8B94	R	10054	Tier3	0180	21-Sep-11	28-Sep-11
Rental	Skyjack	Fork Lift	AH8S98	R	10G12	Tier3	0012	29-Sep-11	
Rental	Gradall	Fork Lift	TBD	R	5444D-10	Tier3	0011	29-Sep-11	

CATTRAC

Rental	CAT	Scraper	AP5J87	F	2302	Tier3	0039	30-Sep-11	
Rental	CAT	Maintainer	TN9K63	F	140H	Tier3	0057	30-Sep-11	
Rental	John Deer	Skip Loader	CX8G94	F	210LE	Tier2	0041	30-Sep-11	
Rental	Paystar 5000	Water Truck	CA 535427	F		On Road	0040	30-Sep-11	
Rental	CAT	Front End Loader	UV8P43	R	216B	? TBD	0164	29-Aug-11	

Sukut Construction, Inc.
CPV Sentinel Energy Project

September 2011 Fuel Report

Date	Fuel Delivered (Gallongs)
09/01/11	151
09/02/11	222
09/06/11	455
09/07/11	136
09/08/11	388
09/09/11	318
09/12/11	192
09/13/11	64
09/14/11	193
09/15/11	195
09/16/11	138
09/19/11	305
09/20/11	344
09/21/11	198
09/22/11	344
09/23/11	195
09/26/11	380
09/27/11	423
09/28/11	317
09/29/11	342
09/30/11	141
Total	5,441

Steven J. Reiser
Project Manager
Sukut Construction, Inc.

URS Corporation
Attn. Anne Runnalls
4225 Executive Square, Suite 1600
La Jolla, CA 92037

09 30 11

Re: CSEP Site Diesel Equipment

Dear Ms. Runnalls,

For site work construction at the CPV Sentinel Energy Project, LLC (CSEP) site, Sukut Construction will use the following diesel-powered equipment:

1.) CAT Excavator URS # 0245
2.) CAT Dozer Rock Bucket URS# 0174
3.) CAT Excavator URS# 0238
4.) CAT Bucket Loader URS # 0237
5.) CAT Dozer URS # 0244
6.) CAT Loader/Dozer URS # 0228
7.) CAT Maintainer URS # 0229

This equipment arrived at the CSEP site starting 07 01 11 and is scheduled to be on-site off and on through October 2011. All off-road equipment exceeding 100 hp is outfitted with Tier 2 or better engines.

As for maintenance, Sukut Equipment certifies that it maintains its equipment on a regular basis to factory specifications.

All diesel fuel sold in California is ultra-low sulfur diesel. Since Sukut Equipment will not be moving its equipment out of state, all fuel purchased for utilization on this project will be ultra-low sulfur diesel.

Name: STEVEN REISIG Date: 9/29/11

Company: SUKUT CONST. INC. Title: PROJECT MANAGER

URS Corporation
Attn. Anne Runnalls
4225 Executive Square, Suite 1600
La Jolla, CA 92037

09 30 11

Re: CSEP Site Diesel Equipment

Dear Ms. Runnalls,

For site work construction at the CPV Sentinel Energy Project, LLC (CSEP) site, RJ&J Construction will use the following diesel-powered equipment:

1.) Case Front End Loader URS# 0189
2.) Case Front End Loader URS# 0198
3.) ZAXIS Excavator URS# 0182

This equipment arrived at the CSEP site starting 08 29 11 and is scheduled to be on-site off and on through October 2011. All off-road equipment exceeding 100 hp is outfitted with Tier 2 or better engines.

As for maintenance, RJ&J Equipment certifies that it maintains its equipment on a regular basis to factory specifications.

All diesel fuel sold in California is ultra-low sulfur diesel. Since RJ&J Equipment will not be moving its equipment out of state, all fuel purchased for utilization on this project will be ultra-low sulfur diesel.

Regards

Name: Mike Ivy Mike Ivy Date: 9-29-11

Company: Morrow-Meadows Corp. Title: G.F.

URS Corporation
Attn. Anne Runnalls
4225 Executive Square, Suite 1600
La Jolla, CA 92037

09 30 11

Re: CSEP Site Diesel Equipment

Dear Ms. Runnalls,

For site work construction at the CPV Sentinel Energy Project, LLC (CSEP) site, Pacific Coast Steel will use the following diesel-powered equipment:

1. Gradall Forklift URS # 001109 30 11

This equipment arrived at the CSEP site starting and is scheduled to be on-site off and on through October 2011. All off-road equipment exceeding 100 hp is outfitted with Tier 2 or better engines.

As for maintenance, Pacific Coast Steel certifies that it maintains its equipment on a regular basis to factory specifications.

All diesel fuel sold in California is ultra-low sulfur diesel. Since Pacific Coast Steel will not be moving its equipment out of state, all fuel purchased for utilization on this project will be ultra-low sulfur diesel.

Regards

Name: Ronnie Grace Date: 9/30/11

Company: _____ Title: SUPERINTENDENT

URS Corporation
Attn. Anne Runnalls
4225 Executive Square, Suite 1600
La Jolla, CA 92037

09 30 11

Re: CSEP Site Diesel Equipment

Dear Ms. Runnalls,

For site work construction at the CPV Sentinel Energy Project, LLC (CSEP) site, Griffith Company will use the following diesel-powered equipment:

1.) Skyjack Forklift URS# 0012

This equipment arrived at the CSEP site starting September 29th and is scheduled to be on-site off and on through October 2011. All off-road equipment exceeding 100 hp is outfitted with Tier 2 or better engines.

As for maintenance, Griffith Company certifies that it maintains its equipment on a regular basis to factory specifications.

All diesel fuel sold in California is ultra-low sulfur diesel. Since Griffith Company will not be moving its equipment out of state, all fuel purchased for utilization on this project will be ultra-low sulfur diesel.

Regards

Name: Ronnie Grace Date: 9/30/11

Company: _____ Title: Superintendent
