OCCIDENTAL OF ELK HILLS INC

365X-35S

Event: NOI - WORKOVER
Event End:
Sec. Reason:

Ground Level: 670.4ft
Datum: ORIGINAL KB @ 693.40ft (default)
API No.: 0403022597

Wellbore: ORIGINAL HOLE
PBMD: 7,084.0ft
Btm TMD: 7,675.0ft
Spud Date: 6/14/2003 00:00
BH Coord X: 6,154,029.81uss ft
BH Coord Y: 2,289,120.97uss ft

Casing Shoes (ft) | Schematic (8/1/2006) | Openings Top/Btm/Type/Status

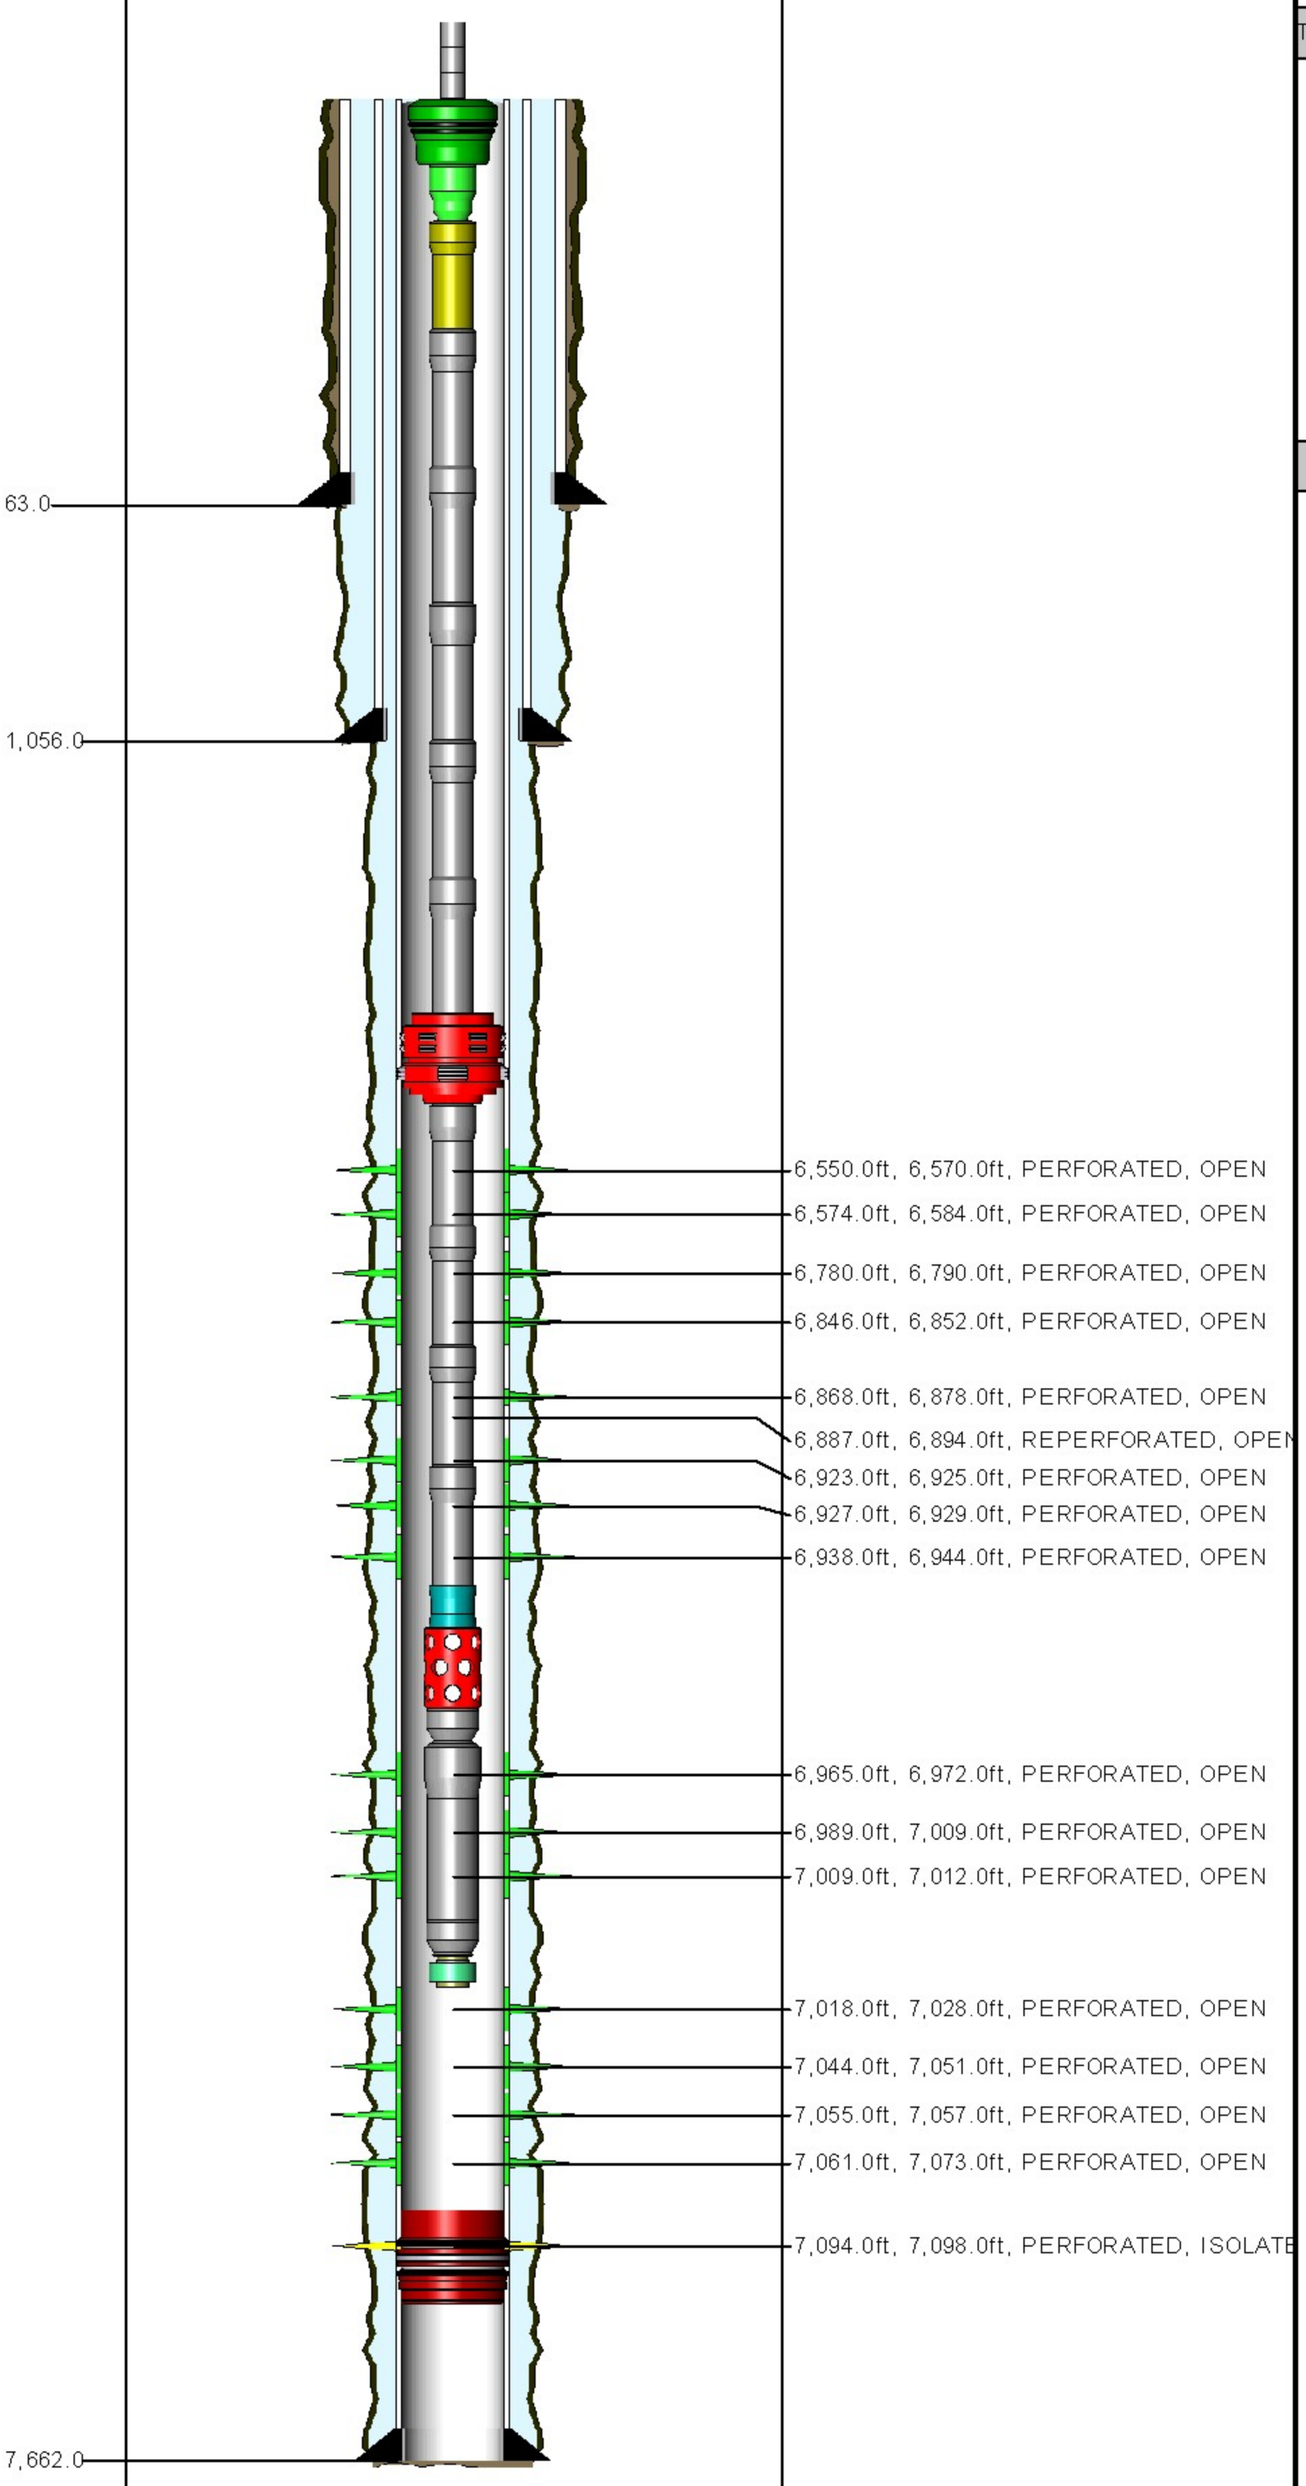

ROD STRING Report Date: 7/21/2006 00:00

Component	Top MD (ft)	Btm MD (ft)
POLROD	0.0	30.0
PNYROD	30.0	44.0
ROD	44.0	2,534.0
ROD	2,534.0	5,054.0
R-4PER	5,054.0	6,854.0
RSTBAR	6,854.0	6,858.0
INSPMP	6,858.0	6,882.0

TUBING STRING Report Date: 11/19/2004 00:0

Component	Top MD (ft)	Btm MD (ft)
TH-D	23.0	23.8
FATNIP	23.8	24.5
PUPJNT	24.5	28.9
TBGJNT	28.9	5,907.6
AC	5,907.6	5,910.0
TBGJNT	5,910.0	6,946.0
STNIP	6,946.0	6,947.1
PERFJT	6,947.1	6,951.1
XO	6,951.1	6,952.3
TBGJNT	6,952.3	7,015.8
XO	7,015.8	7,016.9
PRGVLV	7,016.9	7,017.8

PLUG BACK Report Date: 8/22/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
BRP	7,084.0	7,115.6

CONDUCTOR CASING Report Date: 6/11/2003 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	14.000			23.0	63.0

SURFACE CASING Report Date: 6/15/2003 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	36.00	23.0	1,010.2
	9.625	K-55	36.00	1,010.2	1,010.2
CASING JOINT(S)	9.625	K-55	36.00	1,010.2	1,054.8
GUIDE SHOE	9.625	K-55	36.00	1,054.8	1,056.0

PRODUCTION CASING Report Date: 6/26/2003 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	23.0	40.0
PUP JOINT	7.000	N-80	26.00	40.0	55.0
CASING JOINT(S)	7.000	N-80	26.00	55.0	7,288.1
FLAG JOINT	7.000	N-80	26.00	7,288.1	7,308.1
CASING JOINT(S)	7.000	N-80	26.00	7,308.1	7,570.9
FLOAT COLLAR	7.000	N-80	26.00	7,570.9	7,572.5
CASING JOINT(S)	7.000	N-80	26.00	7,572.5	7,660.2
FLOAT SHOE	7.000	N-80	26.00	7,660.2	7,662.0

Well: 365X-35S S/T/R: 36/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol.: 644 cf
Hole Size: 12.25
Top Job: no
Rtns to Sfc: 39 cf
TOC: sfc
- - -

Interm Csg. Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -

Prod. Csg. Cmt Vol.: 1576 cf
Hole Size: 9.875
Top Job: no
Rtns to Sfc: 0
TTOC: 1706 '
- - -

Liner Cmt Vol.:
Hole Size:
Top Job:
Rtns to Sfc:
TOC:
- - -
Top of Formation:
UBA: 7090'
BLW: 7564'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
JEP
